


APPENDIX 7

**CONTWOYTO LAKE
REMEDICATION PROJECT**

PROJECT SCHEDULE

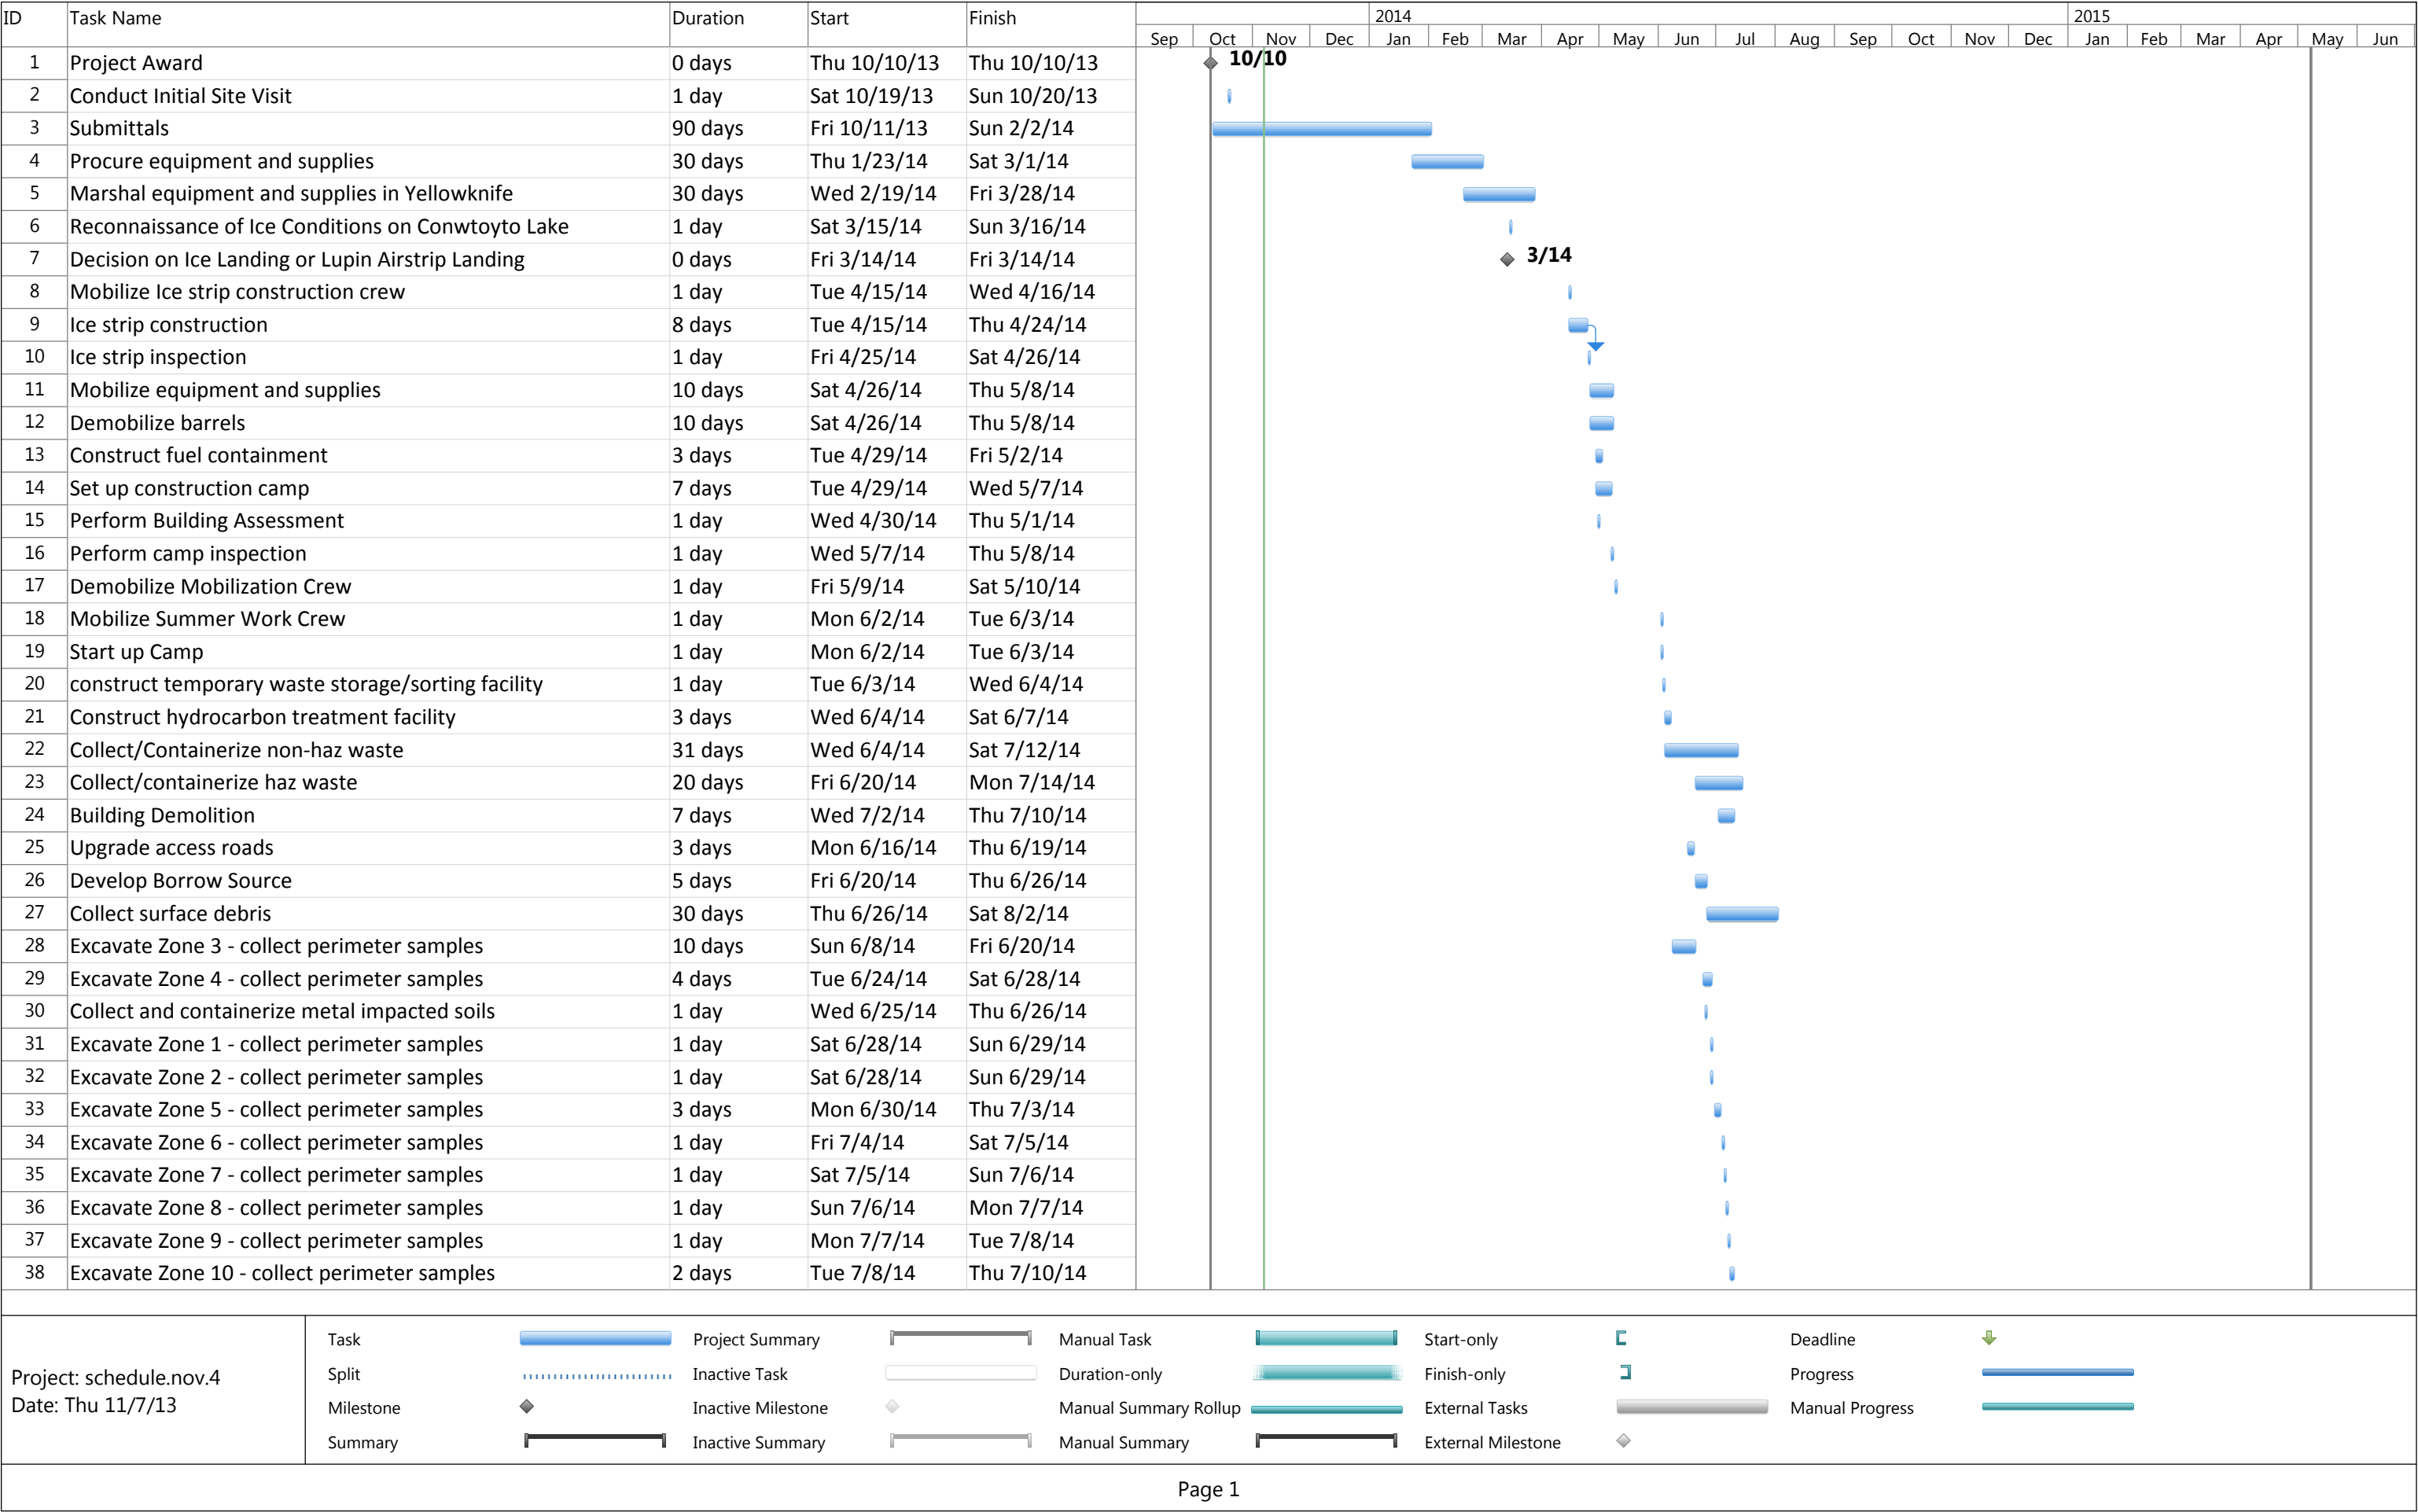

ID	Task Name	Duration	Start	Finish	2014				2014												2015					
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
39	Obtain all zone confirmation samples	25 days	Wed 6/18/14	Sat 7/19/14																						
40	Backfill excavations	30 days	Tue 6/24/14	Thu 7/31/14																						
41	Treat Hydrocarbons	60 days	Tue 6/17/14	Sat 8/30/14																						
42	Test Hydrocarbons	60 days	Fri 6/20/14	Tue 9/2/14																						
43	Grade treated hydrocarbons	30 days	Sun 8/10/14	Tue 9/16/14																						
44	Final Site cleaning/inventory all staged equipment	3 days	Tue 9/16/14	Fri 9/19/14																						
45	Winterize camp/equipment	2 days	Thu 9/18/14	Sat 9/20/14																						
46	Demobilize	1 day	Sat 9/20/14	Sun 9/21/14																						
47	Ice strip Construction	8 days	Tue 4/7/15	Mon 4/20/15																						
48	Airlift Demobilization	10 days	Mon 4/20/15	Wed 5/6/15																						
49	Project Closeout	0 days	Thu 5/7/15	Thu 5/7/15																						

Project: schedule.nov.4
Date: Thu 11/7/13

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress
