


## PROJECT SCHEDULE YEAR 2 - 2006

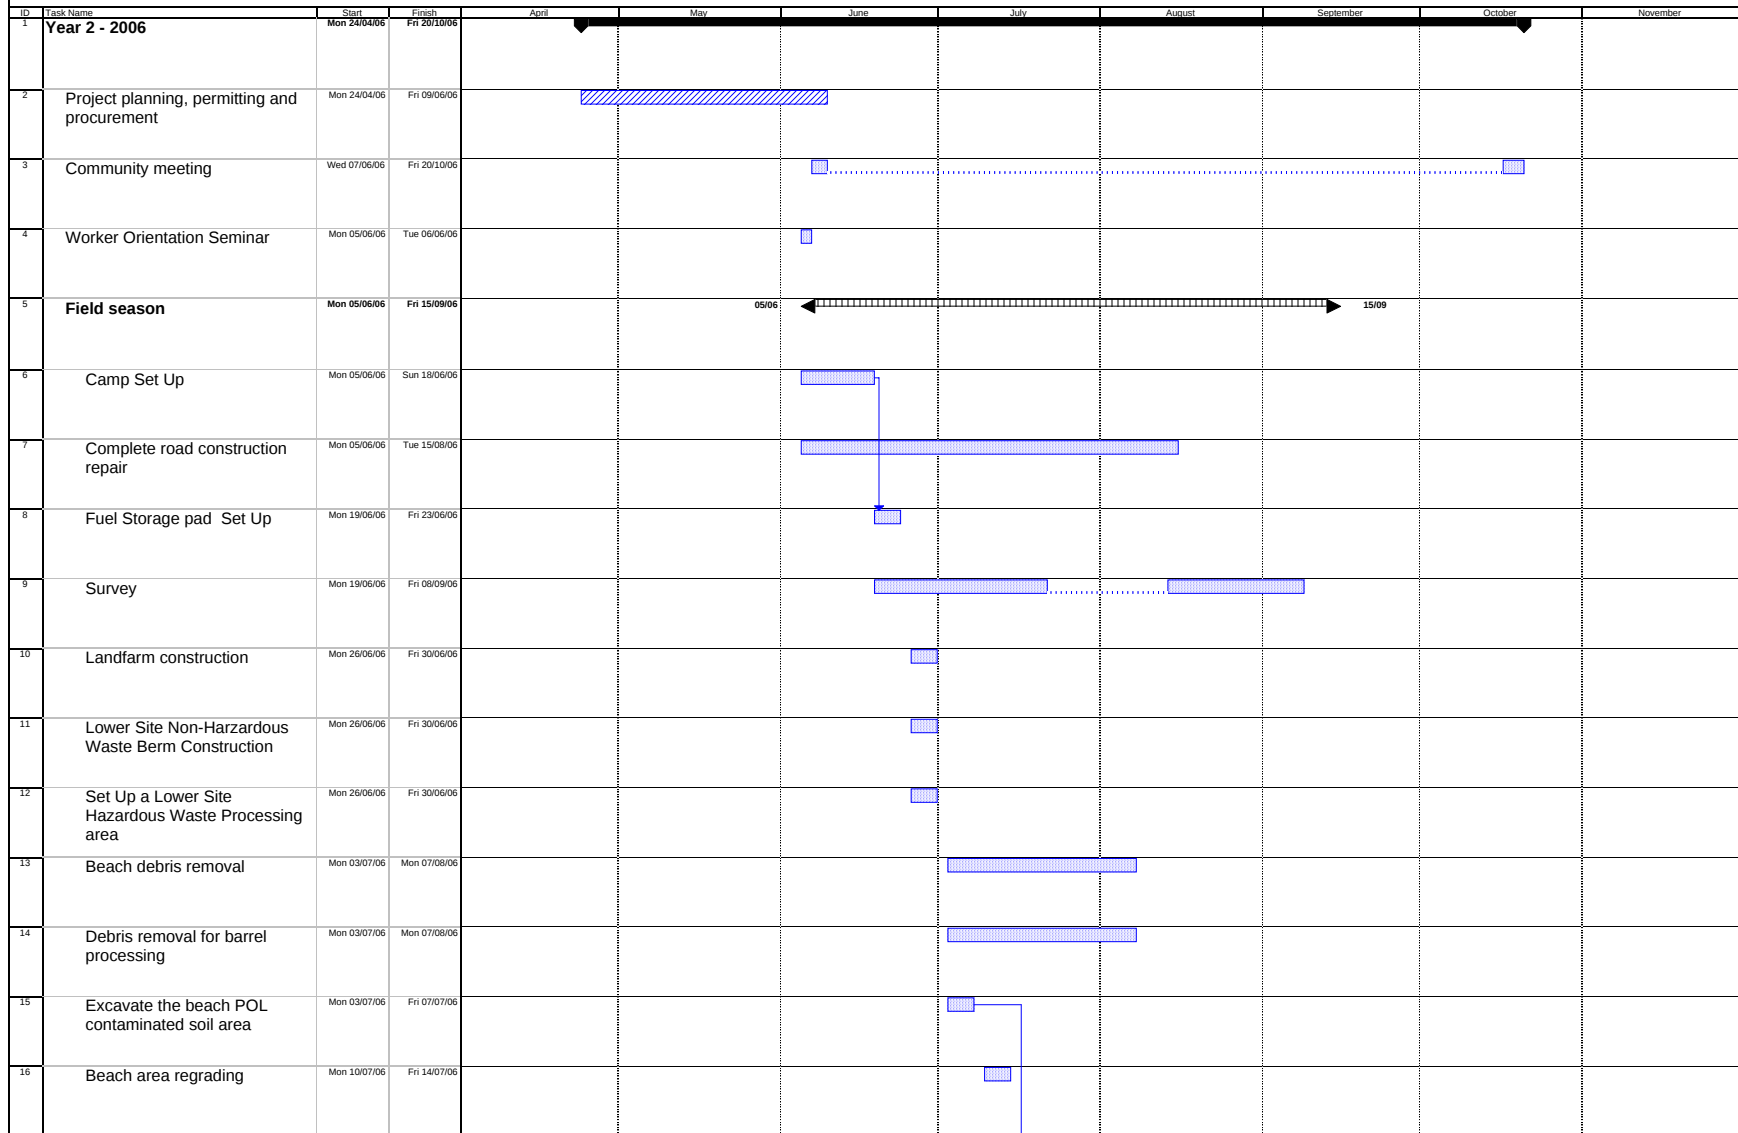

## PROJECT SCHEDULE YEAR 2 - 2006

| ID | Task Name                                                                           | Start        | Finish       | April | May | June | July | August | September | October | November |
|----|-------------------------------------------------------------------------------------|--------------|--------------|-------|-----|------|------|--------|-----------|---------|----------|
| 17 | Installation of monitoring wells                                                    | Mon 10/07/06 | Fri 14/07/06 |       |     |      |      |        |           |         |          |
| 18 | Water Lake contaminated soil excavation                                             | Mon 17/07/06 | Fri 21/07/06 |       |     |      |      |        |           |         |          |
| 19 | Regrading - Water Lake area                                                         | Mon 24/07/06 | Fri 28/07/06 |       |     |      |      |        |           |         |          |
| 20 | Asbestos abatement                                                                  | Mon 07/08/06 | Mon 21/08/06 |       |     |      |      |        |           |         |          |
| 21 | Excavation of mid station pad contaminated soil                                     | Mon 31/07/06 | Fri 04/08/06 |       |     |      |      |        |           |         |          |
| 22 | Relocation of the Hazardous Waste Processing area from the beach to the mid-station | Mon 07/08/06 | Fri 11/08/06 |       |     |      |      |        |           |         |          |
| 23 | Berm Construction of the Non-Hazardous Waste Landfill                               | Mon 07/08/06 | Fri 11/08/06 |       |     |      |      |        |           |         |          |
| 24 | PCB amended Paint removal (all except beach fuel tanks)                             | Mon 14/08/06 | Mon 28/08/06 |       |     |      |      |        |           |         |          |
| 25 | Building demolition                                                                 | Tue 29/08/06 | Mon 11/09/06 |       |     |      |      |        |           |         |          |
| 26 | Mid station dump lobe B excavation                                                  | Mon 14/08/06 | Fri 15/09/06 |       |     |      |      |        |           |         |          |
| 27 | Mid-Station Debris removal and drum processing                                      | Mon 21/08/06 | Fri 15/09/06 |       |     |      |      |        |           |         |          |
| 28 | Mid station regrading                                                               | Mon 14/08/06 | Fri 08/09/06 |       |     |      |      |        |           |         |          |
| 29 | Beach Lanfarm operation                                                             | Mon 17/07/06 | Fri 15/09/06 |       |     |      |      |        |           |         |          |
| 30 | In-situ upper Station landfarm                                                      | Mon 14/08/06 | Fri 15/09/06 |       |     |      |      |        |           |         |          |
| 31 | Winterization                                                                       | Fri 08/09/06 | Fri 15/09/06 |       |     |      |      |        |           |         |          |
| 32 | As-Built drawing and project photographs                                            | Wed 02/08/06 | Sun 15/10/06 |       |     |      |      |        |           |         |          |
