


APPENDIX 7


ENNADAI LAKE REMEDIATION PROJECT

PROJECT SCHEDULE

ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT
CONSTRUCTION SCHEDULE

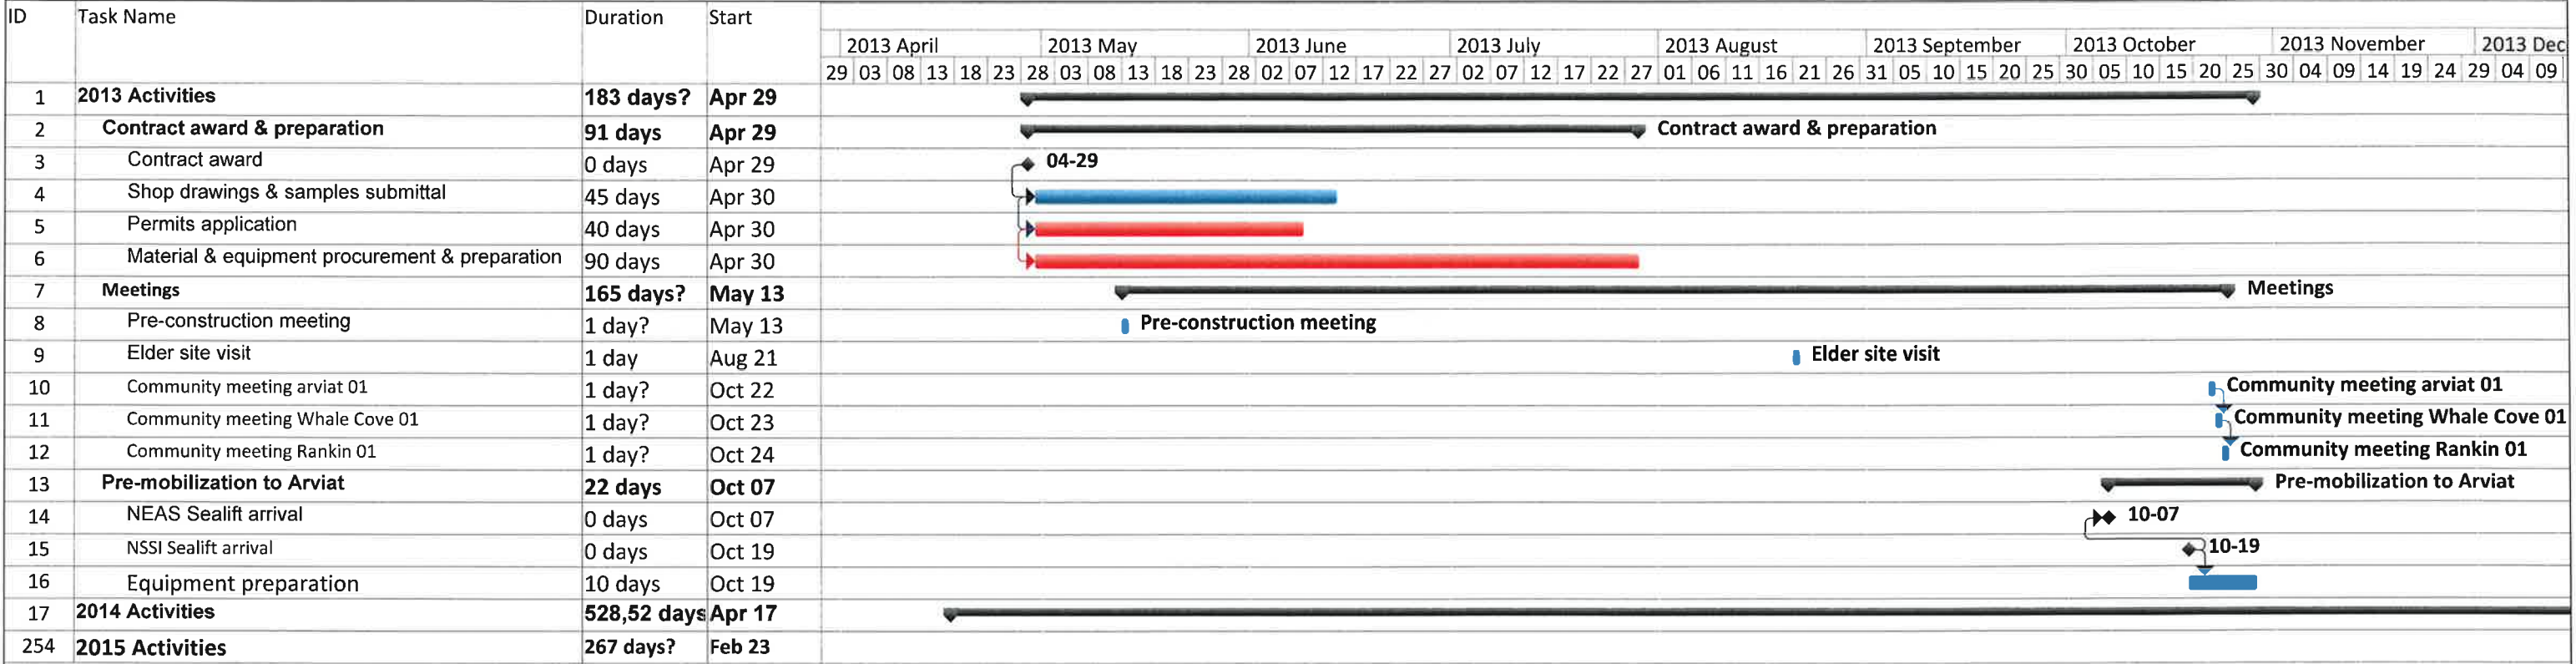

ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT
CONSTRUCTION SCHEDULE

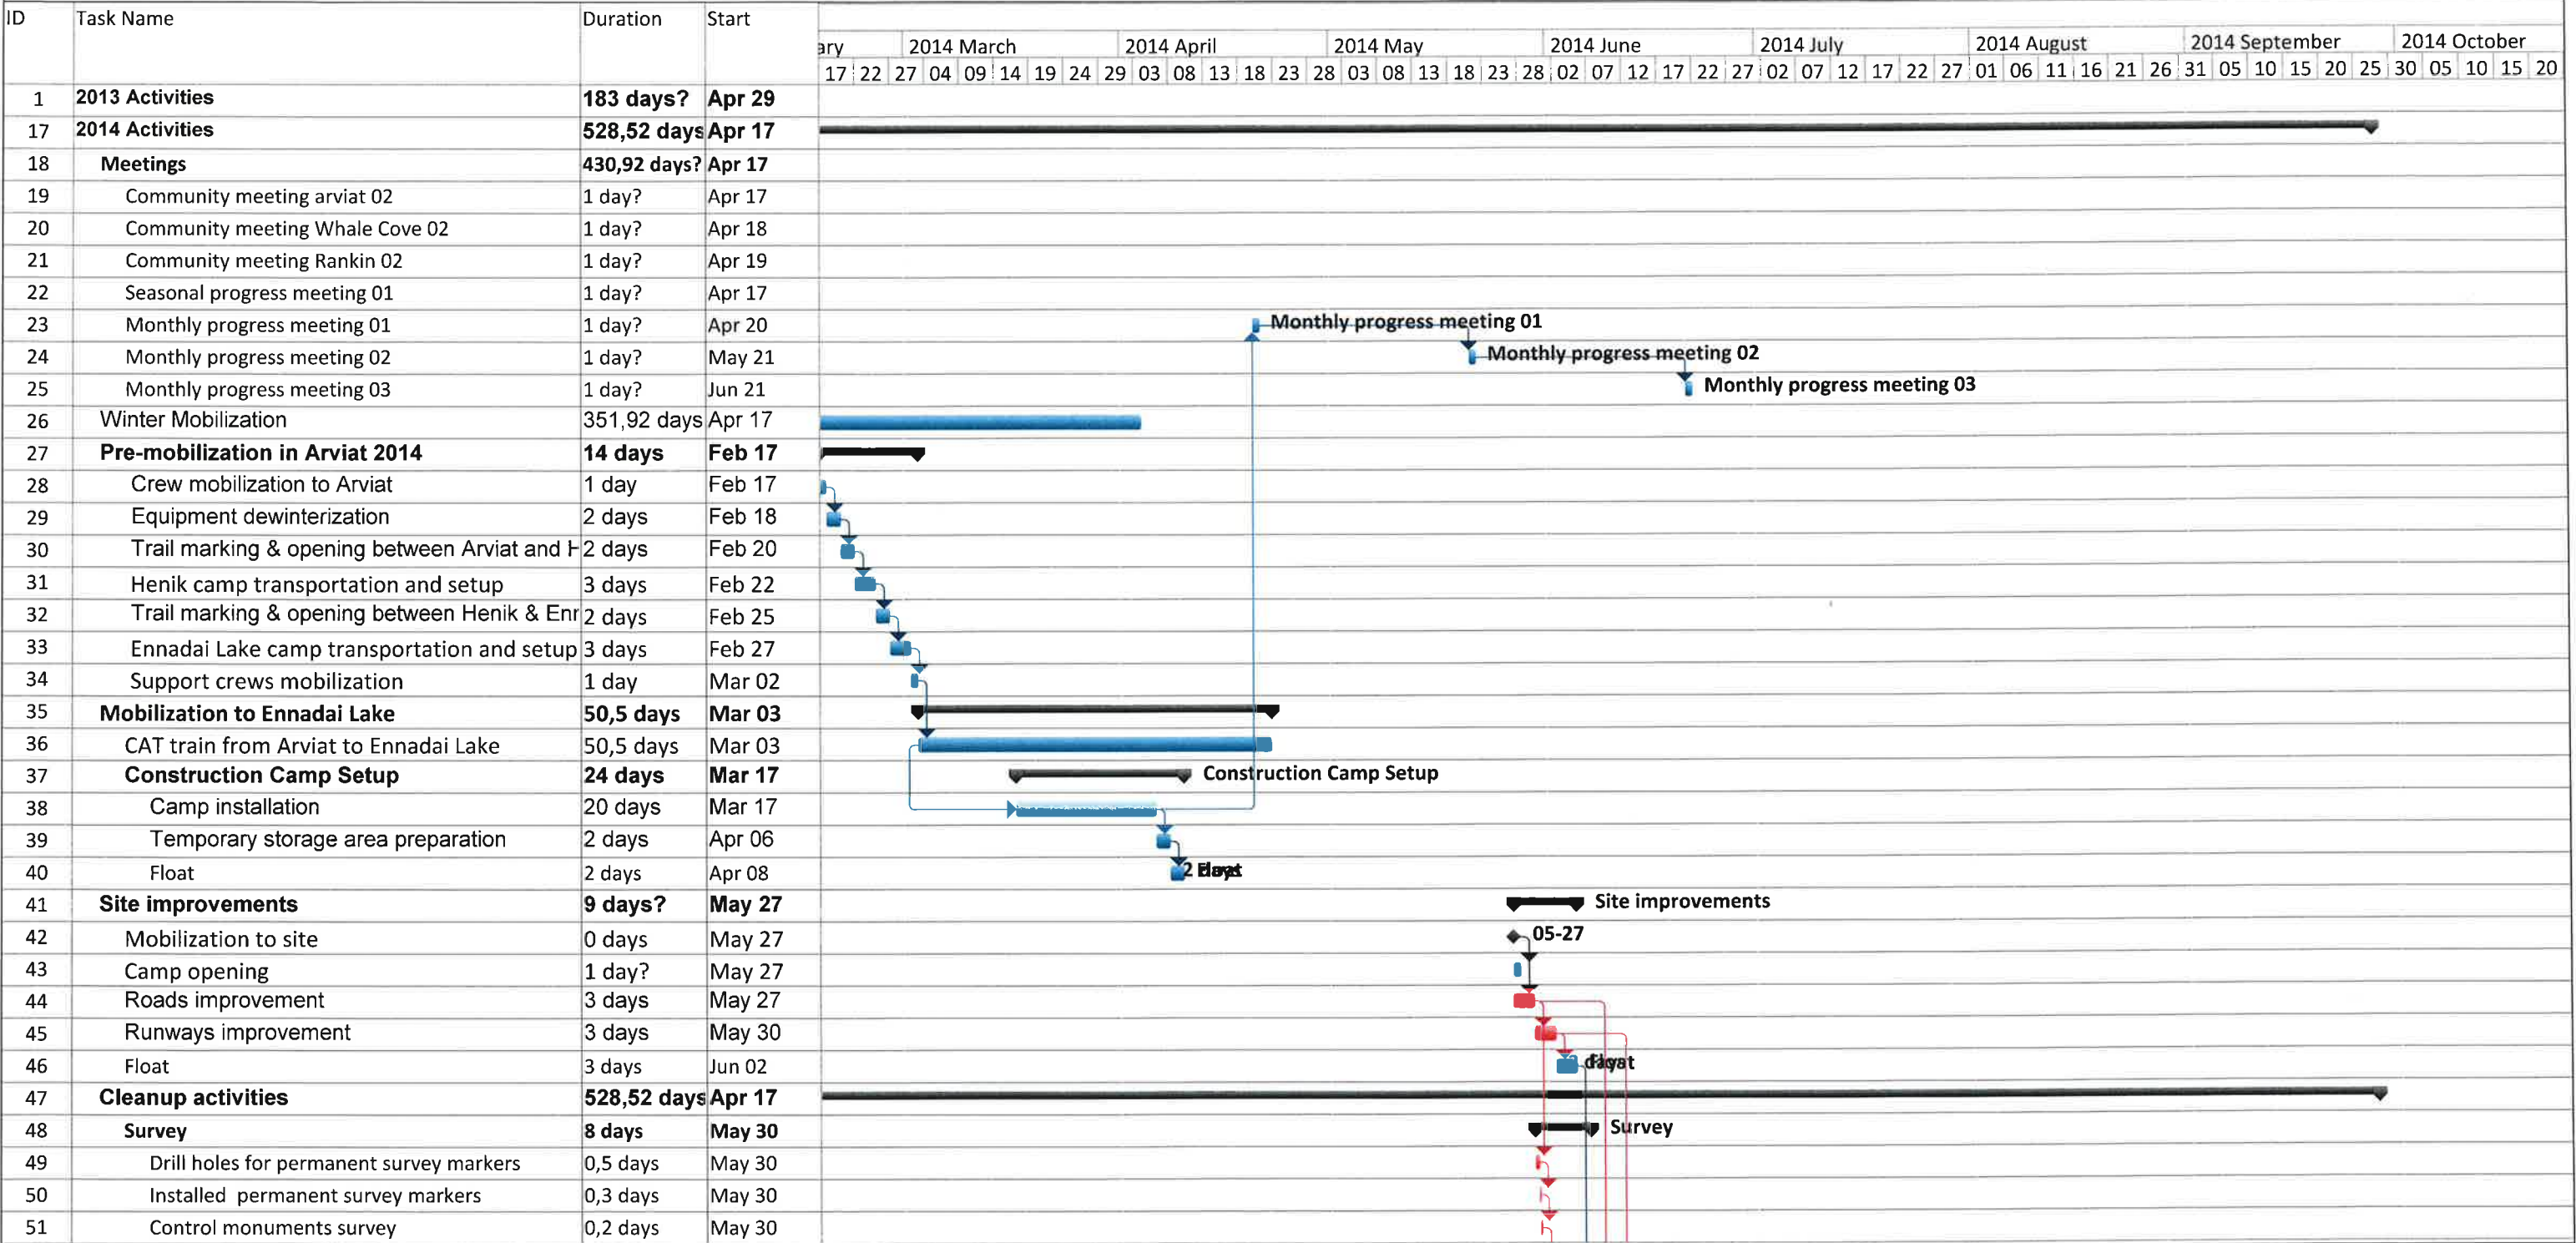

Project: Ennadai Lake schedule dr
Date: Aug 30

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Critical


Critical Split

Progress

Page 2

Kudlik Construction Ltd.	ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT CONSTRUCTION SCHEDULE
--------------------------	--

ID	Task Name	Duration	Start	2014																																															
				May				2014 March				2014 April				2014 May				2014 June				2014 July				2014 August				2014 September				2014 October															
				17	22	27	04	09	14	19	24	29	03	08	13	18	23	28	03	08	13	18	23	28	02	07	12	17	22	27	02	07	12	17	22	27	01	06	11	16	21	26	31	05	10	15	20	25	30	05	10
52	Site survey and implementation	4 days	May 31																																																
53	Float	3 days	Jun 04																																																
54	Monitoring wells	4 days	Apr 17																																																
55	Drilling	2 days	Apr 17																																																
56	Installation	2 days	Apr 17																																																
57	Float	2 days	Apr 19																																																
58	Tanks and pipelines cleanup and removal	15 days	Jun 09																																																
59	Pipelines and overhead pipelines	5 days	Jun 09																																																
60	Remove fuel and containerize	2 days	Jun 09																																																
61	Wash pipes	2 days	Jun 11																																																
62	Cut, remove and store (480m)	1 day	Jun 13																																																
63	Tank 5	2 days	Jun 13																																																
64	Remove and containerize liquid	1 day	Jun 13																																																
65	Move out tank, wash and store	1 day	Jun 14																																																
66	Tanks 1 to 4 and associated pipes	9 days	Jun 15																																																
67	Remove and containerize liquid	2 days	Jun 15																																																
68	Wash tanks	2 days	Jun 17																																																
69	Remove and store	1 day	Jun 19																																																
70	Float	4 days	Jun 20																																																
71	Landfarm construction	24 days	Jun 05																																																
72	Sand production	7 days	Jun 05																																																
73	Reshape surface	2 days	Jun 12																																																
74	Berm construction & access ramp	3 days	Jun 14																																																
75	sand placement	2 days	Jun 17																																																
76	Liner installation	2 days	Jun 19																																																
77	Bedding sand	4 days	Jun 21																																																
78	Float	4 days	Jun 25																																																
79	Landfarm ready	0 days	Jun 28																																																
80	Contaminated soil excavation (2,200 m3)	22 days	Jun 29																																																
81	Apec3, (156 m3) hydr.	2 days	Jun 29																																																
82	Apec4, (76 m3) hydr.	0,5 days	Jul 01																																																
83	Apec2, (12 m3) hydr.	1 day	Jul 01																																																
84	APEC8, Area 1 (17m3) hydr.	0,25 days	Jul 02																																																
85	APEC8, Area 2 (121m3) hydr.	1 day	Jul 02																																																
86	APEC1, (33m3) hydr.	0,25 days	Jul 03																																																
87	APEC 12 (1039 m3) hydr.	3 days	Jul 04																																																


Project: Ennadai Lake schedule dr Date: Aug 30	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

Kudlik Construction Ltd.
ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT
CONSTRUCTION SCHEDULE

ID	Task Name	Duration	Start																																																																												
				2014 February												2014 March								2014 April								2014 May								2014 June								2014 July								2014 August								2014 September								2014 October							
				17	22	27	04	09	14	19	24	29	03	08	13	18	23	28	03	08	13	18	23	28	02	07	12	17	22	27	02	07	12	17	22	27	01	06	11	16	21	26	31	05	10	15	20	25	30	05	10	15	20																										
88	APEC 13.1 (38 m3) hydr.	0,25 days	Jul 07																																																																												
89	APEC 13.2 (60 m3) hydr.	0,25 days	Jul 07																																																																												
90	APEC 23 a (1m3) hydr.	0,25 days	Jul 07																																																																												
91	APEC 23 a (,5m3) metals	0,25 days	Jul 07																																																																												
92	APEC 15 (11m3) hydr.	0,25 days	Jul 08																																																																												
93	APEC 20.2 (103m3) hydr.	1 day	Jul 08																																																																												
94	APEC 20.1 (479 m3) hydr.	2 days	Jul 09																																																																												
95	APEC 22 (,5m3) hydr.	0,25 days	Jul 11																																																																												
96	Excavation completed	0 days	Jul 11																																																																												
97	Float	3 days	Jul 11																																																																												
98	Backfill excavations (1900 m3)	8 days	Jul 13																																																																												
99	Contaminated soil treatment	68 days?	Jul 14																																																																												
100	Treatment starting	0 days	Jul 14																																																																												
101	Tilling 01	0,5 days	Jul 14																																																																												
102	Tilling 02	0,5 days	Jul 18																																																																												
103	Control Sampling 01	0,5 days	Jul 18																																																																												
104	Tilling 03	0,5 days	Jul 21																																																																												
105	Tilling 04	0,5 days	Jul 25																																																																												
106	Tilling 05	0,5 days	Jul 28																																																																												
107	Tilling 06	0,5 days	Aug 01																																																																												
108	Tilling 07	0,5 days	Aug 04																																																																												
109	Tilling 08	0,5 days	Aug 08																																																																												
110	Tilling 09	0,5 days	Aug 11																																																																												
111	Tilling 10	0,5 days	Aug 15																																																																												
112	Control Sampling 02	0,5 days	Aug 15																																																																												
113	Tilling 11	0,5 days	Aug 18																																																																												
114	Tilling 12	0,5 days	Aug 22																																																																												
115	Tilling 13	0,5 days	Aug 25																																																																												
116	Tilling 14	0,5 days	Aug 29																																																																												
117	Nutrient spreading according to results	1 day?	Aug 29																																																																												
118	Tilling 15	0,5 days	Sep 01																																																																												
119	Tilling 16	0,5 days	Sep 05																																																																												
120	Landfarm closing	8 days	Sep 12																																																																												
121	Removing treated soil and sand layer	3 days	Sep 12																																																																												
122	Removing liner	2 days	Sep 15																																																																												
123	Regrading / reshaping the area	3 days	Sep 17																																																																												

Project: Ennadai Lake schedule dr Date: Aug 30	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT
CONSTRUCTION SCHEDULE

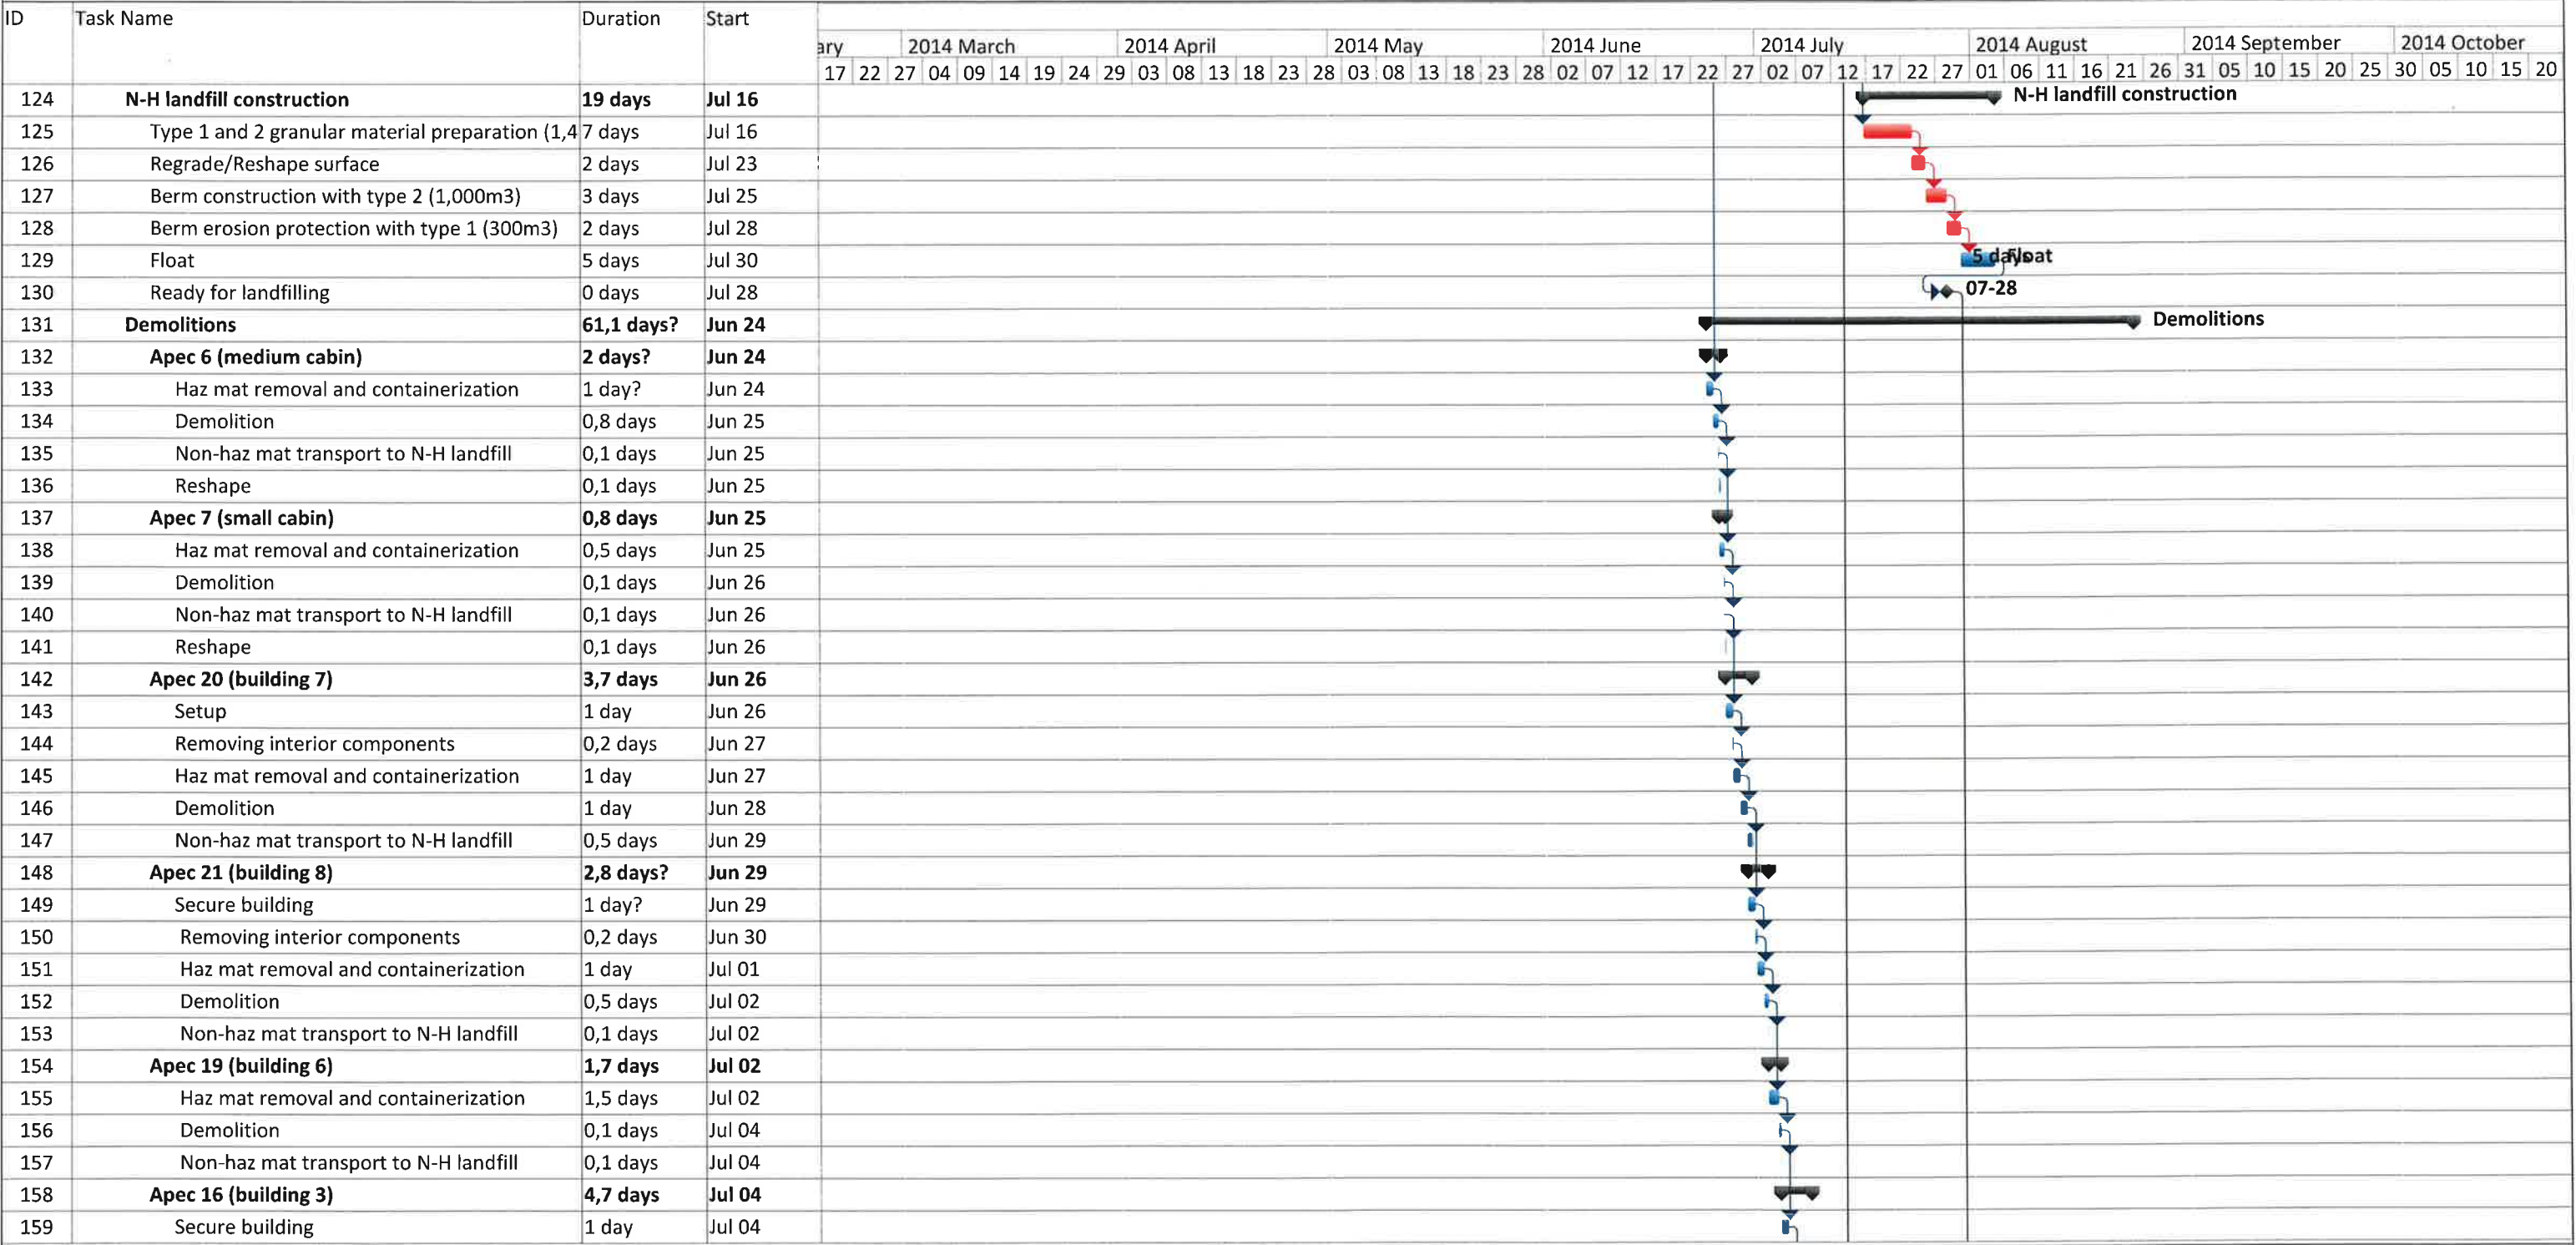

Project: Ennadai Lake schedule dr
Date: Aug 30

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Critical


Critical Split

Progress

Project: Ennadai Lake schedule dr Date: Aug 30	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

Page 8

ENVIRONMENTAL SITE REMEDIATION, ENNADAI LAKE, NUNAVUT
CONSTRUCTION SCHEDULE

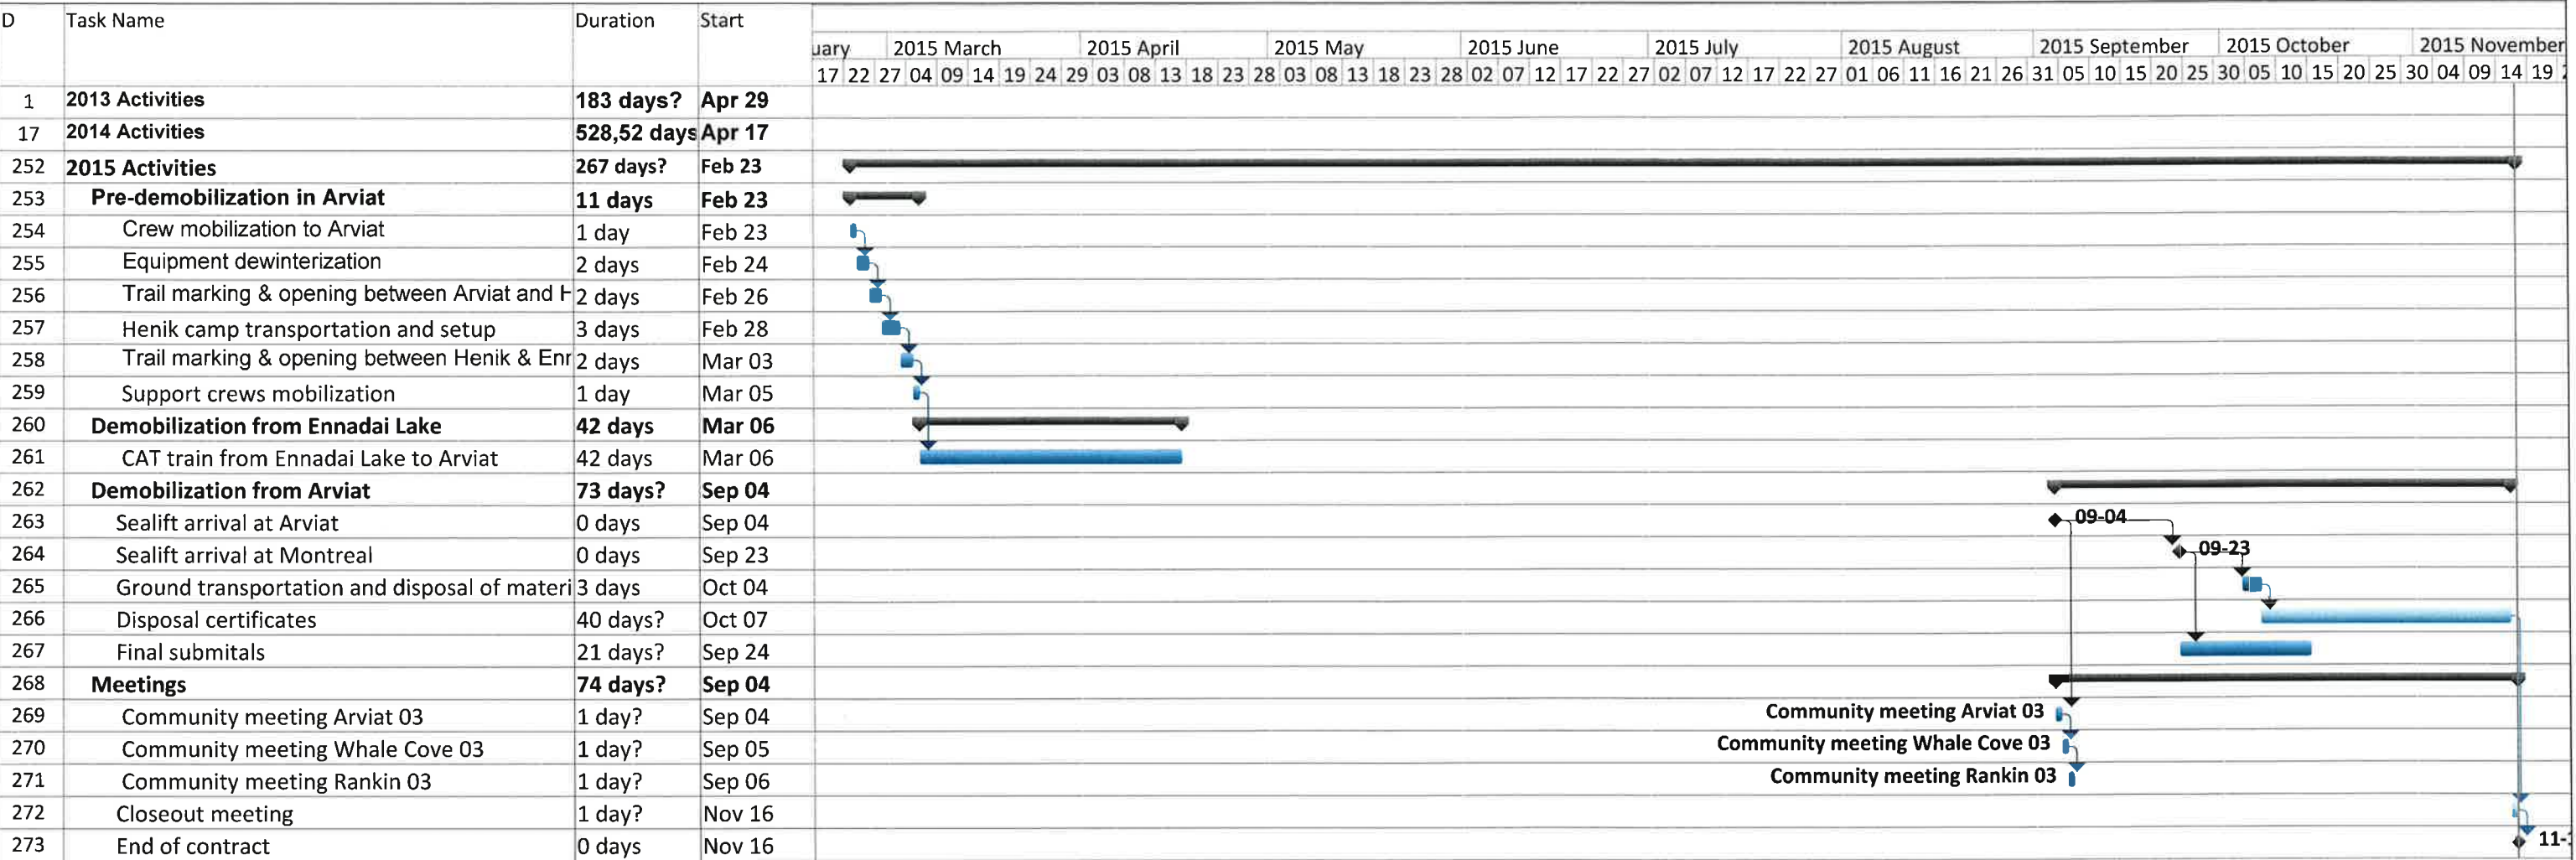

Project: Ennadai Lake schedule dr
Date: Aug 30

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Critical

Critical Split

Progress
