


Remediation of CAM-D DEW Line Site  
Work Schedule



Kudlik Construction Ltd.  
Date: Thu 09-11-05

Task

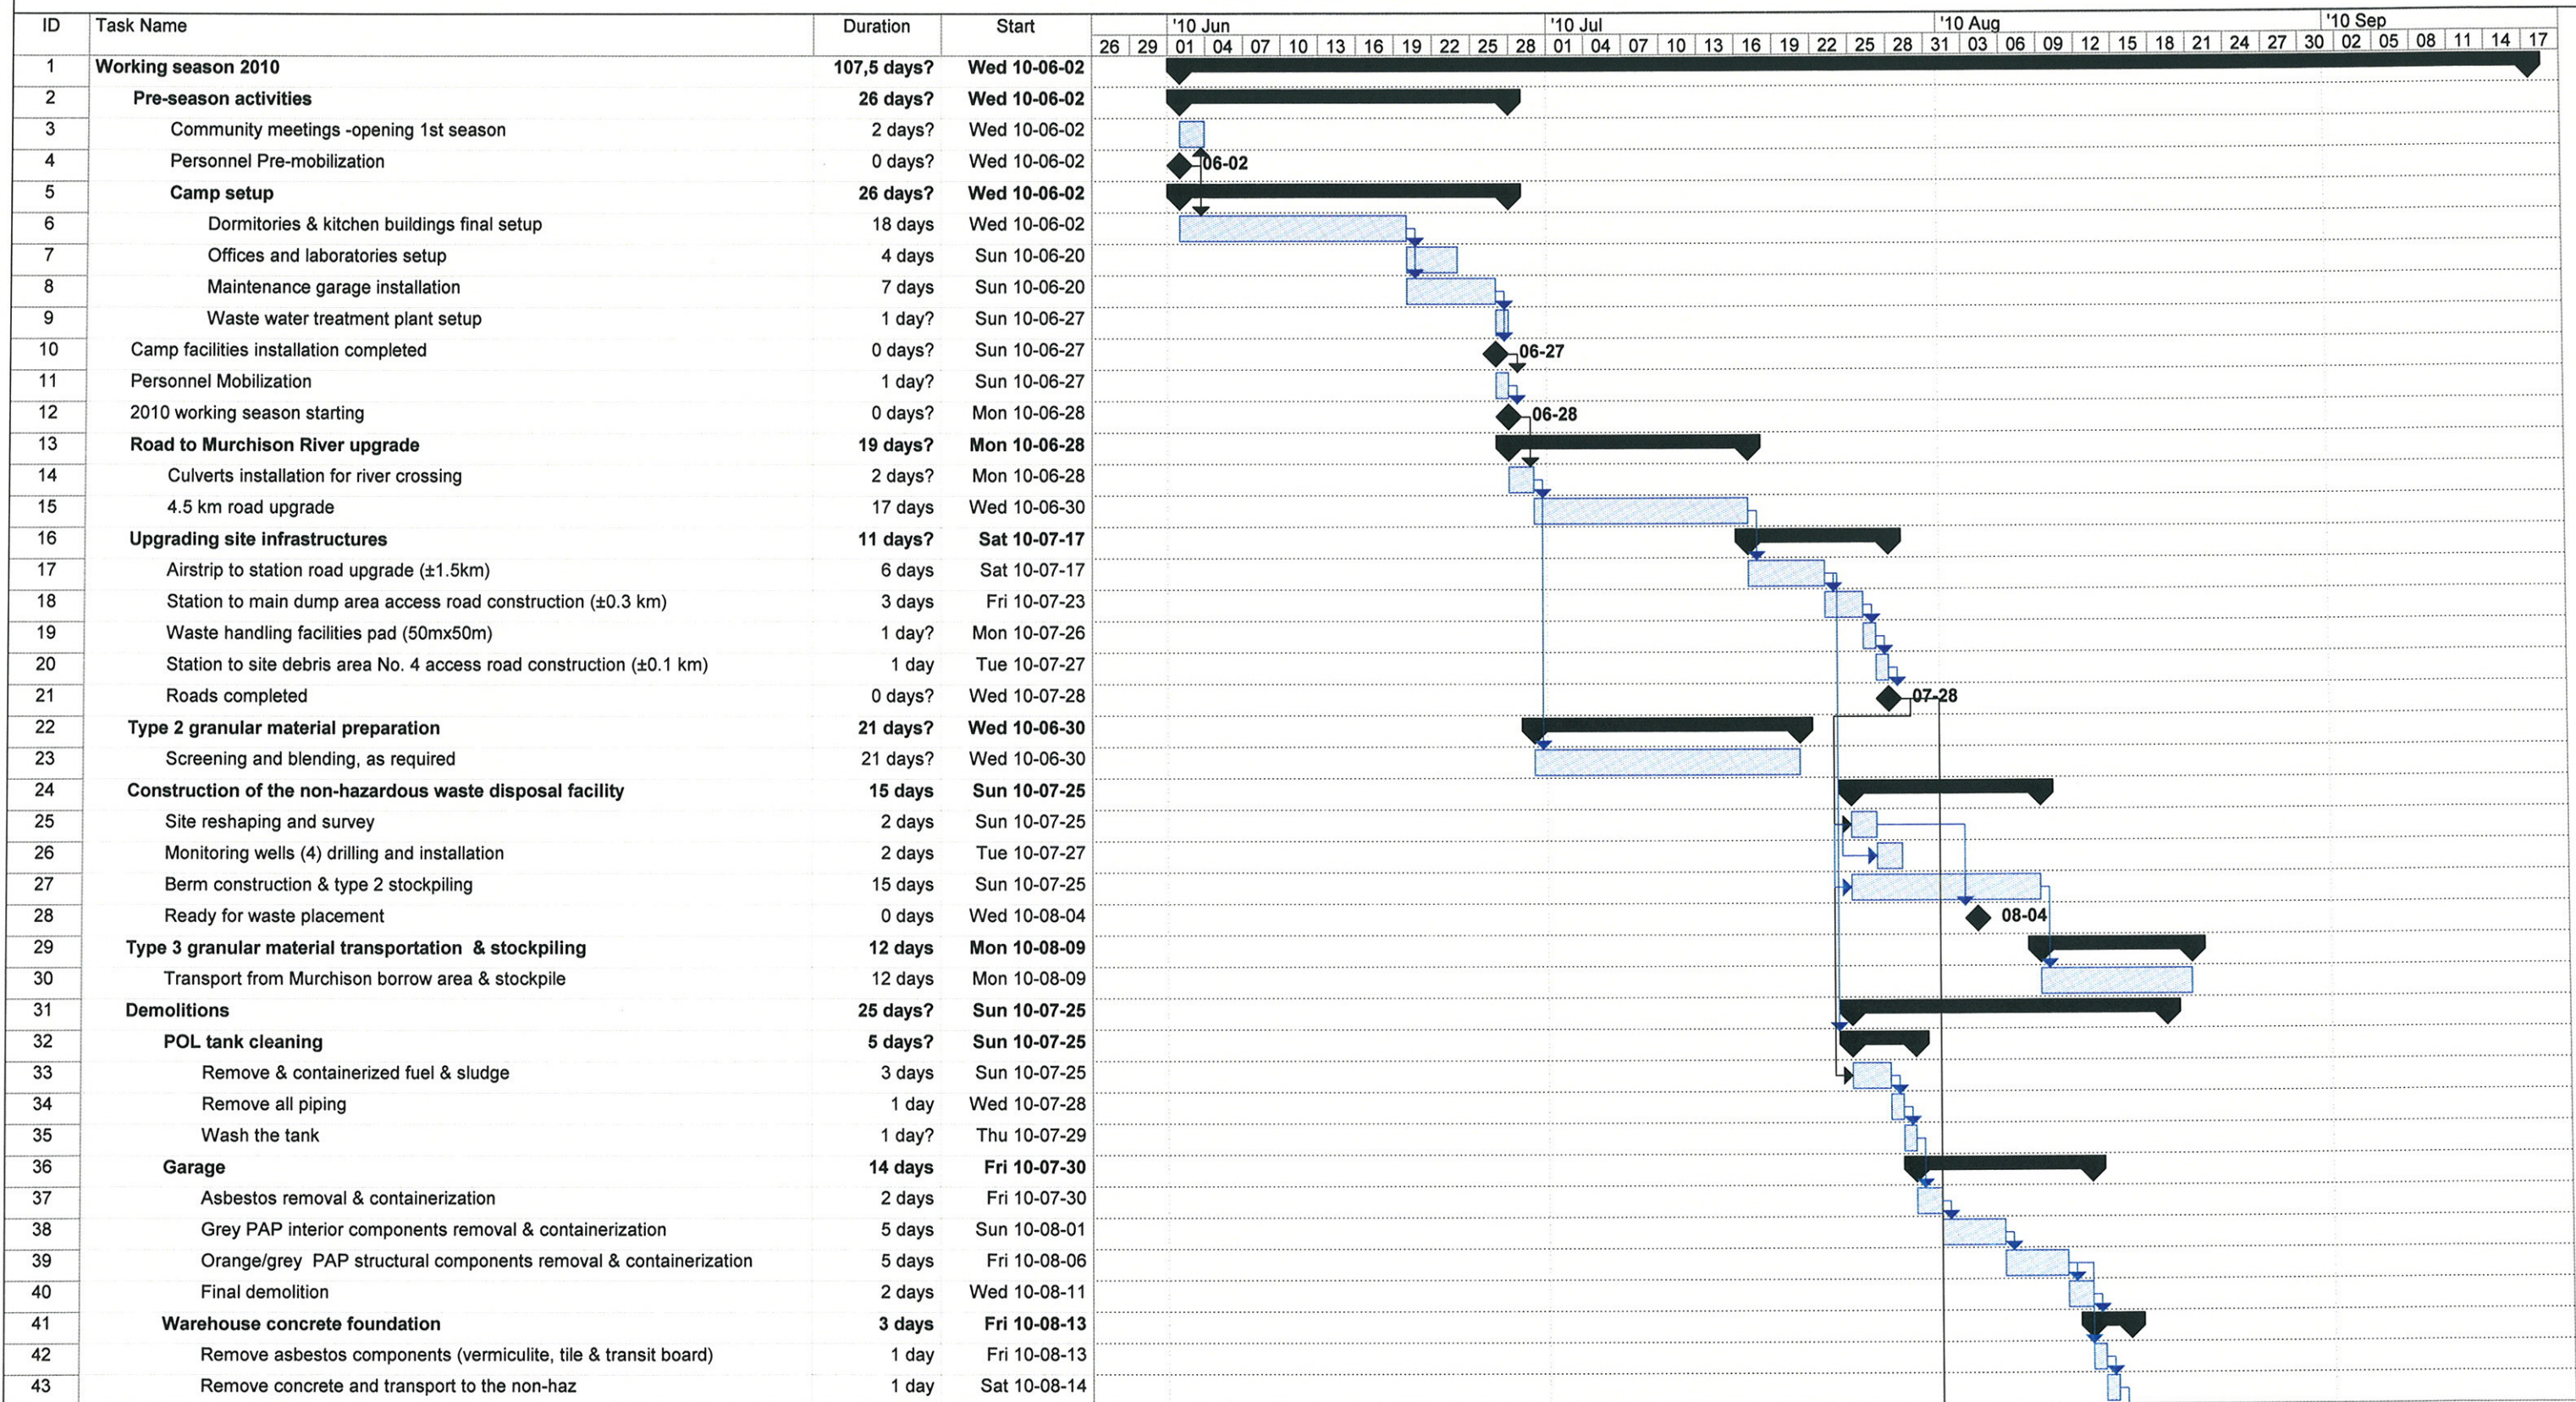

Progress



Summary



External Tasks



Deadline



Split



Milestone



Project Summary



External Milestone






## Remediation of CAM-D DEW Line Site Work Schedule

[illegible]




Remediation of CAM-D DEW Line Site  
Work Schedule

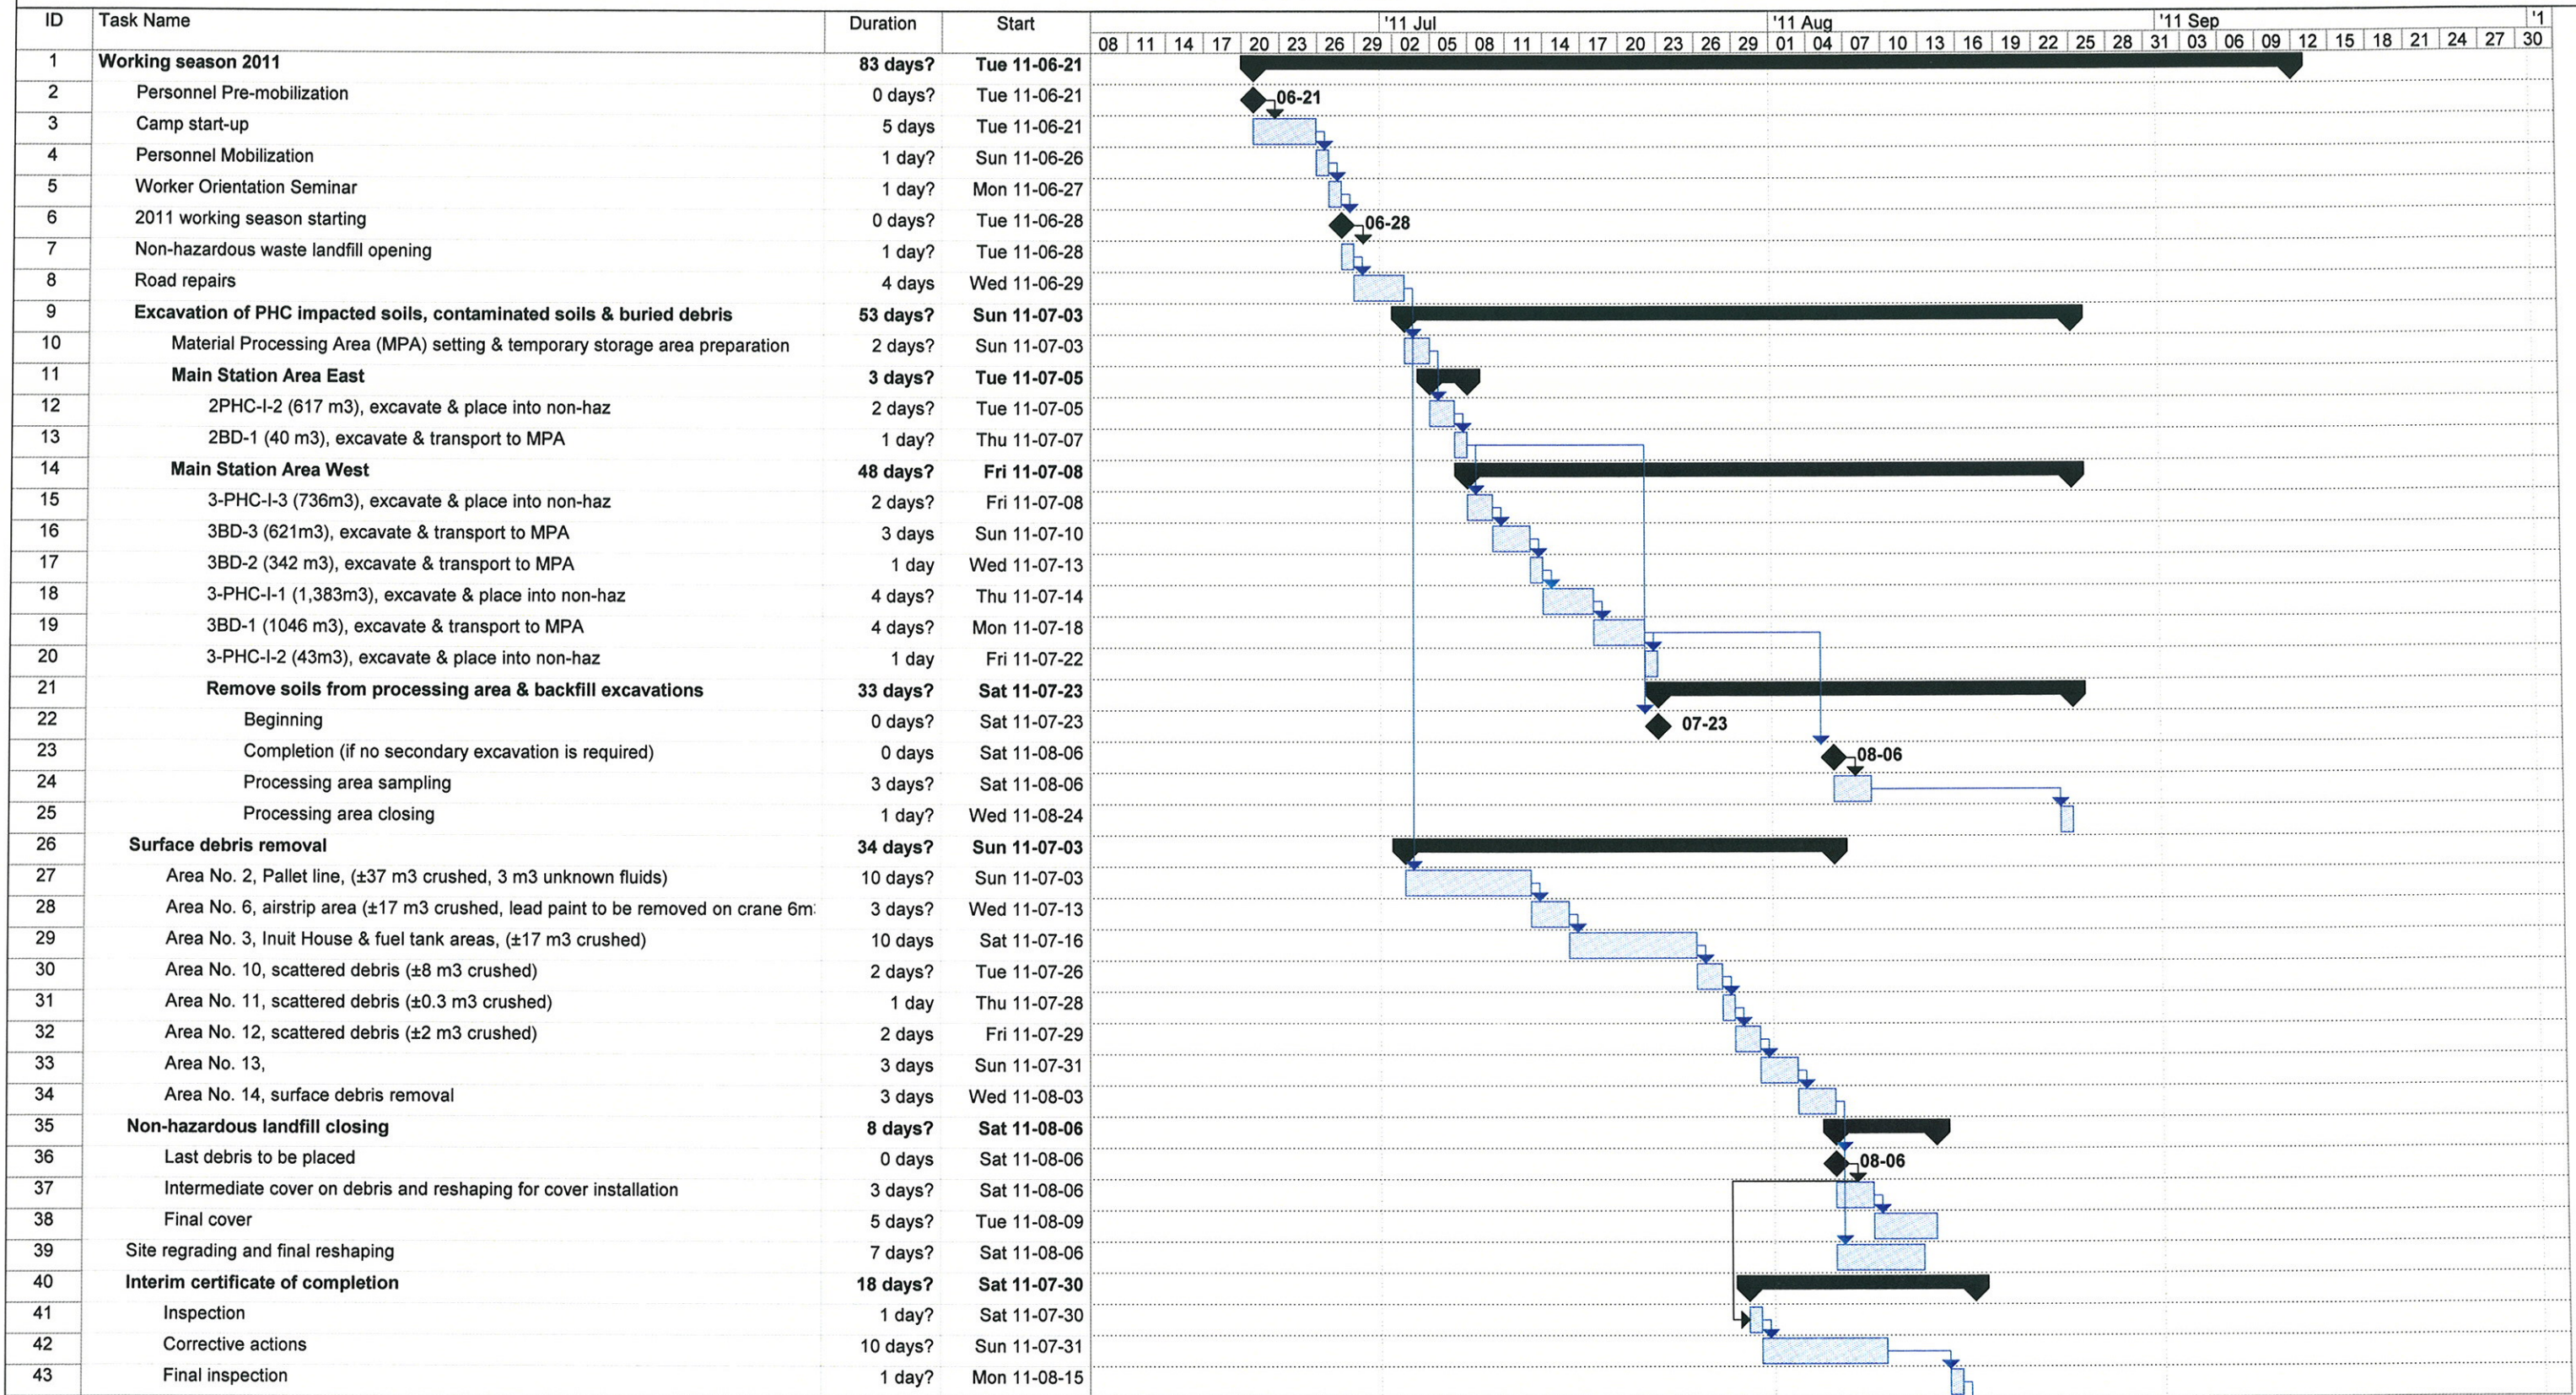

Kudlik Construction Ltd.  
Date: Thu 09-11-05

Task  
Split



Progress  
Milestone



Summary  
Project Summary



External Tasks  
External Milestone



Deadline





## Remediation of CAM-D DEW Line Site Work Schedule

ID	Task Name	Duration	Start	'11 Jul 08 11 14 17 20 23 26 29 02 05 08 11 14 17 20 23 26 29	'11 Aug 01 04 07 10 13 16 19 22 25 28 31	'11 Sep 03 06 09 12 15 18 21 24 27 30
44	Site contractual work completed	1 day?	Tue 11-08-16			
45	<b>Site closing</b>	<b>25 days?</b>	<b>Tue 11-08-16</b>			
46	Personnel pre-demobilization	1 day?	Tue 11-08-16			
47	Temporary camp setup	2 days?	Wed 11-08-17			
48	Camp facilities shut down and preparation for transportation	14 days	Fri 11-08-19			
49	Containerized soils & materiel preparation for winter transportation	5 days?	Fri 11-09-02			
50	Equipment winterization	2 days?	Wed 11-09-07			
51	Personnel demobilization	1 day?	Fri 11-09-09			
52	<b>Post-season activities</b>	<b>2 days?</b>	<b>Sat 11-09-10</b>			
53	Community meetings -end of project	2 days?	Sat 11-09-10			
