


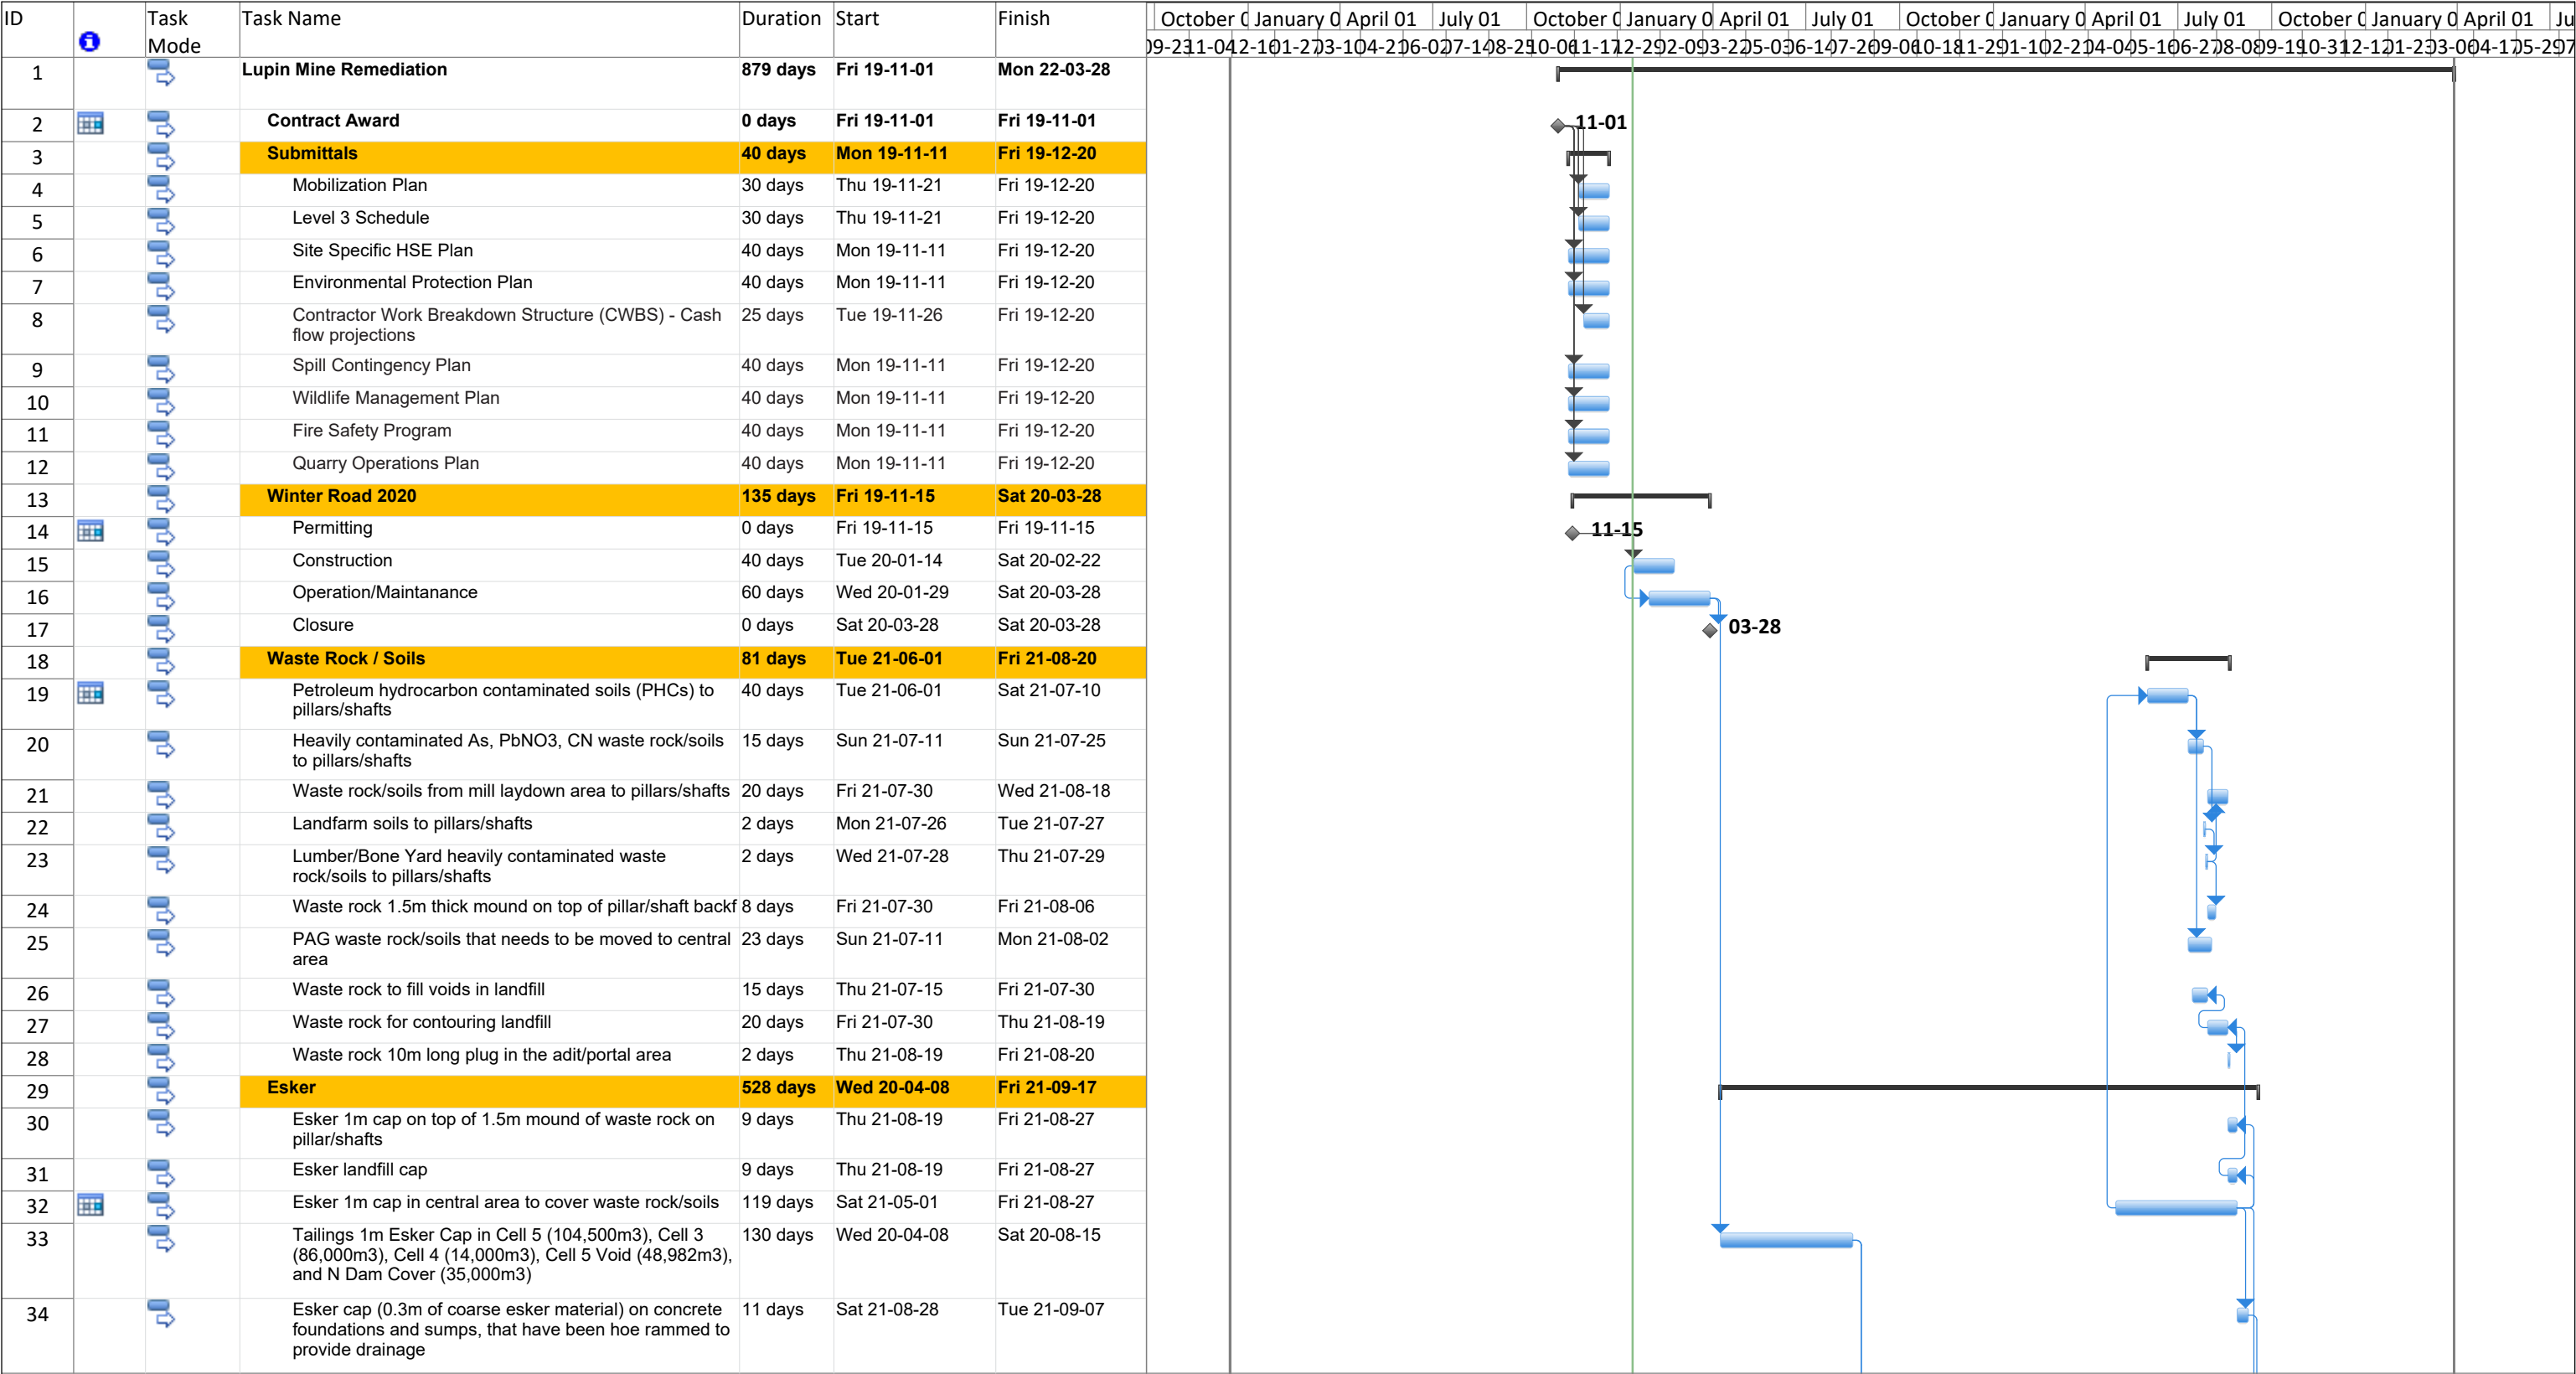

[illegible]

ID		Task Mode	Task Name	Duration	Start	Finish	October 09-23	January 11-04	April 01-27	July 01-18	October 09-23	January 09-23	April 01-27	July 01-18	October 09-23	January 09-23	April 01-27	July 01-18	October 09-23	January 09-23	April 01-27	July 01-18
57			Regrade steep sections of current toe berm on M Dam to 2:1 using in-situ materials	8 days	Sun 20-08-16	Sun 20-08-23																
58			Hoe-ram concrete building foundations and sumps to facilitate drainage	15 days	Sat 20-07-18	Sat 20-08-01																
59			Flush pipeline of sewage facility with clean water	3 days	Fri 21-08-13	Sun 21-08-15																
60			Burn excess fuel at end of closure activities	5 days	Sun 21-08-01	Fri 21-08-06																
61			Remove fluids and clean tanks which contain or have contained oil, fuel or glycol in accordance with the Canadian Environmental Protection Act Regulation	22 days	Fri 21-08-06	Fri 21-08-27																
62			Dismantle and dispose of tanks which contain or have contained oil, fuel or glycol in accordance with the Canadian Environmental Protection Act Regulation.	18 days	Sat 21-08-28	Tue 21-09-14																
63			Scarify all-weather roads and remove 22 culverts	12 days	Sat 21-09-18	Wed 21-09-29																
64			Treat water inventory with lime, operate siphons, water management to maintain freeboard in ponds. Pond 2 water release when owners engineer confirms water quality. Number of bags of 20kg lime used in 2018 shown.	60 days	Wed 20-07-15	Sat 20-09-12																
65			Remove Cell 4 outlet culvert and reinforce remaining channel with coarse esker materials	6 days	Sun 20-08-16	Fri 20-08-21																
66			Excavate spillways to breach Upper and Lower Sewage Lakes and reinforce with coarse esker materials	8 days	Mon 21-08-16	Mon 21-08-23																
67			Winter Road 2022	126 days	Mon 21-11-08	Sun 22-03-13																
68			Permitting	25 days	Mon 21-11-08	Thu 21-12-02																
69			Construction	45 days	Mon 22-01-03	Wed 22-02-16																
70			Operation/Maintanance	25 days	Thu 22-02-17	Sun 22-03-13																
71			Closure	0 days	Sun 22-03-13	Sun 22-03-13																
72			Closeout Documentation	55 days	Wed 22-02-02	Mon 22-03-28																
73			Final Project Completion	0 days	Sun 22-03-13	Sun 22-03-13																

Project: SCHEDULE TEMPLATE

Date: Mon 20-01-13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress

Page 3
