

MONOPROS LIMITED

Tel: (867) 873-4530
Fax: (867) 873-4532

P.O. Box 2520
Yellowknife, NWT
Canada, X1A 2P8

FACSIMILE MESSAGE

TO: Sandra Bradbury, Land Administrator; cc: **FAX NO:** 669-2713; 982-4307;
Ken Leishman, Jim MacPherson, Jack Kaniak 982-3311
FOR: INAC - Lands **REF:** #4031, 4046

FROM: Shirley Standafer Pfister, Lands and Govt.
Relations

No. of Pages (incl. Cover sheet) 3

DATE: 26 May, 2000

**RE: DRILLING UPDATE: KIKERK (KIKKIKTALIK) AND ROCKINGHORSE
(KOAMAOGAKTOK) PROGRAMMES**

- 1) **KIKERK:** The Kikerk (Kikkiktalik) exploration drill programme is scheduled to start Saturday, 27 May, with a move from the Rockinghorse (Koamaogaktok) property located 90km southeast; drilling will commence either on 28 or 29 May. Tentatively, four holes are planned into three anomalies located east of Monopros claim *KL 12*, on the *Tree 1* claim held by Rhonda Mining Corp., with whom Monopros has an agreement in place. (See accompanying *TABLE* and location map). Order of drilling is yet to be established.
- 2) **ROCKINGHORSE:** Drilling on the last hole, #RHL-00-17c, was completed today. An estimated 2511m of small-diameter core was recovered, with #RHL-0014c intersecting kimberlite; a second hole (#RHL-00-15c) was drilled to delineate contacts. On 15 May, a group of elders from Kugluktuk visited the camp at Muskox Lake and received updated maps of the drill programme; the camp met with their approval. The camp now is being shut down and secured; the Kikerk programme will be served out of Kugluktuk, where the project manager, geologist and drill crew will be based.


Further information, including final statistics and summary maps, will be provided at the termination of both programmes. Thank you for the opportunity to provide the foregoing.

Regards,

-- ssp

cc: Pector Bengts - WCB, Mine Safety
Rita Becker - Nunavut Water Board

June 5/00
8/6/00




DVAND June 12/00
EC, bsp,
NIRB

MONOPROS LIMITED - ROCKINGHORSE AND KIKERK, 2000

Hole ID	Eastings	Northings	Elevation (m)	Asimuth	Dip	Estimated Final EOH (m)	Estimated EOH (m)	EOH (m)	Accuracy	Drilling Status
RHL-00-001C	443509	7340817	500	161	85	257	144	191.54	RHL_0045	completed
RHL-00-002C	443553	7340288	500	061	60	148	63	85.35	RHL_0058	completed
RHL-00-003C	443672	7338401	500	353	45	140	70	97.54	RHL_0080	completed
RHL-00-004C	444332	7338069	528	005	65	200	100	103.83	RHL_0090	completed
RHL-00-005C	443311	7338238	525	00	90	150	75	22.88	RHL_0058	completed
RHL-00-006C	443387	7338914	500	270	45	165	78	85.35	RHL_0049	completed
RHL-00-007C	443057	7338576	500	0	90	148	70	73.15	RHL_0062	completed
RHL-00-008C	441848	7339407	533	0	90	100	100	39.62	RHL_0061	completed
RHL-00-009C	443055	7340801	500	0	90	220	120	21.34	RHL_0059	completed
RHL-00-0010	443208	7337845	529	318	-55	150	100	48.19	RHL_0083	completed
RHL-00-0011	443207	7328218	529	318	-55	150	100	103.83	RHL_0084	completed
RHL-00-0012	444228	7330342	-500	318	-60	140	100	N/A	RHL_0085	completed
RHL-00-013C	443827	7339878	529	83	-65	75	155	N/A	RHL_0053	completed
RHL-00-014C	480411	7326948	-500	282	-60	120	80	N/A	RHL_0066	completed
RHL-00-015C	480411	7326988	-500	282	-60	120	80	N/A	RHL_0066	completed
RHL-00-016C	460680	7326302	-500	0	-20	100	80	N/A	RHL_0067	completed
Not drilled	458361	7329821	-500	0	-90	100	100	N/A	RHL_0088	completed
RHL-00-017C	457167	7338709	-500	328	-65	150	74	N/A	RHL_0089	incomplete
Kik-00-001C	408190	7434250	-200	304	-65	140	120		KIK_0001	incomplete
Kik-00-002C	408242	7434215	-200	105	-65	140	100		KIK_0002	incomplete
Kik-00-003C	408190	7434250	-200	124	-65	140	100		KIK_0001	incomplete
Kik-00-004C	408136	7434488	-200	145	-55	140	100		KIK_0003	incomplete

Kikerk Lake Drill Locations Agreement between Monopros Limited Rhonda Mining Corp.

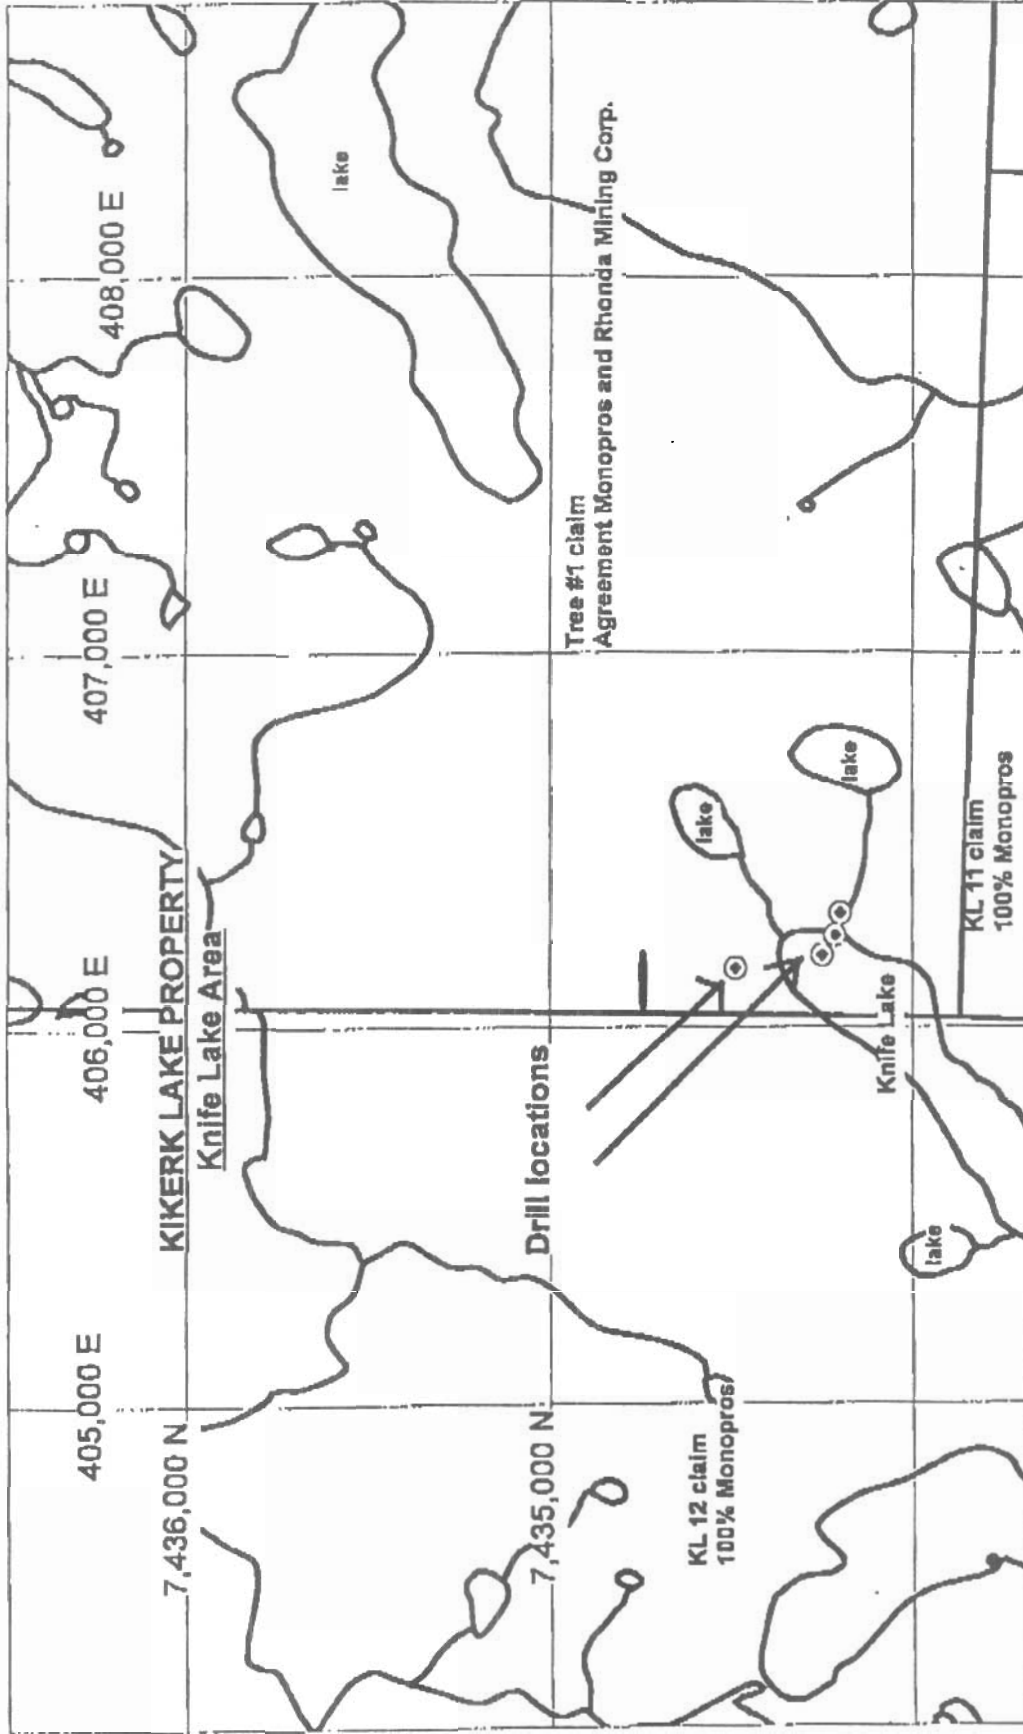

Scale: 1:20,000

May 2000
