

145 King Street East Suite400, Toronto, Ontario M5C 2Y7 416-628-0216

Sent by Email

February 28, 2025

Licensing Nunavut Water Board P.O. Box 119 Gjoa Haven, NU X0B 1J0

Re: January 2025 – Monthly Monitoring Report for Water License 2AM-DOH1335

This report is comprised of the monitoring requirements set out in Part I and Schedule I of water licence 2AM-DOH1335 Amendment 2 (the license), and additional requirements from CIRNAC.

In March 2022, Agnico Eagle made the decision to maintain the suspension of production activities at the Doris Mine site and Madrid North Portal to dedicate the infrastructure of the Hope Bay site to exploration activities. As such, the mill operation will remain suspended and underground activities will focus on exploration development. As the mill will not be operational for the foreseeable future, Table 4: Volume of Reclaim Water from the TIA for Process Water has been removed.

In February 2023, Agnico Eagle made the decision to temporarily cease underground development of the Doris mine. The final blast occurred on April 19, 2023 and all waste rock haulage was completed on April 24, 2023. Until development is restarted, the main focus underground will be on care and maintenance.

During the subject period of this report, the focus of activities at Doris was water management, environmental compliance, and the maintenance of the underground mine.

Sampling locations monitored under this licence (seasonally or when facilities are operational) are provided in Figure 6 through Figure 8 at the end of this report.


Site Wide Water Quality Monitoring Program (Part I Item 3 and Schedule I)

Water quality sampling was conducted throughout the month at monitoring stations identified in Schedule I of the licence (ST-1 through ST-13, TL-1 through TL-12 and MMS-1 through MMS-10). Water quality samples were not collected for monitoring stations that were inactive during the month being reported (e.g., facilities that had not yet been constructed, were frozen during the month, or were not operationally active).

All parameters were compared to the applicable effluent quality limits outlined in Part D and Part F of the licence. No exceedances of effluent quality limits were observed in any samples collected this month. Results of all water quality monitoring are provided in Appendix A attached to this report.

Figure 1 and 2 illustrates effluent quality characteristics for parameters of interest at select monitoring stations.

Figure 1. Biological Oxygen Demand Results Consistently Below Discharge Criteria for Wastewater Treatment Plant (ST8)

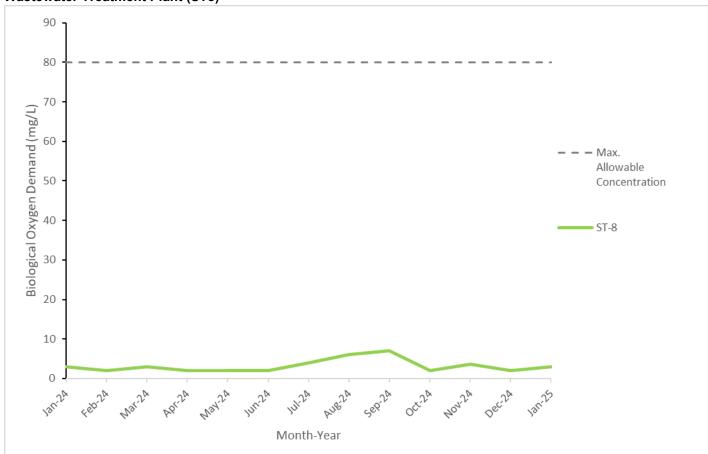

Note: Maximum Average Concentration as per Part F Item 4(b).

Figure 2. Total Suspended Solids Results Consistently Below Discharge Criteria for Wastewater Treatment Plant (ST8)



Note: Maximum Average Concentration as per Part F Item 4(b).

Flow and Volume Measurements (Part F, Part I and Schedule I)

Table 1. Effluent discharge, January 2025

Facility	Station Code	Discharge Volume (m³)	Exceedances of Discharge Criteria	Discharge Location	Licence Reference
Doris Sedimentation Pond *	ST-1	0	N/A	Tailings Impoundment Area	Part F Item 17
Doris Contact Water Pond #1	ST-2	0	N/A	Doris sedimentation pond	Part F Item 17, 18(a)
Non-Hazardous Landfill Sump	ST-3	0	0	Facility not constructed	Part F Item 18(a)
Land farm Sump	ST-4	0	0	Tailings Impoundment Area	Part F Item 18(b)
Doris Plant Site Fuel Storage Area	ST-5	0	0	Tailings Impoundment Area	Part F Item 18(b)
Rob Bay Single 5ML Fuel Storage Area	ST-6a	0	0	Tundra Discharge 13W 432954 7563407	Part F Item 18(b)
Rob Bay Fuel Storage and Containment Berm	ST-6b	0	0	Doris sedimentation pond	Part F Item 18(b)
Doris Sewage Treatment Plant, Effluent	ST-8	788	0	Tundra Discharge 13W 432933 7559057	Part F Item 5(b-c)
Doris Sewage Treatment Plant, Sludge	N/A	9.6	N/A	Tailings Impoundment Area	Part I Item 5(f)
Doris Reagent and Cyanide Storage Facility Sump	ST-11	0	N/A	Tailings Impoundment Area	Part F Item 17
Doris Contact Water Pond #2	ST-13	0	N/A	Facility not constructed	Part F Item 17
Doris Mine Water Discharge	TL-12	54,321	N/A	Tailings Impoundment Area Roberts Bay	
Madrid North Contact Water Pond	MMS-1	0	0	Tailings Impoundment Area	Part F Item 17, 18(a)
Madrid South Primary Contact Water Pond	MMS-2	0	N/A	Facility not constructed	Part F Item 17, 18(a)
Madrid South Secondary Contact Water Pond	MMS-3	0	N/A	Facility not constructed	Part F Item 17, 18(a)
Madrid South Fuel Storage Facility	MMS-5	0	0	Facility not constructed	Part F Item 18(b)
Madrid North Connector	MMS-7	0	N/A	Facility not constructed	
Madrid North Fuel Storage Facility	MMS-8	0	0	Facility not constructed	Part F Item 18(b)
Madrid Mine Water Discharge	MMS-10	0	N/A	Tailings Impoundment Area	

Records of visual monitoring of discharge to tundra are maintained on file as per Part I Item 11.

* Note: Volume reported includes effluent transferred from the Doris Contact Water Pond #1, Landfarm Sump, Doris Plant Site Fuel Storage Area and Madrid North Contact Water Pond.

Table 2. Discharge from TIA to Roberts Bay, January 2025

Month	Number of days of discharge	Discharge Volume (m³)	Exceedances of Discharge Criteria*		
January	31	270,307	0		
Annual Cumulative	31	270,307	0		

^{*} Discharge criteria as outlined in *Metal and Diamond Mining Effluent Regulations*.

Acute Lethality testing conducted as outlined in Part F Item 22 and Part I Item 14

Table 3. Water Usage, January 2025

	Windy Lake (ST-7A)					Doris Lake	Patch Lake	Total Usage		
Month	Domestic Water*	Industrial**	Winter Track	Dust Suppression	Domestic Water*	Industrial Usage**	Dust Suppression	Winter Track	Winter Track	
January	963	0	0	0	0	0	0	0	9,401	10,364
Annual Total	963	0	0	0	0	0	0	0	9,401	10,364
Annual Allowance	43,800					1,930,000			60,000	2,033,800

^{*} As permitted by water licences 2BE-HOP1222 and 2AM-DOH1335 Part E Item 1 and Part I Item 5(a)(b)
** Includes industrial uses such as underground drilling, core processing, milling, concrete batching, etc.

Table 4. Doris Waste Rock and Ore Volumes, January 2025

			Waste F	Rock Manageme	nt		Un	derground Void S	pace	Ore Processing and Tailings Management		
Month	Produced from Mining Activity (tonnes)	Backfilled Directly to Mine (tonnes)	Returned Underground from Temporary Waste Rock Pile* (tonnes)	Waste Hauled for Surface Construction from Surface Stockpile (tonnes)	Moved to Temporary Waste Rock Pile (tonnes)*	Cumulative on Temporary Waste Rock Pile (tonnes)*	Volume Created from Mining Activities (tonnes)	Cumulative Volume Available for Backfill (tonnes)	Cumulative Volume Available for Backfill (m³)	Quantity of Ore Processed** (tonnes)	Total Dry Tailings Placed in TIA** (tonnes)	Total Dry Detoxified Tailings Placed Underground** (tonnes)
December Balance	0	0	0	0	0	765,109	0	1,766,313	862,608	0	0	0
January	0	0	0	0	0	765,109	0	1,766,313	862,608	0	0	0
Cumulative Total	0	0	0	0	0	765,109	0	1,766,313	862,608	0	0	0

^{*} As per Part I Item 5(d)(e)

Note: Void space created from mining activities is determined as the sum of the initial void space as calculated in March 2017 and void space created each month from mining activities. A negative volume of void space created in a month indicates that a higher volume of waste rock and detoxified tailings was returned underground compared to the volume of void space created from new mining activities.

^{**} As per Part I Item 6

Table 5A. Madrid North Waste Rock and Ore Volumes, January 2025

			Waste Rock N	Un	Ore Produced					
Month	Produced from Mining Activity (tonnes)	Backfilled Directly to Underground Mine (tonnes)	Returned Underground from Temporary Waste Rock Pile* (tonnes)	Moved to Temporary Waste Rock Pile (tonnes)*	Moved to Naartok East Crown Pillar Trench for Backfill (tonnes)*	Cumulative on Temporary Waste Rock Pile (tonnes)*	Volume Created from Mining Activities (tonnes)	Cumulative Volume Available for Backfill (tonnes)	Cumulative Volume Available for Backfill (m³)	Quantity of Ore Produced** (tonnes)
December Balance	-	-	-	-	-	289,304	-	360,545	128,766	-
January	0	0	0	0	0	289,304	0	360,545	127,766	0
Cumulative Total	0	0	0	0	0	289,304	0	360,545	127,766	0

^{*} As per Part I Item 5(d)(e)
** As per Part I Item 6

Table 5B. Naartok East Waste Rock and Ore Volumes, January 2025

			Waste Rock N	/lanagement			Un	Ore Produced		
Month	Produced from Mining Activity (tonnes)	Backfilled Directly to Underground Mine (tonnes)	Returned Underground from Temporary Waste Rock Pile* (tonnes)	Moved to Temporary Waste Rock Pile (tonnes)*	Moved to Naartok East Crown Pillar Trench for Backfill (tonnes)*	Cumulative on Temporary Waste Rock Pile (tonnes)*	Volume Created from Mining Activities (tonnes)	Cumulative Volume Available for Backfill (tonnes)	Cumulative Volume Available for Backfill (m³)	Quantity of Ore Produced** (tonnes)
December Balance	-	-	-	-	-	0	-	-	-	-
January	4,955	0	0	0	1,738	0	4,955	4,955	1,738	0
Cumulative Total	4,955	0	0	0	1,738	0	4,955	4,955	1,738	0

^{*} As per Part I Item 5(d)(e)
** As per Part I Item 6

Table 6. Doris Lake Water Level (ST-12), January 2025

In January 2025 Doris Lake water data was not available due to data retrieval issues. Agnico Eagle will continue to troubleshoot the issue and report the data when the issue is resolved.

Month	Minimum Water Level (masl)	Maximum Water Level (masl)	Water Level Water Level		Comparison of Mean Water Level from Month to Month (masl) [^]
January	Not Availab	le due to unreco	0.268	6.033	

^{*} Monthly Water Level Variation is calculated as the difference between the Maximum Water Level and the Minimum Water Level measured during the month.

Waste Management (Part F Item 10 and 11)

In January, Agnico shipped hazardous waste offsite via empty cargo aircraft. Table 7 below summarizes the type and volume of waste shipped offsite for disposal during this month.

Table 7. Waste Backhaul

Waste Type	Volume Shipped* (m³)
Kitchen grease	2

Summary of Assessments of Water Balance and Water Quality Model (Part F Item 24 and Part I Item 12 c)

Average monthly water quality, hydrologic, and climatic monitoring data were collected while in operations during January. Data will contribute to the assessment of the water and load balance model and will be compared to the predicted water quality and elevation within the TIA and will be reported in the annual report for 2025.

Thermal Monitoring (Part I Items 7, 8 and Schedule I)

Thermal monitoring undertaken as per Part I Items 7, 8 and Schedule I is reported in the annual Geotechnical Report.

Site Freshet and Precipitation Conditions (Part I Item 12(d))

Visual monitoring was conducted at the Diversion Berm this month. No issues were identified at the Diversion Berm and associated check dam in January.

Site culvert inspections were suspended of throughout the month of December due to snow build up. Inspections are due to be resumed in freshet of 2025.

[^] Comparison of the change in water level from month to month. This value is calculated by subtracting the Mean Water Level of the current month from the Mean Water Level of the previous month (e.g. February Mean Water level - January Mean Water level). A positive value from this calculation indicates a rise in water level since the previous month; a negative value from this calculation indicates a drop in water level since the previous month.

Incident Reporting

Spill 2025011 - On January 04, 2025, at 03:30 pm, a spill of approximately 15L of sewage was identified by an equipment operator. The spill originated from a leak in a frozen sewage line at the Roberts Bay wash car. The coordinates of the spill are WGS84 68° 10' 29.71" N, 106° 37' 3.03" W and the impacted area is approximately 6m2.

During snow clearing work in the Robert's Bay area, an equipment operator identified frozen sewage coming from the sewage line. The sewage line in question transports sewage from the Robert's Bay wash car to a holding tank next to the wash car.

Once the spill was noticed by the operators, the frozen sewage material was cleaned up and disposed of in the site land farm. The line was repaired to prevent further spillage. Due to frozen conditions, it is not expected that any sewage will be entrained in the gravel pad.

Following an investigation, it was concluded that the root cause of the spill was a failed heat trace on the sewage line to the holding tank. It was further established that the heat trace on that section of the line had remained on the factory setting of 3 °C, which was not high enough to maintain the line's temperature above freezing during the rapid drop in temperature experienced in the days prior.

To reduce recurrence risk, the self-regulating heat trace on the line has been increased to 10o C and all heat tracing on-site has been checked to ensure it is at the required minimum temperature. The heat trace line will be "hardwired" in to prevent it from being accidentally unplugged. An external notifier light will be installed at the wash car to indicate power is flowing through the circuit. Additionally, a temperature set-point check has been added to the monthly preventative maintenance schedule for the heat tracing system.

Should there be any questions regarding this monthly report, please contact me at jason.inkster@agnicoeagle.com.

Yours sincerely,

Jason Inkster

Environmental Coordinator Hope Bay Project

(819) 759-3555 ext. 4600101

Cc:

Jonathan Mesher, Water Resources Officer, CIRNAC Eric Steinmetzer, General Manager – Hope Bay, Agnico Eagle Guy Dufour, Environmental General Supervisor – Hope Bay, Agnico Eagle

Figure 6. 2AM-DOH1335 SNP Monitoring Locations



Figure 7. 2AM-DOH1335 SNP Monitoring Locations



Figure 8. 2AM-DOH1335 SNP Monitoring Locations

