POLARIS MINE

DECOMMISSIONING AND RECLAMATION ACTIVITIES

2004 ANNUAL REPORT

SUBMITTED TO

THE NUNAVUT WATER BOARD

AND TO THE

DEPARTMENT OF INDIAN AND NORTHERN AFFAIRS CANADA

TABLE OF CONTENTS

1. EXECUTIVE SUMMARY IN INUKTITUT

2. INTRODUCTION

3. UNAUTHORIZED DISCHARGES AND SUMMARY OF FOLLOW UP ACTIONS

3.1. Garrow Lake Effluent Discharge

3.2. Hydrocarbon Spills

4. STATUS OF AUTHORIZATIONS AND/OR APPROVALS

5. DECOMMISSIONING AND RECLAMATION PROGRESS REPORT

5.1. Building Demolition

5.1.1. Mill / Offices / Warehouse Facilities / Barge
5.1.2. Cat Generator Building
5.1.3. Concentrate Storage Building
5.1.4. Accommodations Complex
5.1.5. Fuel Tank Farm
5.1.6. Incinerator Building
5.1.7. Foldaway Buildings
5.1.8. Fire Hall
5.1.9. Fresh Water System
5.1.10. Mine Portals
5.1.11. Temporary Dock

5.2. Earthworks

5.2.1. Marine Dock and Adjacent Shoreline
5.2.2. Barge and Adjacent Areas
5.2.3. Garrow Lake Dam
5.2.4. Garrow Lake Wavebreak Structure
5.2.5. Operational Landfill
5.2.6. Little Red Dog Quarry Landfill
5.2.7. Back 40 Area
5.2.8. Roadways

5.3. Contaminated Soil Remediation

5.3.1. Concentrate Storage Shed and Area
5.3.2. Cemented Rock Fill (CRF) Plant Area
5.3.3. Former Quonset Huts Fuel Storage Area
5.3.4. Tailings Thickener Building and Area
5.3.5. Former Fuel Bladder Storage Area
5.3.6. Former Crusher Area
5.3.7. Main Snow Dump
5.3.8. North Portal Ore Stockpile
5.3.9. Exploration Waste Dump / Stockpile Area and Shoreline North of Dock

5.3.10. 2002 Oil Spill Area
5.3.11. Marine Dock and Adjacent Foreshore Area
5.3.12. Barge Area
5.3.13. Accommodations Area
5.3.14. Foldaway Buildings
5.3.15. Fuel Tank Farm and Lube Storage Areas
5.3.16. Tailings Pipelines
5.3.17. Loon Lake Snow Dump
5.3.18. Fire hall Area
5.3.19. Other Areas

5.4. Disposal of Hazardous Materials / Special Wastes
5.4.1. Waste Hydrocarbon Incineration
5.4.2. Confirmation that Fluorescent Light Ballasts Free From PCB's
5.4.3. Shipping of Chemicals / Hazardous Waste Materials

6. PROJECT COST ESTIMATE UPDATE

7. RECLAMATION SECURITY REQUIREMENTS

8. PUBLIC CONSULTATION / PARTICIPATION

9. FRESHWATER USE

10. PHYSICAL MONITORING OF THE SITE

10.1. Summary of Work Done in Response to Inspection / Compliance Reports

10.2. Disposal of Demolition Debris and Contaminated Soils
10.2.1. Disposal of Demolition Debris and Metals Contaminated Soils into the Little Red Dog Quarry Landfill
10.2.2. Disposal of Metals / Hydrocarbon Contaminated Soils Underground into the Mine

10.3. Thermistor Data
10.3.1. Garrow Lake Dam
10.3.2. Operational Landfill
10.3.3. Little Red Dog Quarry Landfill
10.3.4. Mine Workings

10.4. Erosion Monitoring
10.4.1. Garrow Lake Erosion Monitoring
10.4.2. Garrow Creek Erosion Monitoring
10.4.3. Marine Dock and Adjacent Foreshore Monitoring
10.4.4. **Frustration Lake Pier Monitoring**

10.5. Annual Geotechnical Inspection

10.6. Subsidence Monitoring Program

11. GARROW LAKE STRATIGRAPHIC MONITORING

12. WATER LICENCE EFFLUENT MONITORING

12.1. Correspondence Regarding Application of Metal Mining Effluent Regulations

12.1.1. TSS Exceedance at Final Discharge Point
12.1.2. Missed Sublethal Toxicity Testing Event During 2003
12.1.3. Notice of Environment Canada of Alteration of System at Final Discharge Point
12.1.4. 2004 EEM Field Study Program

12.2. Summary of Effluent Monitoring and Effluent Characterization

12.2.1. 2003 Annual MMER Report
12.2.2. 2004 Quarterly and Annual MMER Report

13. GARROW LAKE LIMNOLOGY AND ECOLOGY STUDY

14. STATUS OF SITE AS OF DECEMBER 31, 2004

APPPENDICES

APPENDIX 1	Executive Summary of 2004 Decommissioning and Reclamation Report in Inuktitut – to be completed
APPENDIX 2	Unauthorized Discharges or Spills and Summary of Follow-up Action
APPENDIX 3	Decommissioning and Reclamation Progress Photographs
APPENDIX 4	Project Drawings – partially completed
APPENDIX 5	Geotechnical Reports – to be completed
APPENDIX 6	Contaminated Soil Remediation 2004 Close Out Reports
APPENDIX 7	Hazardous Materials
APPENDIX 8	Miscellaneous Water and Soils Samples Collected From the Site
APPENDIX 9	Project Cost Report
APPENDIX 10	Record of Debris Placed into Little Red Dog Quarry Landfill
APPENDIX 11	Record of Contaminated Soils Excavated and Locations of Disposal In the Mine
APPENDIX 12	Rock Temperatures Measured From the Underground Mine Workings
APPENDIX 13	Garrow Lake Erosion Monitoring
APPENDIX 14	Garrow Creek Erosion Monitoring – to be completed
APPENDIX 15	Marine Foreshore Monitoring – to be completed
APPENDIX 16	Garrow Lake Stratigraphy Monitoring
APPENDIX 17	Correspondence Between Teck Cominco and Environment Canada Regarding the Application of the Metal Mining Effluent Regulations
APPENDIX 18	Garrow Lake Effluent Discharge Monitoring Data
APPENDIX 19	Limnology and Ecology of Garrow Lake
APPENDIX 20	Report and Study CDs and DVDs

1. EXECUTIVE SUMMARY IN INUKTITUT

Refer to Appendix 1 for an executive summary of plans, reports and studies conducted under this licence during the period January 1, 2004 to December 31, 2004 that has been translated into Inuktitut. This report also includes information required as part of the 2003 Annual report that had not been previously reported. Outstanding

2. INTRODUCTION

The Polaris Decommissioning and Reclamation Plan (DRP) dated March 2001 received its initial conditional approval April 15, 2002. The Closure Plan was jointly conditionally approved by the Nunavut Water Board ('NWB') and the Department of Indian and Northern Affairs Canada ('INAC'). The Closure Plan has subsequently received further approvals. The approvals contain reporting requirements and this document has been prepared to consolidate all of the reporting requirements into one document. This report is required by both NWB and INAC on a quarterly basis with an annual report due by March 31st of the subsequent year. This is the fifth report related to the decommissioning, reclamation and monitoring of the Polaris Mine since closure. It combines the annual reporting requirements not previously reported for 2003 as well as all of the reclamation and monitoring activities that occurred during 2004.

3. UNAUTHORIZED DISCHARGES AND SUMMARY OF FOLLOW UP ACTIONS

3.1. Garrow Lake Effluent Discharge

A single grab sample of effluent taken on July 7th, 2004 from the Final Discharge Point of Garrow Lake had a Total Suspended Solids (TSS) level of 117 mg/L which exceed the TSS limits of both the Water Licence and the Metal Mining Effluent Regulations (MMER). Concurrently with taking this sample, the monthly characterization which includes an acute lethality samples were also collected. There was no acute toxicity of either the Rainbow Trout or the Daphnia magna (i.e. LC50s in both cases were > 100% effluent). All of the metals concentrations were within Water Licence and MMER limits. It is apparent that the TSS was the result of high flows in the newly re-established Garrow Creek channel and not a reflection of the water quality within Garrow Lake itself. All subsequent water samples from the Final Discharge Point were compliant for the remainder of the discharge season. A copy of the letter submitted to Environment Canada and their response are included in Appendix 2.

3.2. Hydrocarbon Spills

- During planned clean up of known hydrocarbon contaminated soils in the under Foldaway #1, liquid petroleum was encountered. Approximately 400 litres of hydrocarbon were recovered by pumping it into barrels. The oil was then stored on site until it was incinerated in the on-site hydrocarbon incineration system. While this was in accordance with the DRP, Environment Canada requested that this be reported to the Spill Line, which was done (refer to file note in Appendix 2). As this was in an area of known hydrocarbon contamination, the surrounding contaminated soils were excavated as planned. Gartner Lee Ltd. (GLL) conducted confirmation testing to document that the remediation efforts were

successful. Their report on this area is included site "Contaminated Soil Remediation 2004 Close Out Reports" included in Appendix 5.

- On June 10th, 2004 a hydrocarbon spill was identified. A 205 liter oil drum had been punctured during snow clearing operations. The spill was reported to the N.W.T. Spill Line. The spill was immediately cleaned up and a Gartner Lee Ltd. representative directed the remedial activities and the subsequent confirmatory sampling. As this was a minor spill, it is included in this report in Appendix 2 rather than as part of the more comprehensive site environmental close out reports.
- In March of 2003, a fuel line leaked in the area of the Accommodation complex utilidor. Sampling of the area was conducted confirming that soils had been contaminated by the fuel but remediation of this area was deferred until remediation planned for the area in the DRP was conducted. In the summer of 2004, the contaminated soil was excavated and confirmatory sampling was conducted by Gartner Lee Ltd. confirming the remediation of the area had been successfully completed. Their technical memorandum reporting on the test results is included in Appendix 2.

4. STATUS OF AUTHORIZATIONS AND/OR APPROVALS

Authorizations and/or approvals granted during 2004 were as follows:

1. Request to place metals contaminated soils into Little Red Dog Quarry Landfill ("LRDQL") and additional hydrocarbon contaminated soils underground in the mine workings was approved on February 9, 2004.
2. Request for Modification of Haulage Location (Garrow Lake dam core material into the barge excavation) dated October 15, 2004.
   - Approved March 5, 2004.
3. Letter of Direction regarding the Cover Cap Design for Little Red Dog Quarry. The letter identified technical information to be supplied to INAC and the NWB as part of the design.
4. Letter of Approval for decommissioning the Garrow Lake wavebreak structure was issued July 8, 2004. The letter requires that visual observations be completed during low flows at the end of the summer to confirm that the channel is not obstructed and that a survey of the wavebreak structure is completed.

5. DECOMMISSIONING AND RECLAMATION PROGRESS REPORT

Reclamation activities were at relatively low levels during the beginning of the year due to the end of the Christmas period and the continuation of the cold, dark period of the arctic winter. Maintenance activities increase in advance of other site activities to prepare for the coming construction season.

Manpower levels were as follows:

	Peak	Minimum
January	58	20
February	73	58
March	77	61
April	119	77
May	131	121
June	128	113
July	121	97
August	73	24
September	20	0

5.1. Building Demolition

5.1.1. Mill / Offices / Warehouse Facilities / Barge

- At the beginning of the year, demolition of the barge was 98% complete with only the barge loading ramp remaining intact. In the first quarter, burial of barge hull sections placed into Little Red Dog Quarry Landfill (LRDQL) was accomplished using metals contaminated soils. The final portion of the barge (the loading ramp), was demolished and disposed of in July. Refer to Appendix 3 for photographs.

5.1.2. Cat Generator Building

- After demolition of the main power generation system in the Barge in 2003, site power was supplied by the Cat Generators in a building located to the west of the former barge area. As a result, excavations of contaminated soils had to occur around this facility until it was finally demolished in June 2004. At this time a portable generator system was used to supply power to the Accommodations Complex. Once the Cat Generator Building was demolished, clean up of contaminated soils under the building was completed. Refer to Appendix 3 for photographs of the facility.

5.1.3. Concentrate Storage Building

- At the beginning of the year, demolition was 98% complete with only a few footing remaining in place. This was completed during the summer and the area re-graded. Refer to Appendix 3 for photographs of demolition and site contouring.

5.1.4. Accommodations Complex

- The Accommodations Complex was in use until the beginning of August when a reduced crew size permitted relocation to a temporary camp utilizing former exploration camp trailers, converted storage trailers, converted sea containers and tents. Refer to Appendix 3 for photographs of the Accommodations Complex being demolished and the subsequent contouring of the site. Along with the demolition of the Accommodations Complex, the service corridors were also removed. A photograph of the temporary camp is also included in Appendix 3.

5.1.5. Fuel Tank Farm

- This was one of the final facilities to be demolished as fuel was required through to the end of the project. In March fuel from one of the two main storage tanks was transferred into the other tank. Once the first tank was empty, it was cleaned

and demolished. The second main tank was demolished in August only after a portable fuel storage bladder was set up. Recontouring of the Fuel Tank Farm area was one of the last activities on site continuing until a few days before the site was abandoned in September. Refer to Appendix 3 for photographs of the demolition and of the temporary fuel bladder. During the September INAC and Water Board inspection of the site, this was one of the areas identified as requiring additional re-sloping due to the steepness of the fill remaining in the area.

5.1.6. Incinerator Building

- The Incinerator Building was a temporary structure build specifically to house the custom fabricated incinerator for the reclamation project. The incinerator was used in 2003 and shut down through the early part of 2004. It was restarted in May to complete the incineration process of the waste hydrocarbons. Any hydrocarbons on site at the end of the project were removed from the island for incineration and/or recycling. Demolition of the building occurred in August. The incinerator was salvaged for future use in the north. Refer to Appendix 3 for photographs of the facility and re-contouring of the site after demolition of the building.

5.1.7. Foldaway Buildings

- There were 3 metal buildings located south of the Concentrate Storage Building along the shoreline. These were used for storage and some maintenance activities during operations and reclamation. Excavation of contaminated soils surrounding these buildings was initiated in May and the buildings were demolished in June. Photographs of this are included in Appendix 3.

5.1.8. Fire Hall

- The Fire Hall area continued to be used as a fire hall and emergency training facility through until May. At that time a tent was constructed to house the fire truck once the building demolition began. Refer to Appendix 3 for photographs of this area.

5.1.9. Fresh Water System

- The Fresh Water System was one of the last services systems to be demolished. Once the reduced crews moved to the temporary camp and demolition began on the Accommodations Complex, the pump house and fresh water pipeline were removed after filling the water reservoir. In late August, the reservoir was finally demolished and water was trucked from Frustration Lake for the final days of the project. Refer to Appendix 3 for photographs.

5.1.10. Mine Portals

- There were four portals allowing access underground. They were the Main Portal, the Conveyor Portal (CV03), the Exploration Portal and the North Portal. Once haulage of contaminated soils was completed the portals had concrete seals constructed within the mine openings (at a location deep enough that the overlying strata was at least twice as thick as the drift height). Appendix 3 has photographs of each of these as the sealing activities proceeded. Final contouring of the ground surface makes the locations of these hard to identify now that it has been completed.

5.1.11. Temporary Dock

- The former Temporary Dock consisted of several I Beam piles that remained just off the foreshore by the Foldaway Buildings in several feet of water. Early in 2004 while the sea ice was at its thickest, these were cut-off by excavating through the sea ice to the base of the I Beams.

5.2. Earthworks

Earthworks were the major challenge of the project due to the volume of materials to be moved and the difficulty of working during the dark, cold portion of the winter. While many photographs of the work have been taken, the photographs are of limited value in allowing the reader to visualize the success of the work. The best method of assessing the recontouring efforts is site visits where detailed inspections can be conducted. Appendix 3 contains photographs of key areas of the work as it progressed during 2004.

5.2.1. Marine Dock and Adjacent Shoreline

- Starting in early April, a crew of divers was mobilized to cut off the sheet piles as part of the decommissioning of the marine dock. A second crew of divers was mobilized in May due to slow progress. Removal of the piles was completed in May while the ocean was still covered by the ice pack.
- In the area of the dock and barge, extensive work was done to ensure the remediated areas were gently sloped in accordance with the Westmar designs.
- During 2003 much of the recontouring of the adjacent south foreshore area had been undertaken with a berm left intact along the foreshore. In 2004 the last phase of the recontouring of the foreshore was to remove the berms. This was done while the ocean was still ice covered.
- More extensive recontouring work was required on the north shoreline area due to the amount of fill that was in these areas. Only some of this work had been conducted during 2003 so the majority of the recontouring work had to be completed during the 2004 construction season.
- Work along the foreshore was completed before the ice pack cleared in the summer. By the end of August, the action of ice being pushed onto the shore through the summer season had already started to naturalize the appearance of the beach. Refer to Appendix 3 for photographs of the work.
- Detailed surveys of this area have been completed and as-built drawings are in the draft stage but not yet ready for submission.

5.2.2. Barge and Adjacent Area

- The majority of the barge excavation was completed in 2003. Excavation of hydrocarbon contaminated soils continued as a focus of work between the dock and the Cat Generator Building, and to the north of this area were the focus of work during the first 6 months of 2004.
- During backfilling of the barge excavation, materials from the decommissioning of Garrow Lake dam were hauled and placed into the barge excavation. Appendix 4 has a drawing of the barge excavation showing the location where the dam fill material was placed.

5.2.3. Garrow Lake Dam

- Work on decommissioning the Garrow Lake Dam occurred primarily in March and April 2004 while there was no flow in the creek. Excavation of the dam

materials went smoothly. One blast was required to remove the dam material. The rest of the dam material was excavated using a ripper. For the one blast, non-ammonia type explosives were used. As required by DFO, vibration monitoring in Garrow Lake was conducted but the vibrations were so low that the monitoring device wouldn't record the readings. Once the centre of the dam was removed and the creek channel prepared, geotextile and rip-rap were placed into the channel during April (Refer to photographs in Appendix 3).

- Detailed surveys of this area at the end of construction have been completed but drawings are in the draft stage and must still be submitted.

5.2.4. Garrow Lake Wavebreak Structure

- During the early winter of 2004, using surveyor guidance to locate the former creek channel, remnants of the wavebreak structure were removed down to native materials in the creek channel to ensure that there were no blockages of the channel. Additionally, the top of the wavebreak structure visible above ice level was lowered to minimize the visual impact of the structure.
- The wavebreak was surveyed after the mine ceased production by Focus Engineering as part of the bathymetric survey of Garrow Lake. However a more detailed, updated survey is required.
- This area will be inspected each year as part of the annual geotechnical inspection.

5.2.5. Operational Landfill

- The 1.8 metre thick cap on the Operational Landfill was completed in 2004. During the June 20th to 22nd 2004 inspection by INAC, it was noted that the surface materials in some areas of the cap had been segregated during construction so that materials on the top surface of the landfill were too course while materials on one area of the face of the landfill appeared too fine. Subsequent to the inspection, a layer of finer material was placed over the coarse rock on the top cap of the landfill and additional coarse rock was placed on the face of the landfill in the areas identified as being too fine. Completion of this repair was noted by INAC in its September 9th, 2004 site inspection.
- New thermistors were purchased with closer spacing of the temperature monitoring bulbs at the top of each string (for more detailed monitoring of temperatures within the active zone of the cap). However, in September when contractors demobilized from the site, the new thermistors had not been installed. The thermistors will be installed in the summer of 2005 when crews return to site.
- Detailed surveys of the landfill were done at all key stages of construction and the locations of the thermistors. The drawings are in the draft stage and are not quite ready to be submitted as engineer stamped as-built drawings.

5.2.6. Little Red Dog Quarry Landfill ('LRDQL')

- At the end of 2003, the last major debris from the Barge hull had been cut up and placed in LRDQL for burial.
- Drilling and blasting on the upper areas of the limestone quarry continued through until August to produce adequate materials for the landfill cap.
- On February 9th, 2004 INAC and NWB approved the placement of metals contaminated soils into LRDQL. This material was used as infill material to complete burial of the barge hull debris as well as other debris generated in 2004.

- During 2004, 80,300 cu.m. of metals contaminated soils were disposed of in LRDQL. The capacity of LRDQL was adequate to dispose of the contaminated soils below the limestone bedrock surrounding the quarry. The elevation of the notch in LRDQL was slightly lowered to properly tie in with the design of the landfill cap. This is to ensure that any precipitation can drain out of the quarry without pooling on the cap.
- The thermistor pipes installed while the landfill was being constructed all survived. The new thermistors designed with closer spacing of the temperature monitoring bulbs (for more detailed monitoring of temperatures within the active zone of the cap) had been received. As completion of the cap for LRDQL was one of the last tasks to be completed on site, there was no time to install the monitoring thermistors before crews left site in September. The thermistors will be installed in the summer of 2005 when crews return to site.
- Detailed surveys of this are were done at all key stages of construction of the construction of the cap. The drawings are in the draft stage and are not quite ready to be submitted as engineer stamped as-built drawings.

5.2.7. Back 40 Area (Including CRF Area, New Quarry, North Pit, Subsidence Area, North Portal Area)

- Contouring of the pit walls in the New Quarry area had been completed in 2003. During 2004 additional fill was excavated from the quarry for use throughout the site. These areas were re-graded upon completion. However, in September 2004 some additional material was excavated from the New Quarry to place over an area in the Reclamation Landfill where test pitting indicated some debris was covered by less than 2 metres of fill. This area of excavation in the quarry was not re-sloped at the end of work season. During the September 2004 INAC site inspection, this deficiency was identified. This work will be undertaken when equipment operators are mobilized to site, currently expected to be in 2006.
- Extensive re-contouring in the CRF area, the North Portal area and north of the Subsidence area was competed during 2004.

5.2.8. Roadways

- Recontouring of roadway shoulders was ongoing through most of the summer construction season. In areas where the roads had steeper slopes, they were re-sloped. In late August and the first week of September, culverts in all of the roads were removed to allow natural drainage patterns to be restored. Additionally, areas where water flowing along side road shoulders was being concentrated, water bars were installed. These areas will be the inspected as part of the annual geotechnical monitoring program to ensure that these areas are stable from erosion.

5.3. Contaminated Soil Remediation

5.3.1. Concentrate Storage Shed and Area

- Completed in 2003 although additional discussion of residual metals contamination in this area confirming the adequacy of the remedial efforts is still outstanding.

5.3.2. Cemented Rock Fill (CRF) Plant Area

- Previously completed.

5.3.3. Former Quonset Huts Fuel Storage Area

- Previously completed.

5.3.4. Tailings Thickener Building and Area

- Previously completed

5.3.5. Former Fuel Bladder Storage Area

- Previously completed.

5.3.6. Former Crusher Area

- Previously completed.

5.3.7. Main Snow Dump

- Previously completed.

5.3.8. North Portal Ore Stockpile

- Previously completed.

5.3.9. Exploration Waste Dump / Stockpile Area and Shoreline North of Dock

- Previously completed.

5.3.10. June 2002 Oil Spill Area

- Previously completed.

5.3.11. Marine Dock and Adjacent Foreshore Areas (South Shore and North Shore)

- Extensive work removing contaminated soils in the dock was ongoing through most of the construction season and was successfully completed in 2004. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.12. Barge Area

- Extensive work removing contaminated soils in the area of the Barge and Cat Generator Building continued from early in 2004 through until June. Contamination in this area was more extensive than anticipated. Initially the assumption was that contamination that occurred during operations would be limited by permafrost. However it now appears that substantial contamination occurred during the construction phase of the project when there were more excavations in the area resulting in contamination being found in areas much deeper than anticipated. This resulted in the volumes of contaminated soils increasing substantially over planned volumes. Remediation was successfully completed in this area. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.13. Accommodations Area

- As part of the ESA, an area of concern related to hydrocarbon contamination around the fuel tank located at the north east corner of the Accommodations Complex was identified. Remedial excavations started on July 5, 2004 prior to demolition of the building but final investigations and remediation had to wait until the building was demolished to access underneath it. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.14. Foldaway Buildings (3)

- Excavation of contaminated soils was commissioned in May in areas surrounding the buildings. The buildings were demolished in June and excavations of contaminated soils continued through June and were completed in July. Remediation of the hydrocarbon contamination of this area was successful. Refer

to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.15. Fuel Tank Farm and Lube Storage Areas

- The Fuel Tank Farm was located within a bermed and lined area. In 2002 there was a significant oil spill in an area adjacent to the Fuel Tank Farm which was the subject of a major remedial project and has been previously reported.
- The Lube Storage area located adjacent to the Tank Farm was identified in the 1999 and 2000 ESA investigations as having both metals and hydrocarbon contamination. Additional investigations in the Lube Storage area were conducted in both 2003 and 2004 to outline the boundaries of the contamination. Remediation of these areas was initiated May 1, 2004 and was completed successfully on August 30, 2004. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.16. Tailings Pipelines

- The Tailings Pipelines (2) extended from the process facilities located at the Barge complex to the Thickener Building near Garrow Lake. The Tailings Thickener Building area was remediated in 2003 and the results previously reported. The 1999 and 2000 ESA of the Tailings Pipeline route documented a number of spills that had occurred during operations. These spills had been reported by the mine and immediate clean-up of the spills had been undertaken. However, the spills had been cleaned up without the benefit of guidance by environmental sampling. As a result, residual contamination remained and these were cleaned up during 2003 and 2004. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.17. Loon Lake Snow Dump

- This snow dump was identified in the 1999 and 2000 ESA as an area of potential metals contamination. Sampling at the time identified one sample exceeding remedial objectives for lead but none for zinc. Additional field investigations were undertaken in 2003 indicating that remediation was required for this area. Prior to remedial excavations occurring, the snow dump had to be melted by spreading it out. Excavation of contaminated soils commenced June 10th and was successfully completed on August 8th 2004. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.18. Fire Hall Area

- The 1999 and 2000 ESA identified this as an area of concern for both metals and hydrocarbon contamination. In 2003 additional delineation drilling was done and excavation of contaminated soils was initiated on July 2003. Work continued until September 2003 and was discontinued at that time due to interference from buildings and roads that were still in use. In late April 2004 and continuing through until early July, excavation of contaminated soils continued until confirmatory sampling indicated that the areas of contamination had been successfully remediated. Refer to the Gartner Lee Ltd. "Contaminated Soil Remediation 2004 Close Out Reports" in Appendix 6.

5.3.19. Other Areas

- There were a number of other area identified in the 1999 and 2000 ESA as being areas potentially having contaminated soils or other concerns. These included:

- Construction Landfill – this area was relocated to become part of the Operational Landfill and capped
- Fire Training Area – this area was identified as an area of potential concern prior to the development of site specific remedial objectives (SRQs). Subsequent review of sample data indicated that the area met the SRQs and therefore no remedial work was undertaken in this area.
- Explosives Storage / Detonator Storage Area - this was identified due to the storage of dangerous materials (explosives) which have subsequently been removed.
- Surface Above the Active Mining Area – this was identified as an area of potential concern due to the subsidence of the ground surface over the underground mine workings. This was discussed earlier in this report.

5.4. Disposal of Hazardous Materials / Special Wastes

5.4.1. Waste Hydrocarbon Incineration

- At the end of 2003 a stock of waste hydrocarbon substances was stored on site. In May on-site incineration was re-started to destroy the remaining hydrocarbon liquid wastes. Any hydrocarbon wastes remaining at the end of the project were shipped off site for recycling and/or incineration..

INCINERATOR
INCINERATION OF WASTES BY MONTH - 2004

	Imp. GALLONS		LITERS	
2004	WASTES	FUEL	WASTES	FUEL
JAN				
FEB				
MAR				
APR				
MAY	2,655	313	12,070	1,424
JUN	11,772	2,862	53,515	13,009
JUL	3,904	1,156	17,750	5,254
AUG				
SEP				
YTD TOTALS	18,331	4,331	83,335	19,687
TOTAL BURNT	22,662		103,023	

5.4.2. Confirmation That Fluorescent Light Ballasts Did Not Contain PCB's

- While the mine was constructed after the date when PCB's in electrical equipment had been banned by Federal legislation, GLL still conducted inspections of records, interviewed key maintenance personnel and checked manufacturing dates

on transformers. While the testing that confirmed the absence of PCB's in the transformer oils, there was no formal documentation in the ESA stating that fluorescent light ballasts did not contain PCB's. As a result, GLL prepared a technical memorandum verifying that they had conducted the interviews and that a range of fluorescent fixtures had their manufacturing dates checked to confirm that there were no PCB's in the fluorescent light ballasts. The memorandum is contained in Appendix 7.

5.4.3. Shipping of Chemicals and/or Hazardous Waste Materials

- At the end of the project when personnel and equipment were demobilized from the site, the remaining chemicals and hazardous wastes were shipped out on the sea lift. These materials included:
    - Waste oils
    - Waste batteries (drained)
    - Waste battery acid
    - Various waste gases
    - Waste aerosol tins,
    - Waste Freon
    - Waste Halon

  These materials were transported by Desgagnes to Ste-Catherine, Ontario where it was received by Buckham Transport and delivered to Bennett – MRRI (a registered environmental disposal company) in Cornwall, Ontario for disposal or recycling.

6. PROJECT COST ESTIMATE UPDATE

Appendix 9 contains the cost for the work completed to year end 2004 representing the virtual completion of the reclamation phase of the Decommissioning and Reclamation Plan (DRP).

In summary, total DRP costs to the end of the decommissioning and reclamation portion of the project plus the future monitoring costs were $69,264,000.

Major departures from the original budget were primarily due to the following:

- under estimating the quantities of contaminated soils,
- under estimating manpower and supply costs for equipment maintenance
- travel costs both due to higher than forecast airfares and increased usage due to the increased manpower levels.
- Contractor indirects were higher than forecast partially due to increase volume of work.

7. RECLAMATION SECURITY REQUIREMENTS

As is noted in a number of sections of this report, there are some technical reports and as-built drawings outstanding at this time. In addition, the documentation to rationalize the legal names between permits, licenses and leases is also outstanding. When these outstanding items are submitted, they will be accompanied by a request to reduce security

being held by INAC and the NWB to levels more representative of current reclamation liabilities of the site.

8. PUBLIC CONSULTATION / PARTICIPATION

At this stage of the reclamation process there was little public consultation as the planning and execution of the plan was nearing the last 8 months of the project.

Inuit employment was primarily through participation of Qikiqtaaluk Corporation (QC) who were responsible for the majority of the earth moving on the project. Teck Cominco ensured that GLL utilized at least one Inuit assistant for environmental monitoring through most of the work season. As earthmoving activities were seasonal, Inuit content of the work varied each month and is listed below:

- January 2
- February 3
- March 1
- April 5
- May 15
- June 14
- July 12
- August 4
- September 0

Upon demobilizing from the site, a number of sea containers were loaded primarily with furniture and office materials for delivery and distribution in Resolute Bay.

9. FRESHWATER USE

Freshwater use from Frustration Lake for all uses during 2004 was:

MONTH	Volume (M^3)
January	19,526
February	20,222
March	20,679
April	18,107
May	26,669
June	19,132
July	19,647
August	727
September – December	0
Total for 2004	**144,708**
Quantity Licensed for 2004	**200,000**

Water use in August was low despite having up to 73 people on site as the water reservoir was full so that pumping of water from Frustration Lake was minimal. The system is now demolished so that reporting of water use will cease now that the site is normally vacant except for a few people during site inspections.

10. PHYSICAL MONITORING OF SITE

10.1. Summary of Work Done In Response to Inspection Compliance Reports

There were two site inspections by INAC and/or the Water Board during 2004. The first inspection was conducted from June 20, 2004 to June 22, 2004. A letter from the Water Board and INAC dated July 21, 2004 identified the following issues identified during the inspection to be responded to:

- Garrow Lake Dam

TCL agreed to re-grade some of the soft soils observed at the downstream side of the former dam. This was undertaken in August. There are also some areas on the upstream side of the dam that have snow mixed in with soils and appear to require additional grading. As the majority of this area is thought to be made up primarily of snow and not soils, it will be necessary to review this area once the snow has melted which will be in 2005 at the earliest. Monitoring of the dam slopes will be part of the annual geotechnical inspection of the site.

- Subsidence Zone

TCL was to initiate monitoring of the subsidence zone using a GPS system. This has been done using a GPS system that is accurate within centimeters. In August 2004 a detailed survey of the subsidence area was conducted. Contours of this area were developed by Focus Engineering and are included in Appendix 4 of this report. The drawing also includes a number of cross sections comparing the 2003 survey results to the 2004 survey results. The only significant change between the two surveys was caused by the placement of fill over the Reclamation Landfill area in 2004.

TCL was to submit a geotechnical review of the Subsidence Area by the Golder Associates. TCL is currently reviewing a draft of this report which will be forwarded upon completion.

TCL is expected to initiate any long-term, post closure mitigation measures that may be required. TCL recognizes their responsibility to do so but is confident that conditions in the subsidence area will not result in either public or wildlife safety issues.

TCL was requested to conduct test pitting in the Reclamation Landfill area to confirm that debris is at least 2 metres below the surface. TCL did this in August and found a limited area where there was thinner cover. As discussed in the first paragraph of this section, additional fill was placed on top of this area to ensure at least 2 metres of cover is in place.

- Operational Landfill

The June inspection identified that the top cover on the Operational Landfill was too coarse. During placement of the cover materials, the use of dozers to spread the fill resulted in segregation of the cover materials in some areas. TCL added an additional 300mm (approximate) thick lift of finer material to the top of the landfill to provide a more graded cover. Additionally, although not noted in the inspection report, on the face of the landfill, there was an area where the finer materials that segregated from the coarse materials had been placed. A lift of coarser cap materials was added to this area resolving the concern.

- Product Storage Area

TCL was to prepare a letter more fully explaining the area of residual metals contamination at the Product Storage area to confirm that there is no risk of exceeding remedial targets if migration of the contamination were to occur. This technical memorandum is outstanding at the time of this report.

TCL had requested that one more site inspection be conducted prior to completion of the reclamation and decommissioning work. A second inspection occurred on September 9th, 2004 which was shortly after the contractor had demobilized from site. On November 8th, 2004 a report of the site inspection by BGC Engineering was submitted to the NWB. No formal response from the NWB or INAC was received by TCL during 2004. TCL has the following comments to make with regard to the recommendations contained in BGC's report:

- BGC recommends that the following areas undergo further re-sloping:
  a) below where both the incinerator building, the tank farm, and the exploration portal were located.
     - This will be done but will be coordinated with other earth moving requirements that may become apparent over the next year or two at the site.
- Blade down the crest of the slope above the main portal.
  - Some minor re-sloping will be done here at the same time as the previous items.
- Remove reinforcing steel from above the Main Portal and Exploration Portals
  - This will be done over the next few years as final clean-up of the site proceeds.
- Remove scrap metal from the surface from reclaimed areas for safety and aesthetic reasons.
  - This will be done starting in the summer of 2005.
- Remove piles of snow from the upslope areas of Garrow Dam as they thaw.
  - Will be done as the snow melts and if required. Will be reviewed in the summer of 2005.
- Report on the subsidence assessment by Golder Associates.
  - A draft of this report is currently being reviewed and will be submitted upon receipt of the final report.
- Report on the analysis of the rusty coloured soils in the drained area of Garrow Lake.
  - During the 2004 studies being conducted by Azimuth Consulting group of the Garrow Lake and Garrow Creek areas, rusty coloured sediments were observed in the drained area of Garrow Lake between the lake and the former dam. Patrick Allard of Azimuth took a typical sample of the material on August 26, 2004 and submitted it to ALS laboratories for analysis. Appendix 8 has the laboratory analysis of this soil (Labeled "G Lake"). The zinc concentration of the soil was 1160 mg/L which was well below the site specific remedial soil objectives for the site.
- Provide As-Built Drawings for the Sealing of the Mine Portals
  - All four mine portals were plugged and sealed in conformance with the approved construction drawings. The drawings have been completed to the

approval stage and are attached in Appendix 4. Engineer stamped drawings will be provided in the paper copies of this report and may have minor changes due to the review process.

- Provide As-Built Drawings for Little Red Dog Quarry
  - Detailed surveys of the placement of debris, metals contaminated soils, the cover cap, and the locations of the thermistor pipes have been done but the final drawing not yet complete. This is outstanding but will be completed as it is a necessary part of documenting conditions at the site.
- Install Thermistors and Data Loggers in the Operational and Little Red Dog Quarry Landfills
  - New thermistors with closer spacing of thermistors (to more accurately monitor the landfill cap area), have been purchased. They will be installed in the summer of 2005 when personnel return to site. Data loggers are being considered but in 2005 it is expected that personnel will be at the site on a regular basis to read the thermistors during the summer months.
- Monitor Outflow Through the Wavebreak at Garrow Lake for Erosion
  - This will become a part of the annual geotechnical inspection of the site starting in 2005.
- Monitor the Stability of the Marine Foreshore
  - This will become a part of the annual geotechnical inspection of the site starting in 2005.
- Forward Remaining Contaminated Soil Close Out Reports
  - These are included in Appendix 6 of this report.

10.2. Disposal of Demolition Debris and Contaminated Soils

10.2.1. Disposal of Demolition Debris Into Little Red Dog Quarry Landfill

Refer to Appendix 10 for a listing of general descriptions of the types of demolition debris transported to LRDQL during the year along with a photographic log. Also included in Appendix 10 are drawings of the locations within LRDQL that the debris was placed.

During 2004, metals contaminated soils were placed into LRDQL as well. The as-build drawing of LRDQL in Appendix 4 identifies the locations that these soils were placed. (Drawing is not included at this time – to be completed).

The approval to dispose of metals contaminated soils in LRDQ Landfill specified that if there was any drainage from the quarry, that it be sampled to confirm that the run off does not contain excessive metals. During the spring freshet and the warm months of July, the fills within LRDQ Landfill were below the lip of the quarry pit so that there was no run-off from the landfill materials (including metals contaminated soils) as they were all contained within the pit. In late August when the final cap was being placed, there was no run off to sample. It is important to note that the top of the metals contaminated soil layer at the end of the project was still at a lower elevation that the lip of the limestone quarry. The final cap (1.8m minimum thickness) was graded as per the

approved design drawings to gradually slope towards the notch in the pit so any surface run-off will flow out of the quarry area.

10.2.2. Disposal of Metals / Hydrocarbon Contaminated Soils Underground in the Mine

As noted earlier in the report, on February 9th, 2004 approval was granted to dispose of metals contaminated soils in LRDQ Landfill so that the remaining space in the underground workings could be reserved for the hydrocarbon contaminated soils. Appendix 11 contains a reconciliation of the total tonnes of contaminated materials excavated and their location of disposal by type of contamination (metals contaminated, hydrocarbon contaminated or co-contaminated by both metals and hydrocarbons) soils. By the end of the project, most of the readily available space within the mine had been filled.

Appendix 11 includes the mine level plans indicating the locations that contaminated soils were stored. These plans are complete to the end of the project and represent the conditions as they were when the mine portals were sealed.

10.3. Thermistor Data

10.3.1. Garrow Lake Dam

Siphoning of Garrow Lake was completed in the 3rd Quarter of 2003. Removal of the dam commenced so that the thermistors in the dam have been decommissioned so there is no temperature data to be reported.

10.3.2. Operational Landfill

Capping of the landfill was completed in 2004 but the new thermistors were not installed at the time contractors demobilized from the site in September. In the summer of 2005 when crews return to site, the existing thermistors will be removed and the new thermistors purchased will be installed.

10.3.3. Little Red Dog Quarry Landfill

Completion of the cap on LRDQ Landfill occurred right at the end of the project, just before contractors demobilized from site n September 2004. When crews return to site in 2005, the new thermistor strings custom manufactured for this area will be installed.

10.3.4. Rock Temperatures Surrounding Mine Workings

As part of the approvals for TCL to store additional hydrocarbon contaminated soils in the mine workings, TCL was requested to provide additional ground temperature information surrounding the mine workings. A series of mine plans are presented in Appendix 12 that indicates the rock temperatures 3 metres into the adjacent the walls of the underground tunnels. Thermometers were inserted into existing drill holes for several hours until they stabilized. While these temperatures may not be precise, they do give confidence that the rock temperatures are sufficient to maintain the materials in a frozen state.

10.4. Erosion Monitoring

10.4.1. Garrow Lake Erosion Monitoring

There was no sign of any erosion either through visual inspection or through the monitoring of the erosion pins. It should be noted that these pins are now some distance from the edge of the lake as the shoreline becomes re-exposed as the elevation of the lake decreased during the past few years of siphoning. Snow conditions prevented obtaining readings in June and September as the pins were buried in snow.

The results of the 2004 monitoring are presented in Appendix 13. Currently the photographs from August are not in the report and are being obtained from GLL for inclusion.

10.4.2. Garrow Creek Erosion Monitoring

The data has been collected but has not yet been prepared in report format. It will be presented as Appendix 14.

10.4.3. Marine Dock and Adjacent Foreshore Monitoring

During decommissioning of the dock and adjacent foreshore areas, monitoring of the foreshore area was conducted by Gartner Lee Ltd. The data has been collected but has not yet been finalized in report format. Once work on the dock and foreshore was completed, in August 2004 Azimuth Consulting Group coordinated an intertidal and subtidal survey of the dock and foreshore area as required by the DFO Authorization for the work. A towed underwater video camera referred to as a SeaBed Imagery and Mapping System (SIMS) was used to collect the video images of the sea bottom. Their report titled "Intertidal and Subtidal Photographic Survey – Former Dock Area, Polaris Mine" is included in Appendix 15. In addition, Appendix 20 contains three DVD's. Two of the DVD's depict the SIMS imagery used to develop the report and the third DVD depicts subtidal biota from a SCUBA survey.

10.4.4. Frustration Lake Pier Monitoring

The approvals for decommissioning the freshwater system require annual testing of the water of Frustration Lake during open water for Total Suspended Solids (TSS). Appendix 8 contains the sample results taken on September 3, 2004. TSS was 3.3 mg/L.

10.5. ANNUAL GEOTECHNICAL INSPECTION

Mark Watson of EBA Engineering conducted the annual geotechnical inspection of the Polaris Mine site between August 25th and August 28th of 2004. During the inspection, efforts were made to identify potential future locations of erosion so that future geotechnical inspections could monitor those locations. Inspections also included Garrow Lake Dam, the Operational Landfill, the marine foreshore and Little Red Dog Quarry Landfill. His geotechnical inspection report is currently in draft stage and will be submitted upon completion as part of Appendix 5.

10.6. SUBSIDENCE AREA STABILITY

There was no visible change in the contours of the Subsidence Area in the summer of 2004 relative to the previous summer. During 2004, some fill was added to part of the area over

the Reclamation Landfill to thicken the cover over debris. Some of this material was obtained by dozing material from adjacent areas, and also by hauling in fill from the New Quarry. At the end of this work a detailed GPS survey of the Subsidence Area was conducted to monitor the surface contours. The contour plan prepared by Focus Engineering contains cross sectional drawings showing the elevations as they existed in 2003 and again after the 2004 work was completed. Areas where the cut and fill activities occurred in 2004 are apparent on this drawing (Appendix 4). It is apparent from this drawing that no significant subsidence of this area occurred between 2003 and 2004.

In 2004, Teck Cominco engaged Golder Associates to review the issue of the subsidence area and to provide their view of the future stability of this area. This report is in the final draft stage and will be completed and submitted as an update of this report in Appendix 5.

11. GARROW LAKE STRATIGRAPHIC MONITORING

The Water Licence requires that a monitoring event of Garrow Lake Stratigraphy be conducted during the mid-winter, maximum ice thickness and at maximum ice melt during the summer. Sampling was conducted in January and in March. Garrow Lake did not clear of ice sufficiently to safely collect data during the "minimum ice conditions" during the summer. Results of the sampling indicate that the lake remains stable and metals concentrations have not changed significantly. Refer to Appendix 16 for presentation of the monitoring data.

12. WATER LICENCE EFFLUENT MONITORING

12.1. Correspondence Regarding Application of Metal Mining Effluent Regulations

12.1.1. TSS Exceedance from Final Discharge Point

Refer to Section 3 of this report.

12.1.2. Missed Sublethal Toxicity Testing Event During 2003

On March 29th 2004, Azimuth Consultants provided an explanation of the circumstances regarding missing the 2nd sublethal toxicity testing event from 2003. This was due to the unique discharge characteristics and receiving environment a Polaris which makes the MMER more difficult to interpret and apply compared to mines discharging under more normal conditions. In a letter dated April 27th from Environment Canada, accepted the explanation for the missed sampling event and no formal action by Environment Canada is forthcoming. Both of these letters are included in Appendix 17.

12.1.3. Notice to Environment Canada of Alteration of system at Final Discharge Point

A letter dated April 27th, 2004 was submitted to Environment Canada giving notice that the Final Discharge Point at Garrow Dam was altered due to the decommissioning of the dam and the removal of the effluent siphoning system. The actual location of the Final Discharge Point was not moved so it remains the same as specified in the Water Licence. This letter in included in Appendix 17.

12.1.4. 2004 EEM Field Study Program

On March 9, 2004 Azimuth Consultants on behalf of Teck Cominco submitted a draft plan for the 2004 EEM Study Design. This was done in response to a meeting held with the Technical Advisory Committee of EC (in December 2003) to discuss planning for the 2004 summer field program. EC's response accepting the proposed study outline with some minor modifications was emailed to Teck Cominco and Azimuth on April 4, 2004. In August 2004, Azimuth mobilized to Polaris along with a support crew and other resources on August 14th. It is mid August when the ice normally clears from Garrow Bay but this does not necessarily happen every year. It was apparent that the ice in Garrow Bay was fairly solidly locked to shore so it did not appear it as going to clear. Unless the ice cleared, it was not possible to conduct the planned field program. EC was notified of this and they responded acknowledging that we had informed them and then EC followed up with another email on August 23rd with information from the Canadian Ice Service predicting that the ice would not clear. Teck Cominco had agreement from EC that we would be required to conduct a two week field program to conduct the study program and if it could not be completed within this time frame that Teck Cominco would not be obligated to make further attempts. Azimuth remained on site for the two weeks and the ice did not clear so the field program did not occur. All of this correspondence is included in Appendix 17.

12.2. SUMMARY OF EFFLUENT MONITORING AND EFFLUENT CHARACTERIZATION

12.3. 2003 Annual MMER Report

Under the MMER and the Water Licence, an annual report summarizing the previous years MMER sampling must be submitted. The annual MMER report is included in Appendix 18. All discharge for the year 2003 was compliant with the MMER and the Water Licence.

12.4. 2004 Quarterly and Annual MMER Report

Under the MMER and the Water Licence, the Garrow Lake effluent discharge at the Final Discharge Point must be monitored and reported quarterly and annually. These reports are included in Appendix 18. With the exception of a single TSS exceedance, all effluent discharge was compliant with the MMER and the Water Licence.

13. SUMMARY OF GARROW LAKE DFO STUDY PROGRAM

Enclosed in Appendix 19 a copy of the report titled "Limnology and Ecology of Garrow Lake, Little Cornwallis Island, Nunavut – August 2003" by Azimuth Consulting Group Inc. This study was done as part of the requirements contained in the DFO Fisheries Authorization to lower Garrow Lake back to its original elevation in preparation to remove Garrow Dam. The study conducted by Azimuth examined the limnology and ecology of Garrow Lake to assess the current conditions after being utilized for tailings disposal over 20 years. It concludes that the tailings deposition has not changed the limnological conditions in the mixolimnion. The zinc concentrations in the mixolimnion are currently about 0.22 ppm due to a tailings line break in 1984/1985. No zooplankton species were captured during the 2003 survey of the lake. Invertebrates collected included Oligochaetes, nematodes and Foraminifera. Chironamid larvae were not collected from the sediment but were found in the stomachs of the fourhorn sculpin. All 19 sculpins captured in 2003 appeared to be healthy with no external or internal tumors, scars or other abnormalities. The authors stated "Overall, it appears as if the size, distribution, growth

rate and reproductive status of the sculpin community has not changed markedly since pre-mining studies" They also indicated that the sculpins did not seem to be as abundant as pre-mine studies but there is no data of catch per-unit-effort. They conclude that "Nevertheless sculpins have survived in Garrow Lake throughout the history of mining and tailings deposition to the lake, which is still designated as a tailings disposal facility."

14. STATUS OF SITE AS OF DECEMBER 31, 2004

As of September 7th, 2004 all of the work identified in the Decommissioning and Reclamation Plan (DRP) has been completed with a few minor exceptions that will be completed over the next few summer seasons. Work undertaken was in keeping with the approved DRP or in accordance with approved changes to the DRP. While the volumes of contaminated materials greatly exceeded original estimates, the project was completed on schedule. We have left a small exploration style shelters on site, along with supplies and some heavy equipment to facilitate implementing the monitoring program and to address the minor re-sloping of a few areas on site.

In Teck Cominco's opinion (that we expect to be verified through the on-going site monitoring program), the reclamation activities have accomplished the goals set out in the DRP and the site will be physically and chemically stable in the long term. While some features such as roadways are virtually impossible to reclaim in the arctic, the visual appearance of the site has been substantially restored.

APPENDIX 1

EXECUTIVE SUMMARY

OF

2004 DECOMMISSIONING AND RECLAMATION REPORT

IN INUKTITUT

APPENDIX 2

UNAUTHORIZED DISCHARGES

OR

SPILLS

August 12, 2004

Environment Canada
Nunavut Regional Office
Environmental Protection Branch
P.O. Box 1870
Iqaluit, NU
X0A 0H0

Attention: Sid Bruinsma, Enforcement / Emergencies Officer, Nunavut Northern Division

Dear Sir:

Re: <u>Polaris Mine – Garrow Lake Final Discharge Point Exceedance of TSS Sample Under Schedule 4 of the MMER</u>

In accordance with section 24 (2) of the Metal Mining Effluent Regulations ("MMER"), please be advised that on August 9, 2004 we received laboratory results indicating that a single weekly effluent sample taken July 7th, 2004 from the final discharge point of Garrow Lake (a single grab sample) had a Total Suspended Solids (TSS) level of 117 mg/L which exceeded the TSS limits in Schedule 4 of the MMER (limit of 30 mg/L for a single grab sample). Concurrently on July 7th we also took our monthly acute lethality samples. The results were compliant with the MMER and showed no acute toxicity to either the Rainbow Trout or the Daphnia magna (i.e. LC50s in both cases were > 100% effluent). I have attached copies of both of these laboratory results. The date on the laboratory record for the metals analysis states that the sample was taken on July 6th but this is incorrect. The metals samples were originally scheduled to be taken on the 6th and the bottles were labeled as such by our consultant but fog delayed the plane that ships the samples to the laboratory so the sample was actually taken on the 7th at the same time as the acute lethality samples (and the dates on the bottles and associated chain of custody papers were not updated).

The July 7th sample was taken during the first week of effluent discharge from Garrow Lake. The TSS level was the result of Garrow Lake being ice covered which blocks the creek inlet (Garrow Creek) until the ice melted sufficiently to uncork the lake, and then the flows increase to a peak very quickly causing turbidity in the creek channel. The peak flows last a day or two and then the flows gradually subside with the TSS levels decreasing concurrently. As stated previously, the turbidity is not from tailings being mobilized as evidenced by the metals concentrations in the July 7th sample being in compliance (i.e. Zn concentrations were 0.198 mg/L). The TSS levels in the subsequent weekly water sample (July 13th) was in compliance (TSS was 5.7 mg/L) and metals concentrations continued to be in compliance (Zn was 0.106 mg/L). I have also attached the final results for the July 20th weekly water samples (TSS was <3.0 mg/L and the Zn was 0.0435 mg/L). The July 27th weekly water sample interim laboratory results report TSS at 3.7 mg/L and the Zn results are not available yet. Samples for the acute lethality tests were also taken on July 27th and compliant results were again achieved with the LC50 being >100 for both

the Rainbow Trout and the Daphnia magna (attached). I will forward the final July 27th laboratory results once they are received.

If you have any other questions in the interim, please contact me at (250) 427-8405 or by email at bruce.donald@teckcominco.com

Yours truly,

Bruce Donald

Attachments: July 7th Monthly Water Sample Results
July 7th Acute Lethality Sample Results
July 13th Weekly Water Sample Results
July 20th Weekly Water Sample Results
July 27th Acute Lethality Sample Results

Cc: Walter Kuit (Teck Cominco)
Bob Hutchinson (Teck Cominco)
Patrick Allard (Azimuth Consulting)
Phyllis Beaulieu (Nunavut Water Board)

ALS Environmental

CHEMICAL ANALYSIS REPORT

Date: August 9, 2004

ALS File No. U5572

Report On: Polaris Water Analysis

Report To: **Azimuth Consulting Group Inc.**
218 - 2902 West Broadway
Vancouver, BC
V6K 2G8

Attention: **Mr. Randy Baker**

Received: July 12, 2004

ALS ENVIRONMENTAL
per:

Heather A. Ross-Easton, B.Sc. - Project Chemist
Andre Langlais, M.Sc. - Project Chemist

File No. U5572

RESULTS OF ANALYSIS - Water

Sample ID			G Creek	Dup	F Blank	T Blank
Sample Date			04-07-06	04-07-06	04-07-06	04-07-06
Sample Time			11:00	11:00	11:00	11:00
ALS ID			*1*	*2*	*3*	*4*
Physical Tests						
Hardness	CaCO3		1400	1400	<0.54	<0.54
pH			8.05	8.06	-	-
Salinity	o/oo		7.0	6.9	-	-
Total Suspended Solids			117	120	-	-
Dissolved Anions						
Alkalinity-Total		CaCO3	138	132	-	-
Nutrients						
Ammonia Nitrogen		N	0.071	0.069	-	-
Nitrate Nitrogen		N	0.277	0.284	-	-
Cyanides						
Total Cyanide	CN		<0.0050	<0.0050	-	-
Total Metals						
Aluminum	T-Al		0.34	0.26	<0.10	<0.10
Arsenic	T-As		<0.0010	<0.0010	<0.0010	<0.0010
Cadmium	T-Cd		0.000588	0.000582	<0.000020	<0.000020
Calcium	T-Ca		140	139	<0.050	<0.050
Copper	T-Cu		0.00265	0.00252	0.00012	0.00012
Iron	T-Fe		0.487	0.441	<0.010	<0.010
Lead	T-Pb		0.00269	0.00240	0.00017	0.00021
Magnesium	T-Mg		256	256	<0.10	<0.10
Mercury	T-Hg		<0.000010	<0.000010	<0.000010	<0.000010
Molybdenum	T-Mo		<0.0050	<0.0050	<0.0050	<0.0050
Nickel	T-Ni		0.00442	0.00438	<0.00050	<0.00050
Zinc	T-Zn		0.198	0.196	0.0012	<0.0010
Radiological Parameters						
Radium-226 [1,2]			0.0200	0.0200	<0.0050	0.0060

Results are expressed as milligrams per litre except where noted.
< = Less than the detection limit indicated.
[1]Results are expressed as Becquerels per litre (Bq/L). This analysis is
[2]subcontracted to SRC from Saskatoon.

A Campbell Brothers Limited Company

Appendix 1 - METHODOLOGY

Outlines of the methodologies utilized for the analysis of the samples submitted are as follows

Conventional Parameters in Water

These analyses are carried out in accordance with procedures described in "Methods for Chemical Analysis of Water and Wastes" (USEPA), "Manual for the Chemical Analysis of Water, Wastewaters, Sediments and Biological Tissues" (BCMOE), and/or "Standard Methods for the Examination of Water and Wastewater" (APHA). Further details are available on request.

pH in Water

This analysis is carried out using procedures adapted from APHA Method 4500-H "pH Value". The pH is determined in the laboratory using a pH electrode.

Recommended Holding Time:
Sample: 2 hours
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Solids in Water

This analysis is carried out using procedures adapted from APHA Method 2540 "Solids". Solids are determined gravimetrically. Total dissolved solids (TDS) and total suspended solids (TSS) are determined by filtering a sample through a glass fibre filter, TDS is determined by evaporating the filtrate to dryness at 180 degrees celsius, TSS is determined by drying the filter at 104 degrees celsius. Total solids are determined by evaporating a sample to dryness at 104 degrees celsius. Fixed and volatile solids are determined by igniting a dried sample residue at 550 degrees celsius.

Recommended Holding Time:
Sample: 7 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Alkalinity in Water by Titration

This analysis is carried out using procedures adapted from APHA Method 2320 "Alkalinity". Total alkalinity is determined by potentiometric titration to a pH 4.5 endpoint. Bicarbonate, carbonate and hydroxide alkalinity are calculated from phenolphthalein alkalinity and total alkalinity values.

Recommended Holding Time:
Sample: 14 days
Reference: APHA

A Campbell Brothers Limited Company

For more detail see ALS Environmental "Collection & Sampling Guide"

Ammonia in Water by Selective Ion Electrode

This analysis is carried out, on sulphuric acid preserved samples, using procedures adapted from APHA Method 4500-NH3 "Nitrogen (Ammonia)". Ammonia is determined using an ammonia selective electrode.

Recommended Holding Time:
Sample: 28 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Dissolved Anions in Water by Ion Chromatography

This analysis is carried out using procedures adapted from APHA Method 4110 "Determination of Anions by Ion Chromatography" and EPA Method 300.0 "Determination of Inorganic Anions by Ion Chromatography". Anions are determined by filtering the sample through a 0.45 micron membrane filter and injecting the filtrate onto a Dionex IonPac AG17 anion exchange column with a hydroxide eluent stream. Anions routinely determined by this method include: bromide, chloride, fluoride, nitrate, nitrite and sulphate.

Recommended Holding Time:
Sample: 28 days (bromide, chloride, fluoride, sulphate)
Sample: 2 days (nitrate, nitrite)
Reference: APHA and EPA
For more detail see ALS Environmental "Collection & Sampling Guide"

Cyanide Species in Water

This analysis is carried out using procedures adapted from APHA Method 4500-CN "Cyanide". Total or strong acid dissociable (SAD) cyanide and weak acid dissociable (WAD) cyanide are determined by sample distillation and analysis using the chloramine-T colourimetric method. Cyanate is determined by the cyanate hydrolysis method using an ammonia selective electrode. Thiocyanate is determined by the ferric nitrate colourimetric method.

Recommended Holding Time:
Sample: 14 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Metals in Seawater

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995. The procedures

A Campbell Brothers Limited Company

may involve preliminary sample treatment by acid digestion or filtration (EPA Method 3005A). Instrumental analysis of the seawater is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Trace Metals in Seawater by SPR-IDA Chelation

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995, and with procedures adapted from Cetac Technologies Incorporated. A suspended particulate resin (SPR), consisting of immobilized iminodiacetate (IDA) on a divinylbenzene polymer, is used to chelate and preconcentrate metals in seawater. Instrumental analysis is by inductively coupled plasma mass spectrometry (ICPMS) and/or routine atomic absorption spectrophotometry techniques (EPA 7000 series).

Recommended Holding Time:

Sample/Extract:	6 months
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Metals in Water

This analysis is carried out using procedures adapted from "Standard Methods for the Examination of Water and Wastewater" 20th Edition 1998 published by the American Public Health Association, and with procedures adapted from "Test Methods for Evaluating Solid Waste" SW-846 published by the United States Environmental Protection Agency (EPA). The procedures may involve preliminary sample treatment by acid digestion, using either hotplate or microwave oven, or filtration (EPA Method 3005A). Instrumental analysis is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	EPA
For more detail see:	ALS "Collection & Sampling Guide"

A Campbell Brothers Limited Company

Appendix 1 - METHODOLOGY - Continued

Mercury in Seawater

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995. The procedure involves a cold-oxidation of the acidified seawater sample using bromine monochloride prior to reduction of the sample with stannous chloride. Instrumental analysis is by cold vapour atomic fluorescence spectrophotometry (EPA Method 245.7).

Recommended Holding Time:

Sample:	28 days
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Mercury in Water

This analysis is carried out using procedures adapted from "Standard Methods for the Examination of Water and Wastewater" 20th Edition 1998 published by the American Public Health Association, and with procedures adapted from "Test Methods for Evaluating Solid Waste" SW-846 published by the United States Environmental Protection Agency (EPA). The procedure involves a cold-oxidation of the acidified sample using bromine monochloride prior to reduction of the sample with stannous chloride. Instrumental analysis is by cold vapour atomic fluorescence spectrophotometry (EPA Method 245.7).

Recommended Holding Time:

Sample:	28 days
Reference:	EPA

For more detail see ALS Environmental "Collection & Sampling Guide"

Results contained within this report relate only to the samples as submitted.

This Chemical Analysis Report shall only be reproduced in full, except with the written approval of ALS Environmental.

End of Report

A Campbell Brothers Limited Company

EVS environment consultants

195 Pemberton Avenue
North Vancouver, BC
Canada V7P 2R4
Fax: 604-662-8548
Tel: 604-986-4331
Info@evsenvironment.com
www.evsenvironment.com

FAX TRANSMITTAL SHEET

TO:	Cheryl Mackintosh	**DATE:**	July 16, 2004
	Azimuth Consulting Group	**PROJECT No.:**	09-0302-54
	218 – 2902 West Broadway	**W.O. No.:**	0400304,307
	Vancouver, BC	**FAX No.:**	604-739-9070
	V6K 2G8	**TEL No.:**	604-730-1220
SENT BY:	Robert Harrison	**# PAGES (incl. cover):**	One (1)

This message is intended only for the use of the individual or entity to which it is addressed and may contain information that is privileged confidential and exempt from disclosure under applicable law. If you have received this communication in error please notify us by telephone (collect) and return the original transmission to us by mail without making a copy. Thank you.

Re: Interim data for the 96-h rainbow trout and 48-h *Daphnia magna* LC50 toxicity tests performed on the sample identified as G-Creek acute 070704 (collected July 7, 2004).

Sample ID	Sample Collection Date	**LC50 (95% Confidence Limits) [%vol/vol]**	
		96-h Rainbow Trout	**48-h *Daphnia magna***
G-Creek acute 070704	July 7, 2004 (2200h)	> 100	> 100

Please note that these are draft results and are subject to a QA/QC review. A complete report will follow by mail. Should you have any questions, please contact Edmund Canaria, Manager of Laboratory Services, or myself at 604-986-4331.

Thank you,

Robert Harrison, B.Sc. Hons.
Assistant Bioassay Test Supervisor – Fish Team
rharrison@evsenvironment.com

REH

ALS Environmental

CHEMICAL ANALYSIS REPORT

Date:	August 9, 2004
ALS File No.	U5829
Report On:	Polaris Water Analysis
Report To:	**Azimuth Consulting Group Inc.** 218 - 2902 West Broadway Vancouver, BC V6K 2G8
Attention:	**Mr. Randy Baker**
Received:	July 16, 2004

ALS ENVIRONMENTAL
per:

Heather A. Ross-Easton, B.Sc. - Project Chemist
Andre Langlais, M.Sc. - Project Chemist

ALS CANADA LTD.
1988 Triumph Street, Vancouver, BC Canada V5L 1K5
Phone: 604-253-4188 Fax: 604-253-6700 Website: www.alsenviro.com

REMARKS

The detection limits for some of the metals have been increased for the sample "G Creek" due to sample matrix interferences.

A Campbell Brothers Limited Company

File No. U5829

RESULTS OF ANALYSIS - Water

Sample ID		G Creek
Sample Date		04-07-13
ALS ID		*1*
Physical Tests		
pH		7.90
Salinity	o/oo	4.5
Total Suspended Solids		5.7
Cyanides		
Total Cyanide	CN	<0.0050
Total Metals		
Aluminum	T-Al	<0.40
Arsenic	T-As	<0.0020
Cadmium	T-Cd	0.000332
Copper	T-Cu	0.000703
Iron	T-Fe	0.019
Lead	T-Pb	0.000318
Molybdenum	T-Mo	<0.0050
Nickel	T-Ni	0.00204
Zinc	T-Zn	0.106
Radiological Parameters		
Radium-226 [1,2]		0.0070

Remarks regarding the analyses appear at the beginning of this report.
Results are expressed as milligrams per litre except where noted.
< = Less than the detection limit indicated.
[1]Result is expressed as Becquerels per litre (Bq/L). This analysis is
[2]subcontracted to SRC, Saskatoon.

A Campbell Brothers Limited Company

Appendix 1 - METHODOLOGY

Outlines of the methodologies utilized for the analysis of the samples submitted are as follows

pH in Water

This analysis is carried out using procedures adapted from APHA Method 4500-H "pH Value". The pH is determined in the laboratory using a pH electrode.

Recommended Holding Time:
Sample: 2 hours
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Conventional Parameters in Water

These analyses are carried out in accordance with procedures described in "Methods for Chemical Analysis of Water and Wastes" (USEPA), "Manual for the Chemical Analysis of Water, Wastewaters, Sediments and Biological Tissues" (BCMOE), and/or "Standard Methods for the Examination of Water and Wastewater" (APHA). Further details are available on request.

Solids in Water

This analysis is carried out using procedures adapted from APHA Method 2540 "Solids". Solids are determined gravimetrically. Total dissolved solids (TDS) and total suspended solids (TSS) are determined by filtering a sample through a glass fibre filter, TDS is determined by evaporating the filtrate to dryness at 180 degrees celsius, TSS is determined by drying the filter at 104 degrees celsius. Total solids are determined by evaporating a sample to dryness at 104 degrees celsius. Fixed and volatile solids are determined by igniting a dried sample residue at 550 degrees celsius.

Recommended Holding Time:
Sample: 7 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Cyanide Species in Water

This analysis is carried out using procedures adapted from APHA Method 4500-CN "Cyanide". Total or strong acid dissociable (SAD) cyanide and weak acid dissociable (WAD) cyanide are determined by sample distillation and analysis using the chloramine-T colourimetric method. Cyanate is determined by the cyanate hydrolysis method using an ammonia selective electrode. Thiocyanate is determined by the ferric nitrate colourimetric method.

Recommended Holding Time:

A Campbell Brothers Limited Company

Sample: 14 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Metals in Water

This analysis is carried out using procedures adapted from "Standard Methods for the Examination of Water and Wastewater" 20th Edition 1998 published by the American Public Health Association, and with procedures adapted from "Test Methods for Evaluating Solid Waste" SW-846 published by the United States Environmental Protection Agency (EPA). The procedures may involve preliminary sample treatment by acid digestion, using either hotplate or microwave oven, or filtration (EPA Method 3005A). Instrumental analysis is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	EPA
For more detail see:	ALS "Collection & Sampling Guide"

Metals in Seawater

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995. The procedures may involve preliminary sample treatment by acid digestion or filtration (EPA Method 3005A). Instrumental analysis of the seawater is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Trace Metals in Seawater by SPR-IDA Chelation

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995, and with procedures adapted from Cetac Technologies Incorporated. A suspended particulate resin (SPR), consisting of immobilized iminodiacetate (IDA) on a divinylbenzene polymer, is used to chelate and preconcentrate metals in seawater. Instrumental analysis is by inductively coupled plasma mass spectrometry (ICPMS) and/or routine atomic absorption spectrophotometry techniques (EPA 7000 series).

A Campbell Brothers Limited Company

Appendix 1 - METHODOLOGY - Continued

Recommended Holding Time:

Sample/Extract:	6 months
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Results contained within this report relate only to the samples as submitted.

This Chemical Analysis Report shall only be reproduced in full, except with the written approval of ALS Environmental.

End of Report

A Campbell Brothers Limited Company

CHEMICAL ANALYSIS REPORT

Date: August 11, 2004

ALS File No. U6161

Report On: Polaris Water Analysis

Report To: **Azimuth Consulting Group Inc.**
218 - 2902 West Broadway
Vancouver, BC
V6K 2G8

Attention: **Mr. Randy Baker**

Received: July 24, 2004

ALS ENVIRONMENTAL
per:

Andre Langlais, M.Sc. - Project Chemist
Heather A. Ross-Easton, B.Sc. - Project Chemist

ALS CANADA LTD.
1988 Triumph Street, Vancouver, BC Canada V5L 1K5
Phone: 604-253-4188 Fax: 604-253-6700 Website: www.alsenviro.com

File No. U6161

RESULTS OF ANALYSIS - Water

Sample ID		G-Creek_ Gen_ 072004	Tracer Dye	Injectn. Dye	G-Creek_ Rhod_ 072004
Sample Date		04-07-20	04-07-20	04-07-20	04-07-20
ALS ID		*1*	*2*	*3*	*4*
Physical Tests					
pH		7.86	-	-	-
Salinity	o/oo	3.3	-	-	-
Total Suspended Solids		<3.0	-	-	-
Cyanides					
Total Cyanide	CN	<0.0050	-	-	-
Total Metals					
Aluminum	T-Al	<0.20	-	-	-
Arsenic	T-As	<0.0020	-	-	-
Cadmium	T-Cd	0.000109	-	-	-
Copper	T-Cu	0.000427	-	-	-
Iron	T-Fe	<0.010	-	-	-
Lead	T-Pb	0.000837	-	-	-
Molybdenum	T-Mo	<0.0050	-	-	-
Nickel	T-Ni	0.000876	-	-	-
Zinc	T-Zn	0.0435	-	-	-
Miscellaneous					
Rhodamine		-	see below[1]	76900	0.0380
Radiological Parameters					
Radium-226[2,3]		<0.0050	-	-	-

Results are expressed as milligrams per litre except where noted.
< = Less than the detection limit indicated.
[1]This sample was used to prepare calibration standards
[2]Result is expressed as Becquerels per litre (Bq/L). This analysis is
[3]subcontracted to SRC, Saskatoon.

File No. U6161

Appendix 1 - METHODOLOGY

Outlines of the methodologies utilized for the analysis of the samples submitted are as follows

pH in Water

This analysis is carried out using procedures adapted from APHA Method 4500-H "pH Value". The pH is determined in the laboratory using a pH electrode.

Recommended Holding Time:
Sample: 2 hours
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Conventional Parameters in Water

These analyses are carried out in accordance with procedures described in "Methods for Chemical Analysis of Water and Wastes" (USEPA), "Manual for the Chemical Analysis of Water, Wastewaters, Sediments and Biological Tissues" (BCMOE), and/or "Standard Methods for the Examination of Water and Wastewater" (APHA). Further details are available on request.

Solids in Water

This analysis is carried out using procedures adapted from APHA Method 2540 "Solids". Solids are determined gravimetrically. Total dissolved solids (TDS) and total suspended solids (TSS) are determined by filtering a sample through a glass fibre filter, TDS is determined by evaporating the filtrate to dryness at 180 degrees celsius, TSS is determined by drying the filter at 104 degrees celsius. Total solids are determined by evaporating a sample to dryness at 104 degrees celsius. Fixed and volatile solids are determined by igniting a dried sample residue at 550 degrees celsius.

Recommended Holding Time:
Sample: 7 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Cyanide Species in Water

This analysis is carried out using procedures adapted from APHA Method 4500-CN "Cyanide". Total or strong acid dissociable (SAD) cyanide and weak acid dissociable (WAD) cyanide are determined by sample distillation and analysis using the chloramine-T colourimetric method. Cyanate is determined by the cyanate hydrolysis method using an ammonia selective electrode. Thiocyanate is determined by the ferric nitrate colourimetric method.

Recommended Holding Time:

Appendix 1 - METHODOLOGY - Continued

Sample: 14 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Metals in Water

This analysis is carried out using procedures adapted from "Standard Methods for the Examination of Water and Wastewater" 20th Edition 1998 published by the American Public Health Association, and with procedures adapted from "Test Methods for Evaluating Solid Waste" SW-846 published by the United States Environmental Protection Agency (EPA). The procedures may involve preliminary sample treatment by acid digestion, using either hotplate or microwave oven, or filtration (EPA Method 3005A). Instrumental analysis is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	EPA
For more detail see:	ALS "Collection & Sampling Guide"

Metals in Seawater

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995. The procedures may involve preliminary sample treatment by acid digestion or filtration (EPA Method 3005A). Instrumental analysis of the seawater is by atomic absorption/emission spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Recommended Holding Time:

Sample:	6 months
Reference:	Puget

For more detail see ALS Environmental "Collection & Sampling Guide"

Trace Metals in Seawater by SPR-IDA Chelation

This analysis is carried out using procedures adapted from "Recommended Guidelines for Measuring Metals in Puget Sound Marine Water, Sediment, and Tissue Samples" prepared for the United States Environmental Protection Agency and the Puget Sound Water Quality Authority, 1995, and with procedures adapted from Cetac Technologies Incorporated. A suspended particulate resin (SPR), consisting of immobilized iminodiacetate (IDA) on a divinylbenzene polymer, is used to chelate and preconcentrate metals in seawater. Instrumental analysis is by inductively coupled plasma mass spectrometry (ICPMS) and/or routine atomic absorption spectrophotometry techniques (EPA 7000 series).

Appendix 1 - METHODOLOGY - Continued

Recommended Holding Time:
Sample/Extract: 6 months
Reference: Puget
For more detail see ALS Environmental "Collection & Sampling Guide"

Rhodamine WT in Water

This analysis is carried out using a Waters Model 470 Scanning Fluorescence Detector. Prior to analysis, samples are warmed to room temperature and then an aliquot of the sample is filtered through a 0.45 um cellulose acetate filter to remove some of the potential interferences. After filtration, a portion of the sample, typically 500 uL, is injected into the fluorescence detector. An excitation wavelength of 556 nm is used and fluorescence is measured at an emission wavelength of 580 nm.

Please note the following: This method is non-selective and subject to many interferences. Typical interferences may include; pH, salinity, temperature, suspended matter, photochemical degradation of Rhodamine WT, and some types of algae pigments. Detection for this analysis is not chromatographic; therefore, anything present in the sample that fluoresces at the same wavelength as Rhodamine WT will be detected and reported as Rhodamine WT. Results reported using this method should be considered semi-quantitative in nature.

Recommended Holding Time:
Sample: None Available
Reference: None Available
For more detail see ALS Environmental "Collection & Sampling Guide"

Results contained within this report relate only to the samples as submitted.

This Chemical Analysis Report shall only be reproduced in full, except with the written approval of ALS Environmental.

End of Report

EVS environment consultants

195 Pemberton Avenue
North Vancouver, BC
Canada V7P 2R4
Fax: 604-662-8548
Tel: 604-986-4331
Info@evsenvironment.com
www.evsenvironment.com

FAX TRANSMITTAL SHEET

TO:	Cheryl Mackintosh	**DATE:**	August 9, 2004
	Azimuth Consulting Group	**PROJECT No.:**	09-0302-54
	218 – 2902 West Broadway	**W.O. No.:**	0400342,348
	Vancouver, BC	**FAX No.:**	604-739-9070
	V6K 2G8	**TEL No.:**	604-730-1220
SENT BY:	Rachel DeWynter	**# PAGES (incl. cover):**	One (1)

This message is intended only for the use of the individual or entity to which it is addressed and may contain information that is privileged confidential and exempt from disclosure under applicable law. If you have received this communication in error please notify us by telephone (collect) and return the original transmission to us by mail without making a copy. Thank you.

Re: Interim data for the 96-h rainbow trout and 48-h *Daphnia magna* LC50 toxicity tests performed on the sample identified as G-Creek acute 270704 (collected July 27, 2004).

Sample ID	Sample Collection Date	LC50 (95% Confidence Limits) [%vol/vol]	
		96-h Rainbow Trout	48-h *Daphnia magna*
G-Creek acute 270704	July 27, 2004 (09:30h)	> 100	> 100

Please note that these are draft results and are subject to a QA/QC review. A complete report will follow by mail. Should you have any questions, please contact Edmund Canaria or myself at 604-986-4331.

Thank you,

Jennifer Young, B.Sc.
Bioassay Test Supervisor – Cladoceran Team
jyoung@evsenvironment.com

RSD

Environment Canada | Environnement Canada

Environment Canada
Environmental Protection Branch
Prairie and Northern Region
Northern Division
P.O. Box 1870 Iqaluit, Nunavut
X0A 0H0

PROTECTED
WITHOUT PREJUDICE

11 January 2005

Occurrence Files: 4408-2004-09-13-001
4408-2004-12-01-001

Mr. David Thompson
Deputy Chairman and CEO
Teck Cominco Metals Ltd.
Suite 600 – 200 Burrard Street
Vancouver, British Columbia
V6C 3L9

and

Mr. Bruce Donald
Manager of Operations
Teck Cominco Metals Ltd.
Polaris Mine Operation
Polaris, Little Cornwallis Island, Nunavut
X0A 0Y0

Dear Sirs;

FISHERIES ACT - Metal Mining Effluent Regulations (MMER)

I wish to acknowledge your letter of 12 August 2004 advising Environment Canada of the details surrounding the exceedance of the MMER Total Suspend Solid limits at the Polaris Mine site on July 07th 2004. I also acknowledge you timely submission of the 3rd quarter MMER report dated 17 November 2004 as required by the regulations.

Upon review of the above mentioned supporting documentation supplied by your company no further action will be pursued of this alleged violation. For more information or to comment, on the alleged facts, contained in this letter, please contact the undersigned. Your comments will be considered and, where appropriate, a response

/1

Canada

provided. Any comments you make, as well as Environment Canada's response, will be retained and filed with this letter in Environment Canada's records.

Respectfully,

Sidney F. Bruinsma
Enforcement / Emergencies Officer, Nunavut
Northern Division, Environmental Protection Branch
ENVIRONMENT CANADA
Box 1870, Iqaluit, Nunavut X0A 0H0
Ph. 867-975-4644
Fax 867-975-4645
sid.bruinsma@ec.gc.ca

cc: Craig Broome
Head of Enforcement, Northern Division
Environmental Protection Branch
Prairie and Northern Region
Yellowknife, NWT

FILE NOTE

Bruce Donald,
Reclamation Manager
Environment and Corporate Affairs
Teck Cominco Limited

Date: **June 23, 2004**

Subject: **Polaris Mine - Discovery of Liquid Petroleum Hydrocarbons During Remediation of Maintenance Facilities**

The following is a summary of information related to the discovery of liquid petroleum hydrocarbon within an area of known soil hydrocarbon contamination during the demolition and reclamation program at the Polaris Mine site at the Polaris Mine on Little Cornwallis Island, Nunavut.

Background:

The Polaris Mine has been in operation since 1982. The mine has three metal Foldaway buildings located immediately adjacent to each other where mobile equipment has been stored and maintained over the years when the mine was in operation. The mine is now closed and environmental assessments conducted as part of closure planning identified hydrocarbon contamination of the soils in the area surrounding these three buildings. The buildings are currently being demolished and 2 of the 3 buildings have been removed. Remediation of hydrocarbon contaminated soils by excavation has been completed at the first of the buildings being demolished. Remediation of the contaminated soils at the second building was approximately 20% complete when water with liquid petroleum hydrocarbons were discovered under the foot print of the building. This discovery was made on June 19, 2004.

Source of Hydrocarbons:

A specific time and source of the hydrocarbon leaks and/or spills can not be identified due to the long term use of this area. There are no apparent current or on-going sources of leaks in the area.

Volume Estimation:

The area of contaminated soils in total in the area of the three buildings is approximately 3,000 square metres. Drilling of the area indicated that the contaminated soils extend approximately 3 metres deep. The liquid hydrocarbon products were floating on water in a puddle in the excavation under Foldaway #1. The area of ponding was approximately 9 square metres. The water/oil mixture was recovered by pumping it into barrels and a larger tank. As the water was pumped, additional volumes seeped from surrounding soils. All of the water and free product have now been recovered. Approximately 2,100 liters of water and 400 liters of hydrocarbons were recovered from this area. Observations indicated that heat from the buildings depressed the active layer in this area creating a basin that contained the hydrocarbon limiting both the vertical and horizontal extent of contamination.

Remedial Action:

The contaminated soils in the area were being actively being remediated when the liquid petroleum products were discovered. Upon completion of recovery of the hydrocarbon/water mixture, the surrounding contaminated soils are being excavated. Excavation of the contaminated soils surrounding this building has continued on a continuous (24 hours per day) basis and is nearing completion. No further liquid petroleum products have been in evidence since. Excavation of contaminated soils related to this building is estimated to be 75% complete at this time. The last remaining Foldaway building will be demolished during the next two to three weeks and reclamation of this area will be complete within a maximum of three weeks. Recovery of the hydrocarbon contaminated soils are being conducted under the guidance of a team of independent environmental consultants who are located on-site. Upon completion of remediation of this area, confirmatory sampling will be undertaken to verify remedial efforts meet the remedial targets at the site as approved in the mine's Decommissioning and Reclamation Plan. A formal report presenting the confirmatory sampling data will be prepared and presented as part of the regular project reporting.

Gartner Lee Limited

memorandum

to: Bruce Donald, P.Eng, Reclamation Manager, Teck Cominco Limited
from: Brenda Bolton
date: March 2, 2005
ref: 40-137
re: **2004 Concentrate Shed Sampling Results**

The former concentrate storage shed area was located south of the process barge and shiploading dock. The metal-clad, steel frame shed was used to store lead and zinc concentrates produced in the mill through the winter for shipment to market in the short summer shipping season. The concentrate storage shed was subdivided to provide storage capacity for 40,000 tonnes lead concentrate at the north end and 175,000 tonnes zinc concentrate at the south end. The concentrate load-out conveyors were located along the west wall of the concentrate storage shed and fed the shiploader at the loading dock. The building was demolished in August 2003.

Removal of small quantities of residual soil impacted with lead and zinc concentrate from within the fractured limestone bedrock by the remedial methods originally proposed proved impractical. Therefore, GLL investigated alternative methods to limit the contact of this material to human or ecological receptors and found that the best alternative was to isolate the residual concentrate dust under a durable cover of sand and gravel, a soil cover. The placement of the soil cover meets the principal objective of the original remediation plan, which is to eliminate the exposure pathways of the lead and zinc concentrate to human and ecological receptors at the Polaris Mine site.

Following the demolition and attempted remediation of the Concentrate Shed footprint, the area was used for storage of machinery and pallets of assorted fluids. On June 10, 2004 at 3:15 pm, an employee of Teck Cominco noted that an area surrounding a pallet of oil was saturated. An approximate volume of twenty two cubic meters was removed the same day by 9:00 pm. The dimensions of the excavation were approximately 6 meters by 4 meters, and 0.5 meters deep.

A representative of Gartner Lee Ltd. examined the excavated area on June 11, 2004. There was no sheen observed on a puddle located in the excavated depression, nor was there any detectable odour. Two samples were collected in accordance with standard GLL and TCL sampling procedures and protocols – one composite from the wall of the excavation, and one composite sample from the floor of the excavation. Both samples were sent to Analytical Laboratory Services (ALS) of Vancouver BC, in clean Teflon lined jars to confirm the presence and nature of hydrocarbon compounds.

Analytical laboratory confirmatory results for hydrocarbons are summarized in Table 1, along with the approved Polaris Mine SQROs for hydrocarbons. All samples sent to the analytical laboratory confirmed Extrable Petroleum Hydrocarbons (EPH) below the soil quality remediation objective (SQRO) of 1,000 mg/kg. Based on the laboratory results, no further remedial excavation was required.

Yours very truly,
GARTNER LEE LIMITED

Brenda Bolton
Environmental Geologist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

Rob Dickin.
Principal

Table 1. Utilidor Hydrocarbon Sample Results

Gartner Lee	FEDERAL CCME GUIDELINES[a]		Polaris Mine Soil Quality Remediation Objective	Location	Concentrate Shed	
	Residential / Parkland Land Use Guideline			Sample ID	04-369-11362-W-C	04-369-11363-F-C
				Date Sampled	11/06/2004	12/06/2004
				ALS File No.	U4483	U4483
				Field Screen (ppm)[b]	-	-
Parameter	**CEQG**	**PHC CWS[b,c,d]**	**Site-Specific**	**Units**	**Analytical Results**	
Non-Halogenated Volatiles						
Benzene	*0.5*	-	-	mg/kg	<0.040	<0.040
Ethylbenzene	*1.2*	-	-	mg/kg	<0.050	<0.050
Styrene	-	-	-	mg/kg	<0.050	<0.050
Toluene	*0.8*	-	-	mg/kg	<0.050	<0.050
meta- & para-Xylene	-	-	-	mg/kg	<0.050	<0.050
ortho-Xylene	-	-	-	mg/kg	<0.050	<0.050
Total Xylenes	*1.0*	-	-	mg/kg	<0.10	<0.10
Extractable Hydrocarbons						
F1 (C6-C10)	-	-	-	mg/kg	<10	<10
F1-BTEX	-	*130* (coarse)	-	mg/kg	<10	<10
F2 (C10-C16)	-	*450* (coarse)[f]	-	mg/kg	51	35
F3 (C16-C34)	-	*400* (coarse)[f]	-	mg/kg	261	277
F4 (C34-C50)	-	*2800* (coarse)	-	mg/kg	124	72
F4G-sg[d]	-	-	-	mg/kg	690	<500
F4G-SG Required (yes/no)	-	-	-	mg/kg	yes	yes
Extractable Hydrocarbons						
EPH10-19	-	-	1000	mg/kg	<200	<200
EPH19-32	-	-	1000	mg/kg	290	<200

Bold Concentration greater than or equal to CCME RL Guideline for soil and/or the site-specific SQRO.

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

[a] Canadian Environmental Quality Guidelines (CEQG) and Petroleum Hydrocarbon Canada-Wide Standards (PHC CWS) presented apply to soil.

[b] Guideline is dependant upon depth of sample (surface, subsoil >1.5 m depth). Surface soil analyzed.

[c] Guideline is dependent on median grain size of soil analyzed (Fine≤75 µm, Coarse >75 µm). Median grain size of soil analyzed is >75 µm.

[d] Guideline is based on the site-specific exposure pathway of Ecological Soil Contact

[e] Total Xylene calculated as the sum of meta, para and ortho Xylenes

[f] Use of the guideline requires that PAHs be subtracted from the fraction. Based on the results for soil sample A1 it is assumed that PAHs form a small percentage of the fractions 2 and 3 for the samples not analyzed for PAHs.

d) Fraction 4G measures carbon chain length in excess of C16.

Gartner Lee Limited

memorandum

to: Bruce Donald, P.Eng, Reclamation Manager, Teck Cominco Limited
from: Dennis Lu
date: April 14, 2005
ref: 40-137
re: **2004 Utilidor Sampling Results**

This memo is in response to the fuel leak on March 20, 2003 at the Utilidor. It addresses the nature of the spill, investigation and results of the sampling events.

The Utilidor is a utility corridor that runs from the accommodations complex to the barge. It houses various utilities including sewage, electrical and fuel. On March 20, 2003, a small fuel leak was discovered along the Utilidor near the junction of the haul road above the barge and the road leading to the accommodations. Upon identification of the leak, the fuel was shut off and the leak was patched immediately. There was no documentation of the amount of fuel spilled during this leak. The leak occurred on the east side of the road and followed the Utilidor path beneath the road and ponded in the barge area. The barge area was an area targeted for hydrocarbon remediation and the fuel that leaked from the Utilidor would be handled accordingly during the area remediation.

Inspection of the site occurred after snowmelt by GLL in July 2004. Upon inspection of the site, no visible staining was apparent. Screening samples were collected to identify the surface and sub-surface quality of the soil and any potential hydrocarbon contamination in the soil.

Delineation of the potentially hydrocarbon impacted area was accomplished through screening level sampling of the surface and subsurface material in the targeted area for remediation. Two boreholes were advanced in the area immediately below the fuel spill to confirm the spill had traveled along the Utilidor and not through the roadbed. The subsurface samples were collected using a drill-mounted excavator to allow for observations at depth.

Samples from the boreholes were collected over a 0.75 m interval to bedrock at a depth of 2.25 m. The samples were field screened with a Photo-ionization detector (PID). A subset of the on site field screening samples were sent to Analytical Laboratory Services (ALS) of Vancouver BC, in clean Teflon lined jars to confirm the presence and nature of hydrocarbon compounds.

The olfactory condition and field screening measurements of the concentrations of organic vapours in the soil samples from the southern borehole indicated possible subsurface hydrocarbon contamination. To confirm a clean vertical profile, the sample with the highest organic reading (Barge-10614-BH-C), and the sample below (Barge-10615-BH-C) were submitted to the lab for analysis. The borehole north of the Utilidor did not show signs of potential contamination; the sample with the highest organic reading from the borehole (Barge-10610-BH-C) was submitted for laboratory analysis to determine horizontal extent.

The Utilidor, and soils directly surrounding it were excavated and disposed. Upon removal of the Utilidor, two surface soil samples were collected from the footprint and surrounding area. The two composite samples were collected in accordance with standard GLL and TCL sampling procedures and protocols.

Analytical laboratory confirmatory results for hydrocarbons are summarized in Table 1, along with the approved Polaris Mine SQROs for hydrocarbons. The soil quality results and the lateral limits of samples are shown in the Barge area close out report Figure Barge-01-2. A total of 5 screening samples were submitted for petroleum hydrocarbons (3 borehole samples and 2 composite area samples). All samples sent to the analytical laboratory confirmed Extractable Petroleum Hydrocarbons (EPH) below the soil quality remediation objective (SQRO) of 1,000 mg/kg. Samples collected from the footprint of the Utilidor were also analysed to Canada Wide Standards (CWS) for Petroleum Hydrocarbons (PHC). All samples submitted returned results below the PHC CWS for Parkland Land Use.

Table 1. Utilidor Hydrocarbon Sample Results

Gartner Lee	FEDERAL CCME GUIDELINES[a]		Polaris Mine Soil Quality Remediation Objective	Location	Utilidor				
				Sample ID	Barge-10610-BH-C	Barge-10614-BH-C	Barge-10615-BH-C	Barge-12179-F-C	Barge-12180-F-C
				Date Sampled	13/05/2004	13/05/2004	13/05/2004	27/08/2004	27/08/2004
	Residential / Parkland Land Use Guideline			ALS File No.	U3564rr	U3564rr	U3564rr	U7584	U7584
				Field Screen (ppm)[b]	75	225	85	10	10
Parameter	**CEQG**	**PHC CWS[b,c,d]**	**Site-Specific**	**Units**	**Analytical Results**				
Non-Halogenated Volatiles									
Benzene	*0.5*			mg/kg	-	-	-	<0.040	<0.040
F1 (C6-C10)				mg/kg	-	-	-	<10	<10
F1-BTEX		*130* (coarse)		mg/kg	-	-	-	<10	<10
Ethylbenzene	*1.2*			mg/kg	-	-	-	<0.050	<0.050
Styrene				mg/kg	-	-	-	<0.050	<0.050
Toluene	*0.8*			mg/kg	-	-	-	<0.050	<0.050
meta- & para-Xylene				mg/kg	-	-	-	<0.050	<0.050
ortho-Xylene				mg/kg	-	-	-	<0.050	<0.050
Total Xylenes	*1.0*			mg/kg	-	-	-	<0.10	<0.10
Extractable Hydrocarbons									
F2 (C10-C16)		*450* (coarse)[f]		mg/kg	-	-	-	41	43
F3 (C16-C34)		*400* (coarse)[f]		mg/kg	-	-	-	253	271
F4 (C34-C50)		*2800* (coarse)		mg/kg	-	-	-	176	188
F4G-sg[d]				mg/kg	-	-	-	820	930
F4G-SG Required (yes/no)				mg/kg	-	-	-	YES	YES
Extractable Hydrocabrons									
EPH10-19			1000	mg/kg	<200	<200	<200	<200	<200
EPH19-32			1000	mg/kg	230	330	250	230	220

Bold Concentration greater than or equal to CCME RL Guideline for soil and/or the site-specific SQRO.

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

[a] Canadian Environmental Quality Guidelines (CEQG) and Petroleum Hydrocarbon Canada-Wide Standards (PHC CWS) presented apply to soil.

[b] Guideline is dependant upon depth of sample (surface, subsoil >1.5 m depth). Surface soil analyzed.

[c] Guideline is dependent on median grain size of soil analyzed (Fine≤75 µm, Coarse >75 µm). Median grain size of soil analyzed is >75 µm.

[d] Guideline is based on the site-specific exposure pathway of Ecological Soil Contact

[e] Total Xylene calculated as the sum of meta, para and ortho Xylenes

[f] Use of the guideline requires that PAHs be subtracted from the fraction. Based on the results for soil sample A1 it is assumed that PAHs form a small percentage of the fractions 2 and 3 for the samples not analyzed for PAHs.

d) Fraction 4G measures carbon chain length in excess of C16.

APPENDIX 3

DECOMMISSIONING AND RECLAMATION

PROGRESS PHOTOGRAPHS

BARGE AREA
(Former Mill / Warehouse / Shop / Administration Facilities)



June 2004 - Since the beginning of 2004 only the loading ramp remains to be removed



June 2004 – Final Grading of Area in Progress


August 2004 – Loading Bridge Gone

CAT GENERATOR BUILDING



May 8, 2004 – Cat Generator Building – Contaminated Soil Excavation Proceeding Around The Building as Site Power is Still Required



June 6, 2004 – Contaminated Soil Excavation Around Cat Generator Building Mostly Competed. Building is Being Stripped for Demolition



August 26, 2004 – Cat Generator Building (and Barge) Area After Demolition and Recontouring

CONCENTRATE STORAGE BUILDING



June 2004 – Demolition essentially completed in 2003 but some footings remain



June 2004 – Conveyor Tube Between Mill and Storage Shed Remains to be removed



August 2004 – Recontouring of Concentrate Storage Building Complete

ACCOMMODATIONS COMPLEX



May 2004 – Still In Use



August 2004 – Demolition in Progress



August 2004 – Demolition In Progress

ACCOMODATION COMPLEX - Continued



August 2004 – Accommodation Building Demolished, Contaminated Soils Removed and Final Grading Completed



August 2004 – Temporary Camp

FUEL TANK FARM



May 2004 – Tank Farm Still in Use



June 2004 – Clean Tank Prior to Demolition



August 2004 – Tank Farm Removed on Temporary Fuel Bladder Remains

FUEL TANK FARM - Continued



September 6, 2004 – Tank Farm Demolished and Area Graded

INCINERATOR BUILDING



Incinerator Custom Built for Project – Stored on Site Prior to Use



May 2004 – Incinerator Building Constructed out of Sea Shipping Containers (still in use)

FOLDAWAY BUILDING DEMOLITION



May 10, 2004 – 3 Foldaway Buildings Still In Use



June 8, 2004 – Oil Contaminated Soils Excavated to South of Foldaways



June 11, 2004 – Oil Contaminated Soils Excavated to North of Foldaways

FOLDAWAY BUILIDING DEMOLITION - Continued



June 13, 2004 – First Foldaway Being Demolished



August 26, 2004 – Foldaway Area Demolition & Recontouring Complete

FIREHALL AREA



May 15, 2004 – Firehall Emptied in Preparation for Demolition



May 15, 2004 – Firehall Empty in Preparation for Demolition



August 26, 2004 – Barge and Fire Hall Areas After Completion

FRESHWATER SYSTEM



June 11, 2004 – Freshwater Tank, Pipeline and Pumphouse Still In Operation



July 2002 – Pump House and Jetty into Frustration Lake



August 2004 – Pump House Removed and Jetty Recontoured

FRESH WATER SYSTEM - Continued



Late August, 2004 – Fresh Water Tank Being Demolished

MAIN PORTAL



May 17, 2004 – Main Portal Entrance and Cooling Equipment



August 6, 2004 – Filling of Main Portal in Progress



CONVEYOR PORTAL (CV03)



June 10, 2004 – Conveyor Removed



August 2004 – Blasting Down Thin Cover Over Portal After Plug Installed



August 2004 – Re-sloped Hill Over Portal

EXPLORATION PORTAL



June 2004 – Exploration Portal (note Vent Pipe)



June 11, 2004 – Concrete Plug Inside Portal

EXPLORATION PORTAL - Continued



June 29, 2004 – Placing Fill into Portal



August 27, 2004 – Area of former Exploration Portal

NORTH PORTAL



June 2004 - North Portal Before Sealing

NORTH PORTAL - Continued



August 9, 2004 – Removed Top Cover at Collar of Portal



August 16, 2004 – Demolishing Concrete Wings at Portal Entrance



August 16, 2004 – Recontouring over Plugged Portal

DOCK DECOMMISSIONING



February 2, 2004 – Dock Before Work Starts for the Season



February 2004 – Drilling for Ice Thickness Prior to Starting Work



April 8, 2004 – Divers Cutting Sheet Piles

DOCK DECOMMISSIONING – Continued



May 11, 2004 – Digging Fill From Inside Dock Sheet Piles



May 26, 2004 Loading Sheet Piles to be Hauled to LRD Quarry landfill



May 31, 2004 – Diver Entering Water to Cut Sheet Piles

DOCK DECOMMISSIONING – Continued



June 2, 2004 – Excavation of Dock Continuing



June 18, 2004 - Decommissioning of Dock



June 26, 2004 – Decommissioning of Dock Nearing Completion

DECOMMISSIONING OF DOCK -Continued



July 15, 2004 – Decommissioning of Dock Completed

RECONTOURING MARINE FORESHORE – North of Dock



April 11, 2005 – Excavating Contaminated Soils North of Dock Area



Apr 11, 2005 – Excavated Shoreline North of Previous Picture



April 27, 2004 – Re-grading Area Shown Previously

RECONTOURING MARINE FORESHORE – North of Dock Continued



May 9, 2004 – Recontouring Further North of Dock



June 9, 2004 – Continuing Recontouring



June 9, 2004 – Final Re-grading of Area Shown in Previous Photograph

RECONTOURING MARINE FORESHORE – North of Dock Continued



June 10, June – Previous Area Almost Complete



August 26, 2004 – Area Completed. Photograph is Showing Only the North End of the Re-contoured area.

RECONTOURING MARINE FORESHORE – South of Dock



April 27, 2004 – Excavator Ripping Frozen Ground South of Dock



June 5, 2004 – Snow Pushed Back to Expose Shoreline



June 16, 2004 – Further South Along Shoreline, Berm Being Removed

RECONTOURING MARINE FORESHORE – South of Dock



June 16, 2004 – Excavating Shoreline South Towards Foldaway Buildings



July 4, 2004 – Excavator Doing Final Trimming Above Beach Area Just South of Dock



July 11, 2004 – Work Continuing on Contouring Area Above Beach

RECONTOURING MARINE FORESHORE – South of Dock



August 26, 2004 – Contouring of Foreshore Completed



March 19, 2004 – Excavating Dam



March 19, 2004 Excavating Dam



March 22, 2004 – Excavation Continues



April 13, 2005 – Dam Core Removed, Excavator Working on Centre Channel



April 16, 2004 – Installing Geotextile In Channel



April ? – Placing Rip-Rap Onto Geotextile



April 20, 2004 – Nearing Completion Placing Rip-Rap in Channel Bottom



June 17, 2004 – Dam Removal Completed in April but Now Snow Gone, Can See the Finished Slopes and Channel Better



July 10, 2004 – Flow in Decommissioned Dam Channel




August 26, 2004 – Creek Channel Through Dam After Flow Essentially Complete for the Year

APPENDIX 4

SITE DRAWINGS

KEY PLAN
N.T.S.

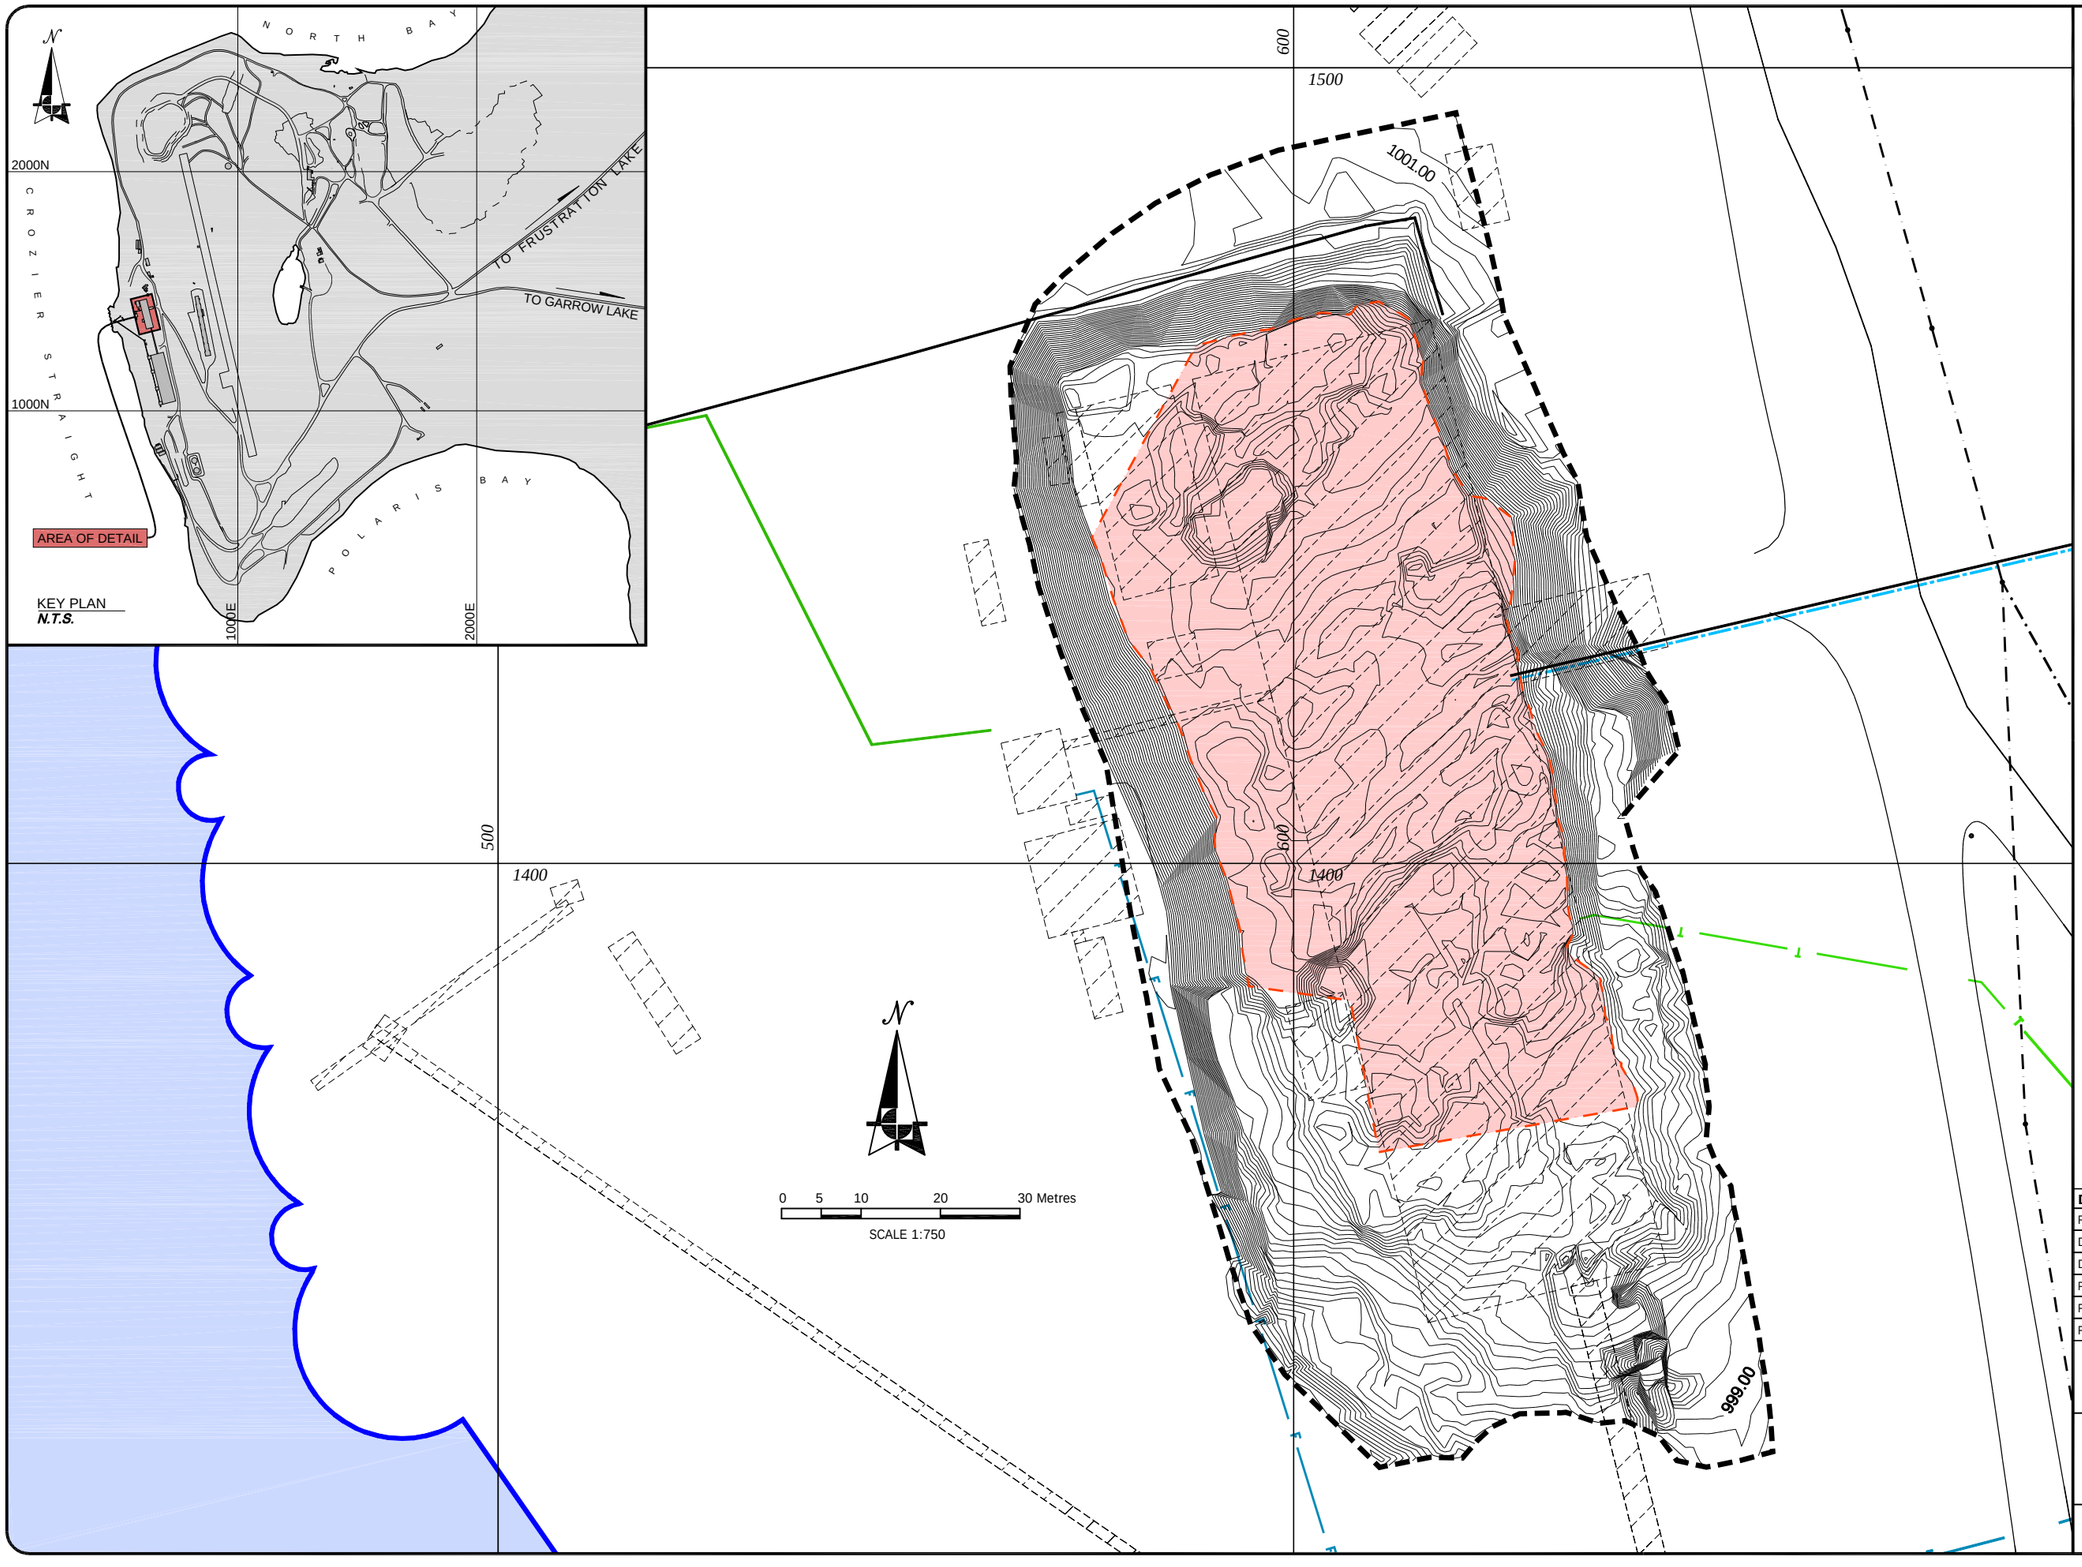

LEGEND:

- 2003 LIMIT OF BARGE EXCAVATION
- EXCAVATED BARGE CONTOURS (0.2m)
- BETWEEN OCT. 12/03 & OCT. 31/03, 6,300 sq. m. OF GARROW DAM CORE MATERIAL PLACED AT THE BASE OF EXCAVATION. 31,500 sq. m. OF CLEAN SAND & GRAVEL ALSO PLACED IN THIS AREA BETWEEN OCT. 12/03 & OCT 31/03. A FURTHER 25,200 sq. m. OF CLEAN SAND & GRAVEL USED TO BACKFILL THE EXCAVATION AFTER OCT. 31/03
- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- WATER LINE
- OVERHEAD POWER LINE
- POWER POLE


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – MAY 25, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–BARGE–2003 BACKFILL.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT


2003 BARGE BACKFILL - FINAL DISPOSAL LOCATION OF GARROW DAM CORE MATERIAL

Gartner Lee

Figure No.
40137-BARGE-1

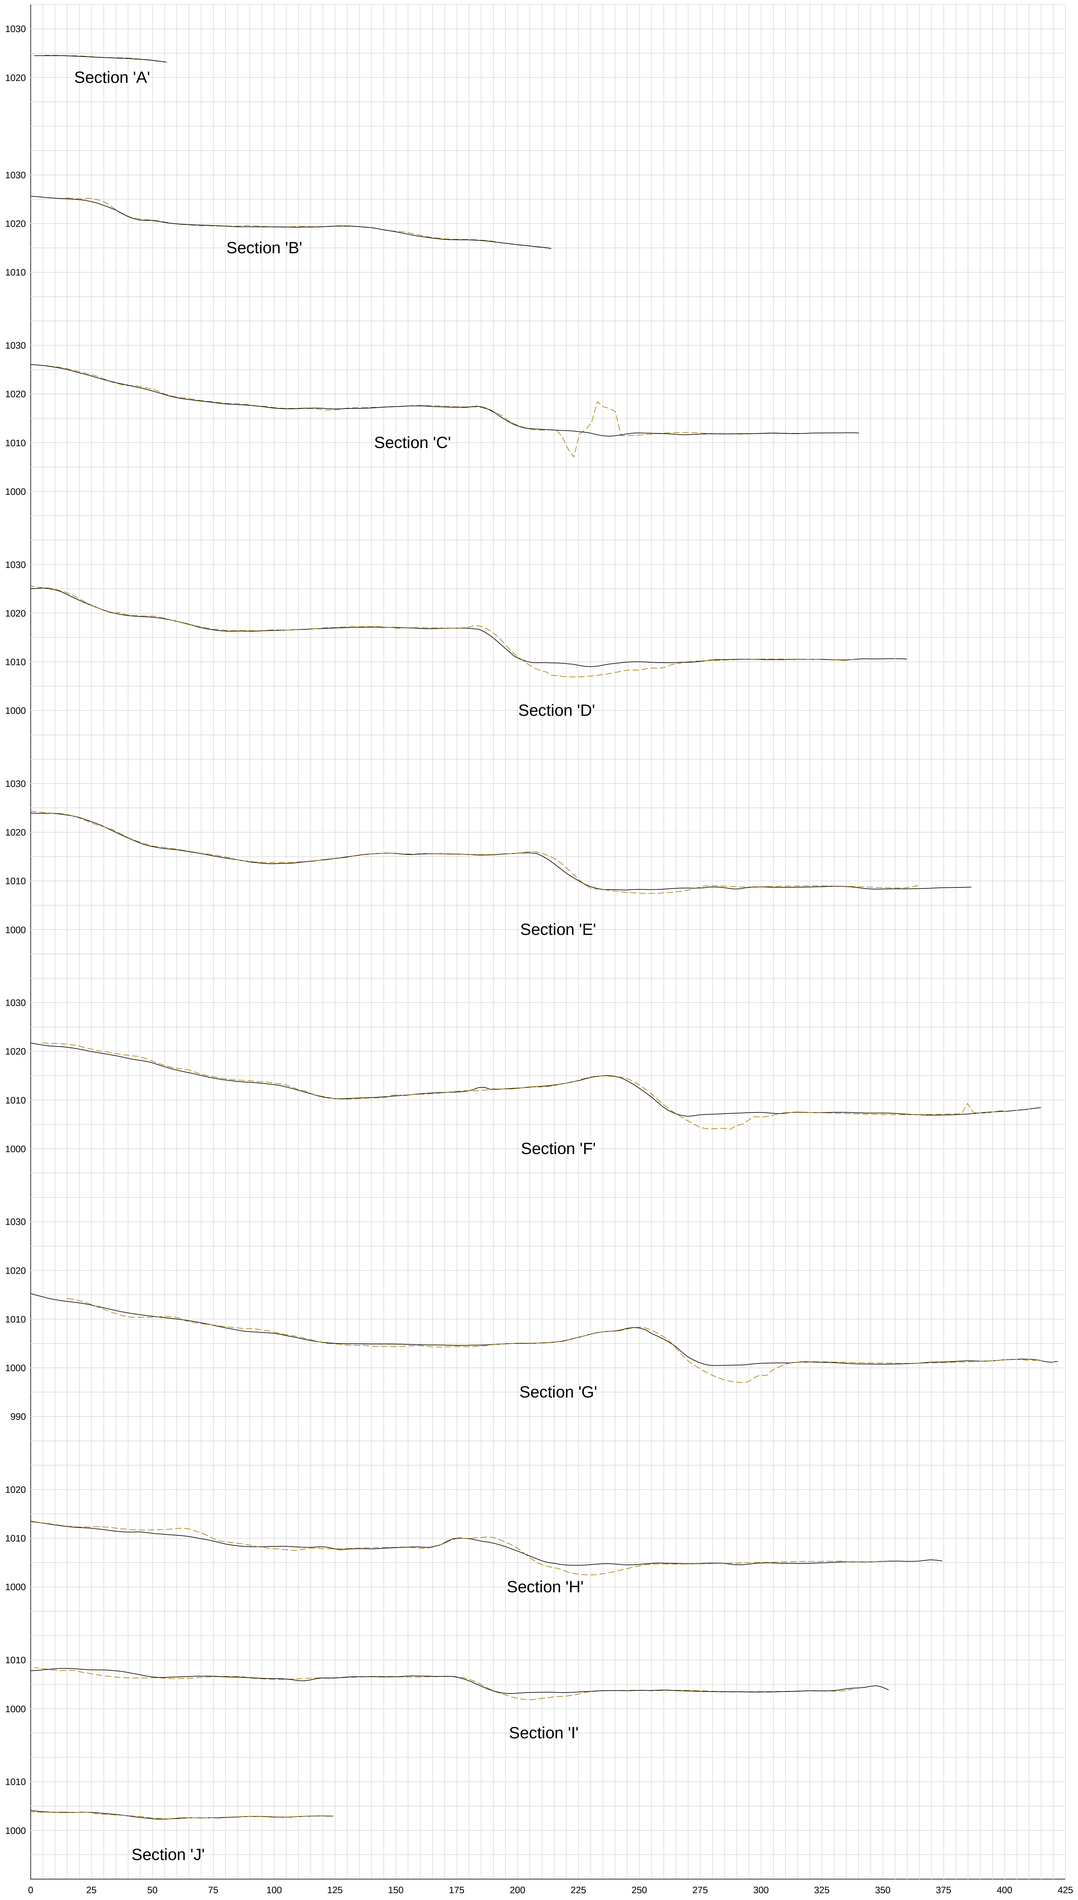

Vertical Scale 1:500
Horizontal Scale 1:1000

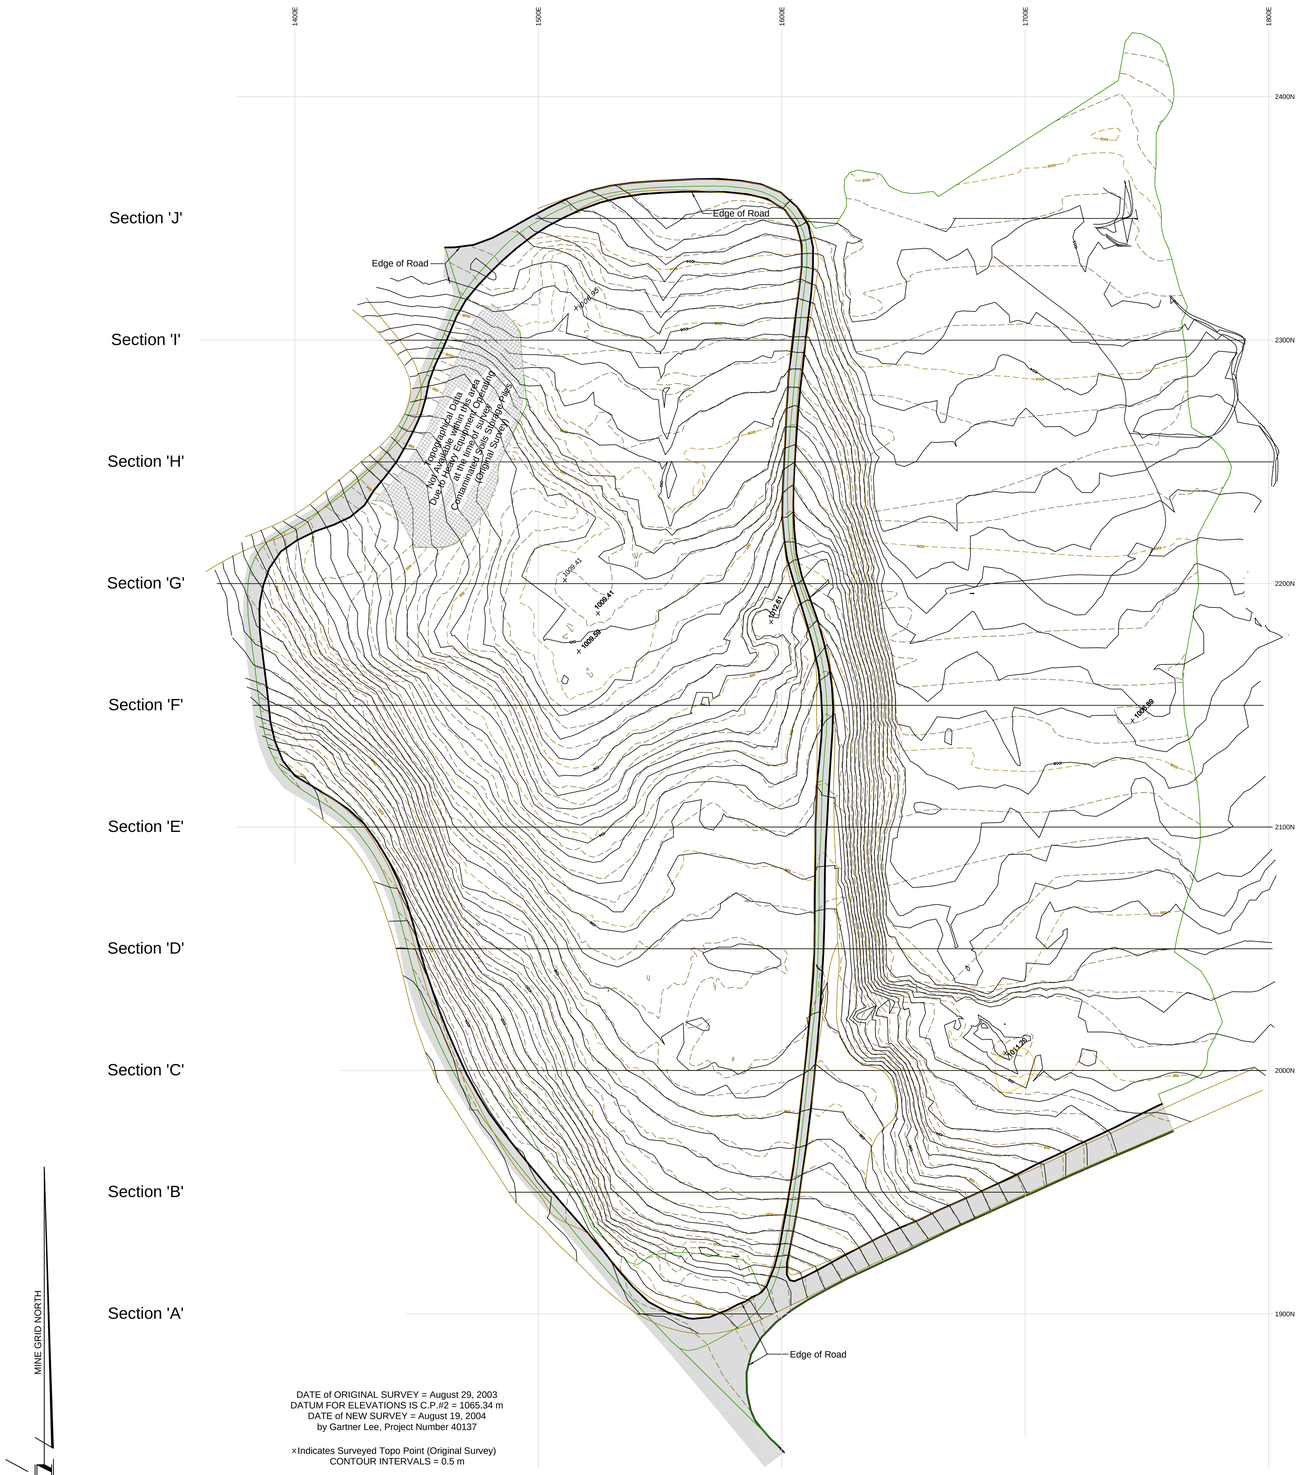



DATE of ORIGINAL SURVEY = August 29, 2003
DATUM FOR ELEVATIONS IS C.P.#2 = 1065.34 m
DATE of NEW SURVEY = August 19, 2004
by Gartner Lee, Project Number 40137

×Indicates Surveyed Topo Point (Original Survey)
CONTOUR INTERVALS = 0.5 m


TOPOGRAPHIC SURVEY
of Subsidence Area
Polaris Mine
Nunavut

teckcominco

DATE	REVISIONS	DR/CK
Jan. 04/05	Added Survey Data by Gartner Lee	TT/CT

FOCUS Focus Surveys
A DIVISION OF THE FOCUS CORPORATION LTD.
Edmonton (780) 466-6555
Calgary (403) 269-2252
Grande Prairie (780) 539-3222
Medicine Hat (403) 527-3707
Regina (306) 586-0837
Fort St John (250) 785-7776

Drawn by : TT	Chk'd by : CT
Date : January 04, 2005	Scale: 1:1000
Job : 322789-00	FILE No.
Dwg : 322789-01-topo.dwg	Sheet 1 of 1

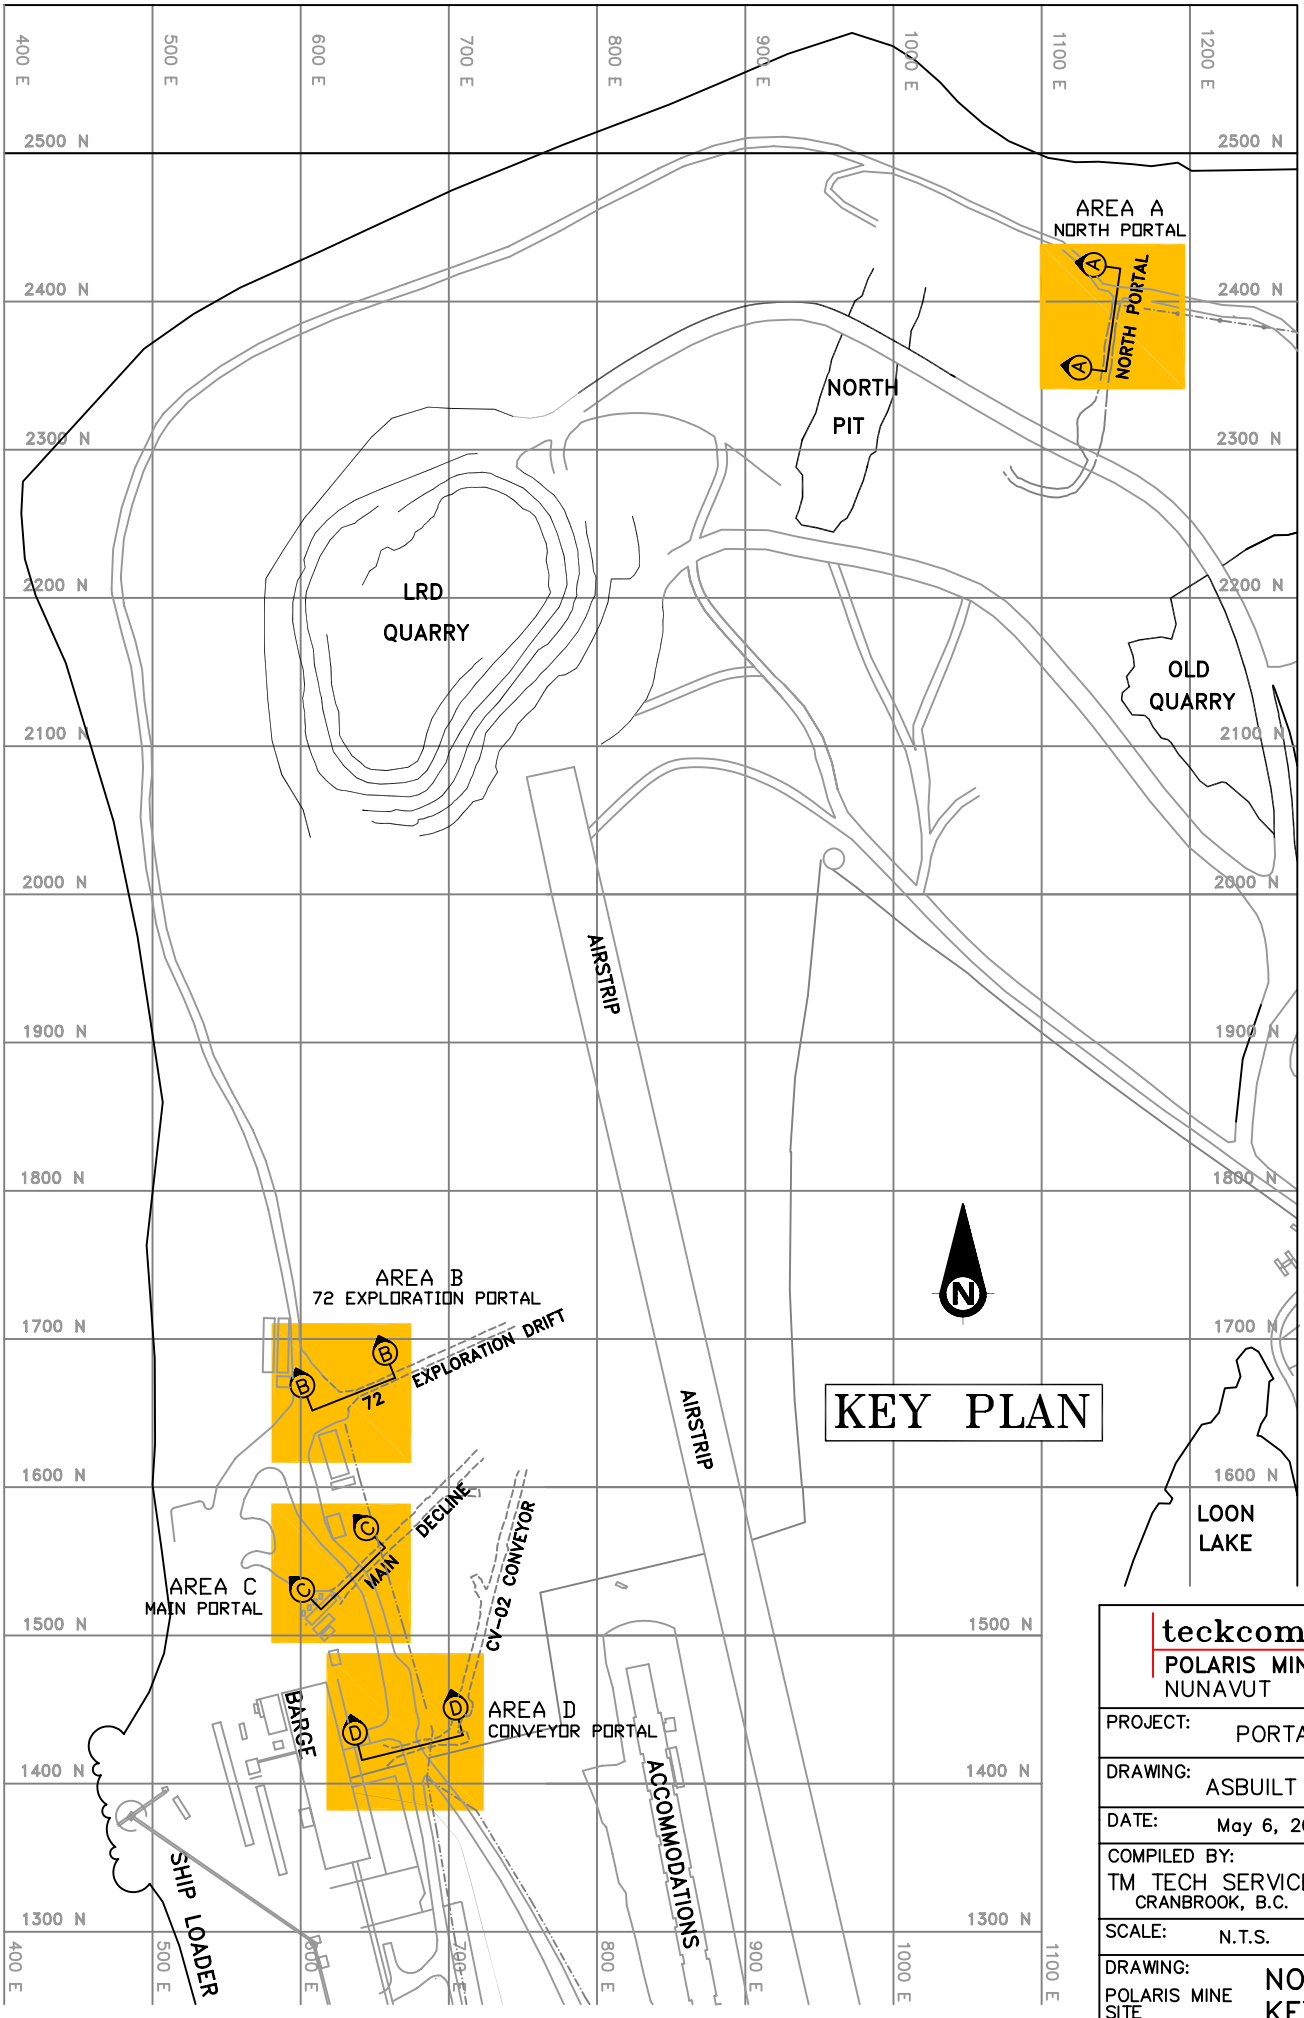


teckcominco

POLARIS MINE
NUNAVUT

PROJECT:	PORTAL PLUGS
DRAWING:	ASBUILT SECTIONS
DATE:	May 6, 2005
COMPILED BY:	TM TECH SERVICES CRANBROOK, B.C.
SCALE:	N.T.S.
DRAWING:	NO. 1 KEY PLAN

POLARIS MINE SITE

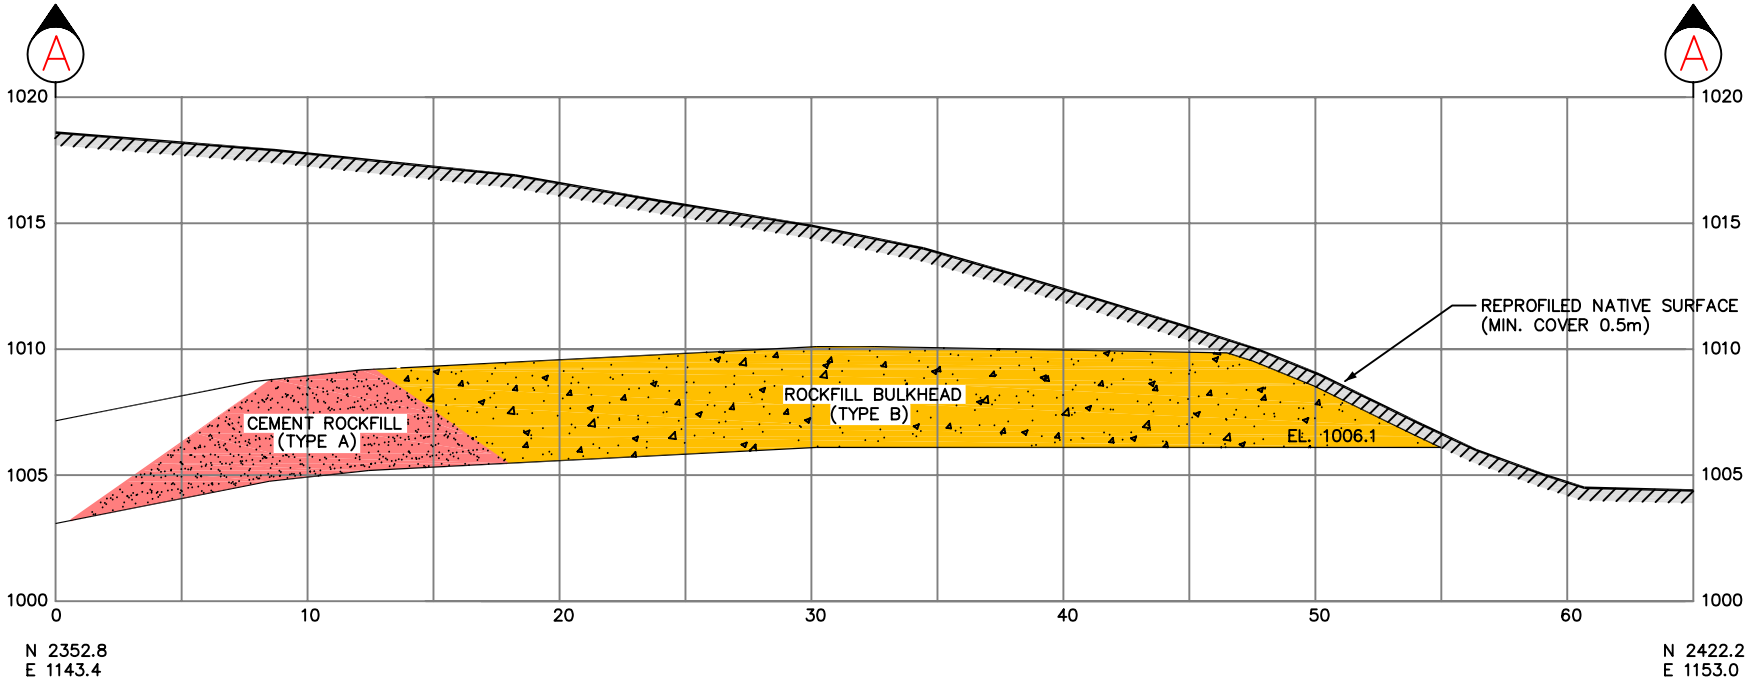

SECTION AA
NORTH PORTAL

teckcominco
POLARIS MINE
NUNAVUT

PROJECT: PORTAL PLUGS


DRAWING: ASBUILT SECTIONS

DATE: May 6, 2005

COMPILED BY:
TM TECH SERVICES
CRANBROOK, B.C.

SCALE: 1:300 (metric)

DRAWING:
NO. 2
SECT-AA
NORTH PORTAL

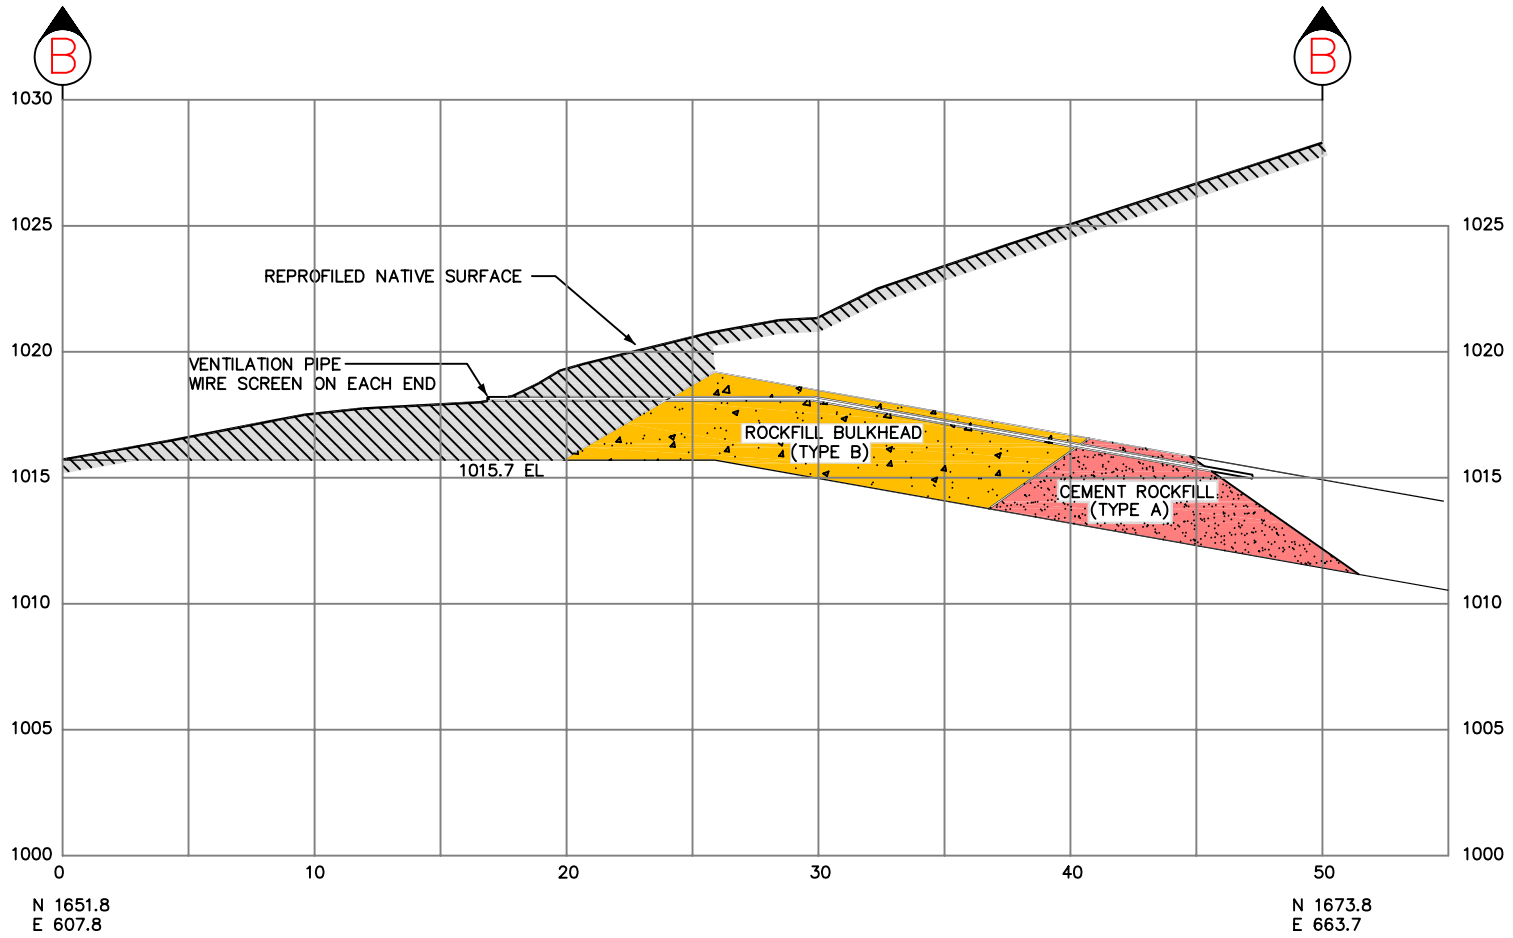

SECTION BB
72 EXPLORATION PORTAL

teckcominco
POLARIS MINE
NUNAVUT

PROJECT: PORTAL PLUGS


DRAWING: ASBUILT SECTIONS

DATE: May 6, 2005

COMPILED BY:
TM TECH SERVICES
CRANBROOK, B.C.

SCALE: 1:300 (metric)

DRAWING: No. 3
72 EXPLORATION PORTAL
SECT-BB

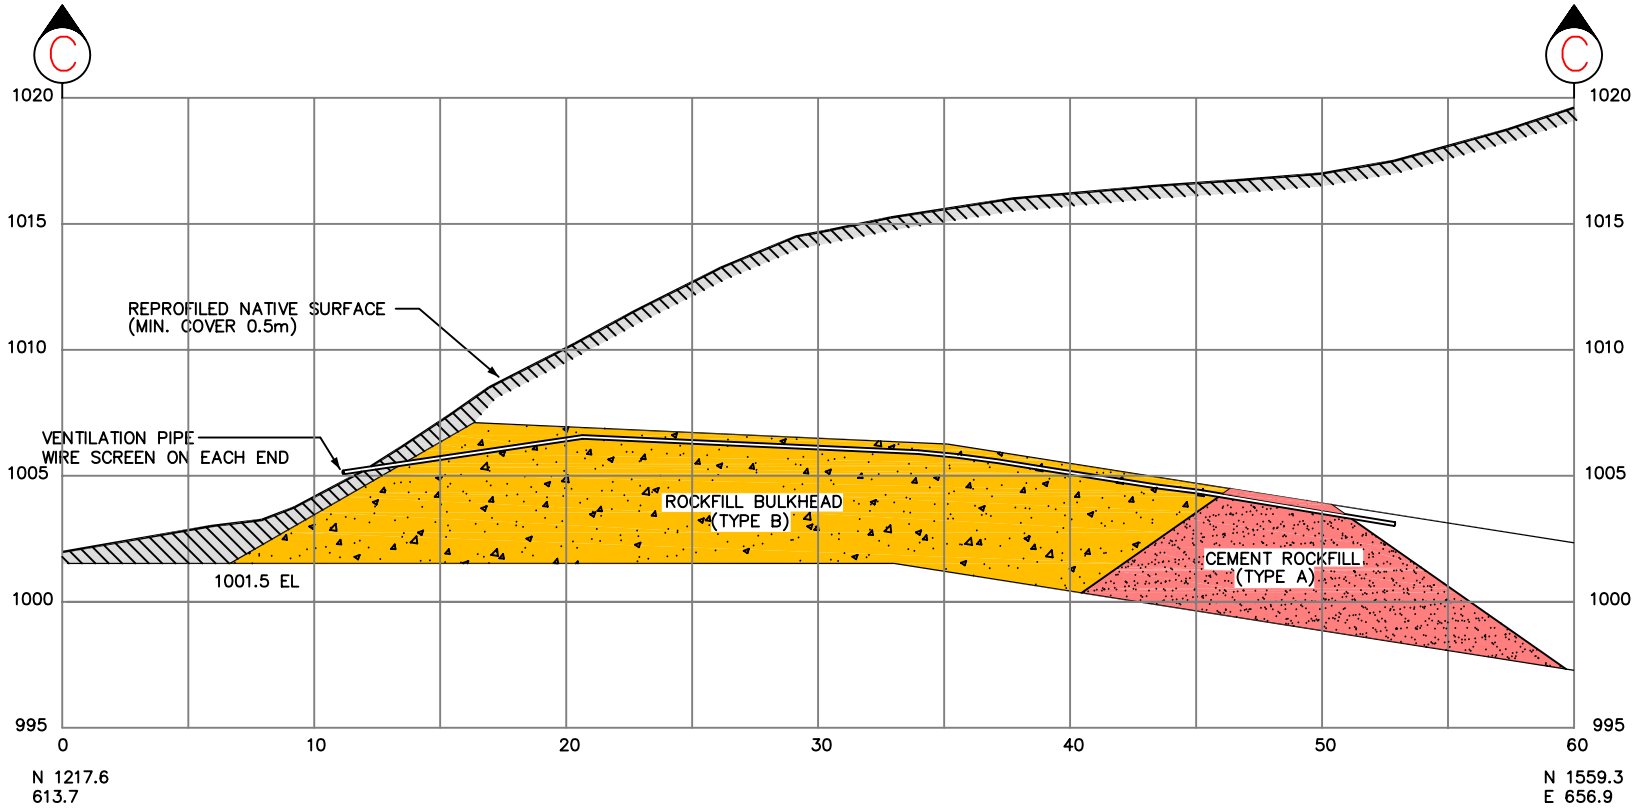

SECTION CC
MAIN PORTAL

teckcominco
POLARIS MINE
NUNAVUT

PROJECT: PORTAL PLUGS


DRAWING: ASBUILT SECTIONS

DATE: May 6, 2005

COMPILED BY:
TM TECH SERVICES
CRANBROOK, B.C.

SCALE: 1:300 (metric)

DRAWING: No. 4
MAIN PORTAL SECT-CC

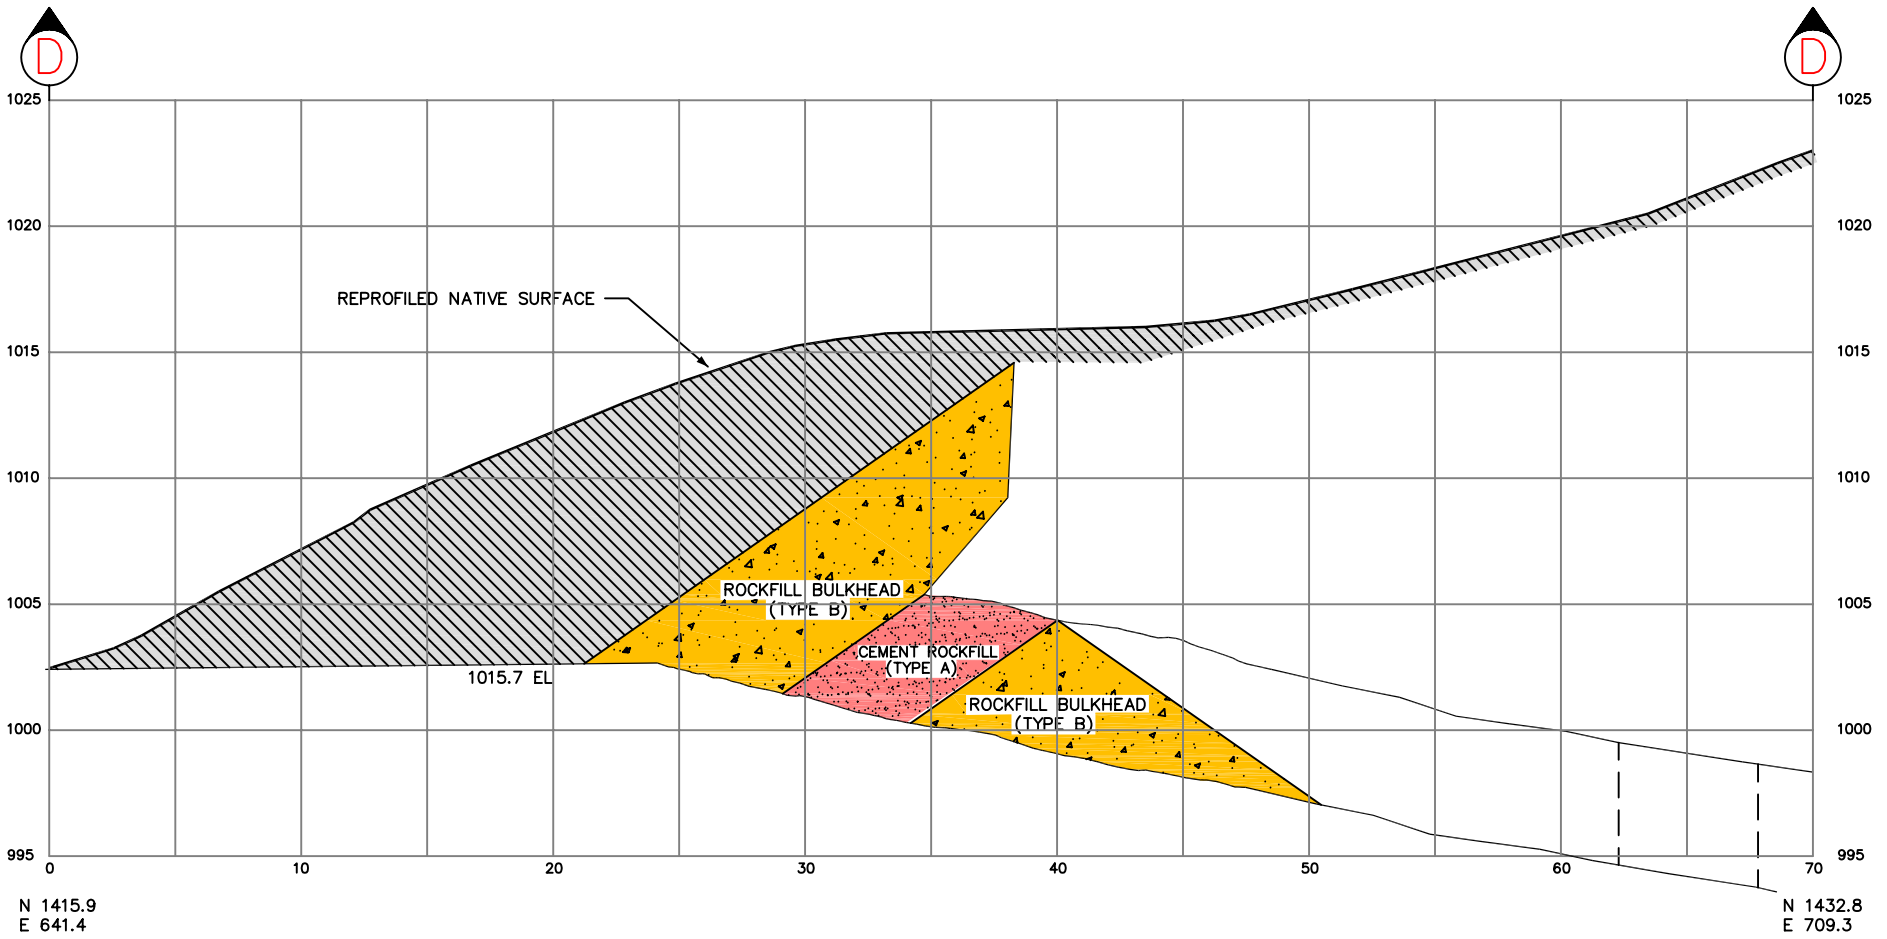

SECTION DD
CONVEYOR PORTAL

teckcominco
POLARIS MINE
NUNAVUT

PROJECT: PORTAL PLUGS

DRAWING: ASBUILT SECTIONS

DATE: May 6, 2005

COMPILED BY:
TM TECH SERVICES
CRANBROOK, B.C.

SCALE: 1:300 (metric)

DRAWING: No. 5
CONVEYOR PORTAL SECT-DD

APPENDIX 5

GEOTECHNICAL REPORTS

APPENDIX 6

CONTAMINATED SOIL REMEDIATION

2004 CLOSE OUT REPORTS

By

GARTNER LEE LTD.

Contaminated Soil Remediation
2004 Close Out Reports
Polaris Mine, Nunavut

Prepared for
Teck Cominco Limited

Submitted by
Gartner Lee Limited

June 2005

Contaminated Soil Remediation 2004 Close Out Reports Polaris Mine, Nunavut

Prepared for
Teck Cominco Limited

June 2005

Reference: **GLL 50063**

Distribution:
10 Teck Cominco Limited
3 Gartner Lee Limited

Gartner Lee Limited

June 22, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 50063 - Contaminated Soil Remediation 2004 Close Out Reports
Polaris Mine, Nunavut

On behalf of Gartner Lee Limited, I am pleased to submit the remaining close out reports on the areas of contaminated soil remediated at the Polaris Mine site. These close out reports serve to document the remedial activities that were undertaken and the sample results that verify completion of activities. The areas remediated were identified as Areas of Potential Environmental Concern in the *Polaris Mine Decommissioning and Reclamation Plan*, March 2001. The areas have been remediated to the meet the approved Polaris Mine site specific remedial targets.

Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* illustrates those areas that were remediated in 2003 and reported previously in the February 16, 2004 Report *23305 – Contaminated Soil Remediation 2003 Close Out Reports, Polaris Mine, Nunavut* (Areas 3, 4, 6, 11, 12, 15, 17, 22, 23, and 24).

Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004* illustrates the areas of contaminated soil remediated subsequently. The results are presented as ten (10) separate appendices to this letter. Each of reports have been subject to detailed peer and management review as follows:

Area 1.	Process Barge, Dr. Dennis Gregor, P.Geol. (NU), Guelph, ON Office Manager
Area 2.	Ship Loading Dock, Dr. Dennis Gregor, P.Geol. (NU)
Area 5.	Accommodation Complex, Robert Dickin, M.Sc., P.Geo. (BC), Burnaby, BC Office Manager, Principal
Areas 7 and 19	Foldaway Buildings, David S. Osmond, B.Sc., R.P.Bio., Principal
Areas 8 and 9:	Tank Farm and Lube Oil Storage, Alistair Kent, P.Eng. (BC), Manager Western Canada Mining Sector
Area 10:	Tailings Pipeline, David S. Osmond, B.Sc., R.P.Bio.
Area 18:	Loon Lake Snow Dump, David S. Osmond, B.Sc., R.P.Bio.

840-7th Avenue SW, Suite 1605, Calgary, Alberta, T2P 3G2 tel 403.262.4299 fax 403.264.8412
www.gartnerlee.com

Area 21:	Firehall, Eric Denholm, B.A.Sc., P.Eng. (NU), Yellowknife, NT Office Manager, Principal
Area 25:	South Shore, Eric Denholm, B.A.Sc., P.Eng. (NU)
Area 26:	North Shore, Dr. Dennis Gregor, P.Geol. (NU)


There are four (4) additional areas that were presented as "Areas of Potential Environmental Concern" in the Polaris Mine Decommissioning and Reclamation Plan, March 2001. These are presented as the following areas on Figures 1 and 2 as Areas 13, 14, 16 and 20. These areas were not targeted for remediation of contaminated soil in the Decommissioning and Reclamation Plan for the following reasons:

Area 13:	Operational and Construction Landfills. These areas were listed as being of potential environmental concern because the Construction Landfill required relocation to the toe of the Operational Landfill and the consolidated landfill area capped with an engineered cover cap.
Area 14:	Fire Training Area. This area was identified as a potential environmental concern in the 1999 Phase 2 Environmental Site Assessment (ESA), which was conducted prior to the development of the risk based site-specific Soil Quality Remediation Objectives (SQRO's). Upon review of the laboratory data gathered during the 1999 Phase 2 ESA it was determined that the laboratory results met the SQRO's and therefore no remediation work was required at this area.
Area 16:	Explosives Storage/Detonator Magazine. This area was listed as being of potential environmental concern due to the presence of hazardous materials (explosives). During demolition the explosives were removed from this area and detonated.
Area: 20:	Surface Above Active Mining Area. These areas were identified as being of potential public safety concern because during the operation of the mine surface subsidence had occurred over certain older underground openings. This is a geotechnical issue, not a contaminated soil issue and is therefore not commented on in this report. Post closure monitoring at the site will include inspection of this area to confirm stability.

As the aforementioned four areas did not require environmental remediation, no Contaminated Soil Remediation Close Out Reports have been prepared.

I trust that this is satisfactory and that you will find the information presented in this report to be complete and thorough. It has been a great pleasure to have had continued involvement in the Polaris Mine Decommissioning and Reclamation project following the development of the plan in 2001 and I look forward to providing on-going support through the post closure monitoring stage.

Yours very truly,
GARTNER LEE LIMITED



Stephen R. Morison, M.Sc., P.Geol. (NU)
Manager Western Canada Business Unit, Project Principal

AL:gc


Figures

Figure 1: Contaminated Soils Remediation Progress Plan, December 31, 2003
Figure 2: Contaminated Soils Remediation Progress Plan, December 31, 2004

Enclosures: Polaris Mine Operations Contaminated Soil Remediation Close Out Reports:

Appendix A	Process Barge
Appendix B	Ship Loading Dock
Appendix C	Accommodation Complex
Appendix D	Foldaway Buildings
Appendix E	Tank Farm and Lube Oil Storage
Appendix F	Tailings Pipeline
Appendix G	Loon Lake Snow Dump
Appendix H	Firehall
Appendix I	South Shore
Appendix J	North Shore

CC: E. Denholm, R. Dickin, D. Gregor, A. Kent, A. Laudrum, D. Osmond, T. Pye

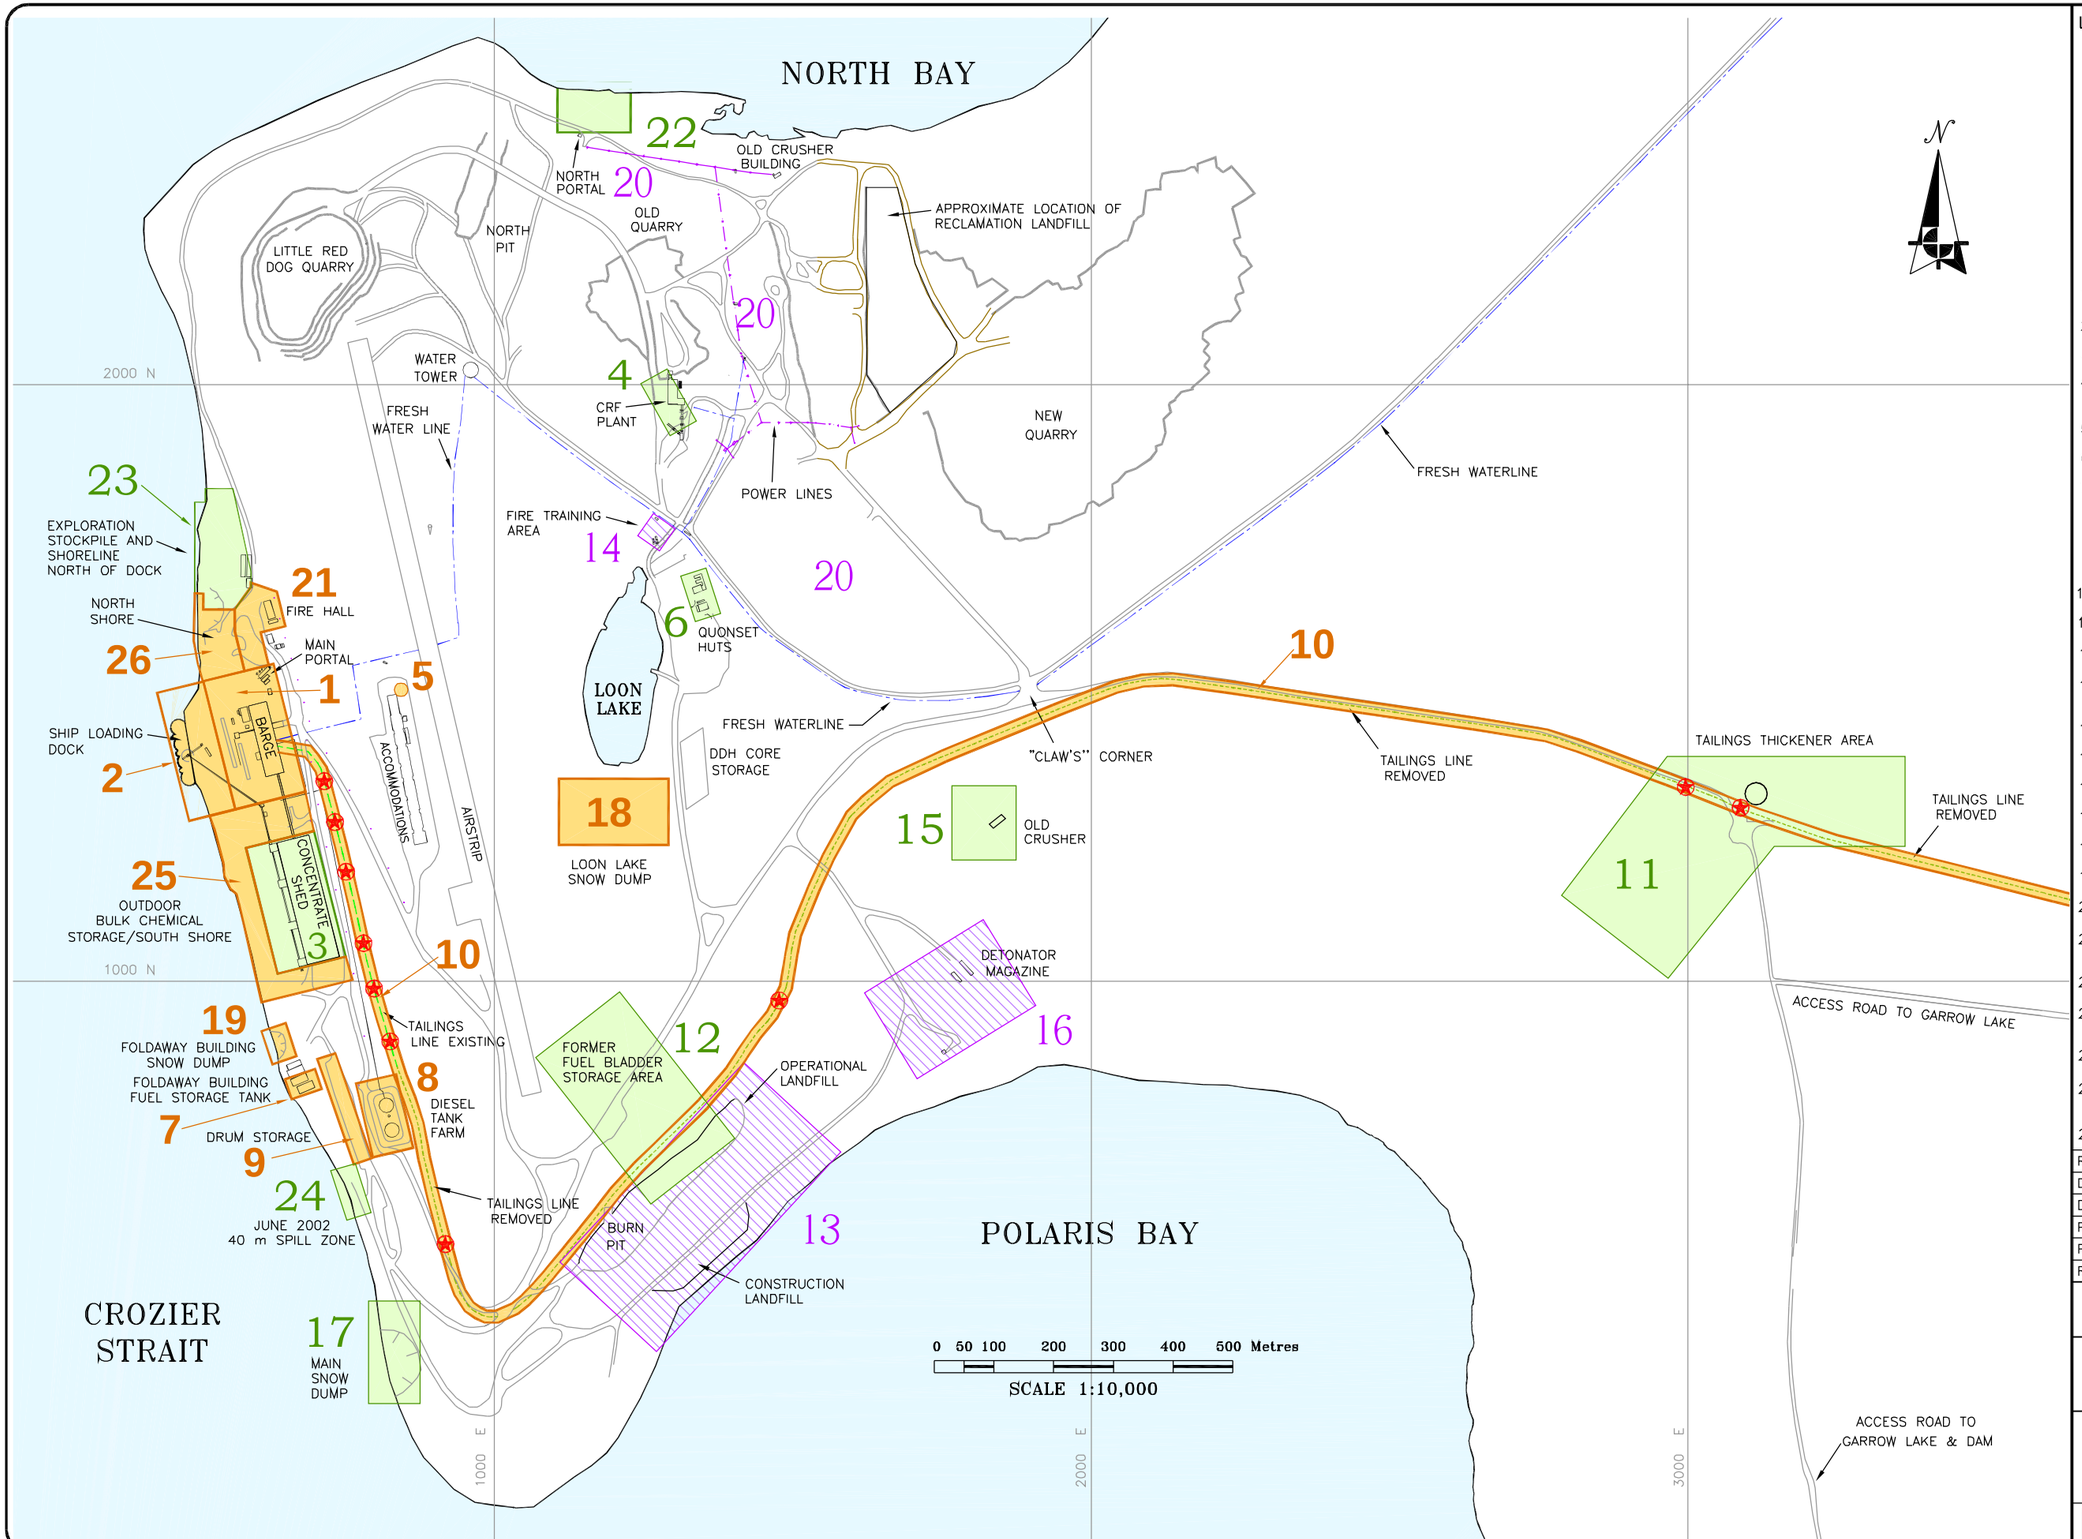

LEGEND:

- TAILINGS LINE
- TAILINGS LINE REMOVED
- POWER LINE
- WATER LINE
- ROADS
- TAILINGS LINE BREAKS
- 1 — AREAS NOT MEETING REMEDIAL TARGETS AS OF DECEMBER 31, 2003
- 15 — AREAS MEETING REMEDIAL TARGETS AS OF DECEMBER 31, 2003
- 16 — AREAS NOT CONSIDERED AN ENVIRONMENTAL CONCERN BASED ON 2000 ENVIRONMENTAL SITE ASSESSMENT

1– PROCESS BARGE
2– SHIP LOADING DOCK
3– CONCENTRATE STORAGE SHED AREA
4– CEMENTED ROCK FILL PLANT FUEL STORAGE TANK AREA
5– ACCOMMODATIONS FUEL STORAGE TANK
6– FORMER QUONSET HUTS FUEL STORAGE AREA
7– FOLDAWAY BUILDINGS FUEL STORAGE TANK
8– DIESEL TANK FARM
9– OUTDOOR LUBE/HYDRAULIC OIL AND GLYCOL DRUM STORAGE
10– TAILINGS PIPELINE
11– TAILINGS THICKENER AREA
12– FORMER FUEL BLADDER STORAGE AREA
13– OPERATIONAL AND CONSTRUCTION LANDFILL AND OPEN STORAGE AREA
14– FIRE TRAINING AREA
15– OLD CRUSHER AREA
16– DETONATOR MAGAZINE
17– MAIN SNOW DUMP
18– LOON LAKE SNOW DUMP
19– FOLDAWAY BUILDING SNOW DUMP
20– SURFACE ABOVE FORMER ACTIVE MINING AREA
21– FIREHALL INCLUDING SNOW DUMP, FUEL STORAGE TANK AND ORE STOCKPILE
22– NORTH PORTAL STOCKPILE
23– EXPLORATION STOCKPILE AND SHORELINE NORTH OF DOCK
24– JUNE 2002 – 40 m SPILL ZONE
25– OUTDOOR BULK CHEMICAL STORAGE/SOUTH SHORE
26– NORTH SHORE

REVIEWED BY:	KT/AL
DRAWN BY:	CPW
DATE ISSUED:	13 FEBRUARY, 2004
PROJECT NUMBER:	23-305
FILE NAME:	23305-6F-01.DWG
REVISION:	0


teckcominco

CONTAMINATED SOIL REMEDIATION
2003 CLOSE OUT REPORT
POLARIS MINE, NUNAVUT

CONTAMINATED SOILS REMEDIATION PROGRESS PLAN, DECEMBER 31, 2003

Gartner Lee

Figure No. 1

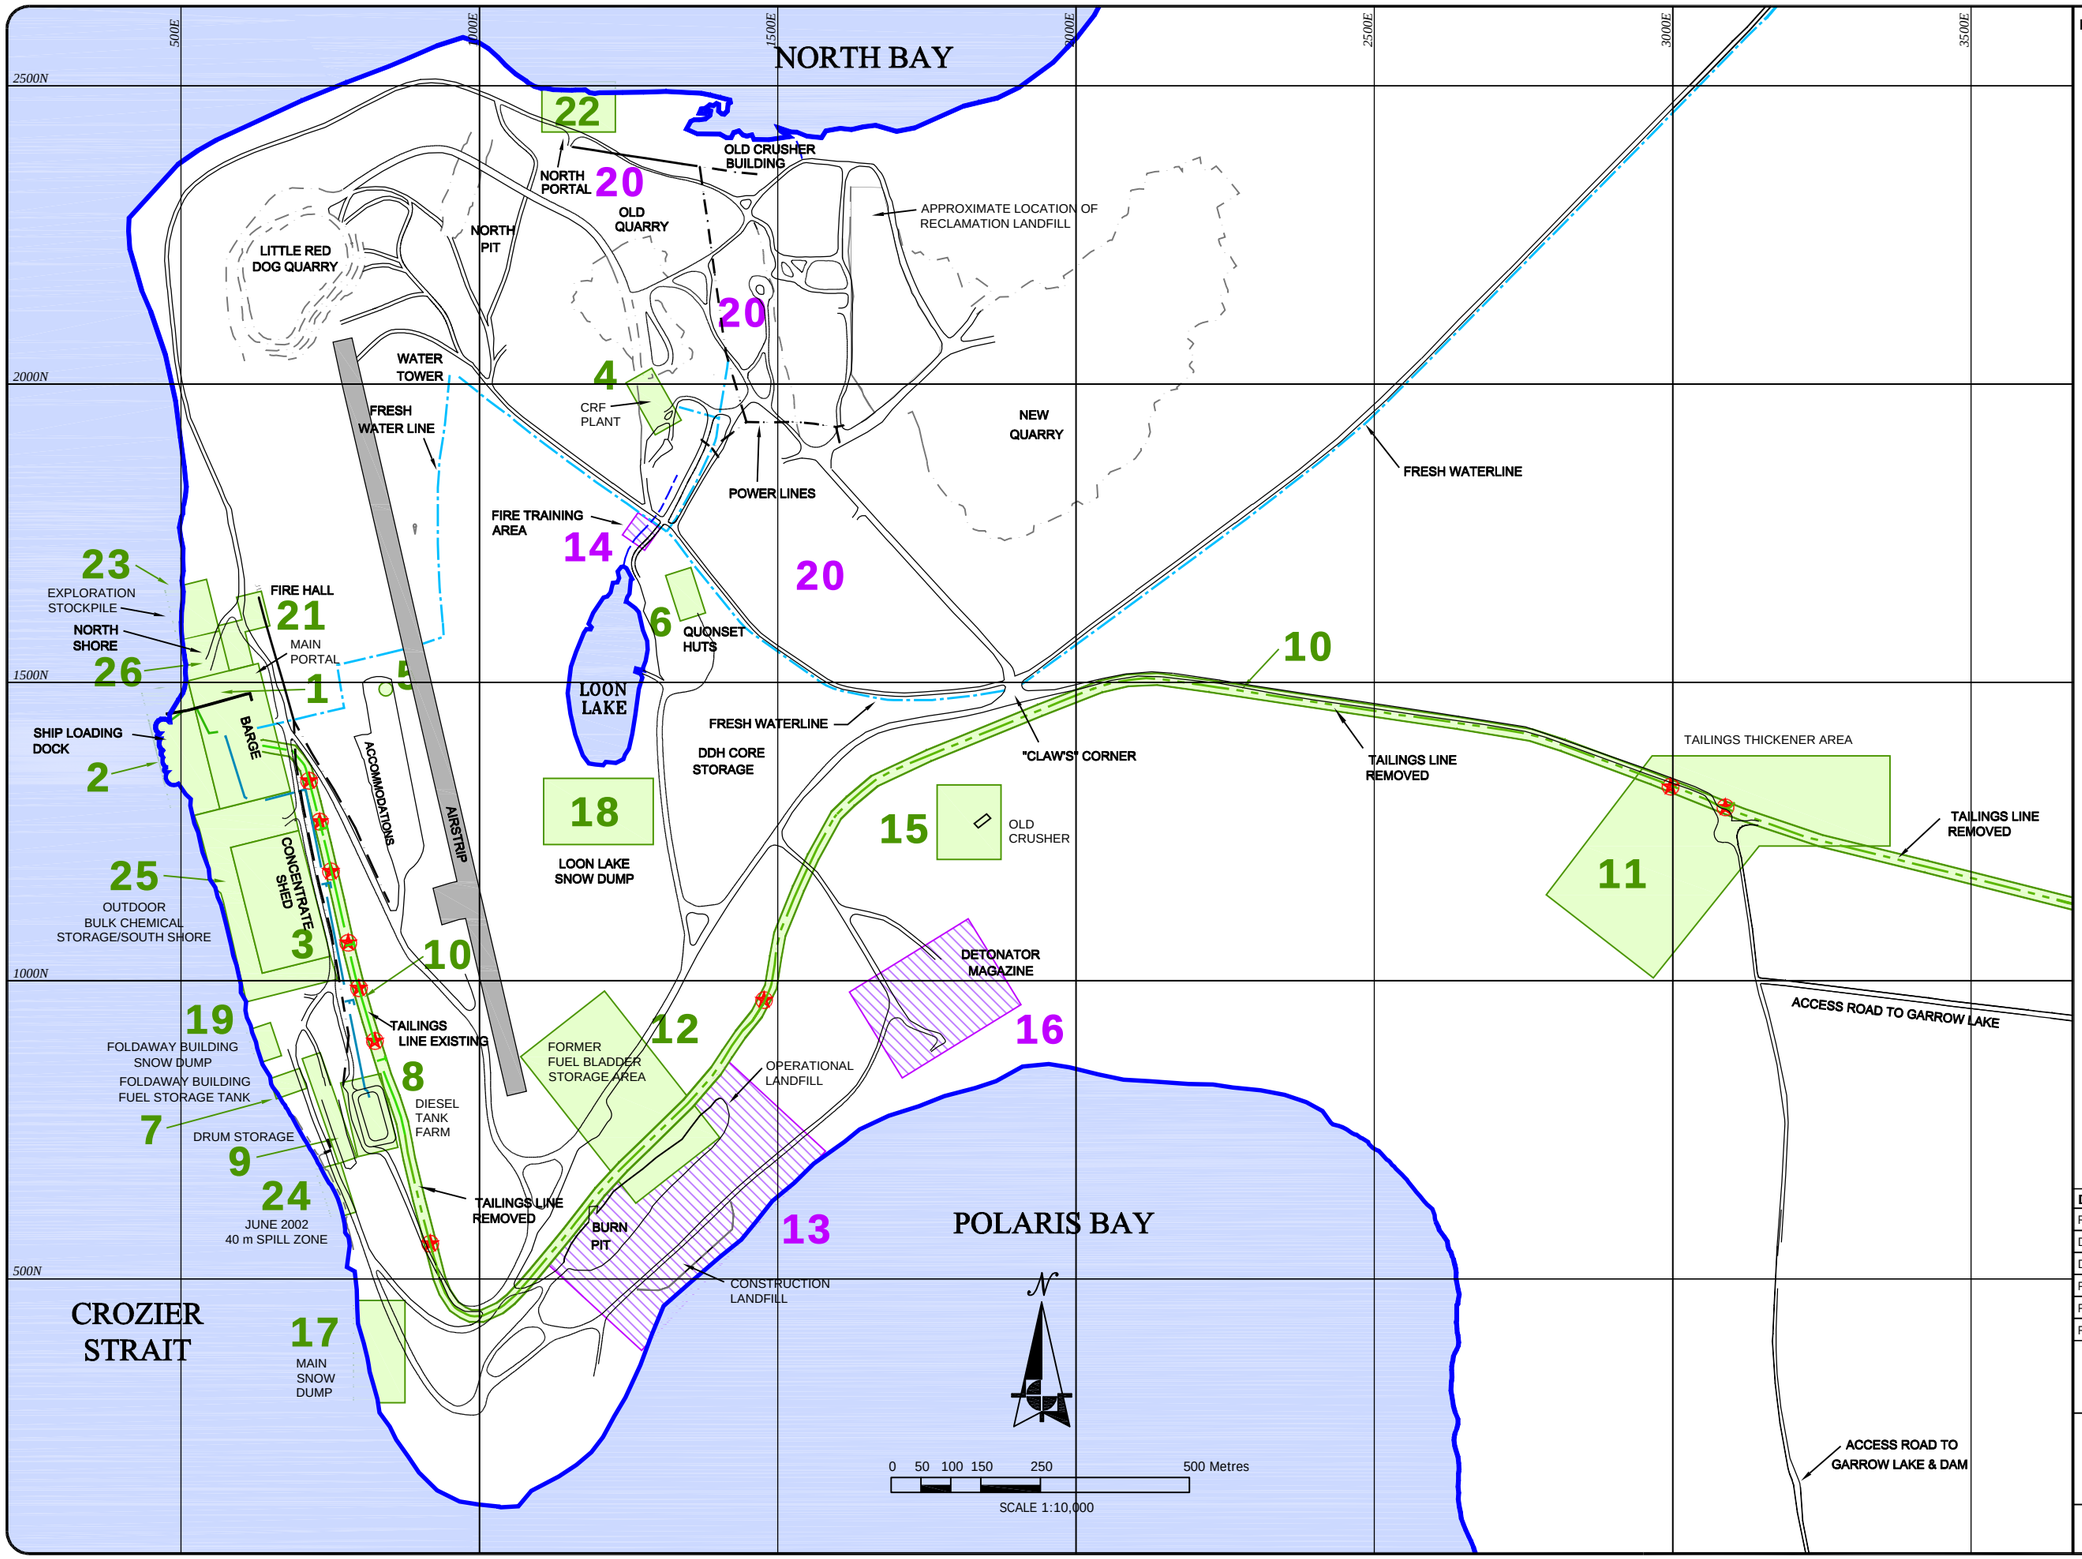

LEGEND:

- TAILINGS LINE
- TAILINGS LINE REMOVED
- POWER LINE
- WATER LINE
- ROADS
- TAILINGS LINE BREAKS
- 1 — AREAS NOT MEETING REMEDIAL TARGETS AS OF DECEMBER 31, 2004
- 15 — AREAS MEETING REMEDIAL TARGETS AS OF DECEMBER 31, 2004
- 16 — AREAS NOT CONSIDERED AN ENVIRONMENTAL CONCERN BASED ON 2000 ENVIRONMENTAL SITE ASSESSMENT

1– PROCESS BARGE
2– SHIP LOADING DOCK
3– CONCENTRATE STORAGE SHED
4– CRF PLANT FUEL STORAGE TANK
5– ACCOMMODATIONS FUEL STORAGE TANK
6– QUONSET HUTS FUEL STORAGE TANK
7– FOLDAWAY BUILDINGS FUEL STORAGE TANK
8– DIESEL TANK FARM
9– OUTDOOR LUBE/HYDRAULIC OIL AND GLYCOL DRUM STORAGE
10– TAILINGS PIPELINE
11– TAILINGS THICKENER AREA
12– FORMER FUEL BLADDER STORAGE AREA
13– OPERATIONAL AND CONSTRUCTION LANDFILL AND OPEN STORAGE AREA
14– FIRE TRAINING AREA
15– OLD CRUSHER
16– DETONATOR MAGAZINE
17– MAIN SNOW DUMP
18– LOON LAKE SNOW DUMP
19– FOLDAWAY BUILDING SNOW DUMP
20– SURFACE ABOVE FORMER ACTIVE MINING AREA
21– FIREHALL INCLUDING SNOW DUMP, FUEL STORAGE TANK AND ORE STOCKPILE
22– NORTH PORTAL STOCKPILE
23– EXPLORATION STOCKPILE
24– JUNE 2002 – 40 m SPILL ZONE
25– OUTDOOR BULK CHEMICAL STORAGE/SOUTH SHORE
26– NORTH SHORE

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – FEB. 25, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

CONTAMINATED SOILS REMEDIATION PROGRESS PLAN (DECEMBER 31, 2004)

Gartner Lee

Figure No. 2

Appendices

Polaris Mine Operations Contaminated Soil Remediation Close Out Reports:

- **Appendix A** **Process Barge**
- **Appendix B** **Ship Loading Dock**
- **Appendix C** **Accommodation Complex**
- **Appendix D** **Foldaway Buildings**
- **Appendix E** **Tank Farm and Lube Oil Storage**
- **Appendix F** **Tailings Pipeline**
- **Appendix G** **Loon Lake Snow Dump**
- **Appendix H** **Firehall**
- **Appendix I** **South Shore**
- **Appendix J** **North Shore**

Appendix A

Process Barge

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Process Barge

BACKGROUND

The Process Barge (shown as Area 1 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*) was located between the main portal and the former concentrate storage shed.

The Process Barge (the "Barge") contained the mill and service facilities (the power house, maintenance shops, warehouse, offices and fuel storage in the bottom of the hull). The Barge was constructed in Quebec and towed to the Polaris Mine Site in August 1981. It was 31 m wide, 122 m long and 18 m high above a 4.3 m deep hull. Prior to the arrival of the Barge a berthing lagoon was excavated south of the main portal. In 1982, the Barge was floated into place. A berm was then constructed across the entrance to the lagoon, the sea water was pumped out and the excavation backfilled.

Infrastructure directly associated with the Barge included a utility corridor that connected it with the Accommodation Complex 200 m to the east. The utilidor was a wooden above ground structure that housed freshwater, sewage, electrical and fuel lines. A CAT generator building and trailers were located 25 m west of the Barge. The Steam Bay and a diesel dispensing tank were located at the northwest corner of the Barge. The diesel tank was 15 m north of the CAT generator building. A sewage holding tank was located at the northeast corner of the Barge and a waste oil collection tank was outside the maintenance bay on the north side of the Barge. The concentrate conveyor way was at the south. On the east side was a second conveyor way that fed ore to the mill from the underground workings through the CV03 portal. The tailings line and reclaim water line were also located on the east side of the Barge.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified petroleum hydrocarbon and Lead and Zinc contamination in the soil surrounding the Barge. Four (4) surface samples were collected, nineteen (19) test pits excavated and four (4) boreholes drilled

during the ESA in the Barge remediation area. The sample results indicated that hydrocarbon contamination was present to a depth of 3.1 m and that lead and zinc contamination was present on surface to a depth of 0.61 m. The soil sample results from the ESA and the original topography of the area prior to site remediation are shown on Figure Barge-01-1: *Barge Conditions Before Remediation*.

METHODOLOGY

Delineation

The preliminary area to be remediated, as identified in the ESA as an "Area of Concern", was further delineated for excavation through the collection and analysis of field screening samples from nineteen (19) boreholes drilled in 2003 and eight (8) boreholes drilled in 2004. The boreholes were advanced with an air rotary quarry drill. The borehole depths ranged from 3 m to 6.7 m. A total of one hundred ninety (190) composite samples were collected from the drill returns that accumulated at the mouth of the boreholes. The composite samples were collected over 0.6 m to 0.8 m intervals. Following the collection of each sample the surface surrounding the borehole was cleared of the drill cuttings, before advancing the hole the next 0.6 m to 0.8 m sample interval.

The visual appearance and odour of the soil, along with field screening measurements obtained from the borehole samples were used to delineate the area to be excavated. The hydrocarbon field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. The samples were field screened for metals using the Niton X-ray fluorescence (XRF) elemental analyser.

The results from the drilling indicated hydrocarbon contamination to a depth of 4.5 m and metal contamination to a depth of 5.5 m.

Excavation

Excavation of the Barge area commenced August 26, 2003, after the structure was dismantled and the hull of the Barge removed. Excavation in 2003 continued until November 3, 2003. The excavation of the Barge area re-commenced again April 21, 2004 and it was completed July 16, 2004.

During 2003, the contaminated soil under the footprint of the former Barge hull was excavated. Beneath the eastern half of the footprint of the former barge the excavation extended to solid bedrock. Soil within the excavation area was ripped and loaded into trucks with an excavator. A smooth lipped bucket on the excavator was used to clean the residual contaminated soils at the base of the excavation. To direct the excavation activities, samples were collected across the

floor and walls of the excavation and field screened using the PID for hydrocarbons and the XRF analyzer for Lead and Zinc. Upon receipt of field screening results that indicated the Soil Quality Remediation Objectives (SQRO's) were met confirmation samples were collected, the excavation the limits were surveyed and the remediated area was backfilled.

That portion of the Barge excavated in 2003 was backfilled prior to the end of the 2003 work with between 4 m and 7 m of fill. The areas were backfilled in order to prevent spring runoff water in 2004 from flowing across the remaining contaminated soils and then into this area and re-contaminating it. At the north end of the area excavated in 2003 hydrocarbon contamination remained present in the walls. As an additional mitigation measure to inhibit hydrocarbon contaminated spring runoff from re-contaminating the remediated area the walls and adjacent floor of the excavation from the utility corridor north, along the northern face and then south to below the CAT generator building were sprayed with water when the air temperature was below –20°C and a barrier of ice established prior to backfilling.

A 50 m by 50 m area at the south end of the Barge was excavated in October 2003 and it was backfilled prior to the receipt of the analytical laboratory results due to the onset of winter conditions. The analytical laboratory results from the floor of the south end of the 2003 excavation did not meet the SQRO's and the backfilled material was re-excavated and the floor of the excavation dug deeper and additional remediation confirmation samples were collected.

In the spring of 2004 the contaminated soil remaining to the west of the former Barge footprint was excavated while the surface was frozen. The excavation program was guided by observations made on the walls of the excavation in 2003 along with field screening results from the boreholes drilled in 2003 and 2004. Following the removal of contaminated material the floor and walls of the excavation were sampled to determine where additional excavation was required to meet the SQRO's. The excavator with a ripper attachment was used to expand the excavation further where required. The excavated area was then backfilled with between 3 m and 7 m of fill in order to establish the final shoreline configuration.

The limits of the excavation are shown on Figure Barge-01-2: *Barge Conditions After Remediation*. The material excavated was disposed in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Upon receipt of field screening results that indicated that the material remaining in the excavation would meet the SQRO's, confirmation samples were collected in accordance with Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols The excavated area was subdivided into individual composite sampling areas approximately 25 m by 25 m required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation. Composite samples were created by collecting four or five

evenly spaced aliquots of soil with in the individual composite sample area. A single aliquot of soil from a specific point is a discrete sample and these samples were collected randomly.

The soil samples were collected at the excavation limits and submitted to ALS Environmental (ALS) for analysis of Extractable Petroleum Hydrocarbons (EPH), metals and Polycyclic Aromatic Hydrocarbons (PAH). Additional excavation was undertaken in areas where the laboratory analytical results did not meet the SQRO's and additional confirmatory samples were taken upon completion of the excavation.

ANALYTICAL RESULTS

Analytical laboratory results for EPH, metals and PAH are summarized in Tables: BA-01-1, BA-01-2, and BA-01-3 along with the approved Polaris Mine SQRO's for petroleum hydrocarbons and metals. Eighty two (82) hydrocarbon and eighty two (82) metal remediation confirmation samples were submitted from the former Barge area. The hydrocarbon samples were analyzed as follows: fifty (50) floor composite samples, ten (10) wall composite samples, seventeen (17) discrete samples and five (5) quality assurance quality control (QA/QC) samples. All hydrocarbon confirmatory samples were analyzed for EPH, and fourteen (14) of these samples were also analyzed for PAH. The metal samples were analyzed for Lead and Zinc as follows: fifty one (51) floor composite samples, fifteen (15) wall composite samples, ten (10) discrete samples and six (6) quality assurance quality control (QA/QC) samples. Thirteen (13) randomly selected samples were analyzed for total metals. The soils quality results and the lateral limits of the excavation are shown on Figure Barge-01-2.

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with the collection and analysis of soil included: the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical laboratory replicates. Relative percent differences (RpDs) for hydrocarbon concentrations of EPH C_{10}-C_{19} and EPH C_{19}-C_{32} have been calculated and compiled in Table: BA-01-4 for six (6) analytical laboratory duplicates and nine (9) analytical laboratory replicates. RpDs for concentrations of Lead and Zinc have been calculated and compiled in Table: BA-01-5 for six (6) field screening duplicates, six (6) laboratory duplicates and five (5) laboratory replicates. In total thirty two (32) QA/QC sample sets have been evaluated, including eleven (11) remediation confirmation sample sets.

Thirty (30) of the sample results and their duplicate/replicate results either returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not applicable) or they returned acceptable RpDs below the site specific objective of 50%. Two analytical laboratory duplicates returned results greater than the objective and therefore require further explanation.

The variance between the EPH C_{10}-C_{19} results for sample Barge-362-F-C (3290 mg/kg) and its blind duplicate, Barge-364-F-Q (1930 mg/kg) is considered representative of the heterogeneity of an area prior to achieving the remediation objectives (further excavation was undertaken in this area in order to meet the remediation objective of 1000 mg.kg EPH C_{10}-C_{19}). The variance between Zinc concentrations in sample Barge-11919-F-D (217 mg/kg) and its blind duplicate, Barge-11986-F-Q (472 mg/kg) is considered indicative the heterogeneity present in samples with relatively low concentrations of Zinc at the Polaris Mine Site.

Polaris Mine Soil Quality Remediation Objectives

Seventy five (75) of the eighty two (82) hydrocarbon remediation confirmation samples (91%) returned results below the Polaris Mines SQRO's for EPH. Five floor composite samples, one discrete sample and one QA/QC sample returned EPH C_{10}-C_{19} concentrations greater than the SQRO. Four of the samples were collected from the south end of the former process barge footprint in 2003 (Barge-301-F-C, Barge-360-F-C, and Barge-369-F-C and it's duplicate Barge-370-F-Q) and most of this area was re-excavated in 2004. Samples Barge-11933-F-C and Barge-11935-F-C (which met the SQRO's for EPH C_{10}-C_{19}) were collected from the base of the area re-excavated in 2004, as shown on Figure: Barge-02-1. In addition, QA/QC sample Barge-363-F-Q is a duplicate of sample Barge-360-F-C and the EPH concentrations in this sample met the SQROs.

Seventy nine (79) of the eighty two (82) metals remediation confirmation samples (96%) returned results that met the Polaris Mine SQRO's for Lead and Zinc. Two of the three samples that returned results greater than the SQROs, including Lead concentrations greater than two times the SQRO, were collected from the south end of the former process barge footprint in 2003 (Barge-360-F-C and Barge-361-F-C). Most of the area covered by these two samples was re-excavated in 2004. Sample Barge-11935-F-C, which met the SQRO's for Lead (2000 mg/kg) and Zinc (10000 mg/kg) was collected from the base of the area re-excavated in 2004. The duplicate QA/QC sample Barge-363-F-Q of Barge-360-F-C returned Lead and Zinc concentrations that sample met the SQROs. Lead concentrations in sample Barge-10492-F-C (2500 mg/kg), collected beneath the former diesel dispensing tank exceeded the SQRO.

The approved site-specific remedial objectives allow for minor exceedances in a small percentage of the confirmatory sample area, as long as the concentration is less than twice the remedial target. Since only a small percentage of the remedial area exceeds the SQROs for EPH, Lead and Zinc and given that the area with Lead concentrations greater than two times the remedial target was mostly re-excavated and that a duplicate sample from the area met the objectives the former Barge area is therefore considered to be in accordance with the site specific remedial objectives.

Discrete samples were collected to discern the homogeneity of the sample area represented by the composite samples. The tables below show a variability in the metal and hydrocarbon concentrations of the discrete samples versus the composite areas they represented as the composite samples represent the area as a whole and the discrete samples indicate the homogeneity of the given sample areas.

Summary of Discrete Hydrocarbon Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	EPH_{10-19} (mg/kg)	EPH_{19-32} (mg/kg)	Discrete Sample ID	EPH_{10-19} (mg/kg)	EPH_{19-32} (mg/kg)
Barge-175-F-C	<200	<200	Barge-169-F-D	<200	<200
Barge-260-F-C	<200	<200	Barge-182-F-D	724	<200
Barge-220-F-C	208	<200	Barge-194-F-D	<200	<200
Barge-220-F-C	208	<200	Barge-195-F-D	686	<200
Barge-221-F-C	230	<200	Barge-199-F-D	554	<200
Barge-224-F-C	**1340**	<200	Barge-207-F-D	259	<200
Barge-224-F-C	**1340**	<200	Barge-209-F-D	**2380**	<200
Barge-222-F-C	436	<200	Barge-211-F-D	206	<200
Barge-11931-F-C	280	480	Barge-251-F-D	<200	<200
Barge-11931-F-C	280	480	Barge-252-W-D	<200	<200
Barge-261-F-C	<200	<200	Barge258-F-D	<200	<200
Barge-360-F-C	**1160**	230	Barge-345-F-D	330	<200
Barge-10683-F-C	860	270	Barge-347-F-D	450	<200
Barge-11935-F-C	<200	240	Barge-355-F-D	780	230
Barge-11933-F-C	<200	380	Barge-357-F-D	320	<200
Barge-10580-F-C	<200	<200	Barge-10525-F-D	<200	<200
Barge-10648-W-C	<200	268	Shore-11985-F-D	<200	<200

Summary of Discrete Metals Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	Lead (mg/kg)	Zinc (mg/kg)	Discrete Sample ID	Lead (mg/kg)	Zinc (mg/kg)
Barge-175-F-C	<100	9	Barge-169-F-D	<100	5
Barge-11931-F-C	<100	55	Barge-174-W-D	<200	5
Barge-224-F-C	<200	2040	Barge-207-F-D	<200	996
Barge-222-F-C	<200	1280	Barge-211-F-D	<200	766
Barge-360-F-C	**5350**	**10200**	Barge-345-F-D	1440	7050
Barge-10684-F-C	970	6930	Barge-347-F-D	720	4660
Barge-10580-F-C	1000	2210	Barge-10525-F-D	370	1480
Barge-11935-F-C	180	653	Barge-11913-F-D	1570	2330
Barge-11933-F-C	120	427	Barge-11919-F-D	<100	217
Barge-11957-F-C	170	469	Shore-12071-W-D	295	473

Generic Federal Soil Quality Guidelines for Parkland Land Use

The concentrations of Barium ranged from 280 mg/kg to 896 mg/kg in the ten remediation confirmation samples analysed for total metals. The generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for Parkland land use for Barium in soil is 500 mg/kg. Three of the samples exceeded this generic objective (Barge 10822-F-C, Barge-11919-F-D and Barge-11935-F-C). The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone. Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results*, are considered to be representative of background conditions. Samples were collected at the following intervals: surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of Barium greater than generic CCME CEQG for Parkland land use were detected in each interval. The variability of Barium concentrations in those samples in listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The immobile nature of the Barium encountered on site was demonstrated in the ESA leachate test results that returned Barium concentrations at levels less than the detection limit of <3 mg/L and Barium was therefore not identified as a contaminant of concern in the ESA.

The concentrations of Cadmium ranged from <1 mg/kg to 18.1 mg/kg in the remediation confirmation samples from the Barge area analysed for total metals. Cadmium results for three of the samples (Barge-263-F-C, Barge-10770-W-C and Barge-10823-F-C) exceeded the CCME CEQG for Parkland land use of 10 mg/kg Cadmium in soil. Cadmium was not identified as a contaminant of concern based on the total metal analyses and leachate test results conducted during the ESA. Given the immobile nature of the Cadmium encountered on site, as demonstrated by the leachate results and the level of concentrations being less than twice the generic CCME CEQG for Parkland land use, no further remedial excavation work is considered necessary.

Two floor composite samples, exceeded the CCME CEQG for Parkland land use of 0.6 mg/kg Naphthalene in soil. The Naphthalene concentration in samples Barge-223-F-C and Barge-301-F-C were 0.84 mg/kg and 1.03 mg/kg respectively. The EPH results for Barge-301-F-C also failed to meet the SQROs and the area was re-excavated in 2004. Results for sample Barge-11935-F-C (which met the SQRO's for EPH C_{10}-C_{19}) were collected from the base of the area re-excavated in 2004, as shown on Figure: Barge-02-1. The area represented by sample Barge-223-F-C has been since covered by between 6 m and 7 m of fill and it is more than 75 m to the existing final shoreline, it is therefore isolated from the marine and terrestrial environment.

CONCLUSION

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former Barge area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

Dr. Dennis Gregor, P.Geol.
Senior Reviewer, Senior Aquatic Scientist

AL:DL:

ATTACHMENTS

Tables

Table BA-02-1:	Barge Area Remediation Confirmation Soil Samples – Hydrocarbons
Table BA-02-2:	Barge Area Remediation Confirmation Soil Samples – Metals
Table BA-02-3:	Barge Area Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table BA-02-4:	Barge Area Quality Assurance and Quality Control Remediation Soil Samples - Metals
Table BA-02-5:	Barge Area Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons

Figures

Figure Barge-01-1:	Barge Conditions Before Remediation
Figure Barge-01-2:	Barge Conditions After Remediation

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge						
		Sample ID	Barge-169-F-D	Barge-175-F-C	Barge-176-F-C	Barge-182-F-D	Barge-194-F-D	Barge-195-F-D	Barge-199-F-D
		Date Sampled	09-Oct-03	09-Oct-03	09-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03
		ALS File Number	T5345	T5345	T5345	T5351	T5351	T5351	T5351
		Field Screen (ppm)[b]	75	-	-	185	100	175	105
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	240	724	<200	686	554
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	<200	<200	-	-	-	-	-
HEPH[c]	1000	mg/kg	<200	<200	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge							
		Sample ID	Barge-207-F-D	Barge-209-F-D	Barge-211-F-D	Barge-218-F-C	Barge-219-F-C	Barge-220-F-C	Barge-221-F-C	Barge-222-F-C
		Date Sampled	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03
		ALS File Number	T5351	T5351	T5351	T5351	T5351	T5351	T5351	T5351
		Field Screen (ppm)[b]	120	1600	85	-	-	-	85	85
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	259	**2380**	206	210	<200	208	230	436
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	210	<200	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	<200	<200	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge							
		Sample ID	Barge-223-F-C	Barge-225-F-Q	Barge-224-F-C	Barge-251-F-D	Barge-252-W-D	Barge-258-F-D	Barge-260-F-C	Barge-261-F-C
		Date Sampled	11-Oct-03	11-Oct-03	11-Oct-03	18-Oct-03	18-Oct-03	18-Oct-03	18-Oct-03	18-Oct-03
		ALS File Number	T5351	duplicate of	T5351	T5735	T5735	T5735	T5735	T5735
		Field Screen (ppm)[b]	155	Barge-223-F-C	145	80	60	85	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	463	406	**1340**	<200	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	462	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	<200	-	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge							
		Sample ID	Barge-263-W-C	Barge-265-F-C	Barge-300-F-C	Barge-301-F-C	Barge-302-F-C	Barge-305-F-C	Barge-312-W-C	Barge-345-F-D
		Date Sampled	19-Oct-06	19-Oct-03	21-Oct-03	21-Oct-03	21-Oct-03	21-Oct-03	24-Oct-03	28-Oct-03
		ALS File Number	T5735	T5735	T5735	T5735	T5735	T5735	T5790	T6195
		Field Screen (ppm)[b]	-	-	30	125	30	25	60	195
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	590	<200	<200	**1030**	<200	<200	<200	330
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	210	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	**1030**	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	210	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge						
		Sample ID	Barge-347-F-D	Barge-363-F-Q	Barge-355-F-D	Barge-357-F-D	Barge-360-F-C	Barge-361-F-C	Barge-369-F-C
		Date Sampled	28-Oct-03	28-Oct-03	28-Oct-03	28-Oct-03	28-Oct-03	28-Oct-03	31-Oct-03
		ALS File Number	T6195	duplicate of	T6195	T6195	T6195	T6195	T6190
		Field Screen (ppm)[b]	180	Barge-347-F-D	95	325	-	30	175
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	450	840	780	320	**1160**	970	**1030**
EPH C_{19}-C_{32}	1000	mg/kg	<200	210	230	<200	230	210	250
LEPH[c]	1000	mg/kg	-	-	-	320	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	<200	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge						
		Sample ID	Barge-370-F-Q	Barge-10492-F-C	Barge-10493-F-C	Barge-10525-F-D	Barge-10580-F-C	Barge-10581-F-C	Barge-10599-F-C
		Date Sampled	31-Oct-03	06-May-04	06-May-04	10-May-04	10-May-04	10-May-04	10-May-04
		ALS File Number	duplicate of	U3342	U3342	U3476r	U3476r	U3476r	U3476r
		Field Screen (ppm)[b]	Barge-369-F-C	-	55	45	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	**1200**	660	<200	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	260	210	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	<200
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	<200

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge					
		Sample ID	Barge-10648-W-C	Barge-10649-F-C	Barge-10650-F-C	Barge-10659-F-C	Barge-10683-F-C	Barge-10729-F-C
		Date Sampled	13-May-04	13-May-04	13-May-04	18-May-04	18-May-04	21-May-04
		ALS File Number	U3564rr	U3564rr	U3564rr	U3761	U3761	U3898r
		Field Screen (ppm)[b]	30	-	-	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	200	<200	860	<200
EPH C_{19}-C_{32}	1000	mg/kg	260	320	380	<200	270	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge					
		Sample ID	Barge-10730-W-C	Barge-10734-W-Q	Barge-10731-F-C	Barge-10733-F-C	Barge-10746-F-C	Barge-10770-W-C
		Date Sampled	21-May-04	21-May-04	21-May-04	20-May-04	20-May-04	24-May-04
		ALS File Number	U3898r	duplicate of	U3898r	U3898r	U3898r	U3969r
		Field Screen (ppm)[b]	10	Barge-10730-W-C	-	-	-	30
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	210	<200	<200	<200	**1520**	270
EPH C_{19}-C_{32}	1000	mg/kg	470	370	220	<200	480	260
LEPH[c]	1000	mg/kg	-	-	-	-	-	270
HEPH[c]	1000	mg/kg	-	-	-	-	-	260

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge						
		Sample ID	Barge-10822-F-C	Barge-10823-F-C	Barge-10824-F-C	Barge-10825-F-C	Barge-11177-F-C	Barge-11207-W-C	Barge-11310-F-C
		Date Sampled	24-May-04	24-May-04	24-May-04	24-May-04	05-Jun-04	02-Jun-04	31-May-04
		ALS File Number	U3969r	U3969r	U3969r	U3969r	U4269r	U4269r	U4137
		Field Screen (ppm)[b]	-	-	-	-	55	45	-
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	450	<200	200	<200	900	210
EPH C_{19}-C_{32}	1000	mg/kg	210	<200	<200	<200	<200	350	270
LEPH[c]	1000	mg/kg	<200	450	-	-	-	-	-
HEPH[c]	1000	mg/kg	210	<200	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Bold

Notes:

"<" = Less than analyt

"-" = Analysis not con

a) The approved Soil Q

Contaminated Sites

b) Field screening resu

to a hexane standar

c) Light Extractable Pe

are determined by su

(EPH), therefore use

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge					
		Sample ID	Barge-11311-F-C	Barge-11325-W-C	Barge-11547-W-C	Barge-11548-W-C	Barge-11549-W-C	Barge-11550-F-C
		Date Sampled	31-May-04	08-Jun-04	17-Jun-04	17-Jun-04	17-Jun-04	17-Jun-04
		ALS File Number	U4137	U4378	U4781	U4781	U4781	U4781
		Field Screen (ppm)[b]	-	-	30	30	40	30
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	230	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge				
		Sample ID	Barge-11927-F-C	Barge-11928-F-C	Barge-11929-F-C	Barge-11930-F-C	Barge-11931-F-C
		Date Sampled	07-Jul-04	07-Jul-04	07-Jul-04	07-Jul-04	07-Jul-04
		ALS File Number	U5597r	U5597r	U5597r	U5597r	U5597r
		Field Screen (ppm)[b]	-	-	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**				
Extractable Hydrocarbons							
EPH C_{10}-C_{19}	1000	mg/kg	340	<200	230	250	280
EPH C_{19}-C_{32}	1000	mg/kg	520	380	380	440	480
LEPH[c]	1000	mg/kg	-	-	-	-	280
HEPH[c]	1000	mg/kg	-	-	-	-	480

Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site

tical method detection limit.
nducted, or no guideline.

Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Regulation for Parkland (PL) Land Use.
ults are measured based on a 'dry headspace' method using a combustible gas meter calibrated rd.
etroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) ubtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons of the EPH remediation objective is conservative.

Table BA-01-1. Barge Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge					
		Sample ID	Barge-11933-F-C	Barge-11934-F-Q	Barge-11935-F-C	Shore-11985-F-D	Barge-12179-F-C	Barge-12180-F-C
		Date Sampled	05-Jul-04	05-Jul-04	05-Jul-04	12-Jul-04	27-Aug-04	27-Aug-04
		ALS File Number	U5597r	duplicate of	U5597r	U5836	U7584(1)	U7584(1)
		Field Screen (ppm)[b]	-	Barge-11933-F-C	-	-	10	10
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	380	390	240	<200	230	220
LEPH[c]	1000	mg/kg	-	-	<200	<200	-	-
HEPH[c]	1000	mg/kg	-	-	240	<200	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge							
				Sample ID	Barge-169-F-D	Barge-174-W-D	Barge-175-F-C	Barge-176-F-C	Barge-207-F-D	Barge-211-F-D	Barge-219-F-C	Barge-222-F-C
				Date Sampled	09-Oct-03	11-Oct-03	09-Oct-03	09-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03
				ALS File Number	T5345	T5351	T5345	T5345	T5351	T5351	T5351	T5351
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	29	12	-	-	79	113	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	111	87	-	-	838	703	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	-	9.2	-	-	-	-	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	<30	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	<20	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	10	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<2	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	<2	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	<6	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	<6	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	<3	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<100	<200	<100	<100	<200	<200	<200	<200
Mercury	T-Hg	-	7	mg/kg	-	<0.05	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<20	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	<20	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	<4	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	<6	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	<20	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	<6	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	5	5	9	10	996	766	2630	1280

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge							
				Sample ID	Barge-223-F-C	Barge-225-F-Q	Barge-224-F-C	Barge-260-F-C	Barge-261-F-C	Barge-263-W-C	Barge-265-F-C	Barge-300-F-C
				Date Sampled	11-Oct-03	11-Oct-03	11-Oct-03	18-Oct-03	18-Oct-03	19-Oct-03	19-Oct-03	21-Oct-03
				ALS File Number	T5351	T5351	T5351	T5735	T5735	T5735	T5735	T5735
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	duplicate of	-	-	-	-	-	150
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	-	-	-	-	-	-	646
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	8.59	-	-	-	-	8.4	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	<30	-	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	<20	-	-	-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	467	-	-	-	-	277	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<2	-	-	-	-	<1.0	-	-
Cadmium	T-Cd	-	10	mg/kg	<2	-	-	-	-	**18.1**	-	-
Chromium	T-Cr	-	64	mg/kg	<6	-	-	-	-	6.7	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<6	-	-	-	-	<4.0	-	-
Copper	T-Cu	-	63	mg/kg	<3	-	-	-	-	8.9	-	-
Lead	T-Pb	2000	-	mg/kg	237	456	<200	<100	<100	1790	1030	120
Mercury	T-Hg	-	7	mg/kg	0.11	-	-	-	-	<0.050	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<20	-	-	-	-	<8.0	-	-
Nickel	T-Ni	-	50	mg/kg	<20	-	-	-	-	<10	-	-
Selenium	T-Se	-	1	mg/kg	<4	-	-	-	-	<2.0	-	-
Silver	T-Ag	-	20[d]	mg/kg	<6	-	-	-	-	<4.0	-	-
Tin	T-Sn	-	50[d]	mg/kg	<20	-	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	8	-	-	-	-	11.4	-	-
Zinc	T-Zn	10000	-	mg/kg	506	420	2040	178	11.6	6670	8910	475

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge						
				Sample ID	Barge-301-F-C	Barge-302-F-C	Barge-305-F-C	Barge-307-W-C	Barge-312-W-C	Barge-345-F-D	Barge-347-F-D
				Date Sampled	21-Oct-03	21-Oct-03	21-Oct-03	24-Oct-03	24-Oct-03	28-Oct-03	28-Oct-03
				ALS File Number	T5735	T5735	T5735	T5790	T5790	T6195	T6195
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	1594	45	376	793	1752	706	534
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	5945	351	2784	2536	6386	3851	2627
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	8.89
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	<20
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	<10
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	311
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	<1.0
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	9.9
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	<4.0
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	<4.0
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	2.8
Lead	T-Pb	2000	-	mg/kg	830	<100	420	1280	1240	1440	720
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	<0.050
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	<8.0
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	<10
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	<2.0
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	<4.0
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	<10
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	6.4
Zinc	T-Zn	10000	-	mg/kg	3000	294	2150	2240	2720	7050	4660

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge						
				Sample ID	Barge-360-F-C	Barge-363-F-Q	Barge-361-F-C	Barge-369-F-C	Barge-370-F-Q	Barge-10492-F-C	Barge-10493-F-C
				Date Sampled	28-Oct-03	28-Oct-03	28-Oct-03	31-Oct-03	31-Oct-03	06-May-04	06-May-04
				ALS File Number	T6195	T6195	T6195	T6190	T6190	U3342	U3342
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	duplicate of	-	-	duplicate of	1109	246
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	Barge-360-F-C	-	-	Barge-369-F-C	22790	349
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	**5350**	440	**5570**	520	800	**2500**	870
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	**10200**	2990	3830	2470	2890	4360	2450

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge						
				Sample ID	Barge-10525-F-D	Barge-10580-F-C	Barge-10581-F-C	Barge-10649-F-C	Barge-10650-F-C	Barge-10684-F-C	Barge-10729-F-C
				Date Sampled	10-May-04	10-May-04	10-May-04	13-May-04	13-May-04	18-May-04	21-May-04
				ALS File Number	U3476r	U3476r	U3476r	U3564rr	U3564rr	U3761	U3898r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	195	-	-	-	-	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	887	-	-	-	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	370	1000	870	260	260	970	160
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	1480	2210	1720	637	2490	6930	500

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge						
				Sample ID	Barge-10732-F-C	Barge-10733-F-C	Barge-10746-F-C	Barge-10770-W-C	Barge-10822-F-C	Barge-10823-F-C	Barge-10824-F-C
				Date Sampled	21-May-04	21-May-04	20-May-04	24-May-04	24-May-04	24-May-04	24-May-04
				ALS File Number	U3898r	U3898r	U3898r	U3969r	U3969r	U3969r	U3969r
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	-	-	-	463	-	-	-
				Field Screen Zn (ppm)[b]	-	-	-	1528	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	8.44	8.68	8.67	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	<20	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	<10	<10	-
Barium	T-Ba	-	500	mg/kg	-	-	-	403	**762**	368	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1.0	<1.0	<1.0	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	**15.9**	<1.0	**12.6**	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	5.5	8.8	9.8	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4.0	<4.0	<4.0	-
Copper	T-Cu	-	63	mg/kg	-	-	-	6.5	12.1	6.9	-
Lead	T-Pb	2000	-	mg/kg	<200	<200	<100	1600	<100	1100	1980
Mercury	T-Hg	-	7	mg/kg	-	-	-	<0.050	0.056	<0.050	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8.0	<8.0	<8.0	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	<10	18	13	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<4.0	<4.0	<4.0	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4.0	<4.0	<4.0	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	<10	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	31.8	48.8	31	-
Zinc	T-Zn	10000	-	mg/kg	173	220	200	6570	233	5870	9790

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Parameter		Polaris Mine Soil Quality Remediation Objectives[a] Site Specific	Polaris Mine Soil Quality Remediation Objectives[a] CEQG (PL)[c]	Units	Location: Barge						
Sample ID					Barge-10825-F-C	Barge-11177-F-C	Barge-11207-W-C	Barge-11310-F-C	Barge-11311-F-C	Barge-11547-W-C	Barge-11548-W-C
Date Sampled					24-May-04	05-Jun-04	02-Jun-04	31-May-04	31-May-04	17-Jun-04	17-Jun-04
ALS File Number					U3969r	U4269r	U4269r	U4137	U4137	U4781	U4781
Field Screen Pb (ppm)[b]					-	357	1389	-	-	145	100
Field Screen Zn (ppm)[b]					-	4952	5110	-	-	577	351
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	640	740	1860	550	1660	110	150
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	3860	6510	17.3	8500	6590	314	374

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge						
				Sample ID	Barge-11549-W-C	Barge-11550-F-C	Barge-11653-W-C	Barge-11654-W-C	Barge-11655-F-C	Barge-11656-F-C	Barge-11819-F-C
				Date Sampled	17-Jun-04	17-Jun-04	24-Jun-04	24-Jun-04	24-Jun-04	24-Jun-04	30-Jun-04
				ALS File Number	U4781	U4781	U5050	U5050	U5050	U5050	U5353r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	109	202	384	330	381	331	420
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	464	614	1521	1494	1194	1086	1884
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	120	190	420	330	380	370	275
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	329	501	1040	734	862	762	808

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Parameter		Polaris Mine Soil Quality Remediation Objectives[a] Site Specific	Polaris Mine Soil Quality Remediation Objectives[a] CEQG (PL)[c]	Units	Location: Barge	Barge	Barge	Barge	Barge	Barge	Barge
Sample ID					Barge-11820-F-C	Barge-11846-W-C	Barge-11874-F-C	Barge-11878-W-C	Barge-11913-F-D	Barge-11919-F-D	Barge-11986-F-Q
Date Sampled					30-Jun-04	02-Jul-04	02-Jul-04	04-Jul-04	07-Jul-04	07-Jul-04	07-Jul-04
ALS File Number					U5353r	U5597r	U5597r	U5597r	U5836	U5836	U5836
Field Screen Pb (ppm)[b]					388	366	98	122	126	309	duplicate of
Field Screen Zn (ppm)[b]					1534	1060	268	218	378	1114	Barge-11919-F-C
Analytical Results											
pH		-	-	-	-	-	-	-	8.32	8.25	8.37
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	<20	<20	<20
Arsenic	T-As	-	12	mg/kg	-	-	-	-	<10	11	<10
Barium	T-Ba	-	500	mg/kg	-	-	-	-	471	**896**	374
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	<1.0	<1.0	<1.0
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	5	<1.0	1.8
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	5.4	13.3	5.2
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	<4.0	6.7	<4.0
Copper	T-Cu	-	63	mg/kg	-	-	-	-	12.2	29	11.1
Lead	T-Pb	2000	-	mg/kg	263	390	<100	<100	1570	<100	120
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	<0.050	0.114	<0.050
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	<8.0	<8.0	<8.0
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	<10	40	<10
Selenium	T-Se	-	1	mg/kg	-	-	-	-	<4.0	<4.0	<4.0
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	<4.0	<4.0	<4.0
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	<10	<10	<10
Vanadium	T-V	-	130	mg/kg	-	-	-	-	31.8	87.2	31.6
Zinc	T-Zn	10000	-	mg/kg	876	1170	103	117	2330	217	472

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	Barge						
				Sample ID	Barge-11927-F-C	Barge-11928-F-C	Barge-11929-F-C	Barge-11930-F-C	Barge-11931-F-C	Barge-11933-F-C	Barge-11934-F-Q
				Date Sampled	07-Jul-04	07-Jul-04	07-Jul-04	07-Jul-04	07-Jul-04	05-Jul-04	05-Jul-04
				ALS File Number	U5597r	U5597r	U5597r	U5597r	U5597r	U5597r	U5597r
				Field Screen Pb (ppm)[b]	86	68	91	128	73	-	duplicate of
				Field Screen Zn (ppm)[b]	139	98	99	249	173	-	Barge-11933-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	8.58	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	490	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	<1.0	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	<1.0	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	10.8	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	8.6	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	31.1	-	-
Lead	T-Pb	2000	-	mg/kg	<100	<100	<100	<100	<100	120	120
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	0.171	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	<8.0	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	43	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	<6.0	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	<4.0	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	83	-	-
Zinc	T-Zn	10000	-	mg/kg	43.3	36.1	32	55.8	55.4	427	587

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Parameter		Polaris Mine Soil Quality Remediation Objectives[a] Site Specific	Polaris Mine Soil Quality Remediation Objectives[a] CEQG (PL)[c]	Units	Location: Barge						
Sample ID					Barge-11935-F-C	Barge-11957-F-C	Barge-11972-W-C	Barge-11973-F-C	Barge-11974-W-C	Barge-11975-W-C	Barge-11976-F-C
Date Sampled					05-Jul-04	09-Jul-04	09-Jul-04	09-Jul-04	09-Jul-04	09-Jul-04	09-Jul-04
ALS File Number					U5597r	U5615r	U5615r	U5615r	U5615r	U5615r	U5615r
Field Screen Pb (ppm)[b]					-	206	187	219	242	367	319
Field Screen Zn (ppm)[b]					-	454	582	630	2674	2737	2336
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	8.26	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	<10	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	**677**	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<1.0	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	1.8	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	8.5	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<4.0	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	14.8	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	180	170	130	210	370	710	310
Mercury	T-Hg	-	7	mg/kg	0.066	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8.0	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	21	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	<4.0	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	<4.0	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	56.2	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	653	469	376	636	3390	4030	4900

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-2. Barge Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Barge		
				Sample ID	Barge-11977-F-C	Barge-11978-F-Q	Shore-12071-W-D
				Date Sampled	09-Jul-04	09-Jul-04	26-Jul-04
				ALS File Number	U5615r	U5615r	U6530rr
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	277	duplicate of	540
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	2663	Barge-11977-F-C	1074
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**		
pH		-	-	-	8.65	-	-
Metals							
Antimony	T-Sb	-	20[d]	mg/kg	<40	-	-
Arsenic	T-As	-	12	mg/kg	<200	-	-
Barium	T-Ba	-	500	mg/kg	280	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	7	-	-
Chromium	T-Cr	-	64	mg/kg	<4	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<4	-	-
Copper	T-Cu	-	63	mg/kg	4	-	-
Lead	T-Pb	2000	-	mg/kg	590	380	295
Mercury	T-Hg	-	7	mg/kg	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8	-	-
Nickel	T-Ni	-	50	mg/kg	<10	-	-
Selenium	T-Se	-	1	mg/kg	<100	-	-
Silver	T-Ag	-	20[d]	mg/kg	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	<20	-	-
Vanadium	T-V	-	130	mg/kg	22	-	-
Zinc	T-Zn	10000	-	mg/kg	3650	4310	473

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-3. Barge Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge					
		ALS Sample ID	Barge-175-F-C	Barge-218-F-C	Barge-219-F-C	Barge-223-F-C	Barge-10599-F-C	Barge-10770-W-C
		Date Sampled	09-Oct-03	11-Oct-03	11-Oct-03	11-Oct-03	10-May-04	24-May-04
		ALS File Number	T5345	T5351	T5351	T5351	U3476r	U3969r
		Field Screen (ppm)[b]				155		30
Parameter	**CEQG[c]**	**Units**	**Analytical Results**					
Polycyclic Aromatic Hydrocarbons								
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.04	<0.06	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	<0.05	0.1	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	0.06	0.27	0.15	**0.84**	<0.05	0.105
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-3. Barge Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Barge			
		ALS Sample ID	Barge-10822-F-C	Barge-10823-F-C	Barge-11931-F-C	Barge-11935-F-C
		Date Sampled	24-May-04	24-May-04	07-Jul-04	05-Jul-04
		ALS File Number	U3969r	U3969r	U5597r	U5597r
		Field Screen (ppm)[b]				
Parameter	**CEQG[c]**	**Units**	**Analytical Results**			
Polycyclic Aromatic Hydrocarbons						
Acenaphthene	-	mg/kg	<0.04	<0.05	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.08	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.08	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	<0.05	<0.2	<0.05	<0.05
Phenanthrene	5[d]	mg/kg	<0.05	0.053	0.131	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table BA-01-4. Barge Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Barge							
				Sample ID	Barge-195-F-D	Barge-220-F-C	Barge-223-F-C	Barge-232-W-D	Barge-252-W-D	Barge-343-F-D	Barge-360-F-C	Barge-362-F-C
				Duplicate ID	QC# 359679	QC# 359678	Barge-225-F-Q	QC# 359680	QC# 361098	QC# 362845	Barge-363-F-Q	Barge-364-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
Analytical Laboratory Duplicates												
EPH C_{10}-C_{19}												
Sample Result	mg/kg	200	1000		-	-	463	-	-	-	1160	3290
Duplicate Result	mg/kg	200	1000		-	-	406	-	-	-	840	1930
RpD	**%**						na				na	**52%**
EPH C_{19}-C_{32}												
Sample Result	mg/kg	200	1000		-	-	<200	-	-	-	230	500
Duplicate Result	mg/kg	200	1000		-	-	<200	-	-	-	210	370
RpD	**%**						na				na	na
Analytical Laboratory Replicates												
EPH C_{10}-C_{19}												
Sample Result	mg/kg	200	1000		686	208	-	203	<200	<200	-	-
Duplicate Result	mg/kg	200	1000		889	<200	-	242	<200	<200	-	-
RpD	**%**				na	na		na	na	na		
EPH C_{19}-C_{32}												
Sample Result	mg/kg	200	1000		<200	<200	-	<200	<200	<200	-	-
Duplicate Result	mg/kg	200	1000		<200	<200	-	206	<200	<200	-	-
RpD	**%**				na	na		na	na	na		

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table BA-01-4. Barge Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Barge						
				Sample ID	Barge 369-F-C	Barge-10615-BH-C	Barge-10730-W-C	Barge-10734-W-Q	Barge-10923-F-C	Barge-11549-F-Q	Barge-11933-F-C
				Duplicate ID	Barge 370-F-Q	QC# 386928	Barge-10734-W-Q	QC# 388375	QC# 388645	QC# 391814	Barge-11934-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
Analytical Laboratory Duplicates											
EPH C_{10}-C_{19}											
Sample Result	mg/kg	200	1000		1030	-	210	-	-	-	<200
Duplicate Result	mg/kg	200	1000		1200	-	<200	-	-	-	<200
RpD	**%**				15%		na				na
EPH C_{19}-C_{32}											
Sample Result	mg/kg	200	1000		250	-	470	-	-	-	380
Duplicate Result	mg/kg	200	1000		260	-	370	-	-	-	390
RpD	**%**				na		na				na
Analytical Laboratory Replicates											
EPH C_{10}-C_{19}											
Sample Result	mg/kg	200	1000		-	<200	-	<200	450	<200	-
Duplicate Result	mg/kg	200	1000		-	<200	-	230	400	<200	-
RpD	**%**					na		na	na	na	
EPH C_{19}-C_{32}											
Sample Result	mg/kg	200	1000		-	250	-	370	<200	<200	-
Duplicate Result	mg/kg	200	1000		-	300	-	440	<200	<200	-
RpD	**%**					na		na	na	na	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table BA-01-5. Barge Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee	Location	Barge								
	Sample ID	Barge 116-W-D	Shore-147-F-C	Barge-223-F-C	Shore-294-I-D	Barge 369-F-C	Barge-343-F-D	Shore 417-I-C	Shore-427-F	Barge-10730-W-C
	Duplicate ID	Barge 89-W-Q	Shore-33-F-Q	Barge-225-F-Q	Shore-37-I-Q	Barge 370-F-Q	QC# 362845	Shore 42-I-Q	QC# 356604	Barge-10734-W-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**						
On Site Field Screening Duplicates										
Lead (Pb)										
Sample Result	mg/kg	70	350	2171	494	237	1161	-	-	3108	-	-
Duplicate Result	mg/kg	70	350	2524	270	456	1592	-	-	3862	-	-
RpD	%			15%	na	na	31%			22%		
Zinc (Zn)										
Sample Result	mg/kg	150	750	13572	2183	506	12103	-	-	11718	-	-
Duplicate Result	mg/kg	150	750	14696	1427	420	16113	-	-	14384	-	-
RpD	%			8%	42%	na	28%			20%		
Analytical Laboratory Duplicates										
Lead (Pb)										
Sample Result	mg/kg	100	500	-	-	-	-	520	-	-	-	3010
Duplicate Result	mg/kg	100	500	-	-	-	-	800	-	-	-	2610
RpD	%							42%				14%
Zinc (Zn)										
Sample Result	mg/kg	2	10	-	-	-	-	2470	-	-	-	7170
Duplicate Result	mg/kg	2	10	-	-	-	-	2890	-	-	-	5900
RpD	%							16%				19%
Analytical Laboratory Replicates										
Lead (Pb)										
Sample Result	mg/kg	100	500	-	-	-	-	-	1930	-	1350	-
Duplicate Result	mg/kg	100	500	-	-	-	-	-	1470	-	1700	-
RpD	%								27%		23%	
Zinc (Zn)										
Sample Result	mg/kg	2	10	-	-	-	-	-	14800	-	5910	-
Duplicate Result	mg/kg	2	10	-	-	-	-	-	15700	-	8300	-
RpD	%								6%		34%	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table BA-01-5. Barge Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Barge							
				Sample ID	Barge-10823-F-C	Barge-11549-W-C	Shore-11590-W-C	Barge-11919-F-D	Barge-11933-F-C	Barge-11977-F-C	Barge-11978-F-Q	Barge-12088-F-D
				Duplicate ID	QC# 388645	QC# 391814	Shore-11707-W-Q	Barge-11986-F-Q	Barge-11934-F-Q	Barge-11978-F-Q	QC# 395283	Barge-12336-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350		-	-	-	-	-	-	-	3399
Duplicate Result	mg/kg	70	350		-	-	-	-	-	-	-	2971
RpD	%											13%
Zinc (Zn)												
Sample Result	mg/kg	150	750		-	-	-	-	-	-	-	24290
Duplicate Result	mg/kg	150	750		-	-	-	-	-	-	-	19320
RpD	%											23%
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		-	-	2998	<100	120	590	-	-
Duplicate Result	mg/kg	100	500		-	-	3089	120	120	380	-	-
RpD	%						3%	na	na	na		
Zinc (Zn)												
Sample Result	mg/kg	2	10		-	-	14543	217	427	3650	-	-
Duplicate Result	mg/kg	2	10		-	-	14973	472	587	4310	-	-
RpD	%						3%	**74%**	32%	17%		
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		1100	120	-	-	-	-	380	-
Duplicate Result	mg/kg	100	500		1060	280	-	-	-	-	350	-
RpD	%				4%	na					na	
Zinc (Zn)												
Sample Result	mg/kg	2	10		5870	329	-	-	-	-	4310	-
Duplicate Result	mg/kg	2	10		8980	209	-	-	-	-	5100	-
RpD	%				42%	45%					17%	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

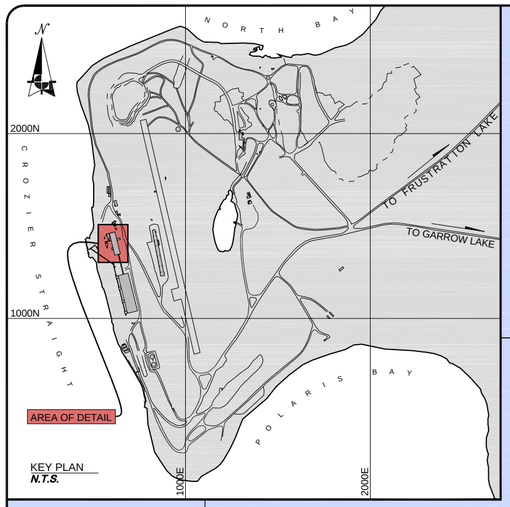

TO FIREHALL

BH-3

BH-2
MAIN
PORTAL

TP-202

SS 4

TP-14

BH-4

TP-8

TP-9

SS 10

TP-7

TP-15

TP-22

BH-1

TP-16

TP-6

BH-5

TP-11

TP-10

TP-17

SS 19

BARGE

TP-5

BH-7

SS 18

SS TL1

TP-4

TP-18

BH-6

TP-12

BH-8

TP-38

TP-3

TP-2

TP-20

SS 21

TP-1

BH-10

TP-19

SS 17

TP-21

SS 12

TP-37

TP-26

TP-36

BH-9

SS 6

TP-25

TP-39

TP-151

TP-35

TP-23

500
600
700
1500
1400
1300
400

N

0 5 10 20 30 Metres

SCALE 1:750

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

SOURCE OF DRAWING:

DRAWING INFORMATION:


REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–BARGE–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

BARGE CONDITIONS BEFORE REMEDIATION

Gartner Lee

FIGURE NO. BA-01-1

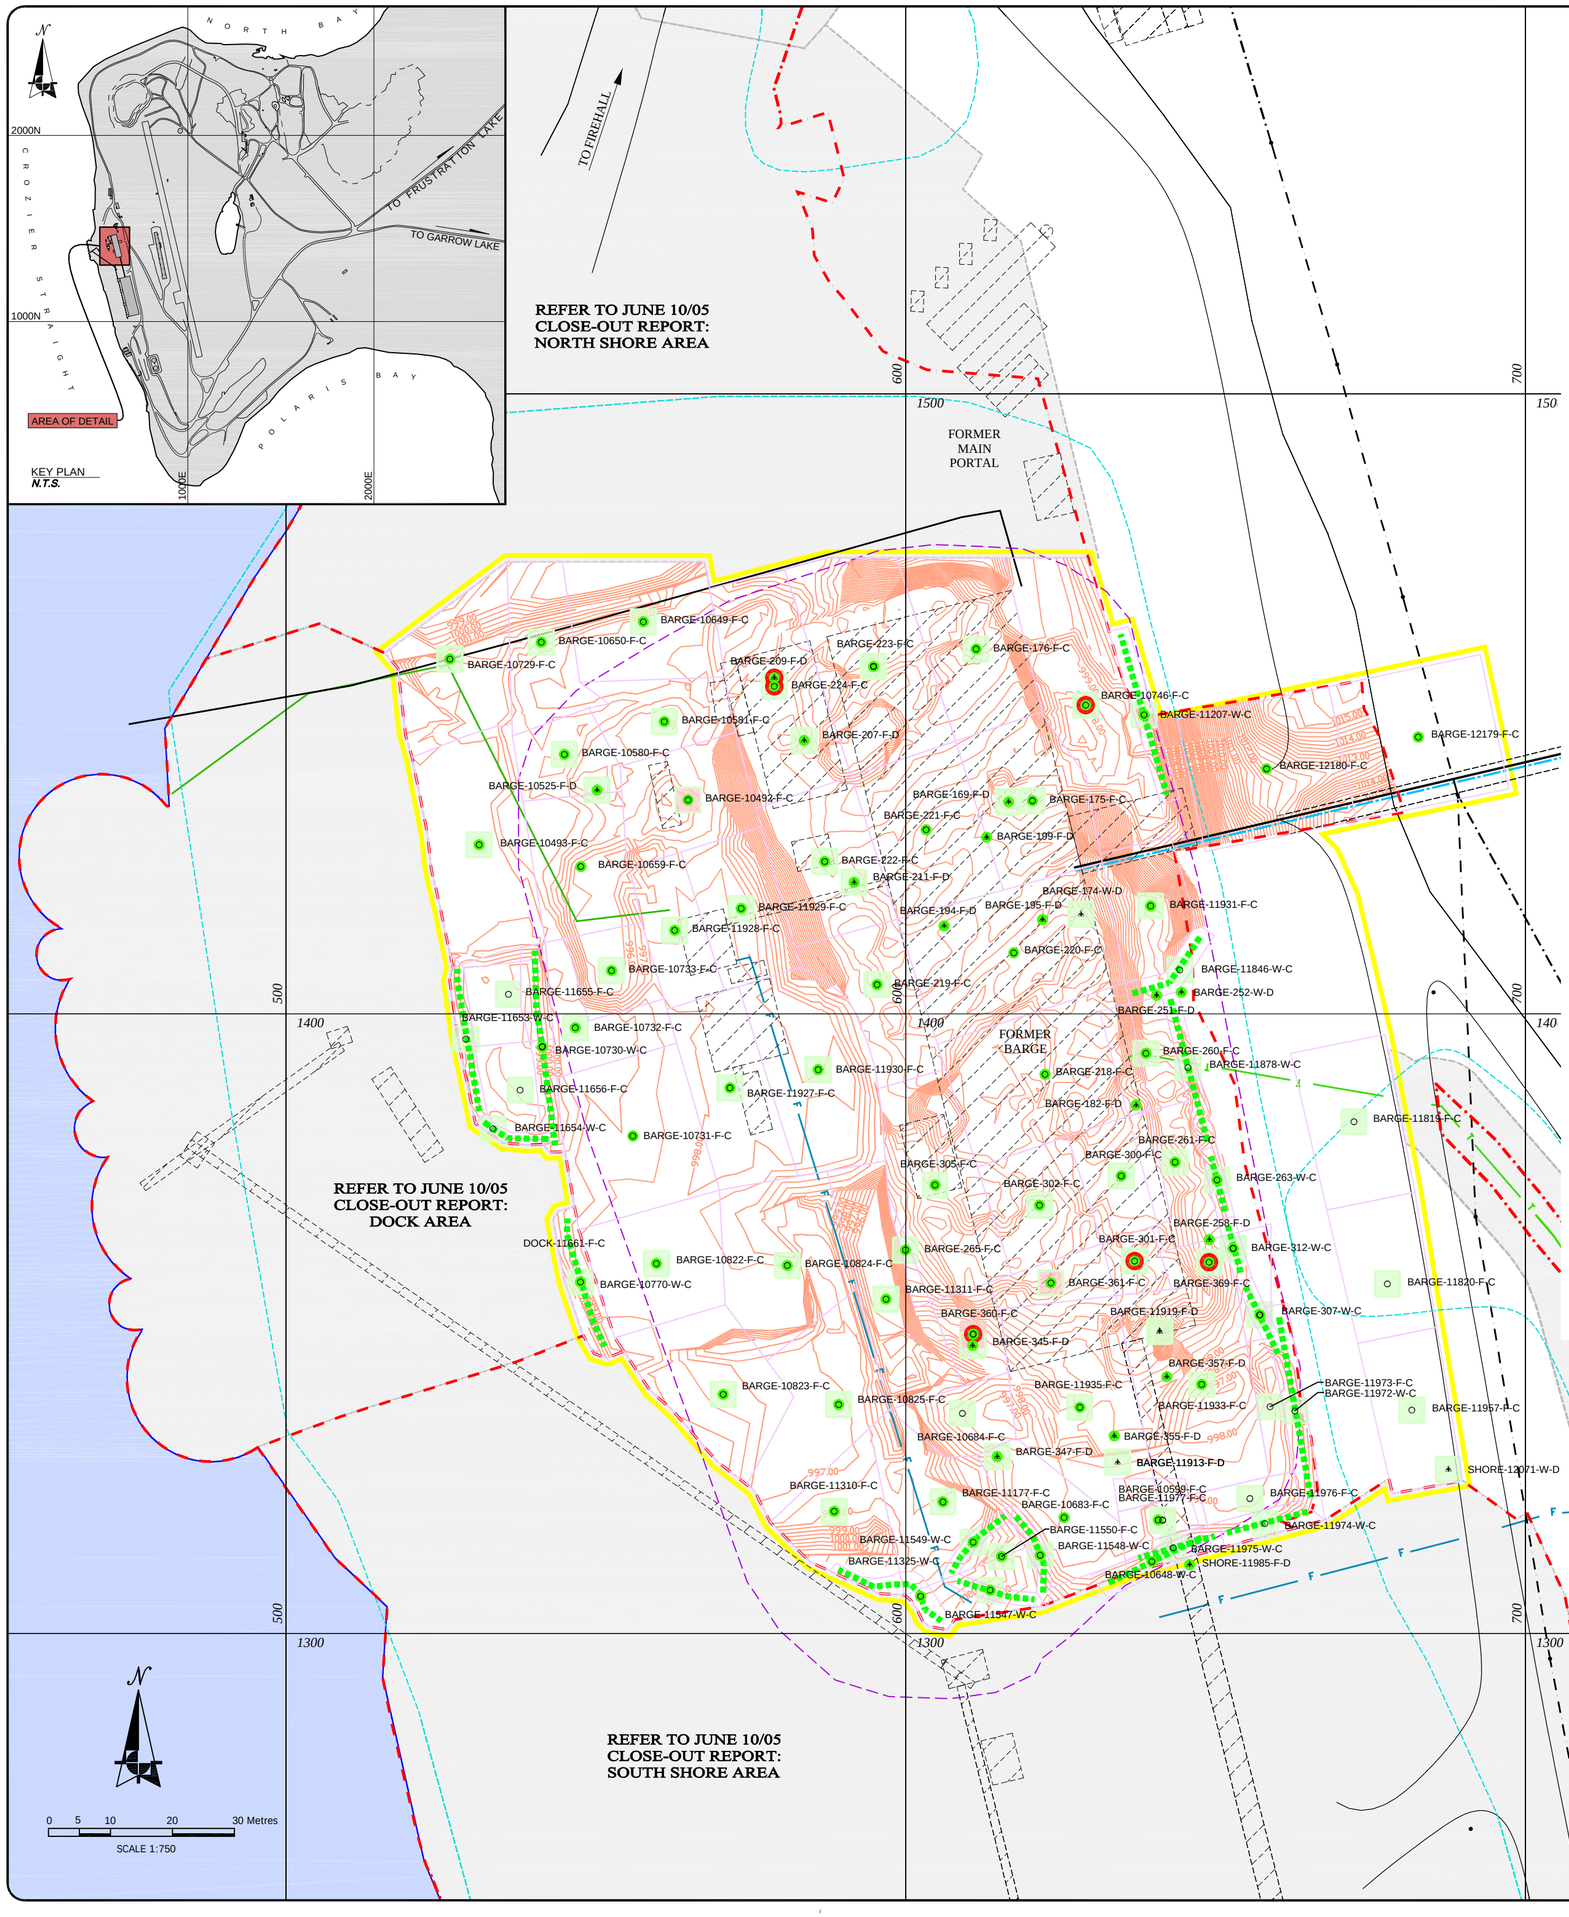

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
Barge-169-F-D	<100	5
Barge-174-W-D	<200	5
Barge-175-F-C	<100	9
Barge-176-F-C	<100	10
Barge-207-F-D	<200	996
Barge-211-F-D	<200	766
Barge-219-F-C	<200	2630
Barge-222-F-C	<200	1280
Barge-223-F-C	237	506
Barge-224-F-C	<200	2040
Barge-225-F-Q duplicate of Barge-223-F-C	456	420
Barge260-F-C	<100	178
Barge261-F-C	<100	11.6
Barge263-W-C	1790	6670
Barge265-F-C	1030	8910
Barge300-F-C	120	475
Barge301-F-C	830	3000
Barge302-F-C	<100	294
Barge305-F-C	420	2150
Barge-307-W-C	1280	2240
Barge-312-W-C	1240	2720
Barge-345-F-D	1440	7050
Barge-347-F-D	720	4660
Barge-360-F-C	**5350**	**10200**
Barge-361-F-C	**5570**	3830
Barge-363-F-Q duplicate of Barge-360-F-C	440	2990
Barge-369-F-C	520	2470
Barge-370-F-Q duplicate of Barge-369-F-C	800	2890
Barge-10492-F-C	**2500**	4360
Barge-10493-F-C	870	2450
Barge-10525-F-D	370	1480
Barge-10580-F-C	1000	2210
Barge-10581-F-C	870	1720
Barge-10649-F-C	260	637
Barge-10650-F-C	260	2490
Barge-10684-F-C	970	6930
Barge-10729-F-C	160	500
Barge-10732-F-C	<200	173
Barge-10733-F-C	<200	220
Barge-10746-F-C	<100	200
Barge-10770-W-C	1600	6570
Barge-10822-F-C	<100	233
Barge-10823-F-C	1100	5870
Barge-10824-F-C	1980	9790
Barge-10825-F-C	640	3860
Barge-11177-F-C	740	6510
Barge-11207-W-C	1860	17.3
Barge-11310-F-C	550	8500
Barge-11311-F-C	1660	6590
Barge-11547-W-C	110	314
Barge-11548-W-C	150	374
Barge-11549-W-C	120	329
Barge-11550-F-C	190	501
Barge-11653-W-C	420	1040
Barge-11654-W-C	330	734
Barge-11655-F-C	380	862
Barge-11656-F-C	370	762
Barge-11819-F-C	275	808
Barge-11820-F-C	263	876
Barge-11846-W-C	390	1170
Barge-11874-F-C	<100	103
Barge-11878-W-C	<100	117
Barge-11913-F-D	1570	2330
Barge-11919-F-D	<100	217
Barge-11927-F-C	<100	43.3
Barge-11928-F-C	<100	36.1
Barge-11929-F-C	<100	32
Barge-11930-F-C	<100	55.8
Barge-11931-F-C	<100	55.4
Barge-11933-F-C	120	427
Barge-11934-F-Q duplicate of Barge-11933-F-C	120	587
Barge-11935-F-C	180	653
Barge-11957-F-C	170	469
Barge-11972-W-C	130	376
Barge-11973-F-C	210	636
Barge-11974-W-C	370	3390
Barge-11975-W-C	710	4030
Barge-11976-F-C	310	4900
Barge-11977-F-C	590	3650
Barge-11978-F-Q duplicate of Barge-11977-F-C	380	4310
Barge-11986-F-Q duplicate of Barge-11919-F-C	120	472
Barge-12071-W-D	295	473

Confirmation Sample ID	EPH C10-C19a mg/kg	EPH C19-C32a mg/kg
Barge-169-F-D	<200	<200
Barge-175-F-C	<200	<200
Barge-176-F-C	240	<200
Barge-182-F-D	724	<200
Barge-194-F-D	<200	<200
Barge-195-F-D	686	<200
Barge-199-F-D	554	<200
Barge-207-F-D	259	<200
Barge-209-F-D	**2380**	<200
Barge-211-F-D	206	<200
Barge-218-F-C	210	<200
Barge-219-F-C	<200	<200
Barge-220-F-C	208	<200
Barge-221-F-C	230	<200
Barge-222-F-C	436	<200
Barge-223-F-C	463	<200
Barge-224-F-C	**1340**	<200
Barge-225-F-Q duplicate of Barge-223-F-C	406	<200
Barge-251-F-D	<200	<200
Barge252-W-D	<200	<200
Barge258-F-D	<200	<200
Barge260-F-C	<200	<200
Barge261-F-C	<200	<200
Barge263-W-C	590	<200
Barge265-F-C	<200	<200
Barge300-F-C	<200	<200
Barge301-F-C	**1030**	210
Barge302-F-C	<200	<200
Barge305-F-C	<200	<200
Barge-312-W-C	<200	<200
Barge-345-F-D	330	<200
Barge-347-F-D	450	<200
Barge-355-F-D	780	230
Barge-357-F-D	320	<200
Barge-360-F-C	**1160**	230
Barge-361-F-C	970	210
Barge-363-F-Q duplicate of Barge-360-F-C	840	210
Barge-369-F-C	**1030**	250
Barge-370-F-Q duplicate of Barge-369-F-C	**1200**	260
Barge-10492-F-C	660	210
Barge-10493-F-C	<200	<200
Barge-10525-F-D	<200	<200
Barge-10580-F-C	<200	<200
Barge-10581-F-C	<200	<200
Barge-10599-F-C	<200	<200
Barge-10648-W-C	<200	260
Barge-10649-F-C	<200	320
Barge-10650-F-C	200	380
Barge-10659-F-C	<200	<200
Barge-10683-F-C	860	270
Barge-10729-F-C	<200	<200
Barge-10730-W-C	210	470
Barge-10731-F-C	<200	220
Barge-10732-F-C	<200	<200
Barge-10733-F-C	<200	<200
Barge-10734-W-Q duplicate of Barge-10730-W-C	<200	370
Barge-10746-F-C	**1520**	480
Barge-10770-W-C	270	260
Barge-10822-F-C	<200	210
Barge-10823-F-C	450	<200
Barge-10824-F-C	<200	<200
Barge-10825-F-C	200	<200
Barge-11177-F-C	<200	<200
Barge-11207-W-C	900	350
Barge-11310-F-C	210	270
Barge-11311-F-C	<200	<200
Barge-11325-W-C	<200	230
Barge-11547-W-C	<200	<200
Barge-11548-W-C	<200	<200
Barge-11549-W-C	<200	<200
Barge-11550-F-C	<200	<200
Barge-11927-F-C	340	520
Barge-11928-F-C	<200	380
Barge-11929-F-C	230	380
Barge-11930-F-C	250	440
Barge-11931-F-C	280	480
Barge-11933-F-C	<200	380
Barge-11934-F-Q duplicate of Barge-11933-F-C	<200	390
Barge-11935-F-C	<200	240
SHORE-11985-F-D	<200	<200
Barge-12179-F-C	<200	230
Barge-12180-F-C	<200	220

Bold — **Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- T — TAILINGS LINE
- T — TAILINGS LINE (FORMER)
- F — FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

AREA – SAMPLE ID – ESP–7–I–D

TYPE: C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL; D= DISCRETE SAMPLE; Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE

LOCATION: F= FLOOR SAMPLE; I= INTERMEDIATE FLOOR SAMPLE; W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

SOURCE OF DRAWING:

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–BARGE–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

BARGE CONDITIONS AFTER REMEDIATION

Gartner Lee

FIGURE NO. BA-01-2

Appendix B

Ship Loading Dock

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald,

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Dock Area

BACKGROUND

The dock structure was located 100 m west of the process barge that contained the former mill and office complex (shown as Area 2 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*). The dock consisted of four main cells with a 92 m long docking face approximately 20 m high, with a minimum of 14 m draft below the mean sea water level. The four cells were constructed through the ice in the winter of 1981 by driving interlocking sheet pilings into the ice and backfilling them with rock. During construction approximately 45 pipes at 1 m spacing were emplaced in the fill to circulate glycol coolant to freeze the rock fill.

The dock contained a shiploading tower that was connected to the concentrate storage building by a conveyor-way. A fuel distribution pipeline and electrical services ran along the conveyor-way to the shiploader.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified Lead and Zinc contamination in the soil at the dock area from surface to a depth of 0.3 m. During the ESA two test pits and one borehole were drilled adjacent to the east side of the dock cells. Seven soil samples were submitted for analysis of hydrocarbons and five soil samples were submitted for Lead and Zinc analysis. Water samples were collected from the borehole in 1999 and 2000 and analysed for metals, glycol and volatile organic compounds. No samples were collected within the dock cells. No hydrocarbon or glycol contamination was encountered during the ESA. The original topography of the area, soil sample results from the ESA, as well as the area estimated during the ESA to be an area of concern, are shown on Figure Dock-02-01.

METHODOLOGY

Delineation

The preliminary boundaries of the remediation area, as identified in the ESA as "Areas of Concern", were further delineated for excavation on the basis of field screening measurements from soil samples obtained from fifteen (15) test pits and eighteen (18) boreholes in May, June and July 2003. Fifty five (55) soil samples were collected from the test pits and included seven (7) discrete samples collected at 0.05 m to 0.36 m intervals based on the visual appearance of the walls of the test pit and forty eight (48) composite samples collected over 0.15 m or 0.3 m intervals. The boreholes were advanced with an air rotary quarry drill and composite soil samples were collected over 0.8 m (2.5 feet) intervals to a depth of 4.0 m (13 feet). The soil samples were collected from the drill returns that accumulated at the mouth of the borehole onto a flat metal footplate. Following the collection of each sample the surface of the footplate was cleared of the drill cuttings.

Visual appearance and odour of the soil, along with field screening measurements obtained from the boreholes and test pits were used to delineate the area to be excavated. The hydrocarbon field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. The samples were field screened for metals using the Niton X-ray fluorescence (XRF) elemental analyser in accordance with Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols.

Based on results of the field screening sampling, it was determined that the entire Dock area would require excavation of metal contaminated soils. Hydrocarbon contamination was found to be present adjacent to the shiploader tower in Dock Cell 2 and in the soil to the east of the Dock Cells. Hydrocarbon contamination was also found to be present in the soil adjacent to Dock Cell 2, in part of Dock Cell 1, and 3. No hydrocarbon contamination was detected in Dock Cell 4.

Excavation

Prior to excavation of the dock cells, the glycol in pipes that were installed in the dock was recovered. Excavation of the soils in the dock area commenced June 21, 2003 and it was completed July 9, 2004 following a break in activities over the winter. The 2003 excavation concentrated on Dock Cells 1 and 2 and the area on the east side of these Dock Cells. Dock Cells 3 and 4 were left in place to allow the ship a point to moor in August 2003. The contaminated soils were removed from Dock Cells 1 and 2 and the sheet piling was cut at the high water level.

In 2004, the contaminated soil in Dock Cells 3 and 4 was excavated. Excavation within the Dock Cells commenced May 11, 2004 and was completed by June 3, 2004. The reclamation plan required the sheet piling from the Dock Cells to be cut at a depth of 3 m below the low tide elevation. Divers were commissioned in April, May and June 2004 to cut the sheet piling after the contaminated soil was removed from all the Dock Cells. Contaminated soil east of the Dock Cells continued to be excavated until July 5, 2004 when field screening results indicated that the Soil Quality Remediation Objectives (SQRO's) would be met.

Due to its proximity to the ocean and foreshore environment, special consideration was taken to minimise the impact to the marine environment. The influx of water into the dock cells could not be prevented, as such; mitigation measures were required to prevent the mobilisation of hydrocarbons and to reduce sedimentation into the marine environment. Water was removed from the excavation using conventional pumps, which were placed in sumps at the lowest portion of the excavation. The water was pumped into a sediment pond, which was lined with geotextile filters to screen out sediment. The water was then skimmed of any residual hydrocarbon sheen and released to the marine environment. Sediment curtains were also installed along the perimeter of the dock cells to filter sediments escaping the dock cells during high tides. Total suspended solids (TSS) levels were monitored daily along the shoreline during periods of work at predetermined stations in accordance with approved site procedures and protocols.

Excavators were used to remove materials from the Dock area. A ripper tooth attached to an excavator was used to break up the frozen and compacted ground to a depth of approximately 1.0 m. The second step in excavating the area utilised a bucket on the excavator to scoop up the material the ripper had lossened. The use of the ripper tooth was repeated until all the contaminated soil was removed from the Dock area. The Contaminated soils were loaded directly into trucks and disposed of in the underground mine workings in accordance with regulatory approvals.

Soil samples were collected across the floor and walls of the excavation. The visual appearance and odour of the soil along with the field screening measurements obtained with the PID and the XRF analyzer were used to further direct the excavation. The limits of the excavation are shown on Figure FH-21-2: *Dock Conditions After Remediation*.

Confirmation Sampling

Samples to confirm the absence of Glycol contamination were collected adjacent to pipes prior to excavation activities commencing as shown in the table below. Upon receipt of the analytical results that demonstrated the absence of Glycol contamination, excavation activities commenced.

Location of Samples Tested for Glycol

Sample ID	Northing	Easting	Location
Dock-62-I	468.4	1433.7	Dock Cell 4
Dock-63-I	464.0	1422.7	Dock Cell 4
Dock-66-I	473.6	1407.8	Dock Cell 3
Dock-67-I	467.4	1396.3	Dock Cell 3
Dock-72-I	485.7	1353.9	Dock Cell 1
Dock-73-Q	485.7	1353.9	Dock Cell 1
Dock-74-I	480.8	1340.9	Dock Cell 1
Dock-264-F-C	478.3	1396.5	Dock Cell 3
Dock-265-F-C	470.7	1424.0	Dock Cell 4

Upon receipt of field screening results that indicated that the soil remaining in the excavation would meet the SQRO's, confirmation soil samples were collected. The excavation area was subdivided into individual composite sampling areas approximately 25 m by 25 m or less as required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation.

Soil samples were collected at the excavation limits and submitted to ALS Environmental for analysis of EPH, metals, Polycyclic Aromatic Hydrocarbons (PAH) and Glycol. Additional excavation was undertaken in areas that did not meet the SQRO's and additional confirmatory samples taken upon completion of excavation. Upon receipt of the analytical results that met the SQRO's the final excavation limits were surveyed.

ANALYTICAL RESULTS

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with collecting and analyzing soil were implemented during the remediation of the Dock area, including the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical laboratory replicates. Relative percent differences (RpDs) have been calculated and compiled in Tables DO-02-5 for five (5) on-site field screened duplicates, three (3) analytical laboratory duplicates, and two (2) analytical laboratory replicates for Lead and Zinc concentrations for a total ten (10) QA/QC samples.

Seven (7) of the sample results and their duplicate/replicate results returned acceptable RpDs, below the site specific remediation protocol of 50%. Two other samples returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not

applicable). One analytical laboratory replicate sample, Shore-498-F-C returned a RpD for Zinc concentrations of 59%, which is above the objective. The variance between the sample and its replicate is considered indicative of sample heterogeneity in an area previously contaminated with Lead and Zinc concentrate dust.

Discussion

Analytical laboratory results for EPH, metals, PAH and Glycol are summarized in Tables DO-02-1, DO-02-2, DO-02-3 and DO-02-4 respectively, along with the approved Polaris Mine SQROs for petroleum hydrocarbons and metals. A total of fifteen (15) hydrocarbon, twenty six (26) metal and nine (9) glycol samples were submitted from the former Dock area. Of the hydrocarbon samples, there were thirteen (13) composite floor samples and two (2) composite wall samples. The twenty six (26) metal samples consisted of twenty two (22) composite floor samples, one (1) composite wall sample, and three (3) quality assurance and quality control (QA/QC) duplicate samples. Seven (7) Glycol samples were collected from the surface of the dock cells prior to excavation to verify the absence of the substance prior to remediation and two (2) Glycol samples were collected from the base of the excavation limits.. The soil quality results for EPH, Lead and Zinc and the lateral limits of the excavation are shown on Figure DOCK-02-2.

Fifteen (15) samples were analysed for EPH, of this set, four (4) randomly selected samples were extracted for PAH. All samples analysed for PAH returned values below the SQROs. All of the hydrocarbon remediation confirmation samples returned results below the Polaris mine SQROs.

All the metal remediation confirmation samples returned results below the Polaris Mine SQRO's for Lead and Zinc. Total metal analyses were performed on four (4) randomly selected confirmation samples. Two samples, DOCK-203-F-C, and DOCK-11546-F-C, returned Barium concentrations greater than the generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guidelines (CEQG) for Parkland land use of 500 mg/kg Barium in soil. The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

The presence of Barium concentrations in the soil above the generic CCME guidelines for parkland land use is attributed to natural background mineralogy. Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone.

Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results,* are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of Barium greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of Barium concentrations in those samples is listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of Barium remaining within the footprint of the Dock area after remediation are within the range of the background concentrations. In addition, the immobile nature of the Barium encountered on site was demonstrated in the ESA leachate test results that returned Barium concentrations at levels less than the detection limit and it was therefore not identified as a contaminant of concern in the ESA.

All of the samples submitted for Glycol analysis met the generic CCME guideline and returned results below the method detection limit of 10 mg/kg indicating no Glycol contaminated soil was present at the dock area.

The confirmatory samples supported by the QA/QC samples from the Dock area provide confidence that the remediation of the dock area complies with the SQROs.

CONCLUSIONS

Based on confirmatory sampling, consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the Dock area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

Dr. Dennis Gregor, P.Geol.
Senior Reviewer, Senior Aquatic Scientist

AL:DL:gc

ATTACHMENTS

Tables

Table DO-02-1:	Dock Area Remediation Confirmation Soil Samples – Hydrocarbons
Table DO-02-2:	Dock Area Remediation Confirmation Soil Samples – Metals
Table DO-02-3:	Dock Area Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table DO-02-4:	Dock Area Remediation Soil Screening Samples – Glycols
Table DO-02-5:	Dock Area Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure DO-02-1:	Dock Conditions Before Remediation
Figure DO-02-2:	Dock Conditions After Remediation

Table DO-02-1. Dock Area Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Dock						
		Sample ID	Dock-202-F-C	Dock-203-F-C	Dock-259-F-C	Dock-260-F-C	Dock-264-F-C	Dock-265-F-C	Dock-10744-F-C
		Date Sampled	28-Aug-03	28-Aug-03	03-Oct-03	03-Oct-03	07-Oct-03	07-Oct-03	20-May-04
		ALS File Number	T3582	T3582	T4927	T4927	T5093	T5093	U3898r
		Field Screen (ppm)[b]	-	-	-	-	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	<200	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	<200	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table DO-02-1. Dock Area Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Dock					
		Sample ID	Dock-11169-F-C	Dock-11214-F-C	Dock-11215-F-C	Dock-11312-W-C	Dock-11313-F-C	Dock-11481-W-C
		Date Sampled	04-Jun-04	02-Jun-04	02-Jun-04	01-Jun-04	31-May-04	15-Jun-04
		ALS File Number	U4269r	U4269r	U4269r	U4137	U4137	U4704r
		Field Screen (ppm)[b]	45	-	-	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	560	520	<200	<200	390
EPH C_{19}-C_{32}	1000	mg/kg	<200	400	390	<200	<200	<200
LEPH[c]	1000	mg/kg	<200	-	-	-	-	390
HEPH[c]	1000	mg/kg	<200	-	-	-	-	<200

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table DO-02-1. Dock Area Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Dock	
		Sample ID	Dock-11482-F-C	Dock-11696-F-C
		Date Sampled	15-Jun-04	28-Jun-04
		ALS File Number	U4704r	U5223
		Field Screen (ppm)[b]	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**	
Extractable Hydrocarbons				
EPH C_{10}-C_{19}	1000	mg/kg	<200	220
EPH C_{19}-C_{32}	1000	mg/kg	<200	440
LEPH[c]	1000	mg/kg	-	220
HEPH[c]	1000	mg/kg	-	440

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table DO-02-02. Dock Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	Dock						
				Sample ID	Dock-76-F-C	Dock-77-F-C	Dock-80-F-Q	Dock202-F-C	Dock203-F-C	Dock-259-F-C	Dock-260-F
				Date Sampled	24-Jun-03	24-Jun-03	24-Jun-03	28-Aug-03	28-Aug-03	03-Oct-03	03-Oct-03
				ALS File Number	S9893	S9893	S9893	T3582	T3582	T4927	T4927
				Field Screen Pb (ppm)[b]	-	-	duplicate of	-	-	-	-
				Field Screen Zn (ppm)[b]	-	-	Dock-77-F-C	-	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-		8.3	-	-	-	8.49	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	<10	-	-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	432	-	-	-	**677**	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<1	-	-	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	8	-	-	-	4	-	-
Chromium	T-Cr	-	64	mg/kg	5	-	-	-	8	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<4	-	-	-	<4	-	-
Copper	T-Cu	-	63	mg/kg	6	-	-	-	11	-	-
Lead	T-Pb	2000	-	mg/kg	619	431	554	199	327	443	<100
Mercury	T-Hg	-	6.6	mg/kg	<0.05	-	-	-	<0.05	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8	-	-	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	<10	-	-	-	10	-	-
Selenium	T-Se	-	1	mg/kg	<4	-	-	-	<3	-	-
Silver	T-Ag	-	20[d]	mg/kg	<4	-	-	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	14	-	-	-	21	-	-
Zinc	T-Zn	10000	-	mg/kg	3970	2600	2940	970	1250	3260	471

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-02. Dock Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Dock						
				Sample ID	Dock-262-I	Dock-263-F-C	Shore-426-F	Shore-427-F	Shore-433-F-Q	Shore-498-F-C	Shore-499-F-C
				Date Sampled	07-Oct-03	07-Oct-03	23-Sep-03	23-Sep-03	23-Sep-03	23-Oct-03	23-Oct-03
				ALS File Number	T5093	T5345	T4504	T4504	T4504	T5790	T5790
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	-	-	-	duplicate of	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	-	-	-	Shore-427-F	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-		-	-	-	8.57	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	371	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	13	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	<4	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	5	-	-	-
Lead	T-Pb	2000	-	mg/kg	977	778	1680	1350	1920	1360	860
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	<0.05	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	<10	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<4	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	11	-	-	-
Zinc	T-Zn	10000	-	mg/kg	3140	3540	8370	5910	7020	5310	3260

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines.The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-02. Dock Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	Dock					
				Sample ID	Dock-10646-F-C	Dock-11482-F-C	Dock-11545-F-C	Dock-11546-F-C	Dock-11627-F-C	Dock-11628-F-Q
				Date Sampled	13-May-04	15-Jun-04	17-Jun-04	17-Jun-04	22-Jun-04	22-Jun-04
				ALS File Number	U3564rr	U4704r	U4781	U4781	U4948	U4948
				Field Screen Pb (ppm)[b]	-	-	86	92	54	duplicate of
				Field Screen Zn (ppm)[b]	-	-	307	287	115	Dock-11627-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-		-	-	-	8.37	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	**578**	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1.0	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	<1.0	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	9.3	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	5.2	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	21.1	-	-
Lead	T-Pb	2000	-	mg/kg	930	430	<50	<100	<100	<100
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	0.103	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8.0	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	28	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<4.0	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4.0	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	73.3	-	-
Zinc	T-Zn	10000	-	mg/kg	1490	1680	75.4	93.7	105	158

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines.The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-02. Dock Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Dock					
				Sample ID	Dock-11660-F-C	Dock-11661-F-C	Dock-11843-F-C	Dock-11844-F-C	Dock-11845-F-C	Dock-11936-F-C
				Date Sampled	25-Jun-04	25-Jun-04	01-Jul-04	01-Jul-04	01-Jul-04	04-Jul-04
				ALS File Number	U5050	U5050	U5353r	U5353r	U5353r	U5597r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	296	269	135	116	80	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	996	877	483	433	161	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-		-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	260	240	490	120	<100	<100
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	631	478	252	325	83.9	99.5

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines.The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-03. Dock Area Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Dock			
		Sample ID	Dock-265-F	Dock-11169-F-C	Dock-11481-W-C	Dock-11696-F-C
		Date Sampled	07-Oct-03	04-Jun-04	15-Jun-04	28-Jun-04
		ALS File Number	T5093	U4269r	U4704r	U5223
		Field Screen (ppm)[b]		45	-	-
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**			
Polycyclic Aromatic Hydrocarbons						
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	<0.05	<0.05	0.52	<0.05
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05	0.091
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-4. Dock Area Remediation Soil Screening Samples - Glycol

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Dock								
		Sample ID	Dock-72-I	Dock-73-Q	Dock-74-I	Dock-62-I	Dock-63-I	Dock-66-I	Dock-67-I	Dock-264-F	Dock-265-F
		Date Sampled	23-May-03	duplicate of	23-May-03	23-May-03	23-May-03	23-May-03	23-May-03	07-Oct-03	07-Oct-03
		ALS File Number	S8646	Dock-72-I	S8646	S8646	S8646	S8646	S8646	T5093	T5093
Parameter	**CEQG (PL)[b]**	**Units**	**Analytical Results**								
Glycols											
Diethylene_Glycol	-	mg/kg	<10	<10	<10	<10	<10	<10	<10	<10	<10
Ethylene_Glycol	97[c]	mg/kg	<10	<10	<10	<10	<10	<10	<10	<10	<10
12_Propylene_Glycol	-	mg/kg	<10	<10	<10	<10	<10	<10	<10	<10	<10

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

c) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table DO-02-5. Dock Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee	Location	Dock									
	Sample ID	Dock-77-F-C	Shore-427-F-C	Dock-11627-F-C	Dock-11627-F-C	Dock-11627-F-C	Dock-85-I-D	Dock-222-I-D	Shore-294-I-D	Shore-427-F-C	Shore-498-F-C
	Duplicate ID	Dock-80-F-Q	Shore-433-F-Q	Dock-11628-F-Q	Dock-11628-F-Q	Dock-11710-F-Q	Dock-86-I-Q	Dock-203-I-Q	Shore-37-I-Q	QC# 356604	QC# 361306
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**							
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350	-	-	-	54	54	2650	951	1162	-	-
Duplicate Result	mg/kg	70	350	-	-	-	16	35	2720	1266	1592	-	-
RpD	%						na	na	3%	28%	31%		
Zinc (Zn)											
Sample Result	mg/kg	150	500	-	-	-	115	115	16998	2216	12103	-	-
Duplicate Result	mg/kg	150	500	-	-	-	147	182	16294	3425	16113	-	-
RpD	%						na	na	4%	43%	28%		
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500	431	1350	<100	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	554	1920	<100	-	-	-	-	-	-	-
RpD	%			na	35%	na							
Zinc (Zn)											
Sample Result	mg/kg	3	15	2600	5910	105	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15	2940	7020	158	-	-	-	-	-	-	-
RpD	%			12%	17%	40%							
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500	-	-	-	-	-	-	-	-	1350	1360
Duplicate Result	mg/kg	100	500	-	-	-	-	-	-	-	-	1700	1900
RpD	%											23%	33%
Zinc (Zn)											
Sample Result	mg/kg	3	15	-	-	-	-	-	-	-	-	5910	5310
Duplicate Result	mg/kg	3	15	-	-	-	-	-	-	-	-	8300	9800
RpD	%											34%	**59%**

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

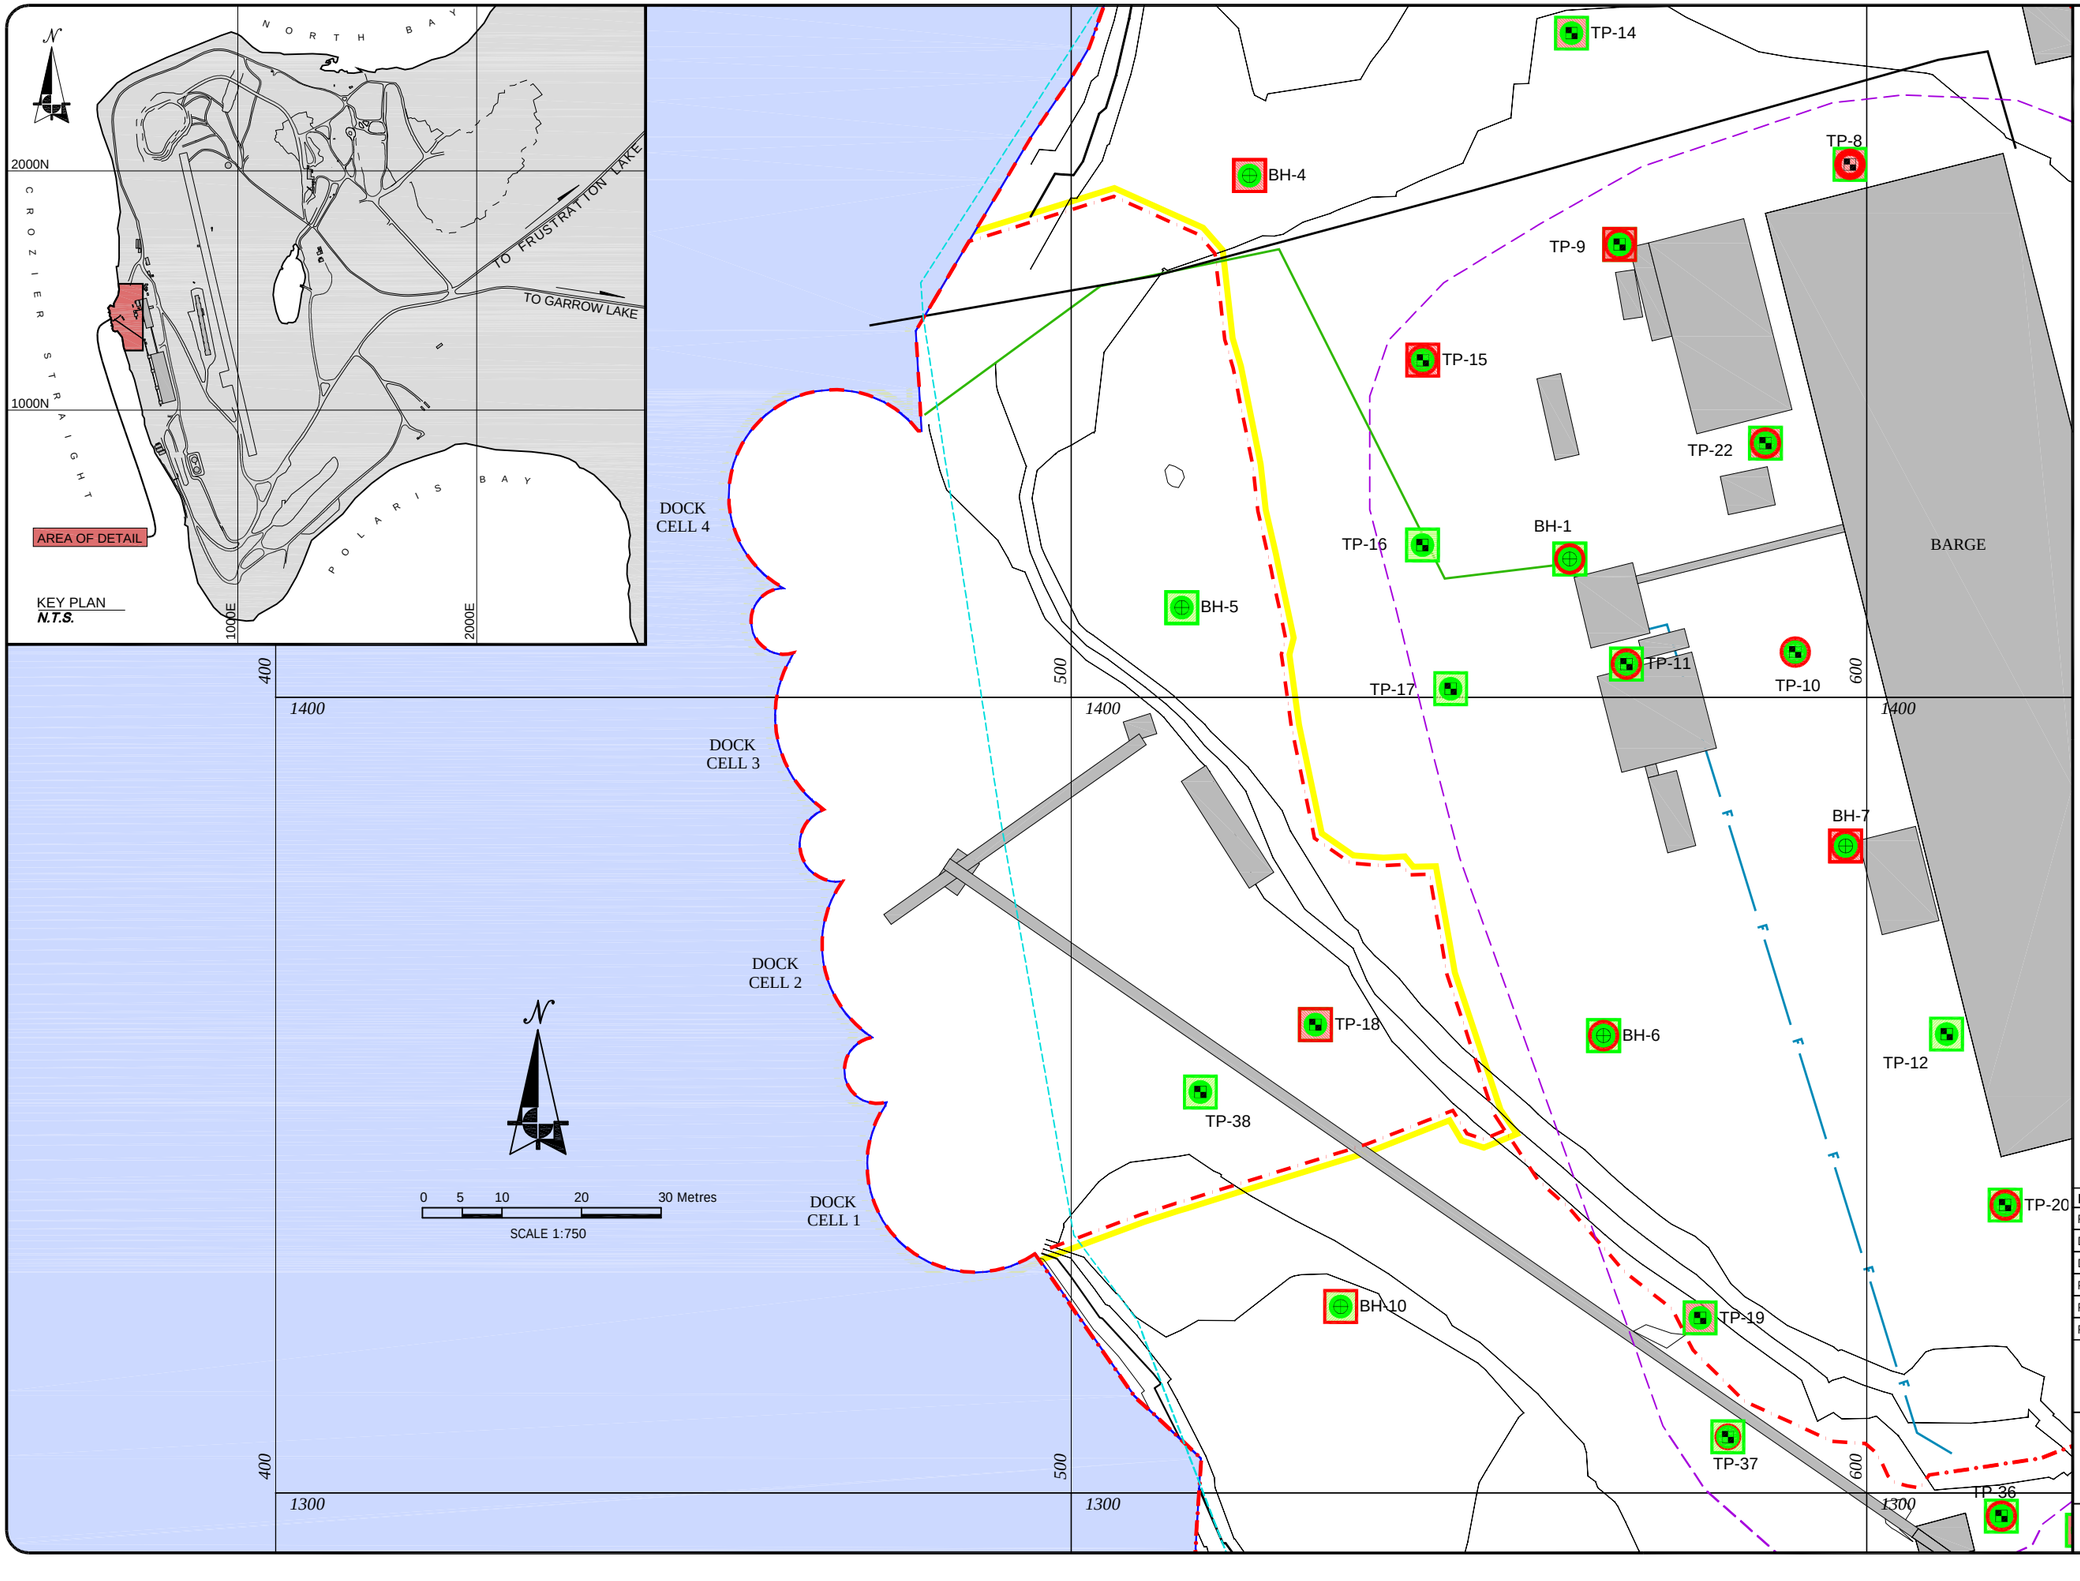

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–DOCK–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

DOCK CONDITIONS BEFORE REMEDIATION

Gartner Lee

Figure No.
DO-02-1

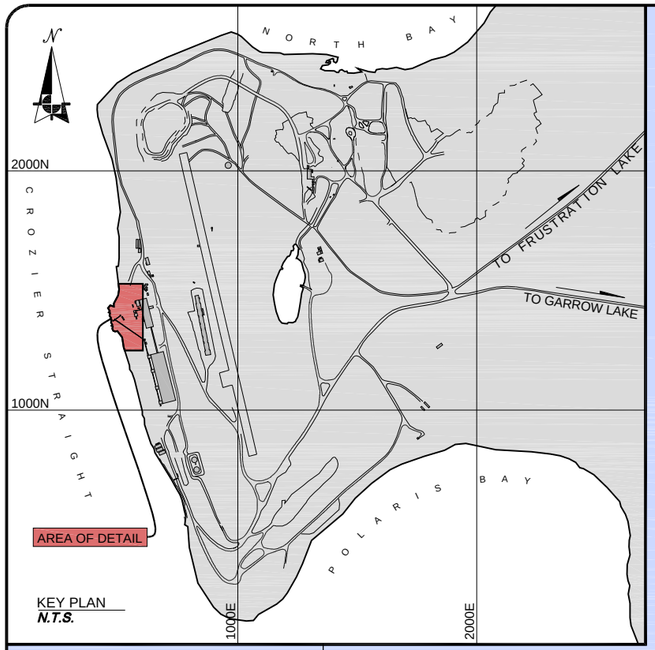

REFER TO JUNE 10/05 CLOSE-OUT REPORT: NORTH SHORE AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: BARGE AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: SOUTH SHORE AREA

DOCK CELL 4

DOCK CELL 3


DOCK CELL 2

DOCK CELL 1

FORMER BARGE

DOCK-11936-F-C
DOCK-11546-F-C
DOCK-11845-F-C
DOCK-11844-F-C
DOCK-265-F-C
DOCK-263-F-C
DOCK-10646-F-C
SHORE-499-F-C
DOCK-11545-F-C
SHORE-498-F-C
DOCK-259-F-C
DOCK-11313-F-C
DOCK-264-F-C
DOCK-262-I
SHORE-426-F-C
DOCK-260-F-C
SHORE-427-F-C
BARGE-11653-W-C
DOCK-11312-W-C
DOCK-11627-F-C
DOCK-11660-F-C
DOCK-11696-F-C
DOCK-11169-F-C
DOCK-10744-F-C
DOCK-11481-W-C
DOCK-11482-F-C
DOCK-11843-F-C
DOCK-11215-F-C
DOCK-77-F-C
DOCK-202-F-C
DOCK-11661-F-C
DOCK-76-F-C
DOCK-203-F-C
DOCK-11214-F-C

400
1400
600
500
1300



Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
Dock-76-F	619	3970
Dock-77-F	431	2600
Dock-80-F-Q duplicate of Dock-77-F-C	554	2940
Dock-202-F-C	199	970
Dock-203-F-C	327	1250
Dock-259-W-C	443	3260
Dock-260-F	<100	471
Dock-262-I	977	3140
Dock-263-F-C	778	3540
Shore-426-F	1680	8370
Shore-427-F	1350	5910
Shore-433-F-Q duplicate of Shore-427-F-C	1920	7020
Shore-498-F-C	1360	5310
Shore-499-F-C	860	3260
Dock-10646-F-C	930	1490
Dock-11482-F-C	430	1680
Dock-11545-F-C	<50	75.4
Dock-11546-F-C	<100	93.7
Dock-11627-F-C	<100	105
Dock-11628-F-Q duplicate of Shore-11627-F-C	<100	158
Dock-11660-F-C	260	631
Dock-11661-F-C	240	478
Dock-11843-F-C	490	252
Dock-11844-F-C	120	325
Dock-11845-F-C	<100	83.9
Dock-11936-F-C	<100	99.5

Confirmation Sample ID	EPH C10-C19 mg/kg	EPH C19-C32 mg/kg
Dock202-F-C	<200	<200
Dock203-F-C	<200	<200
Dock-259-F	<200	<200
Dock-260-F	<200	<200
Dock-264-F	<200	<200
Dock-265-F	<200	<200
Dock-10744-F-C	<200	<200
Dock-11169-F-C	<200	<200
Dock-11214-F-C	560	400
Dock-11215-F-C	520	390
Dock-11312-W-C	<200	<200
Dock-11313-F-C	<200	<200
Dock-11481-W-C	390	<200
Dock-11482-F-C	<200	<200
Dock-11696-F-C	220	440

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

ESP–7–I–D
- ESP–7 = AREA / SAMPLE ID
- I = LOCATION
- D = TYPE
  - C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL
  - D= DISCRETE SAMPLE
  - Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
  - F= FLOOR SAMPLE
  - I= INTERMEDIATE FLOOR SAMPLE
  - W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- *EPH – EXTRACTABLE PETROLEUM HYDROCARBONS
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–DOCK–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

DOCK CONDITIONS AFTER REMEDIATION

Gartner Lee

Figure No. **DO-02-2**

Appendix C

Accommodation Complex

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Accommodation Complex

BACKGROUND

The Accommodation Complex (shown as Area 5 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*) was located near the crest of the slope overlooking the former mill and office complex within the barge, and concentrate storage shed.

The foundations lied on about 1.5 m of sand and gravel fill, which overlies fractured limestone. The active soil zone is approximately 0.6 m deep. The building was raised above the existing grade by 1.2 m to 2.1 m, permitting preservation of the thermal regime under the building. The foundations consisted of concrete pads and columns, and the footprint of the building covered an area of 5,120 m^2. The building was an all-steel construction.

There were about 240 rooms in four residential modules, each module was connected to the other by alternating service modules containing the kitchen and dining room, commissary and swimming pool, nursing station and offices. The electrical/mechanical services module was at the north end of the building, and included three 450 kw emergency generators, the vacuum sewage system, fire pumps, boilers, laundry and glycol heat transfer system. An above ground storage diesel tank, used for the emergency generators, was located at the northeast side of the Accommodation Complex. Primary heat supply was from a glycol waste heat recovery system attached to the barge diesel generators. Food freezers, coolers and dry goods storage were located at the south end of the building beneath a gymnasium. During demolition a truck wash station was operated at the north end of the Accommodation Complex.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified hydrocarbon contamination in the soil at the north end of the accommodation complex. Petroleum hydrocarbon contamination was observed in test pits excavated adjacent to the above-ground storage tank (AST) and at the north side of the building. The eastern, up-gradient extent of hydrocarbon contamination was delineated during the ESA. Figure ACC-05-1: *Accommodation Complex Conditions Before Remediation* illustrates the original topography of the area, sample

results from the ESA, as well as the area estimated by the ESA as an area of concern for hydrocarbon contamination.

METHODOLOGY

Delineation

The preliminary boundary of the remedial area, as identified in the ESA as an "Area of Concern", was further delineated through the drilling of boreholes on October 25, 2003. A total of six boreholes were drilled using the air rotary quarry drill at the northwest corner of the accommodation complex, on the downgradient side of the building.

The borehole investigation also served to investigate the presence of contamination resulting from the use of the wash station during demolition. Each hole was drilled to a depth of three meters, and composite soil samples were collected over 0.6 m intervals. The soil samples were collected from the drill returns that accumulated at the mouth of the borehole. Following the collection of each sample the surface surrounding the borehole was cleared of the drill cuttings, and fresh snow was exposed.

The visual appearance and odour of the soil was used to delineate the area to be excavated, along with field screening measurement of the concentrations of organic vapours in the composite soil samples. The field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. As a result of the October 25, 2004 drilling, the interpreted extent of the area to be remediated was revised as indicated by the "Limit of Remedial Excavation" shown on Figure ACC-05-1.

Excavation

Excavation of the contaminated soils at the Accommodation Complex began on July 5, 2004, prior to the demolition of the Accommodations Complex. At this time only the northwestern portion of the delineated hydrocarbon contamination was excavated due to limited access and vehicle safety concerns.

Demolition of the Accommodation Complex commenced August 4, 2004 and was completed by August 27, 2004. Excavation of remaining hydrocarbon contaminated soil that had been previously delineated started August 17, 2004, and was completed by September 4, 2004.

Soil within the excavation boundaries was ripped and loaded out into trucks with an excavator. The excavation was completed in two lifts, each approximately 0.6 m thick.

The final limits of the excavation are shown on Figure ACC-05-2: *Accommodation Complex Conditions After Remediation*. An in-situ volume of approximately 2,000 m^3 was excavated from the former Accommodation Complex area. This material was disposed of in the underground mine workings in accordance with regulatory approvals.

Confirmation Sampling

Field screening sampling was undertaken at the base of the first lift and along the excavation boundaries to determine where additional excavation was required to meet the Soil Quality Remediation Objectives (SQROs).

Soil samples were collected across the floor and along the wall of the excavation limits in accordance with Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols. Soil samples were collected at the final excavation limits and sent to the analytical laboratory, ALS Environmental for extractable petroleum hydrocarbons (EPH) and polycyclic aromatic hydrocarbons (PAH). Composite samples were collected from areas of the floor approximately 25 m x 25 m and over a length of 25 m along the perimeter walls of the excavation.

The results of field sampling indicated that a second excavation pass was required over the eastern portion of the area delineated by the ESA. The re-excavated area was sampled again, and field-screening results indicated that the remaining soil exposed across the excavation would meet the SQROs. The excavation limits were surveyed, and are show on Figure ACC-05-2.

ANALYTICAL RESULTS

Analytical laboratory results for EPH and PAH are summarized in Tables ACC-05-1 and ACC-05-02 respectively, along with the approved Polaris Mine SQRO's for petroleum hydrocarbons.

A total of fifteen (15) confirmation soil samples from the former Accommodation Complex were submitted for laboratory analysis. The fifteen remediation confirmation soil samples were collected as follows: six (6) composite floor samples, one (1) discrete floor, six (6) composite walls, and two (2) quality assurance/quality control (QA/QC) duplicate samples. The soil quality results and the lateral limits of the excavation are shown on Figure ACC-05-2.

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with collecting and analyzing soil were implemented during the remediation of the Accommodations Complex area, including the submission of blind duplicates to the analytical laboratory, analysis of analytical laboratory replicates, and comparison of

analytical laboratory EPH results with the portable photoionization detector (PID) organic vapour headspace measurements.

Relative percent differences (RpDs) have been calculated and compiled in Table ACC-05-03 for the two (2) analytical laboratory duplicates and three (3) laboratory replicate results. The laboratory duplicate and replicates returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not available).

Confirmation Sample Results

All samples were analyzed for EPH, and two samples were analyzed for PAH. The two samples submitted for PAH analyses were collected from the floor of the excavation where the hydrocarbon contamination had been the most pervasive.

A discrete sample was collected from the same area as a composite sample, and both were submitted for laboratory analysis. The results are as follows:

Summary of Discrete Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	EPH C_{10}-C_{19} (mg/kg)	EPH C_{19}-C_{32} (mg/kg)	Discrete Sample ID	EPH C_{10}-C_{19} (mg/kg)	EPH C_{19}-C_{32} (mg/kg)
ACC-12182-F-C	<200	<200	ACC-12186-F-D	280	<200

All confirmatory soil sample results from the Accommodation Complex met the SQRO's set forth for the Polaris Mine.

CONCLUSIONS

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former Accommodation Complex area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of

such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgment in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Brenda Bolton, B.A., B.Sc.
Environmental Geologist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:BB:gc

ATTACHMENTS

Tables

Table ACC-05-1: Accommodation Complex Remediation Confirmation Soil Samples – Hydrocarbons
Table ACC-05-2: Accommodation Complex Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table ACC-05-3: Accommodation Complex Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons

Figures

Figure ACC-05-1: Accommodation Complex Conditions Before Remediation
Figure ACC-05-2: Accommodation Complex Conditions After Remediation

Table ACC 05-1. Accomodation Complex Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Accommodation Complex							
		Sample ID	ACC-11749-F-C	ACC-11923-W-C	ACC-11924-W-C	ACC-12163 -W-C	ACC-12164-F-C	ACC-12168-F-Q	ACC-12165-F-C	ACC-12166-F-C
		Date Sampled	05-Jul-04	06-Jul-04	06-Jul-04	20-Aug-04	20-Aug-04	20-Aug-04	20-Aug-04	20-Aug-04
		ALS File Number	U5597r	U5597r	U5597r	U7328	U7328	duplicate of	U7328	U7328
		Field Screen (ppm)[b]	10	25	25	10	10	ACC-12164-F-C	15	15
Parameter	**Site Specific[b]**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	200	290	380	280	380	380
EPH C_{19}-C_{32}	1000	mg/kg	<200	310	320	520	780	500	550	700
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table ACC 05-1. Accomodation Complex Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Accommodation Complex						
		Sample ID	ACC-12167-W-C	ACC-12181-F-C	ACC-12182-F-C	ACC-12183-F-Q	ACC-12184-W-C	ACC-12185-W-C	ACC-12186-F-D
		Date Sampled	20-Aug-04	28-Aug-04	28-Aug-04	28-Aug-04	28-Aug-04	28-Aug-04	28-Aug-04
		ALS File Number	U7328	U7700	U7700	duplicate of	U7700	U7700	U7700
		Field Screen (ppm)[b]	20	20	25	ACC-12182-F-C	10	15	10
Parameter	**Site Specific[b]**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	320	<200	<200	<200	<200	<200	280
EPH C_{19}-C_{32}	1000	mg/kg	620	<200	<200	<200	340	<200	<200
LEPH[c]	1000	mg/kg	-	-	<200	<200	-	-	-
HEPH[c]	1000	mg/kg	-	-	<200	<200	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table ACC-05-2. Accommodation Complex Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Accommodation Complex	
		ALS Sample ID	ACC-12182-F-C	ACC-12183-F-Q
		Date Sampled	28-Aug-04	28-Aug-04
		ALS File No	U7700	duplicate of
		Field Screening (ppm)[b]	25	ACC-12182-F-C
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**	
Polycyclic Aromatic Hydrocarbons				
Acenaphthene	-	mg/kg	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05
Napthalene	0.6	mg/kg	0.06	0.078
Phenanthrene	5[d]	mg/kg	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table ACC-05-3. Accommodation Complex Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Accommodation Complex				
					Analytical Laboratory Duplicates		Analytical Laboratory Replicates		
				Sample ID	ACC-12182-F-C	ACC-12164-F-C	ACC-11923-W-C	ACC-12165-F-C	ACC-12183-F-Q
				Duplicate ID	ACC-12183-F-Q	ACC-12168-F-Q	QC#395245	QC#402847	QC#404398
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**		**Analytical Results**		
Extractable Hydrocarbons									
EPH C_{10}-C_{19}									
Sample Result	mg/kg	200	1000		<200	280	<200	380	<200
Duplicate Result	mg/kg	200	1000		<200	380	240	280	<200
RpD	**%**				na	na	na	na	na
EPH C_{19}-C_{32}									
Sample Result	mg/kg	200	1000		<200	500	310	550	<200
Duplicate Result	mg/kg	200	1000		<200	780	380	520	<200
RpD	**%**				na	na	na	na	na

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:


na *RpD value is not applicable because one or both results are less than the PQL.*


RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

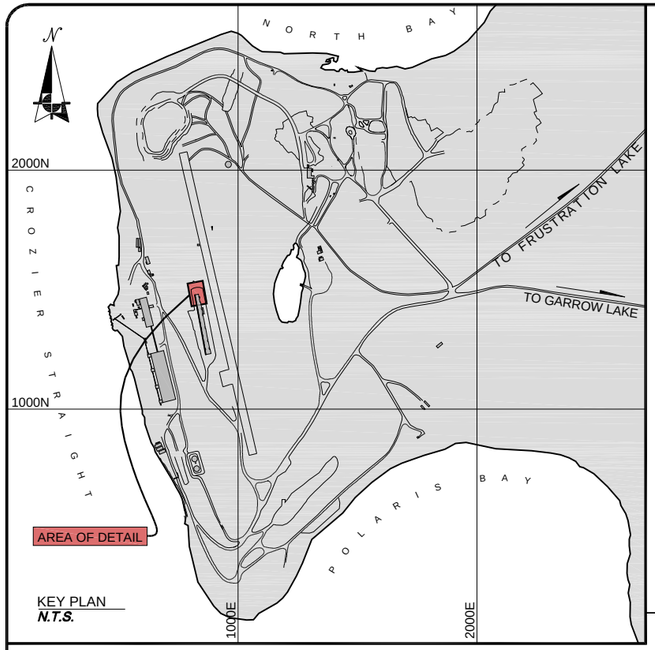



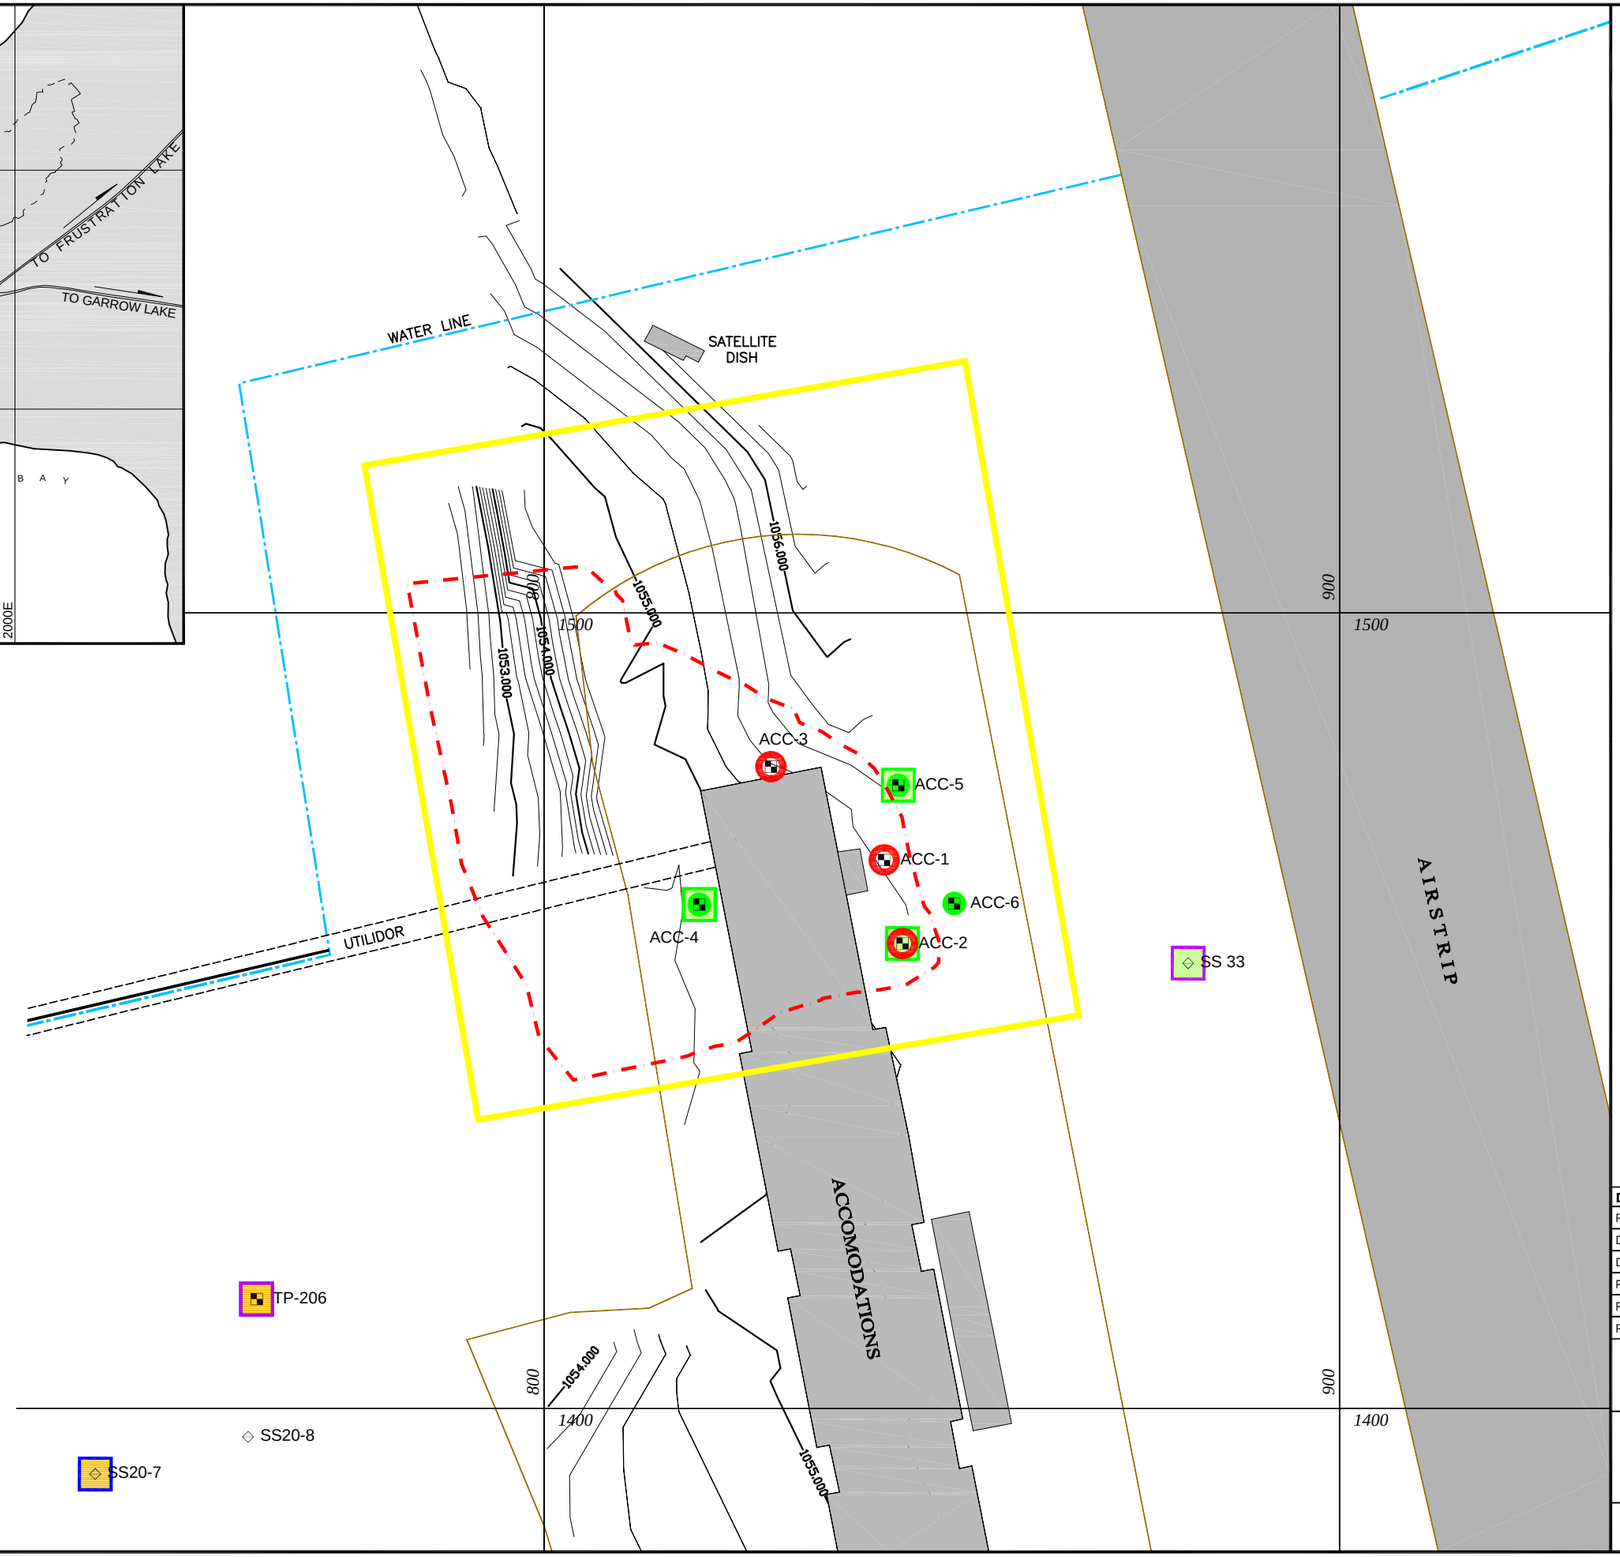

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20-6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–ACC–M1–01.DWG
REVISION:	0


POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

ACCOMMODATION COMPLEX CONDITIONS BEFORE REMEDIATION

Gartner Lee

Figure No. ACC-05-1

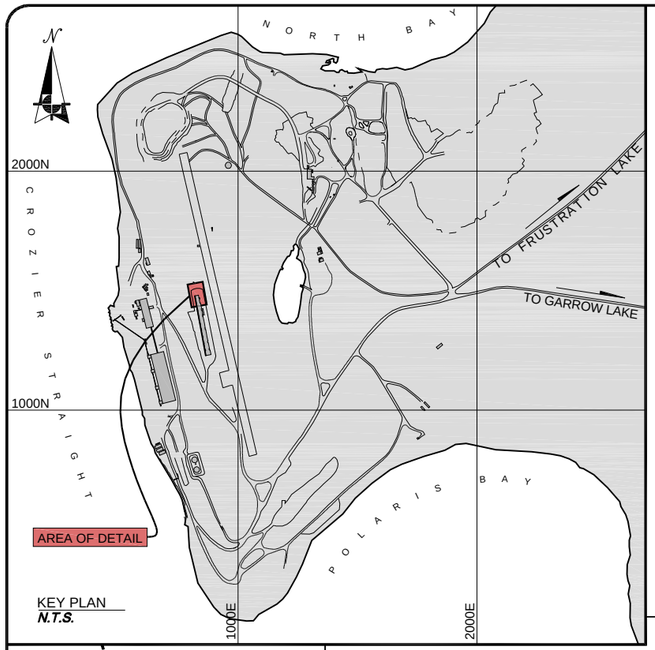

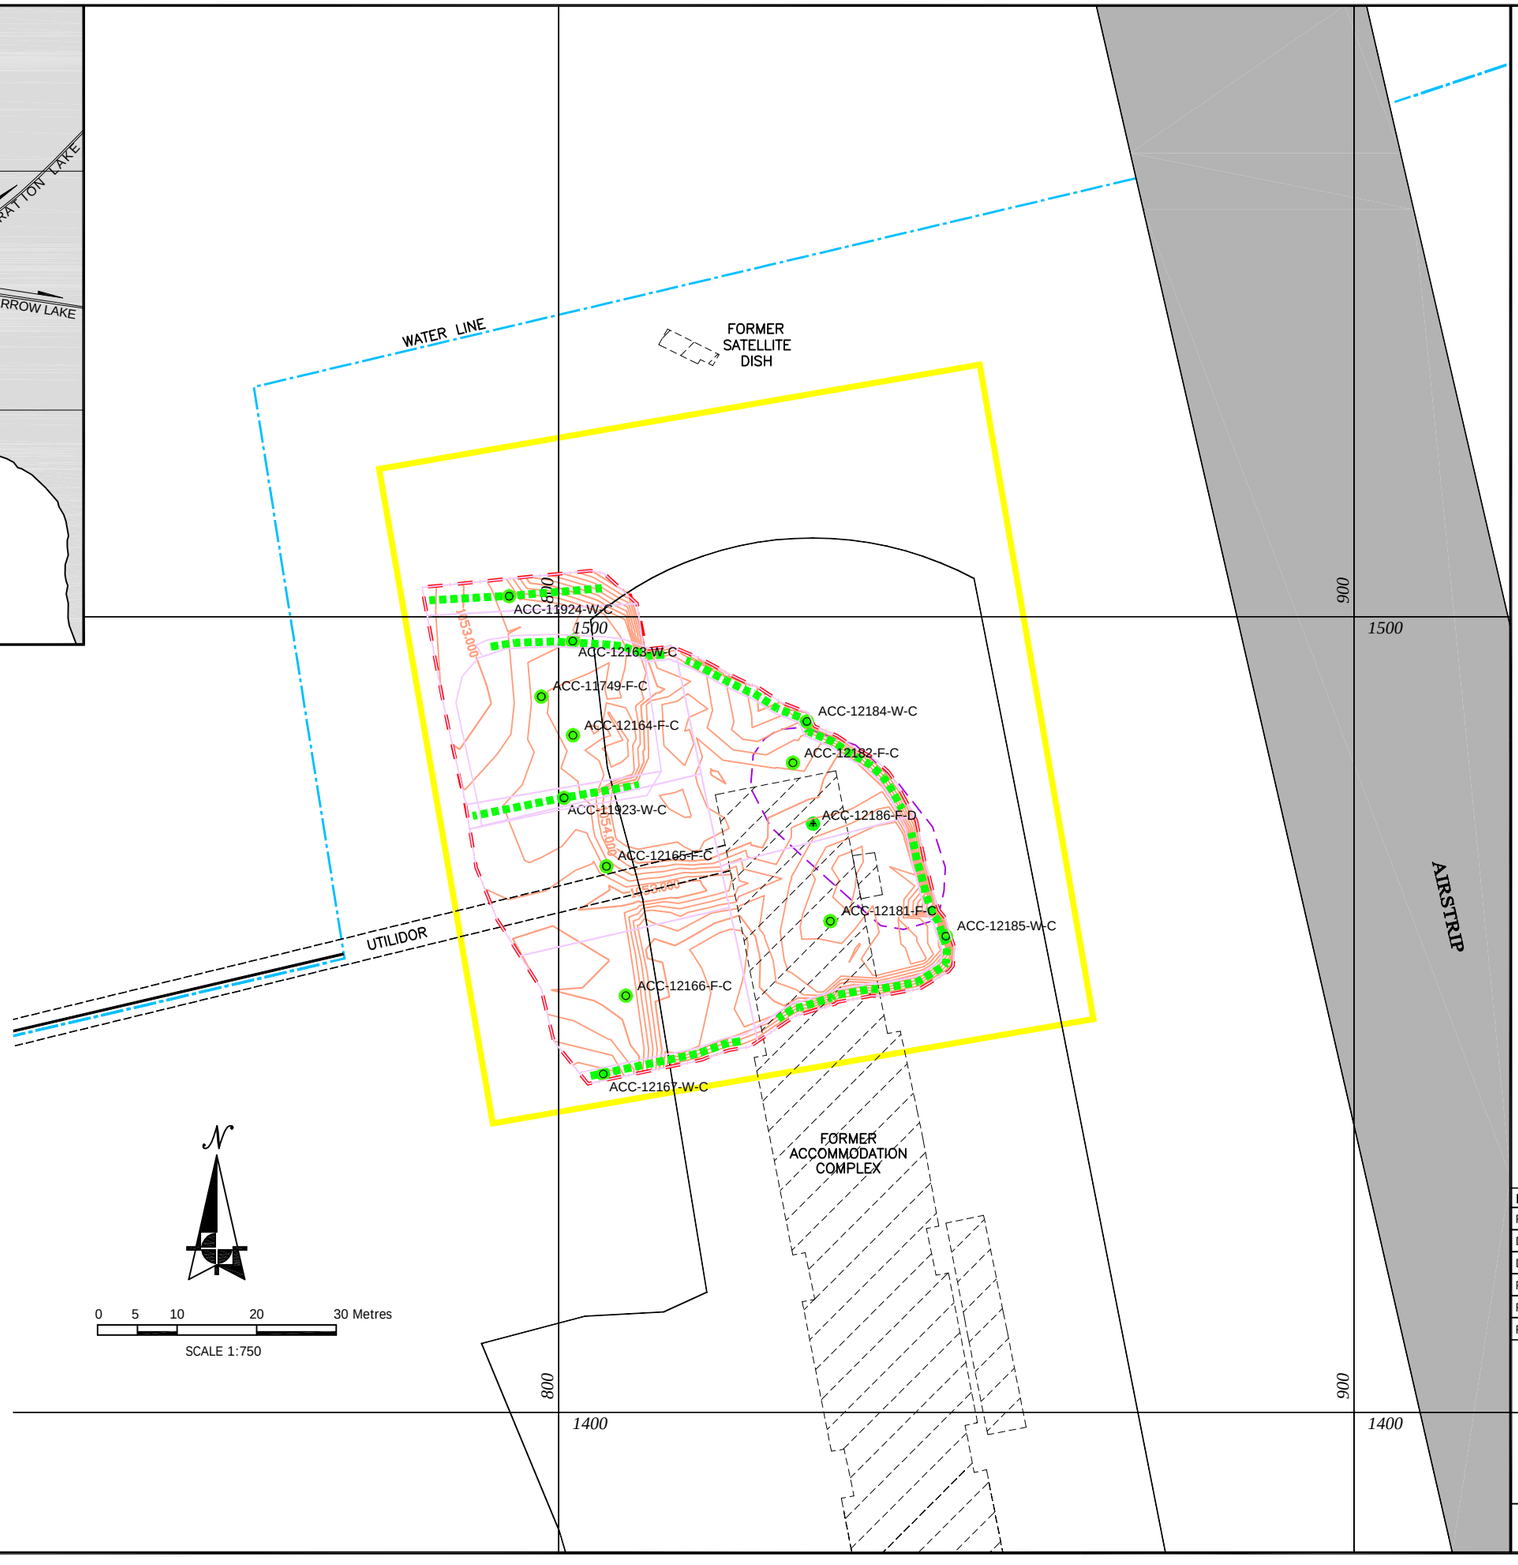

Confirmation Sample ID	EPH C10-C19[a] mg/kg	EPH C19-C32[a] mg/kg	LEPH[a] mg/kg	HEPH[a] mg/kg
ACC-11749-F-C	<200	<200	-	-
ACC-11923-W-C	<200	310	-	-
ACC-11924-W-C	200	320	-	-
ACC-12163 -W-C	290	520	-	-
ACC-12164-F-C	380	780	-	-
ACC-12165-F-C	380	550	-	-
ACC-12166-F-C	380	700	-	-
ACC-12167-W-C	320	620	-	-
ACC-12168-F-Q duplicate of ACC-12164-F-C	280	500	-	-
ACC-12181-F-C	<200	<200	-	-
ACC-12182-F-C	<200	<200	<200	<200
ACC-12183-F-Q duplicate of ACC-12182-F-C	<200	<200	<200	<200
ACC-12184-W-C	<200	340	-	-
ACC-12185-W-C	<200	<200	-	-
ACC-12186-F-D	280	<200	-	-

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

AREA – SAMPLE ID

ESP-7-I-D

TYPE:
- C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL
- D= DISCRETE SAMPLE
- Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE

LOCATION:
- F= FLOOR SAMPLE
- I= INTERMEDIATE FLOOR SAMPLE
- W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–ACC–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

ACCOMMODATION COMPLEX CONDITIONS AFTER REMEDIATION

Gartner Lee

Figure No. ACC-05-2

Appendix D

Foldaway Buildings

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Foldaway Buildings

BACKGROUND

The foldaway buildings were located south of the former concentrate storage shed and to the west of the former fuel tank farm, shown as Area 7 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan , December 31, 2004.*

The foldaway buildings and adjacent temporary dock were some of the first facilities constructed at the Polaris Mine site. During the operation of the mine, the foldaway buildings were used for vehicle storage. During demolition the buildings served as mechanical shops. Fuel and lubricants were stored and handled in this area during the construction, operation and demolition of the mine.

A snow dump, located north of the foldaway buildings, was used during mine operations. The Foldaway Snow Dump area is shown as Area 19 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan , December 31, 2004*. Snow from the south end of the Concentrate Storage Shed and from around the Foldaway Buildings was occasionally deposited into a snow dump in this area.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified petroleum hydrocarbon contamination present in the soil surrounding the foldaway buildings. Soil samples collected from test pits up to 15 m away from the buildings determined that hydrocarbon contamination extended from surface to greater than 1.0 m below ground level. The ESA did not identify hydrocarbon contaminated soil test pits excavated more than 15 m from the buildings.

In the vicinity of the Foldaway Snow Dump, the ESA documented the presence of total lead and zinc concentrations greater than the site-specific Soil Quality Remediation Objectives (SQROs) in one of six sites sampled for metals.

The original topography of the area, sample locations and results, and the preliminary remediation area that was indicated as a concern for either metal and hydrocarbon contamination by the ESA investigations, are shown on Figure FA-07-1: *Foldaway Buildings Conditions Before Remediation*.

METHODOLOGY

Delineation

The preliminary boundaries of the remediation areas, as identified in the ESA as "Areas of Concern", were delineated for excavation on the basis of field screening measurements obtained from twenty-one (21) boreholes drilled and sampled in 2003, and from an additional forty-five (45) boreholes drilled and sampled in 2004. Boreholes were advanced with an air rotary quarry drill and with a mobile rotary drill mounted on an excavator. Composite soil samples were collected over 0.8 m (2.5 feet) intervals to a depth of 6.0 m (20 feet). The soil samples were collected from the drill returns that accumulated at the mouth of the borehole onto a flat metal footplate. Following the collection of each sample the surface of the footplate was cleared of the drill cuttings.

The visual appearance and odour of the soil, along with field screening measurements obtained from the borehole samples were used to delineate the area to be excavated. The hydrocarbon field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. The samples were field screened for metals using the Niton X-ray fluorescence (XRF) elemental analyser. Based on results of the field screening sampling, GLL modified the extent of the area to be excavated as indicated by the "Limit of Remedial Excavation" shown on Figure FA-07-1.

Excavation

Excavation of the soils underlying and surrounding the foldaway buildings occurred from May 28 to July 9, 2004. Due to its proximity to the ocean and foreshore environment, the excavation was completed in two stages. The first stage consisted of demolition of the buildings and removal of soils, while leaving a berm between the ocean and the excavation to limit the interaction with the foreshore environment. An isolated occurrence of liquid petroleum hydrocarbons was encountered at the northeast corner of the foldaway buildings and this product was pumped into barrels and incinerated on site. The second stage was the removal of the berm. The majority of contaminated soils were removed from the footprint of the buildings before excavation of the berm proceeded. The berm was excavated only during periods of low tide.
Total suspended solids (TSS) levels were monitored daily during periods of work in the foreshore along the shoreline at predetermined stations in accordance with approved site procedures and protocols.

Excavators were used to remove materials from the foldaway building area. The first pass on each lift utilised a ripper tooth to break up frozen and compacted ground. The second pass utilised a bucket to scoop up the loose material. Contaminated material was stockpiled on the footprint of the foldaways then loaded into trucks for disposal. To further direct the excavation, soil samples were collected across the floor excavation limits in accordance with standard GLL and TCL sampling procedures and protocols. These samples were field screened using the PID to evaluate hydrocarbon concentrations, and the XRF to evaluate metal concentrations in order to determine where additional excavation was required to meet the SQROs. The northern extent of the Foldaway Snow Dump was not excavated since field screening results indicated the area would meet the SQROs. The limits of the excavation are shown on Figure FA-07-2: *Foldaway Buildings Conditions After Remediation*.

All material excavated was disposed of in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Upon receipt of field screening results that indicated that the material remaining in the excavation would meet the SQRO's, confirmation samples were collected in accordance with Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols. The floor of the excavated area was subdivided into individual composite sampling areas approximately 25 m by 25 m required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation. Composite samples were created by collecting four or five evenly spaced aliquots of soil within the individual composite sample area. A discrete sample is a single aliquot of soil from a specific point and these samples were collected randomly.

The soil samples were collected at the excavation limits and submitted to ALS Environmental (ALS) for analysis of Extractable Petroleum Hydrocarbons (EPH), metals and Polycyclic Aromatic Hydrocarbons (PAH). Additional excavation was undertaken in areas where the laboratory analytical results did not meet the SQRO's and additional confirmatory samples were taken upon completion of the excavation. Upon receipt of analytical results that met the SQROs the final excavation limits were surveyed and the area backfilled to final grade.

ANALYTICAL RESULTS

Analytical laboratory results for EPH, metals and PAH are summarized in Tables FA-07-1, FA-07-2 and FA-07-3 respectively, along with the approved Polaris Mine SQROs for petroleum hydrocarbons and metals. A total of thirty one (31) hydrocarbon and five (5) metals samples were submitted for the foldaway building area. Of the hydrocarbon samples, there were sixteen (16) composite floors, nine (9) composite walls, two (2) discrete walls and four (4) Quality

Assurance/Quality Control (QA/QC) duplicate samples. The five (5) metals samples consisted of four (4) composite floors and one (1) QA/QC duplicate sample. The soil quality results and the lateral limits of the excavation are shown on Figure FA-12-2.

Quality Assurance and Quality Control (QA/QC)

Relative percent differences (RpDs) have been calculated and compiled in Tables FA-07-4 for hydrocarbons and FA-07-5 for metals; two (2) on site field screened duplicates, five (5) analytical laboratory duplicates, three (3) analytical laboratory replicates were compiled for a total of ten (10) QA/QC samples.

Eight (8) of the sample results and their duplicate/replicate results returned results below the Practical Quantitation Limit (PQL) in which case the RpD value has been identified as "n/a" (not applicable). One sample pairing (FA-11758-F-C and FA-11770-F-Q) was prepared as both an on site field screened duplicate and an analytical laboratory duplicate. The on site field screened duplicate RpDs were 19% for Lead and 30% for Zinc, which is below the site specific remediation protocol of 50%. The analytical laboratory duplicate RpD for Zinc was 185%. No RpD for Lead could be calculated since the duplicate results was below the PQL. This sample, FA-11758-F-C, was the one confirmation soil sample that returned concentrations of Lead and Cadmium above the SQROs. The sample duplicate, FA-11700-F-Q returned a result of below the SQRO for Lead.

The variance between the on site field screening results, and the laboratory sample and its duplicate is likely due to sample heterogeneity caused by the presence of zinc concentrate dust in the sample collected outside of the excavation limits. Therefore, the metal QA/QC samples from the Foldaway Buildings area serve to document the variable nature of the metal concentrations in the soil.

Discussion

Thirty one (31) samples were analysed for EPH, of this set, four randomly selected samples were extracted for PAH. All samples analysed for PAH returned values below the SQROs. All of the hydrocarbon remediation confirmation samples returned results below the Polaris mine SQRO's.

Two discrete samples were collected and submitted for laboratory analysis of hydrocarbons along with composite samples collected in the same area and results were as follows:

Summary of Discrete Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	EPH C_{10}-C_{19} (mg/kg)	EPH C_{19}-C_{32} (kg/kg)	Discrete Sample ID	EPH C_{10}-C_{19} (µg/kg)	EPH C_{19}-C_{32} (mg/kg)
FA-11170-W-C	<200	<200	FA-11127-W-D	<200	<200
FA-11145-W-C	330	<200	FA-11206-W-D	270	<200

Total metals analysis was performed on the sample that yielded the highest field screening result, FA-11758-F-C. The sample returned concentrations of Lead (2,290 mg/kg) above the SQRO of 2,000 mg/kg as well as Cadmium concentration (14 mg/kg) above the generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for parkland land use of 10 mg/kg. Cadmium was not identified as a contaminant of concern in the total metal analyses and leachate analyses conducted during the ESA. The approved site-specific remedial objectives allow for minor exceedances in a small percentage (less than 5%) of the confirmatory sample area, so long as the concentration is less than twice the remedial target. The total area of the foldaway building excavation was 6,790 m^2, of that; the sample (FA-11758-F-C) covered an area of 230 m^2. The total area not meeting the SQRO but falling below twice the remedial target in the foldaway area is 3.4%. In addition, given the immobile nature of the Cadmium encountered on site, as demonstrated by the leachate results and the relatively low level of concentrations, no further remedial excavation work is considered necessary to meet the approved closure plan objectives.

The confirmation samples supported by the QA/QC samples from the Foldaway Buildings area provide confidence that the remediation of the foldaway area complies with the SQRO's.

CONCLUSIONS

Based on confirmatory sampling, consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the foldaway building area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:DL:gc

ATTACHMENTS

Tables

Table FA-07-1:	Foldaway Buildings Remediation Confirmation Soil Samples – Hydrocarbons
Table FA-07-2:	Foldaway Buildings Remediation Confirmation Soil Samples – Metals
Table FA-07-3:	Foldaway Buildings Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table FA-07-4:	Foldaway Buildings Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons
Table FA-07-5:	Foldaway Buildings Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure FA-07-1:	Foldaway Buildings Conditions Before Remediation
Figure FA-07-2:	Foldaway Buildings Conditions After Remediation

Table FA-07-1. Foldaway Buildings Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings						
		Sample ID	FA-11127-W-D	FA-11145-W-C	FA-11170-W-C	FA-11173-F-C	FA-11174-F-Q	FA-11206-W-D	FA-11331-F-C
		Date Sampled	June 3, 2004	June 3, 2004	June 4, 2004	June 3, 2004	June 4, 2004	June 2, 2004	June 8, 2004
		ALS File Number	U4269R	U4269R	U4269R	U4269R	duplicate of	U4269R	U4378
		Field Screen (ppm)[b]	30	45	-	-	FA-11173-F-C	40	-
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	330	<200	<200	<200	270	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FA-07-1. Foldaway Buildings Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings						
		Sample ID	FA-11333-W-C	FA-11371-W-Q	FA-11334-F-C	FA-11358-F-C	FA-11365-W-C	FA-11624-F-C	FA-11625-W-C
		Date Sampled	June 9, 2004	June 9, 2004	June 9, 2004	June 10, 2004	June 9, 2004	June 22, 2004	June 22, 2004
		ALS File Number	U4484	duplicate of	U4484	U4484	U4484	U4948	U4948
		Field Screen (ppm)[b]	45	FA-11333-W-C	40	50	45	40	40
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	290	820	<200	<200	240
EPH C_{19}-C_{32}	1000	mg/kg	550	320	300	800	380	<200	390
LEPH[c]	1000	mg/kg	-	-	-	820	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	800	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FA-07-1. Foldaway Buildings Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings						
		Sample ID	FA-11626-W-C	FA-11632-F-C	FA-11689-F-C	FA-11766-F-C	FA-11847-F-C	FA-11745-F-Q	FA-11848-F-C
		Date Sampled	June 22, 2004	June 23, 2004	June 28, 2004	July 7, 2004	July 2, 2004	July 2, 2004	July 2, 2004
		ALS File Number	U4948	U5050	U5223	U5598	U5353R	duplicate of	U5353R
		Field Screen (ppm)[b]	45	15	10	-	5	FA-11847-F-C	10
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	210	<200	<200	250	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	320	280	300	450	340	440	400
LEPH[c]	1000	mg/kg	-	-	-	250	<200	-	-
HEPH[c]	1000	mg/kg	-	-	-	450	340	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FA-07-1. Foldaway Buildings Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings					
		Sample ID	FA-11849-F-C	FA-11850-F-C	FA-11851-F-C	FA-11875-W-C	FA-11876-W-C	FA-11877-W-C
		Date Sampled	July 2, 2004	July 2, 2004	July 2, 2004	July 4, 2004	July 4, 2004	July 4, 2004
		ALS File Number	U5353R	U5353R	U5353R	U5597	U5597	U5597
		Field Screen (ppm)[b]	10	10	5	20	10	15
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	210	240	240	230
EPH C_{19}-C_{32}	1000	mg/kg	360	390	440	450	420	370
LEPH[c]	1000	mg/kg	-	-	-	-	240	-
HEPH[c]	1000	mg/kg	-	-	-	-	420	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FA-07-1. Foldaway Buildings Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings			
		Sample ID	FA-11969-F-C	FA-11970-F-C	FA-11769-F-Q	FA-11971-F-C
		Date Sampled	July 9, 2004	July 9, 2004	July 8, 2004	July 9, 2004
		ALS File Number	U5615R	U5615R	duplicate of	U5615R
		Field Screen (ppm)[b]	25	25	FA-11970-F-C	25
Parameter	**Site Specific**	**Units**	**Analytical Results**			
Extractable Hydrocarbons						
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	230
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	430
LEPH[c]	1000	mg/kg	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FA-07-2. Foldaway Buildings Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Foldaway Buildings				
				Sample ID	FA-11358-F-C	FA-11758-F-C	FA-11770-F-Q	FA-11932-F-C	FA-11969-F-C
				Date Sampled	June 10, 2004	July 12, 2004	July 12, 2004	July 7, 2004	July 9, 2004
				ALS File Number	U4484	U5836	U5836	U5597R	U5615R
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	157	972	duplicate of	98	-
				Field Screen Zn (ppm)[b]	897	6704	FA-11758-F-C	135	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**				
pH		-	-	-	-	8.74	-	-	-
Total Metals									
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	-
Arsenic	T-As	-	12	mg/kg	-	<10	-	-	-
Barium	T-Ba	-	500	mg/kg	-	205	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	**13.7**	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	5	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	<4	-	-	-
Copper	T-Cu	-	63	mg/kg	-	8	-	-	-
Lead	T-Pb	2000	-	mg/kg	850	**2290**	<100	<100	<200
Mercury	T-Hg	-	6.6	mg/kg	-	<0.05	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	<10	-	-	-
Selenium	T-Se	-	1	mg/kg	-	<4	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	<4	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	-
Vanadium	T-V	-	130	mg/kg	-	25	-	-	-
Zinc	T-Zn	10000	-	mg/kg	986	5370	214	50	1480

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FA-07-3. Foldaway Buildings Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Foldaway Buildings			
		Sample ID	FA-11358-F-C	FA-11766-F-C	FA-11847-F-C	FA-11876-W-C
		Date Sampled	June 10, 2004	July 7, 2004	July 2, 2004	July 4, 2004
		ALS File Number	U4484	U5598R	U5353R	U5597
		Field Screen (ppm)[b]	50	-	5	10
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**			
Polycyclic Aromatic Hydrocarbons						
Acenaphthene	-	mg/kg	<0.06	<0.04	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.08	<0.05	<0.06
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	0.07	<0.05	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	<0.4	<0.05	<0.05	<0.05
Phenanthrene	5[d]	mg/kg	<0.05	0.167	<0.05	0.139
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline include: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FA-07-4. Foldaway Buildings Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Foldaway Buildings						
					Analytical Laboratory Duplicates				Analytical Laboratory Replicates		
				Sample ID	FA-11173-F-C	FA-11333-W-C	FA-11847-F-C	FA-11970-F-C	FA-11173-F-C	FA-11850-F-C	FA-11875-W-C
				Duplicate ID	FA-11174-F-Q	FA-11371-W-Q	FA-11745-F-Q	FA-11769-F-Q	QC#389861	QC#394457	QC#395246
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**				**Analytical Results**		
Extractable Hydrocarbons											
EPH C_{10}-C_{19}											
Sample Result	mg/kg	200	1000		<200	<200	<200	<200	<200	<200	240
Duplicate Result	mg/kg	200	1000		<200	<200	<200	<200	<200	220	300
RpD	**%**				na	na	na	na	na	na	22%
EPH C_{19}-C_{32}											
Sample Result	mg/kg	200	1000		<200	550	340	<200	<200	390	450
Duplicate Result	mg/kg	200	1000		<200	<200	<200	<200	<200	450	510
RpD	**%**				na	na	na	na	na	14%	12%

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table FA-07-5. Foldaway Buildings Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee			Location	Foldaway Buildings	
			Sample ID	FA-11932-F-C	FA-11758-F-C
			Duplicate ID	FA-11792-F-Q	FA-11770-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**	
On Site Field Screening Duplicates					
Lead (Pb)					
Sample Result	mg/kg	20	100	86	972
Duplicate Result	mg/kg	20	100	61	807
RpD	%			na	19%
Zinc (Zn)					
Sample Result	mg/kg	60	300	<60	6704
Duplicate Result	mg/kg	60	300	<60	4978
RpD	%			na	30%
Analytical Laboratory Duplicates					
Lead (Pb)					
Sample Result	mg/kg	100	500	-	2290
Duplicate Result	mg/kg	100	500	-	<100
RpD	%				na
Zinc (Zn)					
Sample Result	mg/kg	3	15	-	5370
Duplicate Result	mg/kg	3	15	-	214
RpD	%				**185%**

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

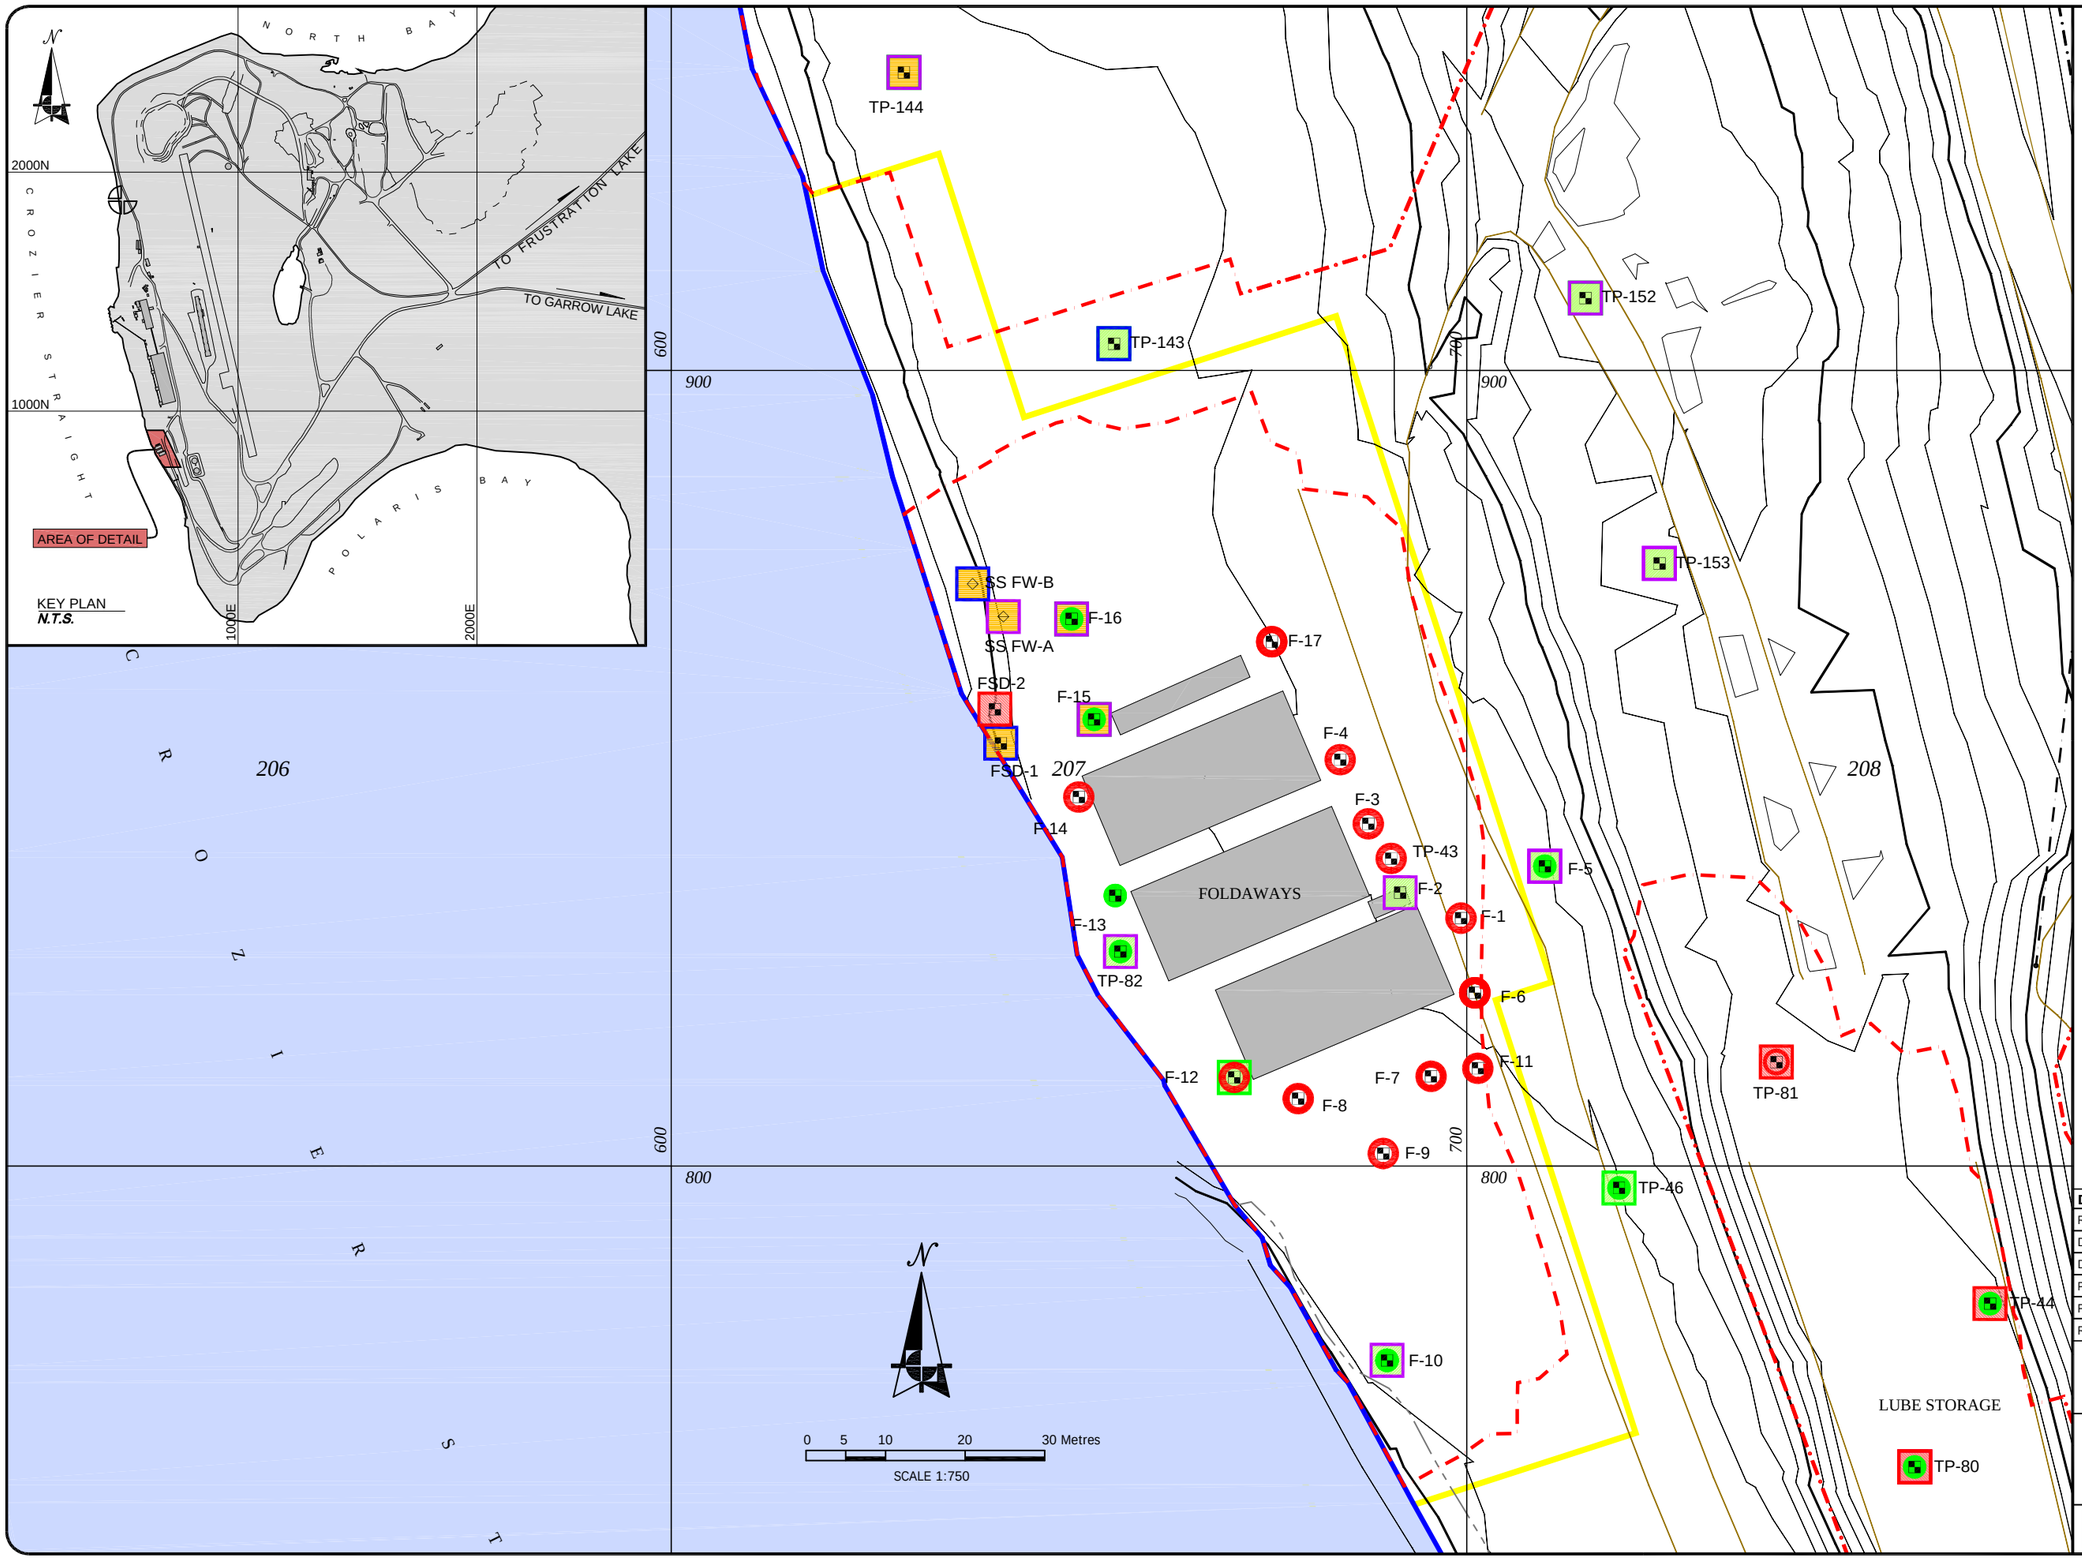

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–FA–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

FOLDAWAY BUILDINGS CONDITIONS BEFORE REMEDIATION

Gartner Lee

Figure No. **FA-07-1**

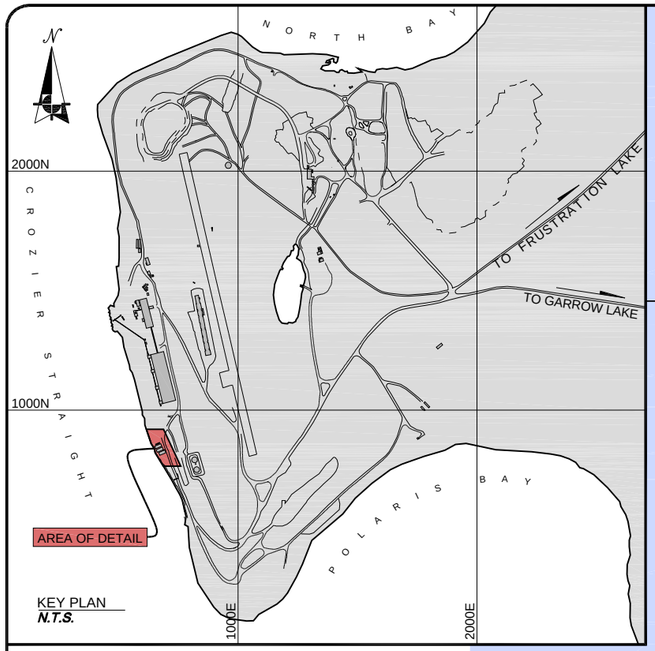

KEY PLAN
N.T.S.


Confirmation Sample ID	EPH C10-C19 mg/kg	EPH C19-C32 mg/kg
FA-11127-W-D	<200	<200
FA-11145-W-C	330	<200
FA-11170-W-C	<200	<200
FA-11173-F-C	<200	<200
FA-11174-F-Q duplicate of FA-11173-F-C	<200	<200
FA-11206-W-D	270	<200
FA-11331-F-C	<200	<200
FA-11333-W-C	<200	550
FA-11371-W-Q duplicate of FA-11333-W-C	<200	320
FA-11334-F-C	290	300
FA-11358-F-C	820	800
FA-11365-W-C	<200	380
FA-11624-F-C	<200	<200
FA-11625-W-C	240	390
FA-11626-W-C	210	320
FA-11632-F-C	<200	280
FA-11689-F-C	<200	300
FA-11766-F-C	250	450
FA-11847-F-C	<200	340
FA-11745-F-Q duplicate of FA-11847-F-C	<200	440
FA-11848-F-C	<200	400
FA-11849-F-C	<200	360
FA-11850-F-C	<200	390
FA-11851-F-C	210	440
FA-11875-W-C	240	450
FA-11876-W-C	240	420
FA-11877-W-C	230	370
FA-11969-F-C	<200	<200
FA-11970-F-C	<200	<200
FA-11769-F-Q duplicate of FA-11970-F-C	<200	<200
FA-11971-F-C	230	430

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
FA-11358-F-C	850	986
FA-11758-F-C	**2290**	5370
FA-11770-F-Q duplicate of FA-11758-F-C	<100	214
FA-11932-F-C	<100	50
FA-11969-F-C	<200	1480

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

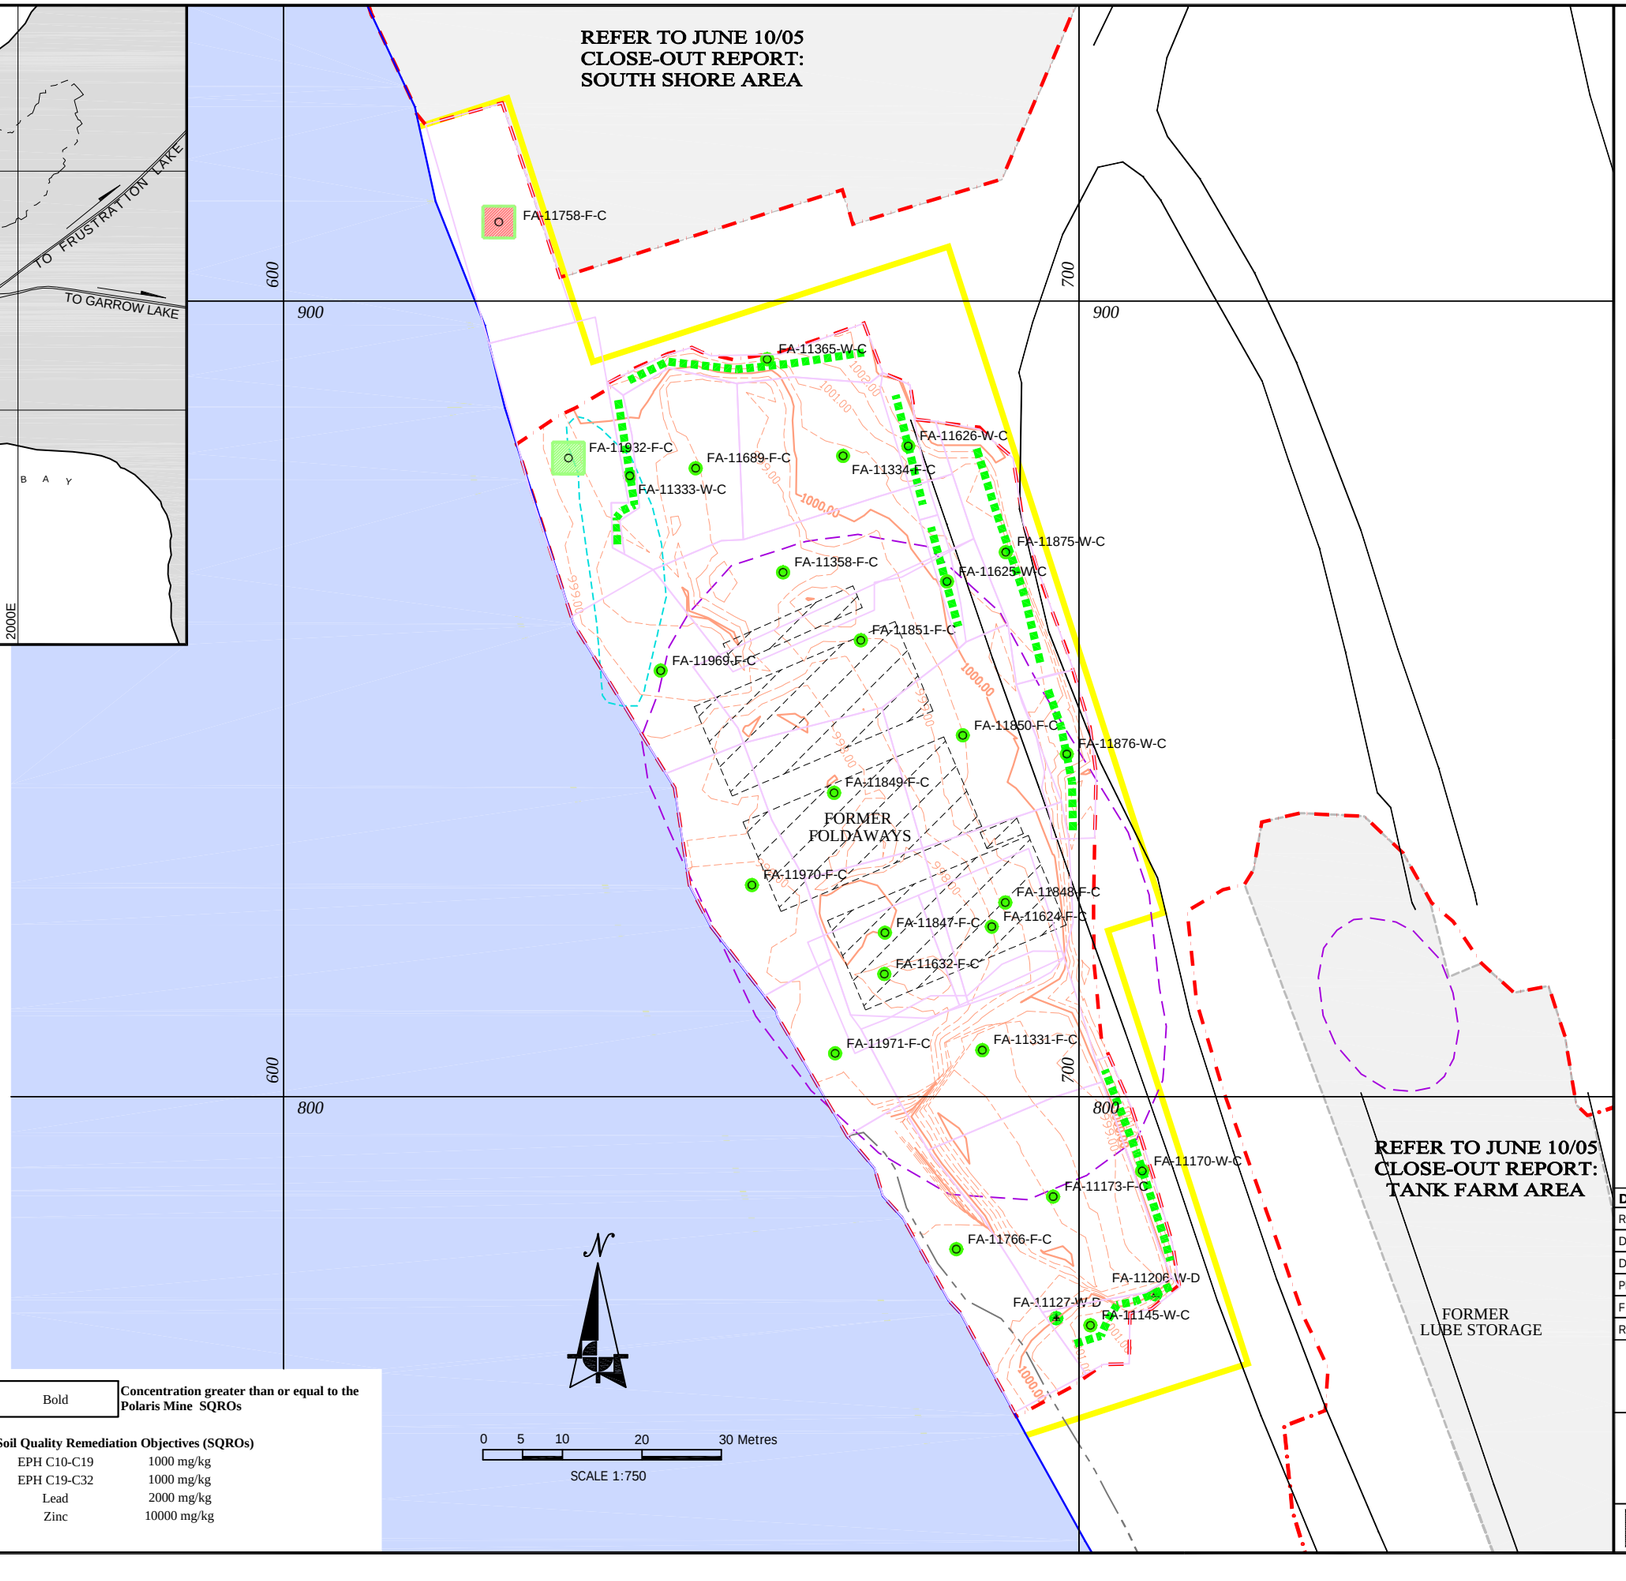

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

AREA – SAMPLE ID
ESP–7–I–D
TYPE:
C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL
D= DISCRETE SAMPLE
Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
LOCATION:
F= FLOOR SAMPLE
I= INTERMEDIATE FLOOR SAMPLE
W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- *EPH – EXTRACTABLE PETROLEUM HYDROCARBONS
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–FA–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

FOLDAWAY BUILDINGS CONDITIONS AFTER REMEDIATION

Gartner Lee

Figure No.
FA-07-2

Appendix E

Tank Farm and Lube Oil Storage

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Tank Farm and Lube Oil Storage

BACKGROUND

The fuel tank farm and lube oil storage area were located to the south of the former concentrate storage shed (shown as Area 8 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*).

The fuel tank farm consisted of two above-ground steel tanks, each with a capacity of 5.5 million litres and one small tank with a capacity of 100,000 litres. The two large tanks had been used to store P20 and P60 diesel fuel. The small tank was originally used to store gasoline, but at the time of the decommissioning it contained the remains of the crude oil (from Bent Horn Island) used in a generator trial in the late 1980's. All tanks were located within a bermed area lined with an impermeable membrane.

The lube oil storage pad was located west of the tank farm. Hydraulic and lube oils used for stationary, mobile and power generation equipment were stored here. The solvent Varsol was also stored here. The oils and solvents were delivered in 205 litre drums, and the hydraulic and grease were stored in kegs or tubes. All of these items were stored on pallets. An incinerator was constructed at the south end of the pad during reclamation activities.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified hydrocarbon and metal contamination in the soil at the lube oil storage area. Nine (9) test pits were excavated during the ESA. The sample results indicated that elevated metal concentrations were present to at least 0.6 m below surface (maximum depth of test pits) on the north half of the lube oil storage pad. No elevated metal concentrations were detected on the south half of the pad. Hydrocarbon contamination was encountered in one test pit and it was limited to the upper 0.3 m. No samples were collected from within the fuel tank farm area during the ESA. The sample locations and an indication of results are shown on Figure TF-08-1: *Tank Farm Conditions Before Remediation.*

METHODOLOGY

Delineation

The preliminary area to be remediated, as identified in the ESA as an "Area of Concern", was further delineated for excavation through the collection and analysis of field screening samples from five (5) boreholes drilled in 2003 and eleven (11) boreholes drilled in 2004 The boreholes were advanced with an air rotary quarry drill. The boreholes were drilled to a depth of 3 m. A total of seventy (70) composite samples were collected from the drill returns that accumulated at the mouth of the boreholes. The composite samples were collected over 0.6 m to 0.75 m intervals. Following the collection of each sample the surface surrounding the borehole was cleared of the drill cuttings, before advancing the hole to collect the next sample.

The visual appearance and odour of the soil, along with field screening measurements obtained from the borehole samples were used to delineate the area to be excavated. The hydrocarbon field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. The samples were field screened for metals using the Niton X-ray fluorescence (XRF) elemental analyser.

The results from the drilling indicated a second area of hydrocarbon contamination at the south end of the pad to a depth of 3.0 m along with metal contamination.

There was no formal delineation attempted at the tank farm location. The lined berm was expected to be in good condition, thus creating a continuous barrier to the migration of hydrocarbon contamination.

Excavation

Excavation of the contaminated soils at the Lube Oil Storage area commenced on May 1, 2004 and it was completed on August 30, 2004. In the spring of 2004 the contaminated soil at the north end of the pad was drilled and blasted while the surface was frozen. The drilling and blasting program was guided by the field screening results from the boreholes drilled in 2003 and 2004. Following the blasting and removal of contaminated material the floor and walls of the excavation were sampled to determine where additional excavation was required to meet the Soil Quality Remediation Objectives (SQRO's). The excavator with a ripper attachment was used to expand the excavation further where required.

The contaminated soil at the south end of the Lube Oil Storage pad and at the Tank Farm was removed during July and August 2004, following the decommissioning of the incinerator building and fuel tanks. Contaminated soil here was ripped and loaded out into trucks with an excavator and the liner in the fuel tank farm removed. Gartner Lee Limited (GLL) was demobilized from site August 28, 2004 prior to the completion of the excavation activities and Teck Cominco Limited (TCL) directed the final two days of excavation of these areas.

The limits of the excavation are shown on Figure TF-08-2: *Tank Farm Area Conditions After Remediation*. The material excavated was disposed in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Upon receipt of field screening results that indicated that the material remaining in the excavation would meet the SQRO's, confirmation samples were collected in accordance with Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols. The floor of the excavated area was subdivided into individual composite sampling areas approximately 25 m by 25 m required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation. Composite samples were created by collecting four or five evenly spaced aliquots of soil within the individual composite sample area. A discrete sample is a single aliquot of soil from a specific point and these samples were collected randomly.

The soil samples were collected at the excavation limits and submitted to ALS Environmental (ALS) for analysis of Extractable Petroleum Hydrocarbons (EPH), metals and Polycyclic Aromatic Hydrocarbons (PAH). Additional excavation was undertaken in areas where the laboratory analytical results did not meet the SQRO's and additional confirmatory samples were taken upon completion of the excavation.

ANALYTICAL RESULTS

Analytical laboratory results for EPH, metals and PAH are summarized in Tables: TF-08-1, TF-08-2, and TF-08-3 along with the approved Polaris Mine SQRO's for petroleum hydrocarbons and metals. Twenty two (22) hydrocarbon and twenty two (22) metal remediation confirmation samples were submitted from the former Fuel Tank Farm and Lube Oil Storage area. The hydrocarbon samples were analyzed as follows: eleven (11) floor composite samples, eight (8) wall composite samples, and three (3) quality assurance quality control (QA/QC) samples. All hydrocarbon confirmatory samples were analyzed for EPH, and five (5) of these samples were also analyzed for PAH. The metal samples were analyzed for Lead and Zinc as follows: eight (8) floor composite samples, six (6) wall composite samples, four (4) discrete samples and four (4) quality assurance quality control (QA/QC) samples. Seven (7) randomly selected samples were analyzed for total metals. The soils quality results and the lateral limits of the excavation are shown on Figure TF-08-2.

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with the collection and analysis of soil included: the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical laboratory replicates. Relative percent differences (RpDs) for hydrocarbon concentrations of EPH C_{10}-C_{19} and EPH C_{19}-C_{32} have been calculated and compiled

in Table: TF-08-4 for three (3) analytical laboratory duplicates and one (1) analytical laboratory replicates. RpDs for concentrations of Lead and Zinc have been calculated and compiled in Table: TF-08-5 for four (4) field screening duplicates, four (4) laboratory duplicates and one (1) laboratory replicates. In total thirteen (13) QA/QC sample sets have been evaluated, including nine (9) remediation confirmation sample sets.

Eleven (11) of the sample results and their duplicate/replicate results either returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not applicable) or they returned acceptable RpDs below the site specific objective of 50%. Two analytical laboratory duplicates returned results greater than the objective and therefore require further explanation and discussion.

The variance between Zinc concentration in sample TF-12196-W-C (7,210 mg/kg) and its blind duplicate, TF-12197-W-Q (12,000 mg/kg) and the Lead concentration in sample TF-12198-F-C (2,074 mg/kg) and its blind duplicate, TF-12190-F-Q (4,630 mg/kg) is considered indicative of the heterogeneity present at the Polaris Mine Site.

Polaris Mine Soil Quality Remediation Objectives

All of the twenty two (22) hydrocarbon remediation confirmation samples returned results below the Polaris Mines SQRO's for EPH.

Fourteen (14) of the twenty two (22) metals remediation confirmation samples returned results that met the Polaris Mine SQRO's for Lead (2000 mg/kg) and Zinc (10000 mg/kg). Five of the samples that returned results greater than the SQROs were part of QA/QC sample sets. One sample (TF-12190-F-Q) that returned results greater than the SQROs, included Lead concentrations greater than two times the SQRO, was part of a triplicate QA/QC sample set (including TF-12198-F-C and TF-12199-F-Q). One of the triplicate QA/QC samples, TF-12199-F-Q returned Lead concentrations (1616 mg/kg) that met the SQROs and the other triplicate QA/QC sample TF-12198-F-C returned Lead concentrations (2074 mg/kg) slightly above the SQRO for Lead. The average Lead concentration of the triplicate sample set was 2773 mg/kg. A second sample (TF-12197-W-Q) that returned Lead and Zinc concentrations greater than the SQROs was part of a duplicate sample set. Lead and Zinc results of the duplicate QA/QC sample (TF-12196-W-C) met the SQROs. Both duplicate QA/QC samples TF-12194-W-C and TF-12195-W-Q returned Lead concentrations greater than the SQROs. Two discrete samples (TF-10895-W-D, TF-12192-F-D) that returned Lead results greater than the SQRO were collected in composite sample areas that met the SQRO's.

The approved site-specific remedial objectives allow for minor exceedances in a small percentage of the confirmatory sample area, as long as the concentration is less than twice the remedial target. Since only a small percentage of the remedial area exceeds the SQROs for Lead and Zinc and given that the area with Lead concentrations greater than two times the remedial target was part of a triplicate QA/QC sample set with results that met the objectives for the former Tank

Farm and Lube Oil Storage area is therefore consider that the overall results for the site are in accordance with the site specific remedial objectives.

Discrete samples were collected to discern the homogeneity of the sample area represented by the composite samples. The tables below show a variability in the metal concentrations of the discrete samples versus the composite areas they represented as the composite samples represent the area as a whole and the discrete samples indicate the homogeneity of the given sample areas at the Polaris Mine.

Summary of Discrete Metals Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	Lead (mg/kg)	Zinc (mg/kg)	Discrete Sample ID	Lead (mg/kg)	Zinc (mg/kg)
TF-10959-F-C	600	3130	TF-10883-F-D	980	494
TF-10960-F-C	550	5770	TF-10889-F-D	1330	920
TF-10961-F-C	1780	6630	TF-10895-W-D	**2520**	9350
TF-12191-F-C	1530	7110	TF-12192-F-D	**2630**	7760

Generic Federal Soil Quality Guidelines for Parkland Land Use

The concentrations of Barium ranged from 245 mg/kg to 533 mg/kg in the seven remediation confirmation samples analysed for total metals. The generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for Parkland land use for Barium in soil is 500 mg/kg. One of the samples exceeded this generic objective |(TF-10926-W-C). The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone. Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results*, are considered to be representative of background conditions. This sampling program included the collection of samples at the following intervals: surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of Barium greater than generic CCME CEQG for Parkland land use were detected in each interval. The variability of Barium concentrations in those samples is listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

In addition, the immobile nature of the Barium encountered on site was demonstrated in the ESA leachate test results that returned Barium concentrations at levels less than the detection limit of <3 mg/L and Barium was therefore not identified as a contaminant of concern in the ESA.

The concentrations of Cadmium ranged from 6.6 mg/kg to 29.4 mg/kg in the seven remediation confirmation samples from the Fuel Tank and Lube Oil Storage area analysed for total metals. Cadmium results for six samples (TF-10895-W-D, TF-10926-W-C, TF-10960-F-C, TF-12194-W-C, TF-12195-W-Q and TF-12190-F-Q) exceeded the CCME CEQG for Parkland land use of 10 mg/kg Cadmium in soil. Cadmium was not identified as a contaminant of concern based on the total metal analyses and leachate test results conducted during the ESA. Given the immobile nature of the Cadmium encountered on site, as demonstrated by the leachate results and the level of concentrations being less than twice the generic CCME CEQG for Parkland land use, no further remedial excavation work is considered necessary.

CONCLUSIONS

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former Fuel Tank Farm and Lube Oil Storage area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Limited during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Brenda Bolton, B.A., B.Sc.
Environmental Geologist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

Alistair Kent, P.Eng.
Senior Reviewer

AL:BB:AK:gc

ATTACHMENTS

Tables

Table TF-08-1:	Tank Farm Remediation Confirmation Soil Samples – Hydrocarbons
Table TF-08-2:	Tank Farm Remediation Confirmation Soil Samples – Metals
Table TF-08-3:	Tank Farm Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table TF-08-4:	Tank Farm Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons
Table TF-08-5:	Tank Farm Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure TF-08-1:	Tank Farm Conditions Before Remediation
Figure TF-08-2:	Tank Farm Conditions After Remediation

Table TF-08-1. Tank Farm Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Tank Farm							
		Sample ID	TF-10494-F-C	TF-10495-F-C	TF-10663-F-C	TF-10826-W-C	TF-12168-F-C	TF-12178-F-Q	TF-12169-F-C	TF-12170-F-C
		Date Sampled	06-May-04	07-May-04	18-May-04	25-May-04	27-Aug-04	27-Aug-04	27-Aug-04	27-Aug-04
		ALS File Number	U3342	U3342	U3761	U3969r	U7584(1)	duplicate of	U7584(1)	U7584(1)
		Field Screen (ppm)[b]	-	-	-	70	10	TF-12168-F-C	10	10
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	240	290	260	230	320
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	470	450	440	550
LEPH[c]	1000	mg/kg	-	-	-	240	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	<200	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table TF-08-1. Tank Farm Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Tank Farm						
		Sample ID	TF-12171-F-C	TF-12172-F-C	TF-12173-F-C	TF-12174-F-C	TF-12175-W-C	TF-12176-W-C	TF-12177-W-C
		Date Sampled	27-Aug-04	27-Aug-04	27-Aug-04	27-Aug-04	27-Aug-04	27-Aug-04	27-Aug-04
		ALS File Number	U7584(1)	U7584(1)	U7584(1)	U7584(1)	U7584(1)	U7584(1)	U7584(1)
		Field Screen (ppm)[b]	10	15	15	15	15	-	15
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	320	320	300	280	300	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	550	540	490	490	510	220	250
LEPH[c]	1000	mg/kg	-	-	-	-	-	<200	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	220	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table TF-08-1. Tank Farm Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Tank Farm						
		Sample ID	TF-12187-F-C	TF-12188-W-C	TF-12189-W-C	TF-12194-W-C	TF-12195-W-Q	TF-12196-W-C	TF-12197-W-Q
		Date Sampled	29-Aug-04	29-Aug-04	29-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04
		ALS File Number	U7700	U7700	U7700	U7700	duplicate of	U7700(1)rr	duplicate of
		Field Screen (ppm)[b]	-	-	-	-	TF-12194-W-C	-	TF-12196-W-C
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	870	<200	930	<200	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	380	220	360	210	<200	240	<200
LEPH[c]	1000	mg/kg	-	-	-	-	<200	<200	<200
HEPH[c]	1000	mg/kg	-	-	-	-	<200	200	<200

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table TF-08-2. Tank Farm Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Tank Farm							
				Sample ID	TF-10494-F-C	TF-10495-F-C	TF-10663-F-C	TF-10826-W-C	TF-10883-F-D	TF-10889-F-D	TF-10895-W-D	TF-10926-W-C
				Date Sampled	06-May-04	07-May-04	18-May-04	25-May-04	27-May-04	27-May-04	28-May-04	28-May-04
				ALS File Number	U3342	U3342	U3761	U3969r	U4504	U4504	U4054	U4054
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	972	807	98	842	410	392	946	388
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	6704	4978	135	1327	445	1679	6447	2058
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH								8.28			7.98	8.88
Total Metals												.
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	-	-	<20	<20
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	-	-	<10	<10
Barium	T-Ba	-	500	mg/kg	-	-	-	347	-	-	252	**533**
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1.0	-	-	<1.0	<1.0
Cadmium	T-Cd	-	10	mg/kg	-	-	-	6.6	-	-	**29.4**	**27**
Chromium	T-Cr	-	64	mg/kg	-	-	-	9.3	-	-	6.3	6.2
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4.0	-	-	<4.0	<4.0
Copper	T-Cu	-	63	mg/kg	-	-	-	15.4	-	-	6.6	11.1
Lead	T-Pb	2000	-	mg/kg	1380	<150	<100	460	980	1330	**2520**	510
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	<0.050	-	-	<0.050	<0.050
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8.0	-	-	<8.0	<8.0
Nickel	T-Ni	-	50	mg/kg	-	-	-	<10	-	-	<10	<10
Selenium	T-Se	-	1	mg/kg	-	-	-	<4.0	-	-	<4.0	<4.0
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4.0	-	-	<4.0	<4.0
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	-	-	<10	<10
Vanadium	T-V	-	130	mg/kg	-	-	-	22.2	-	-	21.8	27.1
Zinc	T-Zn	10000	-	mg/kg	6170	84	212	2620	494	920	9350	3310

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TF-08-2. Tank Farm Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Tank Farm							
				Sample ID	TF-10959-F-C	TF-10960-F-C	TF-10961-W-C	TF-11302-F-C	TF-12191-F-C	TF-12192-F-D	TF-12193-W-C	TF-12194-W-C
				Date Sampled	27-May-04	27-May-04	27-May-04	31-May-04	30-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04
				ALS File Number	U4054	U4054	U4054	U4137	U7700	U7700	U7700	U7700
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	254	881	969	-	-	1563	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	1994	6649	6773	-	-	4944	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH						8.99						8.40
Total Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	-	-	-	<20
Arsenic	T-As	-	12	mg/kg	-	<10	-	-	-	-	-	<10
Barium	T-Ba	-	500	mg/kg	-	317	-	-	-	-	-	251
Beryllium	T-Be	-	4[d]	mg/kg	-	<1.0	-	-	-	-	-	<1.0
Cadmium	T-Cd	-	10	mg/kg	-	**19**	-	-	-	-	-	**28.1**
Chromium	T-Cr	-	64	mg/kg	-	4.6	-	-	-	-	-	7.1
Cobalt	T-Co	-	50[d]	mg/kg	-	<4.0	-	-	-	-	-	<4.0
Copper	T-Cu	-	63	mg/kg	-	5.8	-	-	-	-	-	11.3
Lead	T-Pb	2000	-	mg/kg	600	550	1780	1440	1530	**2630**	**2000**	**2360**
Mercury	T-Hg	-	6.6	mg/kg	-	<0.050	-	-	-	-	-	<0.050
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8.0	-	-	-	-	-	<8.0
Nickel	T-Ni	-	50	mg/kg	-	<10	-	-	-	-	-	14
Selenium	T-Se	-	1	mg/kg	-	<4.0	-	-	-	-	-	<10.0
Silver	T-Ag	-	20[d]	mg/kg	-	<4.0	-	-	-	-	-	<4.0
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	-	-	-	<10
Vanadium	T-V	-	130	mg/kg	-	25.5	-	-	-	-	-	27.5
Zinc	T-Zn	10000	-	mg/kg	3130	5770	6630	5280	7110	7760	8580	8230

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TF-08-2. Tank Farm Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Tank Farm					
				Sample ID	TF-12195-W-Q	TF-12196-W-C	TF-12197-W-Q	TF-12198-F-C	TF-12190-F-Q	TF-12199-F-Q
				Date Sampled	30-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04	30-Aug-04
				ALS File Number	U7700	U7700	U7700	U7700	U7700	U7700
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	duplicate of	-	duplicate of	-	duplicate of	duplicate of
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	TF-12194-W-C	-	TF-12196-W-C	-	TF-12198-F-C	TF-12198-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH					8.46				8.42	
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	<10	-	-	-	<10	-
Barium	T-Ba	-	500	mg/kg	249	-	-	-	245	-
Beryllium	T-Be	-	4[d]	mg/kg	<1.0	-	-	-	<1.0	-
Cadmium	T-Cd	-	10	mg/kg	**28.5**	-	-	-	**26.8**	-
Chromium	T-Cr	-	64	mg/kg	6.3	-	-	-	6.6	-
Cobalt	T-Co	-	50[d]	mg/kg	<4.0	-	-	-	<4.0	-
Copper	T-Cu	-	63	mg/kg	13.6	-	-	-	10.6	-
Lead	T-Pb	2000	-	mg/kg	**2680**	1490	**2020**	**2074**	**4630**	1616
Mercury	T-Hg	-	6.6	mg/kg	<0.050	-	-	-	<0.050	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8.0	-	-	-	<8.0	-
Nickel	T-Ni	-	50	mg/kg	13	-	-	-	14	-
Selenium	T-Se	-	1	mg/kg	<5.0	-	-	-	<4.0	-
Silver	T-Ag	-	20[d]	mg/kg	<4.0	-	-	-	<4.0	-
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	28.6	-	-	-	28.2	-
Zinc	T-Zn	10000	-	mg/kg	8190	7210	**12000**	7807	7820	5690

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TF-08-3. Tank Farm Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location Sample ID Date Sampled ALS File Number Field Screen (ppm)[b]	Tank Farm TF-10826-W-C 25-May-04 U3969r 70	 TF-12176-W-C 27-Aug-04 U7584(1) -	 TF-12195-W-C 30-Aug-04 U7700 -	 TF-12196-W-C 30-Aug-04 U7700 -	 TF-12197-W-Q 30-Aug-04 duplicate of TF-12196-W-C
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**				
Polycyclic Aromatic Hydrocarbons							
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.04	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TF-08-4. Tank Farm Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Tank Farm			
				Sample ID	TF-12168-F-C	TF-12194-W-C	TF-12196-W-C	TF-12171-F-C
				Duplicate ID	TF-12178-F-Q	TF-12195-W-Q	TF-12197-W-Q	QC# 403990
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**			
Analytical Laboratory Duplicates								
EPH C_{10}-C_{19}								
Sample Result	mg/kg	200	1000		290	<200	<200	-
Duplicate Result	mg/kg	200	1000		260	<200	<200	-
RpD	**%**				na	na	na	
EPH C_{19}-C_{32}								
Sample Result	mg/kg	200	1000		470	210	<200	-
Duplicate Result	mg/kg	200	1000		450	240	<200	-
RpD	**%**				na	na	na	
Analytical Laboratory Replicates								
EPH C_{10}-C_{19}								
Sample Result	mg/kg	200	1000		-	-	-	320
Duplicate Result	mg/kg	200	1000		-	-	-	330
RpD	**%**							na
EPH C_{19}-C_{32}								
Sample Result	mg/kg	200	1000		-	-	-	550
Duplicate Result	mg/kg	200	1000		-	-	-	550
RpD	**%**							na

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table TF-08-5. Tank Farm Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee	Location	Tank Farm								
	Sample ID	TF-10883-F-D	TF-12129-W-D	TF-12130-W-D	TF-12131-W-D	TF-12132-W-D	TF-12194-W-C	TF-12196-W-C	TF-12198-F-C	TF-12198-F-C
	Duplicate ID	U4054r	TF-12353-W-Q	TF-12354-W-Q	TF-12355-W-Q	TF-12356-W-Q	TF-12195-W-Q	TF-12197-W-Q	TF-12190-F-Q	TF-12199-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**						
On Site Field Screening Duplicates										
Lead (Pb)										
Sample Result	mg/kg	70	350	-	2851	739	2510	8314	-	-	-	-
Duplicate Result	mg/kg	70	350	-	2323	834	1945	8458	-	-	-	-
RpD	%				20%	12%	25%	2%				
Zinc (Zn)									-	-	-
Sample Result	mg/kg	150	750	-	18429	5421	10978	44636	-	-	-	-
Duplicate Result	mg/kg	150	750	-	16974	8908	10250	46915	-	-	-	-
RpD	%				8%	49%	7%	5%				
Analytical Laboratory Duplicates										
Lead (Pb)										
Sample Result	mg/kg	100	500	-	-	-	-	-	2360	1490	2074	2074
Duplicate Result	mg/kg	100	500	-	-	-	-	-	2680	2020	4630	1616
RpD	%								13%	30%	**76%**	25%
Zinc (Zn)												
Sample Result	mg/kg	3	15	-	-	-	-	-	8230	7210	7807	7807
Duplicate Result	mg/kg	3	15	-	-	-	-	-	8190	12000	7820	5690
RpD	%								0%	**50%**	0%	31%
Analytical Laboratory Replicates										
Lead (Pb)										
Sample Result	mg/kg	100	500	980	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	400	-	-	-	-	-	-	-	-
RpD	%			na								
Zinc (Zn)												
Sample Result	mg/kg	3	15	494	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15	342	-	-	-	-	-	-	-	-
RpD	%			36%								

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.


*RpD Relative Percent Difference = (Difference/Average)*100.*


*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

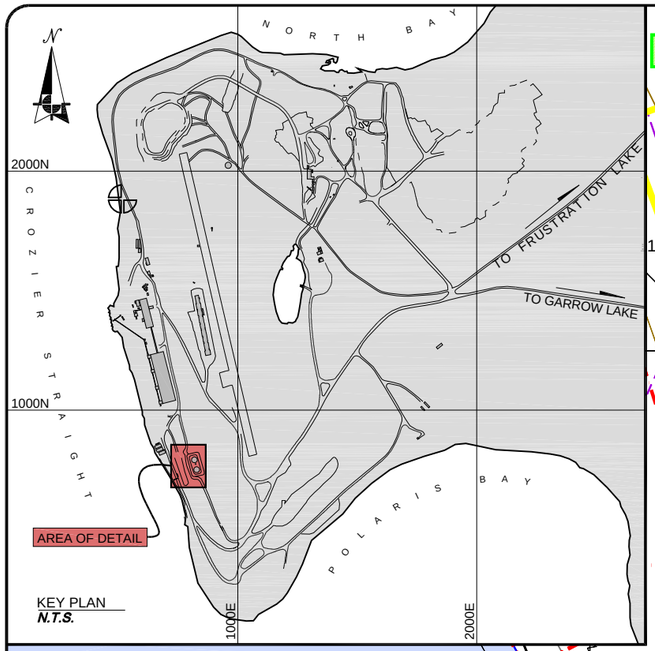

KEY PLAN
N.T.S.

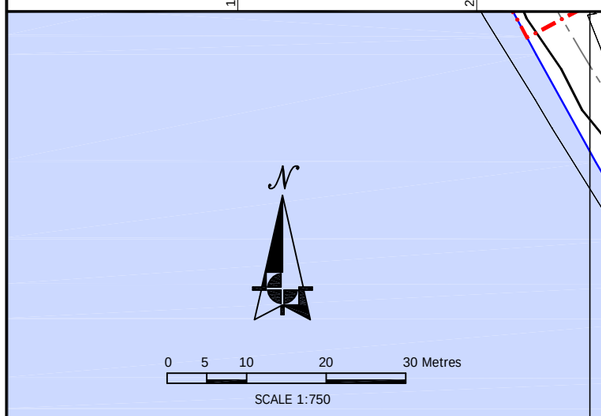

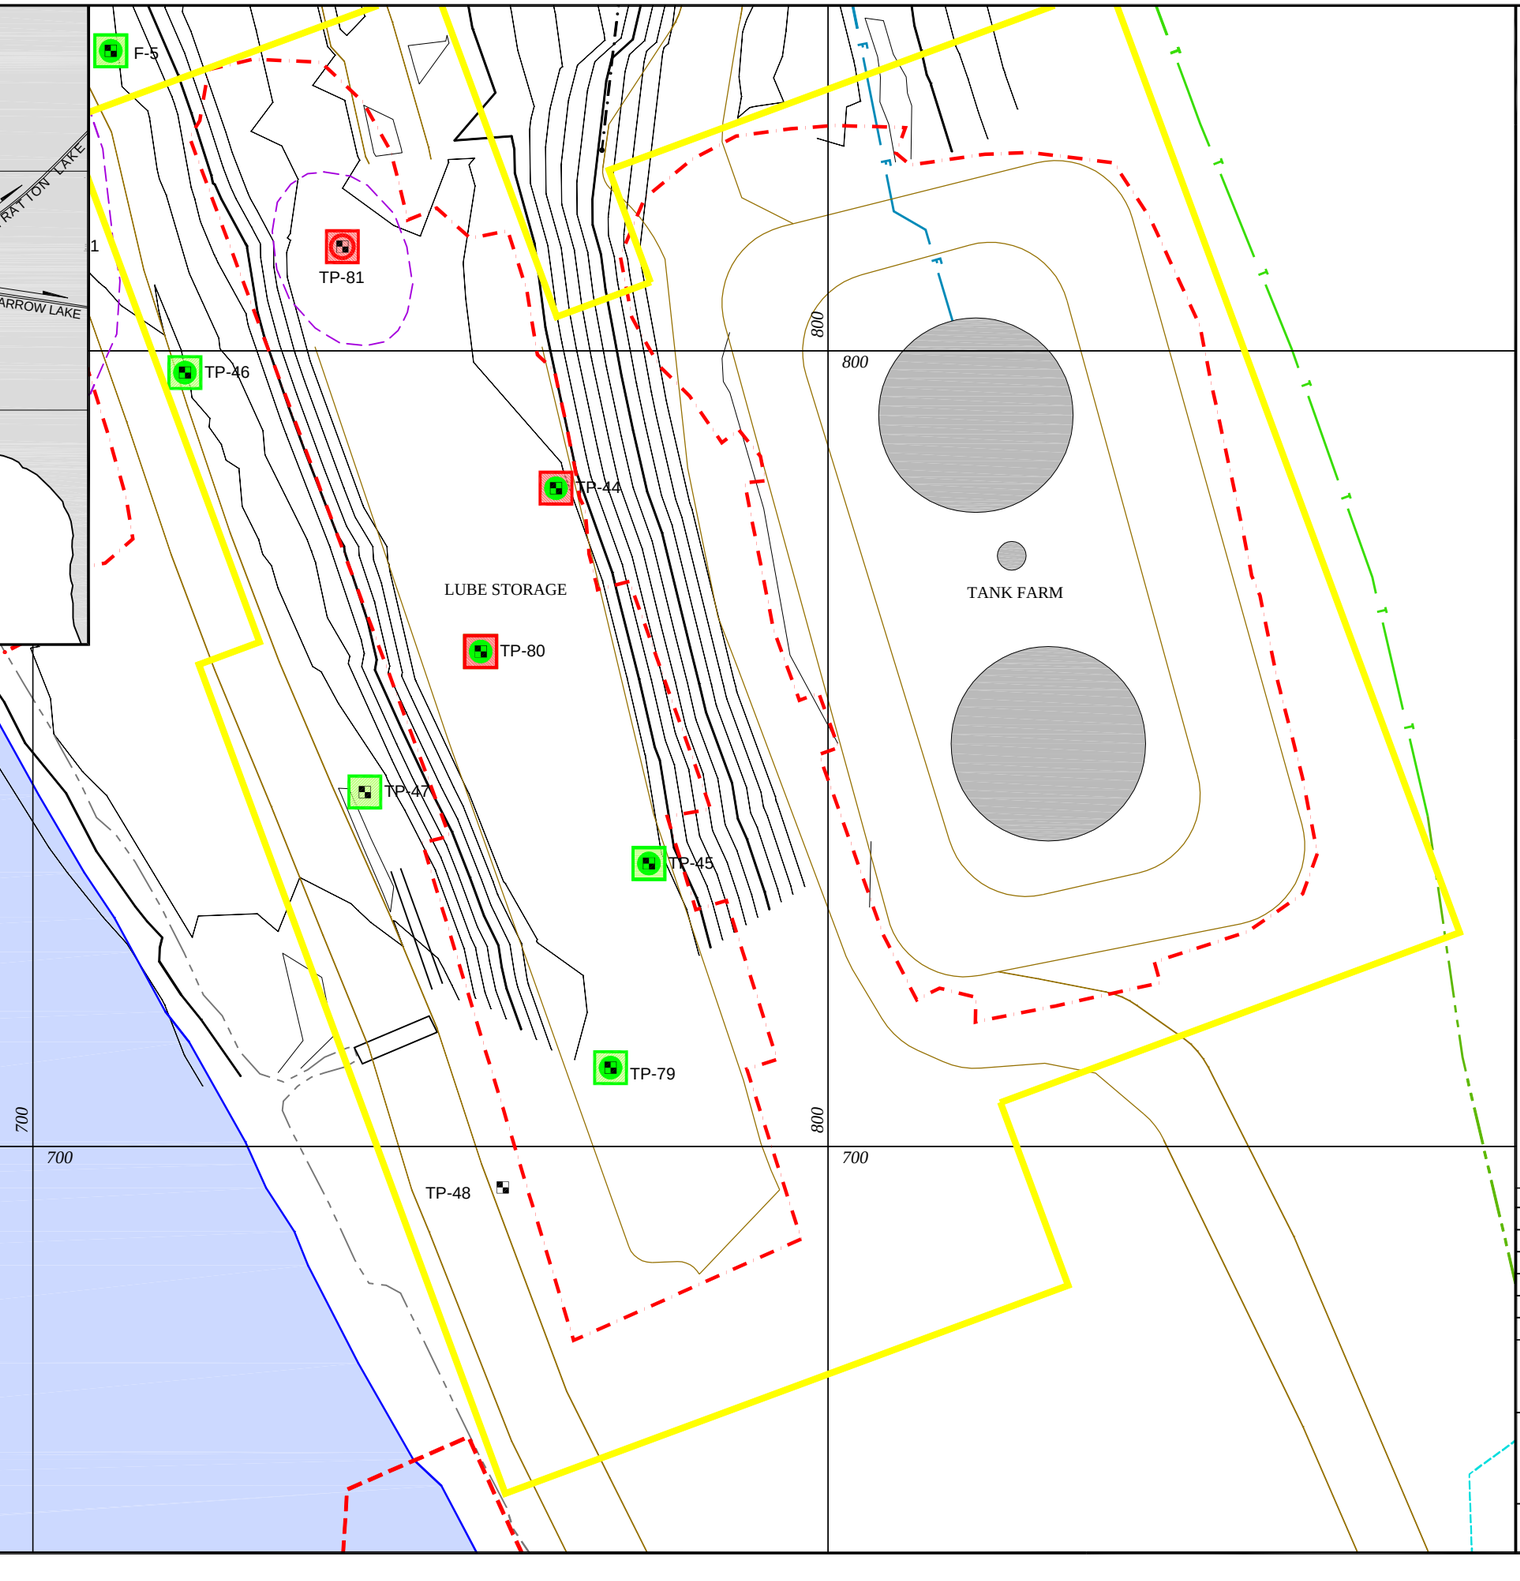

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–LS–M1–01.DWG
REVISION:	0


POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT


TANK FARM CONDITIONS BEFORE REMEDIATION

Gartner Lee

Figure No.
TF-08-1

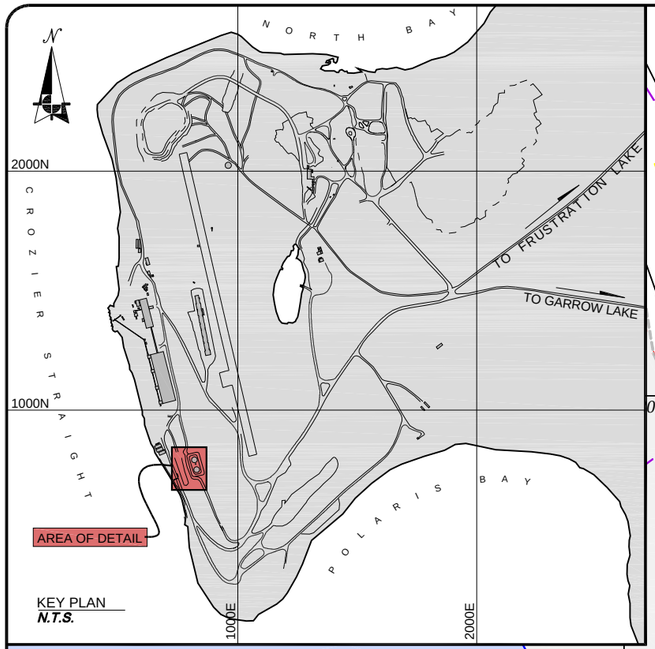

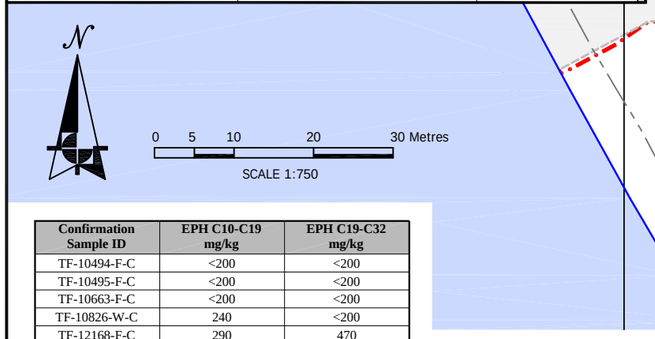

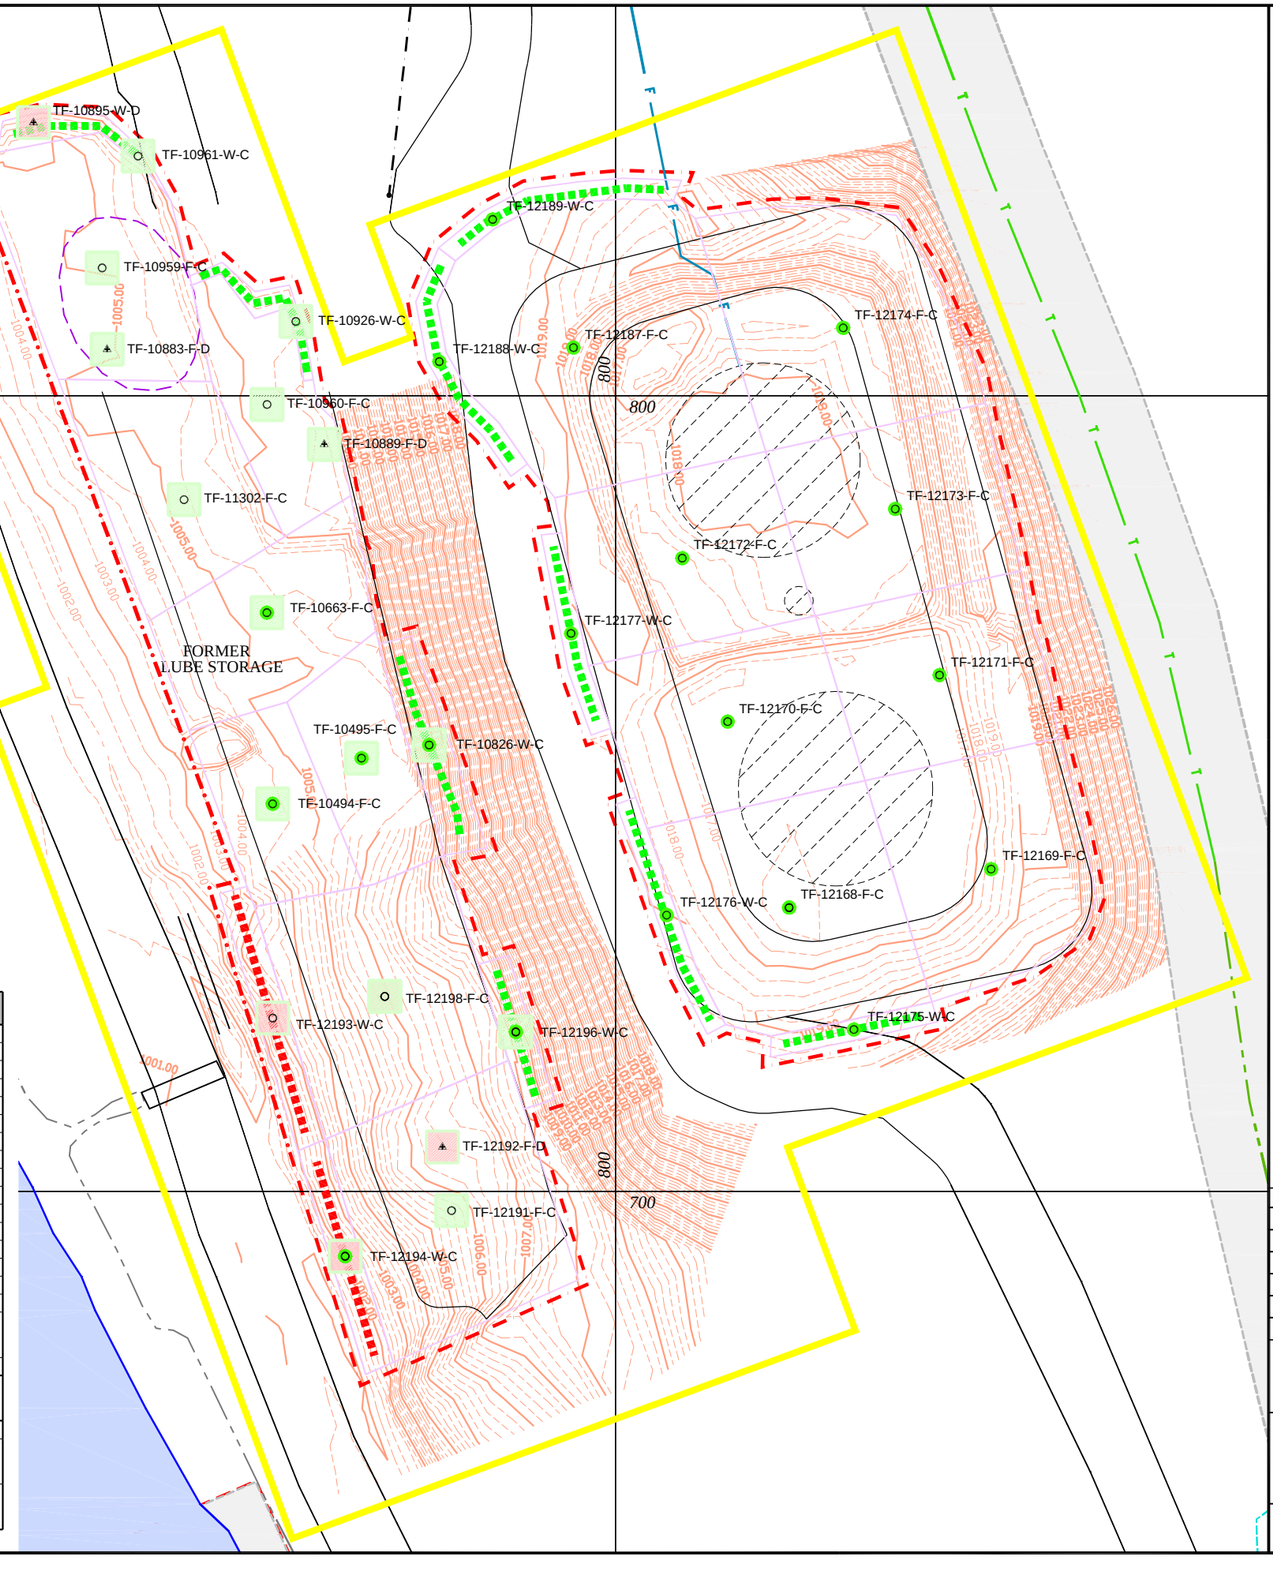

Confirmation Sample ID	EPH C10-C19 mg/kg	EPH C19-C32 mg/kg
TF-10494-F-C	<200	<200
TF-10495-F-C	<200	<200
TF-10663-F-C	<200	<200
TF-10826-W-C	240	<200
TF-12168-F-C	290	470
TF-12178-F-Q duplicate of TF-12168-F-C	260	450
TF-12169-F-C	230	440
TF-12170-F-C	320	550
TF-12171-F-C	320	550
TF-12172-F-C	320	540
TF-12173-F-C	300	490
TF-12174-F-C	280	490
TF-12175-W-C	300	510
TF-12176-W-C	<200	220
TF-12177-W-C	<200	250
TF-12187-F-C	870	380
TF-12188-W-C	<200	220
TF-12189-W-C	930	360
TF-12194-W-C	<200	210
TF-12195-W-Q duplicate of TF-12194-W-C	<200	<200
TF-12196-W-C	<200	240
TF-12197-W-Q duplicate of TF-12196-W-C	<200	<200

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
TF-10494-F-C	1380	6170
TF-10495-F-C	<150	84
TF-10663-F-C	<100	212
TF-10826-W-C	460	2620
TF-10883-F-D	980	494
TF-10889-F-D	1330	920
TF-10895-W-D	**2520**	9350
TF-10926-W-C	510	3310
TF-10959-F-C	600	3130
TF-10960-F-C	550	5770
TF-10961-W-C	1780	6630
TF-11302-F-C	1440	5280
TF-12191-F-C	1530	7110
TF-12192-F-D	**2630**	7760
TF-12193-W-C	**2000**	8580
TF-12194-W-C	**2360**	8230
TF-12195-W-Q duplicate of TF-12194-W-C	**2680**	8190
TF-12196-W-C	1490	7210
TF-12197-W-Q dupliate of TF-12196-W-C	**2020**	**12000**
TF-12198-F-C	**2074**	7807
TF-12190-F-Q duplicate of TF-12198-F-C	**4630**	7820
TF-12199-F-Q duplicate of TF-12198-F-C	1616	5690

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

ESP–7–I–D
- AREA
- SAMPLE ID
- TYPE: C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL; D= DISCRETE SAMPLE; Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
- LOCATION: F= FLOOR SAMPLE; I= INTERMEDIATE FLOOR SAMPLE; W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–LS–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

TANK FARM CONDITIONS AFTER REMEDIATION

Gartner Lee

Figure No. **TF-08-2**

Appendix F

Tailings Pipeline

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Tailings Pipeline

BACKGROUND

The tailings pipeline corridor (shown as Area 10 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan , December 31, 2004*) was located between the process barge and Garrow Lake. Two pipe lines, approximately 4 km long, were installed from the process barge to a tailings thickener. One line was used to carry tailings from the concentrator in the process barge to the thickener, and the other line return recycled water from the thickener to the process barge. The tailings thickener had three discharge lines between it and Garrow Lake. Two lines discharging from the tailings thickener carried the thickened tails to Garrow Lake, approximately 1 km to the east. A third pipe line discharging from the tailings thickener was approximately 100 m long and it lead to the emergency tailings impoundment. The impoundment was remediated in 2003 and reported on in Appendix D *23305–Polaris Mine Operations Contaminated Soil Remediation Close Out Report: Tailings Thickener Area* of the February 16, 2004 Report *23305–Contaminated Soil Remediation 2003 Close Out Reports, Polaris Mine, Nunavut.*

Incidents of tailing spills along the pipeline corridor were documented as part of the Environmental Site Assessment (ESA) conducted in 1999 and 2000. Between January 1982 and May 1999 there were eleven tailings spills along the corridor. In all cases the spills were reported to Department of Indian and Northern Development (DIAND) Water Resources. Spill clean up was carried out by mine operations immediately after each incident. In cases where spills occurred in winter, further clean up was carried out when the surface thawed the following summer. The spilt tailings and contaminated soils and gravels were disposed into the underground workings. No environmental sampling was conducted during operations to evaluate the effectiveness of the clean up activities.

Five areas along the tailings pipeline were identified in the ESA as areas impacted by spilt tailings due to the eleven breaks in the tailings pipeline. These five areas included:

1. an area between the concentrate storage shed and the process barge;
2. an area between the concentrate storage shed and the fuel tank farm;
3. an area just south of the fuel tank farm;
4. an area immediately southwest of the road to the detonator magazine; and
5. an area adjacent the tailings thickener building, that was remediated in 2003.

One soil sample collected during the ESA in the area between concentrate storage shed and the process barge (listed as the first area above) returned lead and zinc concentrations greater than the Polaris Mine Soil Quality Remediation Objectives (SQROs). Twelve additional soil samples were collected along the tailings pipeline corridor during the ESA and all twelve sample results met the SQROs for lead and zinc. However, no samples were collected from the spill area just south of the fuel tank farm (listed as the third area above). Figure TL-10-1: *Tailings Pipeline Conditions Before Remediation,* shows the approximate locations of the tailings pipeline breaks and results of the soil samples collected during the ESA investigations. Each of the five areas identified as being impacted by the eleven tailings spills was identified as an area of concern for metals in the ESA.

Two of the eleven spills occurred due to breaks in the tailings pipeline adjacent to the tailings thickener building (listed as the fifth area above) and this area was remediated in 2003 as documented in Appendix D *23305 – Polaris Mine Operations Contaminated Soil Remediation Close Out Report: Tailings Thickener Area* of the February 16, 2004 Report: *23305 – Contaminated Soil Remediation 2003 Close Out Reports, Polaris Mine, Nunavut*.

METHODOLOGY

Delineation

The preliminary boundaries of the areas of concern for metal contamination, as identified in the ESA, was further delineated by inspecting the entire length of the footprint of the tailings pipeline for visual evidence of fine grained sand or silt that would indicate remnant spilt tailings and then collecting soil samples at these locations. Field screening samples were collected from 0 cm to 5 cm, and 5 cm to 10 cm depths on July 3, 4 and 5, 2003 in accordance with standard Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols. The samples were analyzed on site using a portable Niton X-ray fluorescence (XRF) elemental analyzer. Based on the results of the field screening sampling, GLL collected confirmatory results from those areas indicated as not requiring remediation and modified the boundaries of the

areas to be remediated and directed excavation. Field screening results from the area impacted by a tailings line break immediately southwest of the road to the detonator magazine (listed as the fourth area above) indicated that the soil met the SQROs for lead and zinc. The field screening results also indicated that where metals contamination was present it was restricted to the surface, within the upper 5 cm.

Excavation

Excavation of the areas along the tailings pipeline occurred intermittently throughout 2003 and 2004. The excavation was limited to the surface and was undertaken with an excavator in more extensive areas, and with a hand shovel in smaller areas. When machinery was used for the excavation, soil within the excavation boundaries was loaded out into trucks with an excavator. When a hand shovel was used, the soil was deposited into sacks that were then loaded onto the back of an All-terrain vehicle (ATV) and stockpiled in areas readily accessible to an excavator.

Soil samples were collected from the base of the excavated areas and field screened using the Niton XRF elemental analyzer. Upon receipt of field screening results that indicated the SQROs would be met the excavation limits were surveyed.

The final limits of the excavation areas are shown on Figure TL-10-02: *Tailings Pipeline Conditions After Remediation*. The material excavated was disposed in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Soil samples were collected within the excavation limits and submitted to ALS Environmental of Vancouver, BC, for metals analysis to verify the concentration of metals. Additional excavation was undertaken in areas that did not meet the SQROs for lead and or zinc and additional confirmatory samples were taken upon completion of the excavation. Composite samples were collected over a length of 25 m along the footprint of the tailings line.

Confirmation soil samples were also collected from the area immediately southwest of the road to the detonator magazine (listed as the fourth area above) and submitted to ALS Environmental. Based on the laboratory results, no remedial excavation was required in this area.

ANALYTICAL RESULTS

Analytical laboratory confirmatory results for total metals are summarized in Tables TL-10-01, along with the approved Polaris Mine SQROs for metals. A total of twenty four (24) remediation

confirmation soil samples were submitted from the footprint of the former tailings pipeline as follows: sixteen (16) composite floor samples, five (5) discrete floor, and three (3) quality assurance/ quality control (QA/QC) duplicate samples. The soil quality results and the lateral limits of the excavations are shown on Figure TL-10-2.

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with collecting and analyzing soil were implemented during the remediation of the tailings pipeline corridor, including the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical replicates. Relative percent differences (RpD) have been calculated and compiled in Table TL-10-02 for twenty (20) on-site field screened duplicates, three (3) analytical laboratory duplicates, three (3) analytical laboratory replicates for a total of twenty six (26) QA/QC sample sets for lead and zinc concentrations.

All twenty (20) on-site field screened sample results and their duplicate results either returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not applicable) or they returned acceptable RpDs below the site specific objective of 50%. . The three analytical laboratory duplicates and one of the analytical replicates returned RpDs greater than the objective, 50% for either lead or zinc.

The variance between the sample and its duplicate or replicate is indicative of sample heterogeneity due to the presence of trace amounts of concentrate dust in the sample. Therefore, the metal QA/QC samples from the tailings pipeline area serve to document the variable nature of the metal concentrations in the soil.

Discussion

All confirmatory soil sample results from the former tailings pipeline corridor meet the SQROs for lead and zinc. Four soil samples were analyzed for addition metals. Arsenic concentrations ranged from <10 mg/kg to 13 mg/kg and barium concentrations ranged from 452 mg/kg to 776 mg/kg. The generic Canadian Council of Ministers of the Environment (CCME) Canadian Environmental Quality Guidelines (CEQG) for Parkland land use is 12 mg/kg arsenic and 500 mg/kg barium in soil. The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results,* are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of arsenic and barium

greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of arsenic and barium concentrations in those samples in listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Arsenic and Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Arsenic	12	<5	15.1	12	11 +/- 2.7	13	12.25
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of arsenic and barium remaining along the tailings pipeline corridor after remediation is within the range for the background area. The presence of arsenic and barium concentrations in soil above the generic CCME guidelines for Parkland land use is therefore attributed to natural background mineralogy. In addition, the immobile nature of the arsenic and barium encountered on site was also demonstrated in the 1999 ESA leachate analysis that returned arsenic and barium concentrations at levels less than the detection limit and they were therefore not identified as a contaminants of concern in the Polaris Mine ESA.

CONCLUSIONS

Based on confirmatory sampling, consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former tailings pipeline corridor has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at

specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Brenda Bolton, B.A., B.Sc.
Environmental Geologist.

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:BB:gc

ATTACHMENTS

Tables

Table TL-10-1: Tailings Pipeline Remediation Confirmation Soil Samples – Metals
Table TL-10-2: Tailings Pipeline Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure TL-10-1: Tailings Pipeline Conditions Before Remediation
Figure TL-10-2: Tailings Pipeline Conditions After Remediation

Table TL-10-1. Tailings Pipeline Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Tailings Pipeline							
				Sample ID	TL-21-1	TL-24-1	TL-12092-F-C	TL-12093-F-C	TL-12094-F-C	TL-12095-F-C	TL-12096-F-C	TL-12097-F-Q
				Date Sampled	11-Jul-03	11-Jul-03	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04
				ALS File Number	T1536	T1536	U6826rr	U6826rr	U6826rr	U6826rr	U6826rr	U6826rr
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	725	453	112	448	160	394	192	duplicate of
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	2840	1590	523	1637	722	2551	556	TL-12096-F-C
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH							-					
Metals												
Antimony	T-Sb	-	20[d]	mg/kg			<20					
Arsenic	T-As	-	12	mg/kg			<10					
Barium	T-Ba	-	500	mg/kg			452					
Beryllium	T-Be	-	4[d]	mg/kg			<1					
Cadmium	T-Cd	-	10	mg/kg			<1					
Chromium	T-Cr	-	64	mg/kg			7					
Cobalt	T-Co	-	50[d]	mg/kg			<4.0					
Copper	T-Cu	-	63	mg/kg			9					
Lead	T-Pb	2000	-	mg/kg	1600	525	<100	370	120	450	130	240
Mercury	T-Hg	-	7	mg/kg			-					
Molybdenum	T-Mo	-	10[d]	mg/kg			<8					
Nickel	T-Ni	-	50	mg/kg			13					
Selenium	T-Se	-	1	mg/kg			<6					
Silver	T-Ag	-	20[d]	mg/kg			<4					
Tin	T-Sn	-	50[d]	mg/kg			<10					
Vanadium	T-V	-	130	mg/kg			30					
Zinc	T-Zn	10000	-	mg/kg	5410	2110	348	1310	565	3090	369	952

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TL-10-1. Tailings Pipeline Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	Tailings Pipeline							
				Sample ID	TL-12098-F-C	TL-12099-F-C	TL-12100-F-C	TL-12101-F-C	TL-12102-F-C	TL-12103-F-D	TL-12118-F-C	TL-12119-F-D
				Date Sampled	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04	1-Aug-04	4-Aug-04	4-Aug-04
				ALS File Number	U6826rr	U6826rr	U6826rr	U6826rr	U6826rr	U6826rr	U6770(1)	U6770(1)
				Field Screen Pb (ppm)[b]	750	545	322	356	570	312	207	96
				Field Screen Zn (ppm)[b]	2695	1572	970	680	945	946	740	220
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH												
Metals												
Antimony	T-Sb	-	20[d]	mg/kg				<20		<20		
Arsenic	T-As	-	12	mg/kg				<10		<10		
Barium	T-Ba	-	500	mg/kg				**707**		**594**		
Beryllium	T-Be	-	4[d]	mg/kg				<1		<1		
Cadmium	T-Cd	-	10	mg/kg				2.1		2.1		
Chromium	T-Cr	-	64	mg/kg				8		14		
Cobalt	T-Co	-	50[d]	mg/kg				<4		<4		
Copper	T-Cu	-	63	mg/kg				13		12		
Lead	T-Pb	2000	-	mg/kg	850	640	350	590	530	300	200	<100
Mercury	T-Hg	-	7	mg/kg				-		-		
Molybdenum	T-Mo	-	10[d]	mg/kg				<8		<8		
Nickel	T-Ni	-	50	mg/kg				12		15		
Selenium	T-Se	-	1	mg/kg				<6		<8		
Silver	T-Ag	-	20[d]	mg/kg				<4		<4		
Tin	T-Sn	-	50[d]	mg/kg				<10		<10		
Vanadium	T-V	-	130	mg/kg				47		40		
Zinc	T-Zn	10000	-	mg/kg	2430	1510	916	459	756	744	515	120

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TL-10-1. Tailings Pipeline Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Tailings Pipeline					
				Sample ID	TL-12120-F-C	TL-12121-F-C	TL-12122-F-C	TL-12127-F-D	TL-12134-F-C	TL-12162-F-C
				Date Sampled	4-Aug-04	4-Aug-04	4-Aug-04	5-Aug-04	5-Aug-04	18-Aug-04
				ALS File Number	U6770(1)	U6770(1)	U6770(1)	U6770	U6770	U7328
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	149	304	337	99	-	160
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	409	788	879	202	-	475
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**					
pH								8.3		
Metals										
Antimony	T-Sb	-	20[d]	mg/kg				<20		
Arsenic	T-As	-	12	mg/kg				**13**		
Barium	T-Ba	-	500	mg/kg				**776**		
Beryllium	T-Be	-	4[d]	mg/kg				<1		
Cadmium	T-Cd	-	10	mg/kg				<1		
Chromium	T-Cr	-	64	mg/kg				13		
Cobalt	T-Co	-	50[d]	mg/kg				10		
Copper	T-Cu	-	63	mg/kg				39		
Lead	T-Pb	2000	-	mg/kg	<100	380	180	<100	<100	<100
Mercury	T-Hg	-	7	mg/kg				0.11		
Molybdenum	T-Mo	-	10[d]	mg/kg				<8		
Nickel	T-Ni	-	50	mg/kg				42		
Selenium	T-Se	-	1	mg/kg				<20		
Silver	T-Ag	-	20[d]	mg/kg				<4		
Tin	T-Sn	-	50[d]	mg/kg				<10		
Vanadium	T-V	-	130	mg/kg				92		
Zinc	T-Zn	10000	-	mg/kg	308	637	1120	106	90	58

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table TL-10-2. Tailings Pipeline Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee			Location	Tailings Pipeline								
			Sample ID	TL-31-1-D	TL-47-1-D	TL-54-2-D	TL-12095-F-C	TL-12096-F-C	TL-12100-F-C	TL-12113-F-C	TL-12114-F-C	TL-12114-F-C
			Duplicate ID	TL-31-1-Q	TL-47-1-Q	TL-54-2-Q	QC# 400695	TL-12097-F-Q	QC# 400696	TL-12337-F-Q	TL-12133-F-Q	TL-12338-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**								
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350	1340	1220	337	-	192	-	1059	-	1297
Duplicate Result	mg/kg	70	350	1280	1280	248	-	261	-	1124	-	1276
RpD	**%**			5	5	na	-	na	-	6	-	2
Zinc (Zn)												
Sample Result	mg/kg	150	750	7597	3888	868	-	557	-	1741	-	1635
Duplicate Result	mg/kg	150	750	7507	4288	885	-	933	-	1740	-	1610
RpD	**%**			1	10	2	-	na	-	0	-	2
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	-	-	-	130	-	-	8650	8650
Duplicate Result	mg/kg	100	500	-	-	-	-	240	-	-	4520	<100
RpD	**%**			-	-	-	-	na	-	-	**63**	na
Zinc (Zn)												
Sample Result	mg/kg	2	10	-	-	-	-	369	-	-	1890	1890
Duplicate Result	mg/kg	2	10	-	-	-	-	952	-	-	1450	185
RpD	**%**			-	-	-	-	**88**	-	-	26	**165**
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	-	-	450	-	350	-	-	
Duplicate Result	mg/kg	100	500	-	-	-	370	-	380	-	-	
RpD	**%**			-	-	-	na	-	na	-	-	
Zinc (Zn)												
Sample Result	mg/kg	2	10	-	-	-	3090	-	916	-	-	
Duplicate Result	mg/kg	2	10	-	-	-	2080	-	1010	-	-	
RpD	**%**			-	-	-	39	-	10	-	-	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table TL-10-2. Tailings Pipeline Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Tailings Pipeline								
				Sample ID	TL-12115-F-C	TL-12116-F-C	TL-12117-F-C	TL-12118-F-C	TL-12119-F-D	TL-12120-F-C	TL-12121-F-C	TL-12122-F-C	TL-12123-F-C
				Duplicate ID	TL-12339-F-Q	TL-12340-F-Q	TL-12341-F-Q	TL-12342-F-Q	TL-12343-F-Q	TL-12344-F-Q	TL-12345-F-Q	TL-12346-F-Q	TL-12347-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		935	764	255	208	97	150	305	338	76
Duplicate Result	mg/kg	70	350		1047	662	254	194	88	131	269	252	90
RpD	**%**				11	14	na	na	na	na	na	na	na
Zinc (Zn)													
Sample Result	mg/kg	150	750		2581	2238	812	740	220	409	788	879	149
Duplicate Result	mg/kg	150	750		2510	2439	720	681	265	420	841	848	220
RpD	**%**				3	9	na	na	na	na	7	4	na
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-	-	-	-
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-	-	-	-
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-	-	-	-
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-	-	-	-

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table TL-10-2. Tailings Pipeline Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Tailings Pipeline					
				Sample ID	TL-12124-F-C	TL-12125-F-C	TL-12126-F-C	TL-12127-F-D	TL-12133-F-Q	TL-12162-F-C
				Duplicate ID	TL-12348-F-Q	TL-12349-F-Q	TL-12350-F-Q	TL-12351-F-Q	QC# 400261	TL-12377-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**					
On Site Field Screening Duplicates										
Lead (Pb)										
Sample Result	mg/kg	70	350		79	91	93	99	-	160
Duplicate Result	mg/kg	70	350		88	96	79	95	-	104
RpD	**%**				na	na	na	na	-	na
Zinc (Zn)										
Sample Result	mg/kg	150	750		145	198	151	202	-	475
Duplicate Result	mg/kg	150	750		223	225	185	59	-	203
RpD	**%**				na	na	na	na	-	na
Analytical Laboratory Duplicates										
Lead (Pb)										
Sample Result	mg/kg	100	500		-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-
Zinc (Zn)										
Sample Result	mg/kg	2	10		-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-
RpD	**%**				-	-	-	-	-	-
Analytical Laboratory Replicates										
Lead (Pb)										
Sample Result	mg/kg	100	500		-	-	-	-	4520	-
Duplicate Result	mg/kg	100	500		-	-	-	-	2340	-
RpD	**%**				-	-	-	-	**64**	-
Zinc (Zn)										
Sample Result	mg/kg	2	10		-	-	-	-	1450	-
Duplicate Result	mg/kg	2	10		-	-	-	-	1010	-
RpD	**%**				-	-	-	-	36	-

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

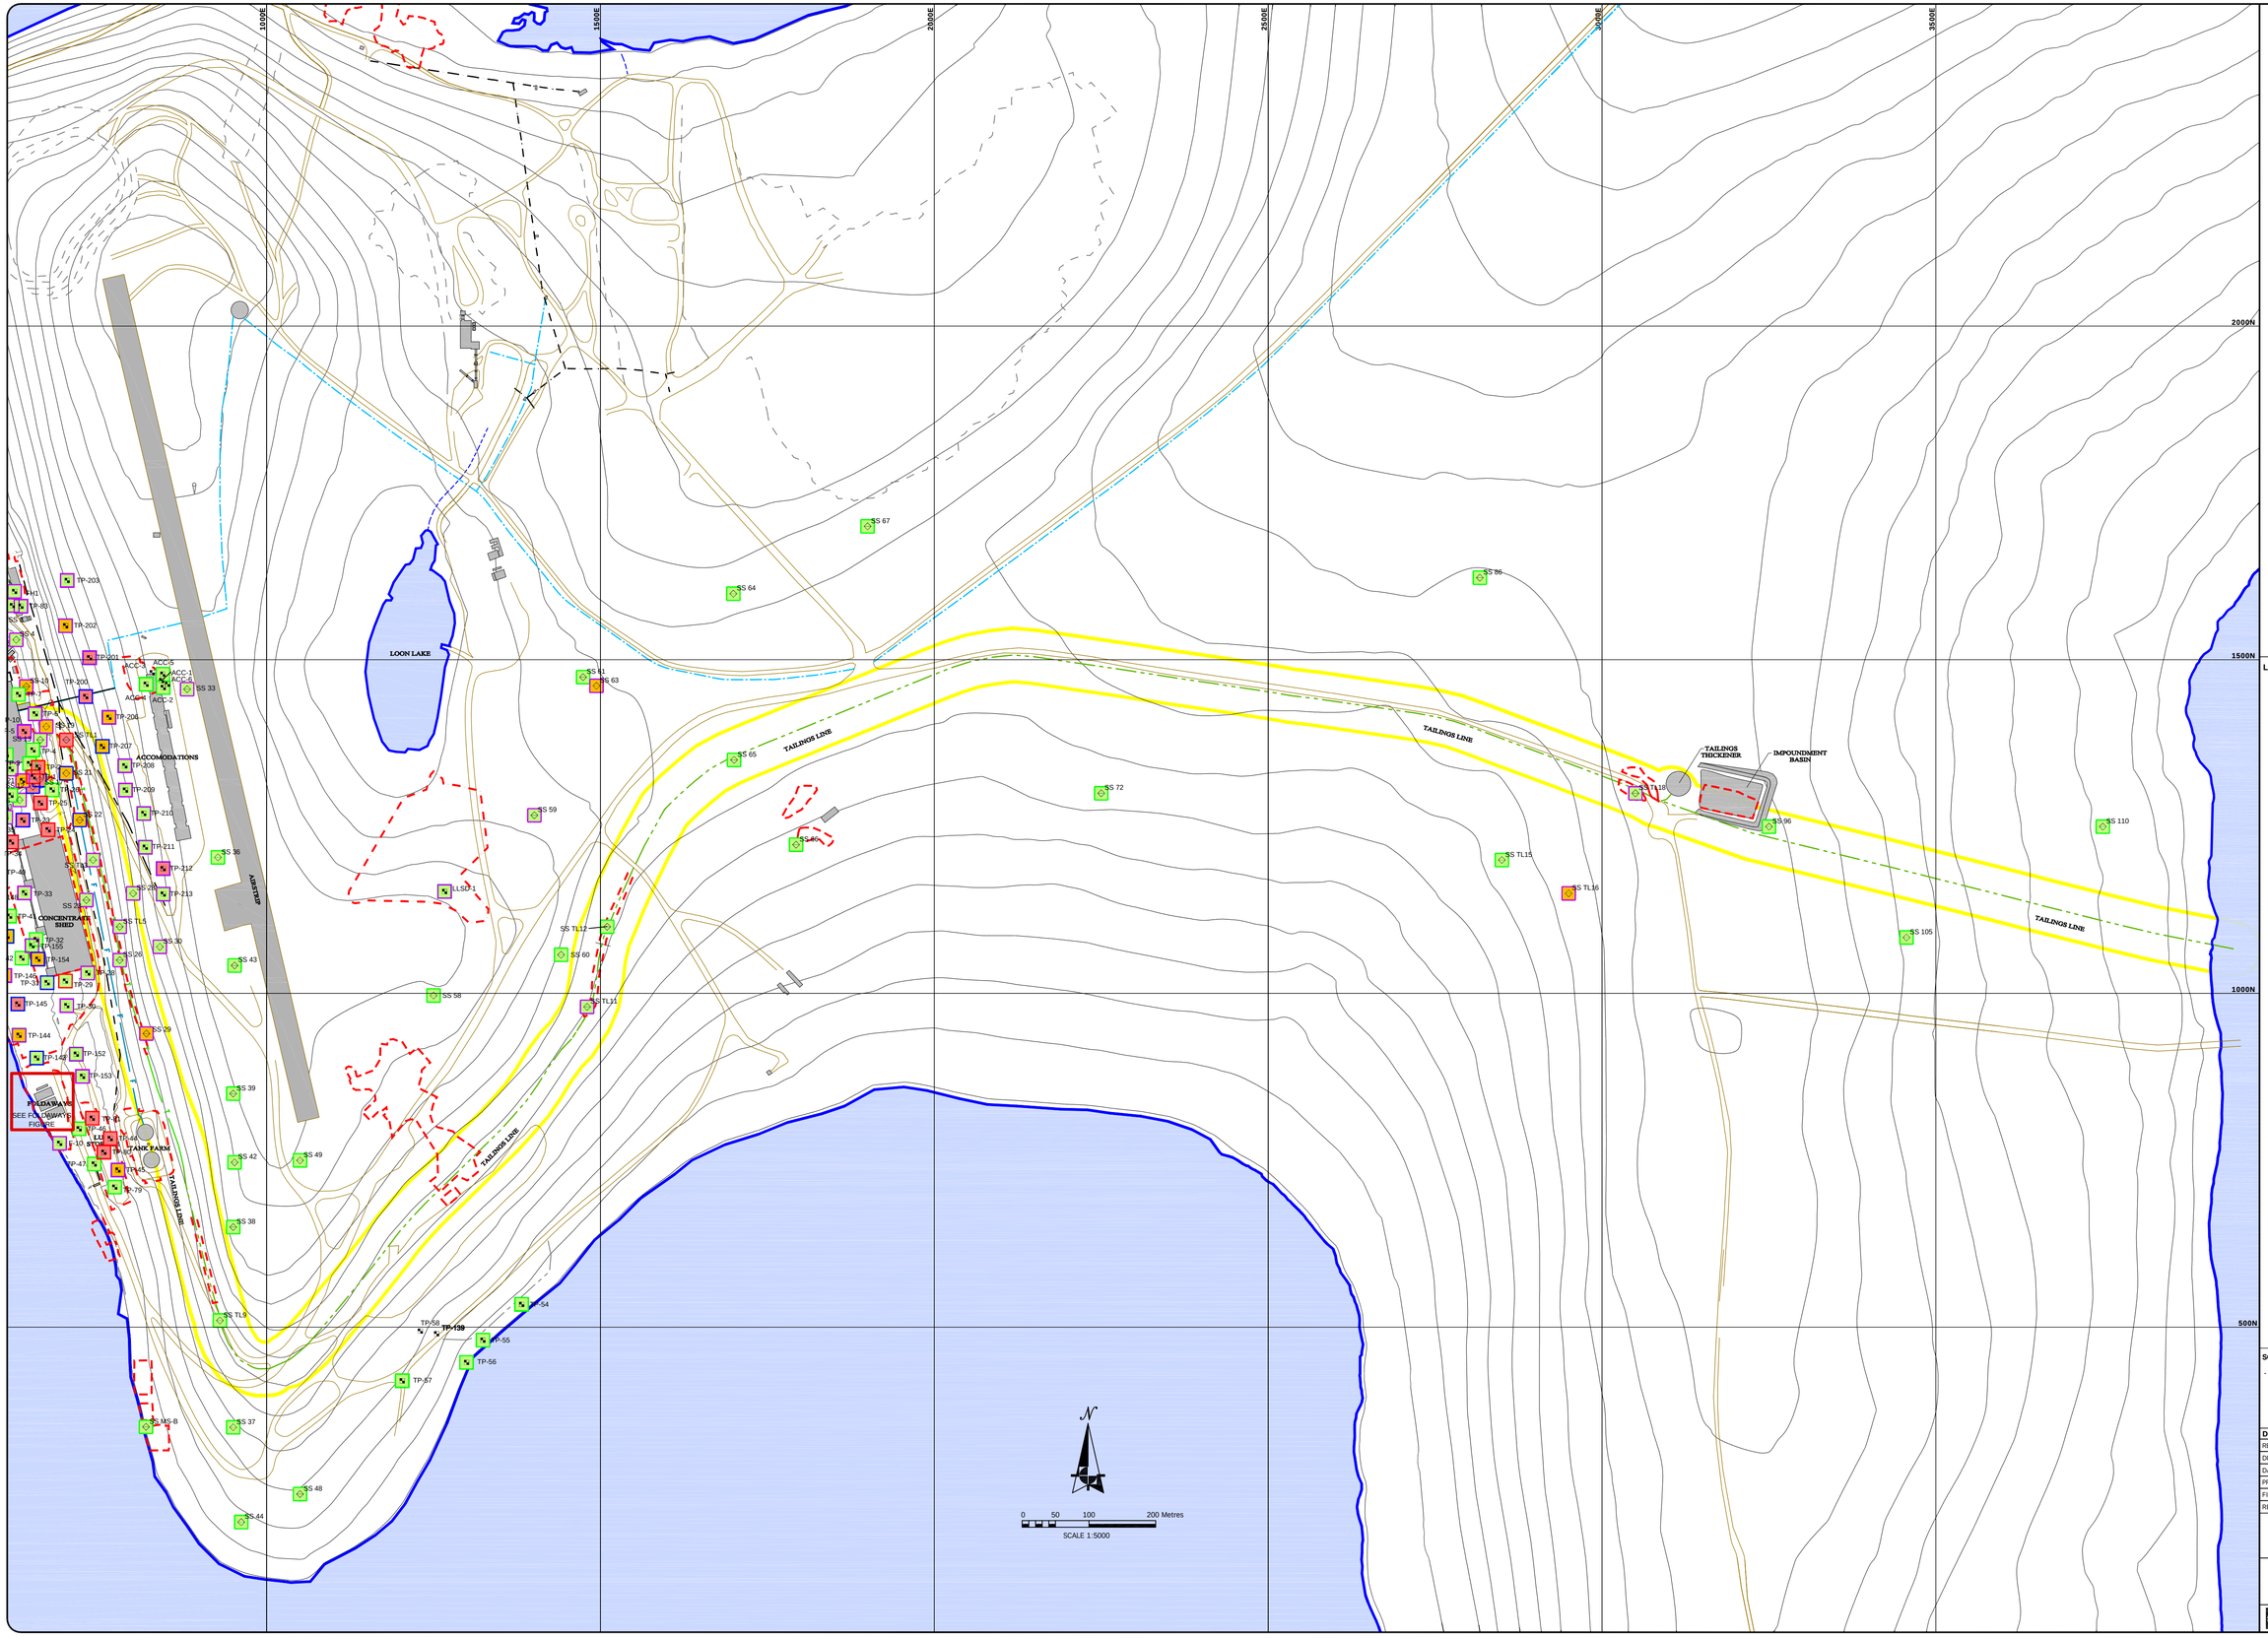

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

* EPH DATA FROM THE 1999/2000 ESA IS NOT ILLUSTRATED ON THIS FIGURE AS HYDROCARBONS ARE NOT A CONCERN ASSOCIATED DIRECTLY WITH THE TAILINGS PIPELINE. ANY AREAS CO–CONTAMINATED WITH METALS AND HYDROCARBONS ARE ADDRESSED IN SEPARATE CLOSE–OUT REPORTS.

SOURCE OF DRAWING:

-

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–TL–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

TAILINGS PIPELINE CONDITIONS BEFORE REMEDIATION

Gartner Lee

FIGURE NO. TL-10-1

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
TL-21-1	1600	5410
TL-24-1	525	2110
TL-12092-F-C	<100	348
TL-12093-F-C	370	1310
TL-12094-F-C	120	565
TL-12095-F-C	450	3090
TL-12096-F-C	130	369
TL-12097-F-Q duplicate of TL-12096-F-C	240	952
TL-12098-F-C	850	2430
TL-12099-F-C	640	1510
TL-12100-F-C	350	916
TL-12101-F-C	590	459
TL-12102-F-C	530	756
TL-12103-F-D	300	744
TL-12118-F-C	200	515
TL-12119-F-D	<100	120
TL-12120-F-C	<100	308
TL-12121-F-C	380	637
TL-12122-F-C	180	1120
TL-12127-F-D	<100	106
TL-12134-F-C	<100	90
TL-12162-F-C	<100	58

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

Lead	2000 mg/kg
Zinc	10000 mg/kg

1000E 1500E 2000E 2500E 3000E

1500N 1000N 500N

REFER TO DEC. 31/03 CLOSE-OUT REPORT: NORTH PORTAL STOCKPILE

REFER TO DEC. 31/03 CLOSE-OUT REPORT: CEMENT ROCK FILL (CRF) PLANT FUEL STORAGE TANK

REFER TO JUNE 10/05 CLOSE-OUT REPORT: FIREHALL AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: BARGE AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: ACCOMMODATIONS COMPLEX

REFER TO JUNE 10/05 CLOSE-OUT REPORT: LOON LAKE SNOW DUMP

REFER TO DEC. 31/03 CLOSE-OUT REPORT: OLD CRUSHER AREA

REFER TO DEC. 31/03 CLOSE-OUT REPORT: FORMER FUEL BLADDER STORAGE AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: CONCENTRATE STORAGE SHED AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: SOUTH SHORE

REFER TO JUNE 10/05 CLOSE-OUT REPORT: FOLDAWAY BUILDINGS

REFER TO JUNE 10/05 CLOSE-OUT REPORT: TANK FARM AND LUBE STORAGE AREA

REFER TO DEC. 31/03 CLOSE-OUT REPORT: 2002 FUEL SPILL

REFER TO DEC. 31/03 CLOSE-OUT REPORT: MAIN SNOW DUMP

REFER TO DEC. 31/03 CLOSE-OUT REPORT: TAILINGS THINCKENER AREA

WATER LINE

LOON LAKE

TAILINGS LINE

TAILINGS THICKENER

IMPOUNDMENT BASIN

ACCOMODATIONS

CONCENTRATE SHED

ARRSTRIP

FOLDAWAYS

LUBE STORAGE

TANK FARM

TL-12_20S-F-C
TL-12_03-F-C
TL-12_04-F-C
TL-12_05-F-C
TL-12_06-F-C
TL-12_09-F-C
TL-121 10-F-C
TL-12_03-F-D
TL-121 11-F-C
TL-121 12-F-C
TL-12_12-F-C
TL-12_18-F-C
TL-12_19-F-D
TL-121 10-F-C
TL-12_11-F-C
TL-12_12-F-C
TL-12_27-F-D
TL-12_34-F-C
TL-1-I
TL-4-I

N

0 50 100 200 Metres

SCALE 1:5000

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

AREA – SAMPLE ID – ESP-7-I-D

LOCATION: F= FLOOR SAMPLE; I= INTERMEDIATE FLOOR SAMPLE; W= WALL SAMPLE

TYPE: C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 12.5x25m AREA WALL–3 SAMPLES ALONG 25m OF WALL; D= DISCRETE SAMPLE; Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

SOURCE OF DRAWING:

-

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–TL–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

TAILINGS PIPELINE CONDITIONS AFTER REMEDIATION

Gartner Lee

FIGURE NO. TL-10-2

Appendix G

Loon Lake Snow Dump

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Loon Lake Snow Dump

BACKGROUND

The Loon Lake Snow Dump, shown as Area 18 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan , December 31, 2004,* was one of four areas at the mine site used to store snow collected from travel routes on the Polaris mine site. The snow dumps were identified as areas of environmental concern in the Environmental Site Assessment (ESA) conducted in 1999 and 2000 due to the inclusion of particulates with elevated lead and zinc concentrations. Melting of the snow dumps during the summer may have resulted in the elevated concentrations of metals in soils.

There were twenty (20) soil samples collected from the Loon Lake snow dump as part of the ESA. The samples were collected from eight test pits and four surface soil sampling locations. Two (2) samples, surface sample LL-A and the sample collected from 0 to 0.1 m depth in test pit LLSD-4, returned lead concentrations greater than the Polaris Mine Soil Quality Remediation Objective (SQRO) of 2,000 mg/kg. None of the samples collected exceeded the SQRO for zinc (10 000 mg/kg). Figure LL-18-1: *Loon Lake Snow Dump Conditions Before Remediation* illustrates the original topography of the area, sample results from the ESA, as well as the area estimated following the ESA to be the area of concern for metal contamination.

METHODOLOGY

Delineation

Commencing August 27, 2003, the preliminary boundary of the area to be remediated, identified in the ESA as an "Area of Concern", was further delineated for excavation through the collection and analysis of field screening samples of surface and subsurface material. Gartner Lee Limited (GLL) sampled the soil in accordance with standard GLL and (Teck Cominco Limited) TCL sampling procedures and protocols. One-hundred and thirteen (113) discrete field screening samples were collected from sixty-three (63) surface samples sites and fourteen (14) test pits. This included eleven (11) field duplicate quality assurance quality control samples. GLL collected the samples at 25 meter spaced intervals and analyzed these samples with the Niton portable X-Ray Fluorescence (XRF) elemental analyzer. The results of the analysis are indicated on Figure LL-18-1. Based on the results of the field screening sampling, GLL modified the area to be excavated as indicated by the "Limit of Remedial Excavation" shown on Figure LL-18-1.

Excavation

The excavation at Loon Lake snow dump commenced June 10, 2004 and was completed by August 8, 2004. Melting of the snow dump was accelerated by spreading the piles of snow and ice around with a bulldozer within the area delineated for excavation. The soil and remaining snow and ice within the excavation boundaries was ripped using a ripper tooth on and excavator, and pushed into stockpiles that were loaded out into trucks with an excavator. Field screening samples were collected across the base of the excavation and analysed on-site for metals using the XRF. Additional excavation was undertaken in areas with contiguous lead concentrations greater than 1,200 mg/kg and zinc concentrations greater than 8,500 mg/kg based on results obtained with the XRF. The areas where additional excavation was required were generally associated with ice patches that had not melted. The material excavated was disposed of in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Confirmation soil samples were collected across the floor of the excavation limits in accordance with standard GLL and TCL sampling procedures and protocols. Composite confirmation samples were collected from areas of the floor that measured approximately 25 m x 25 m. The soil samples were submitted to the analytical laboratory, ALS Environmental of Vancouver, BC to verify that the remaining concentrations of metals in soil met the SQROs. Upon receipt of the soil results that met the SQROs the final excavation limits were surveyed.

ANALYTICAL RESULTS

Analytical laboratory results are summarized in Table L-18-1, along with the approved Polaris Mine SQROs for lead and zinc. A total of seventy-one (71) confirmation soil samples from the former Loon Lake snow dump area were submitted for laboratory analysis fifty-eight (58) composite floor samples, seven (7) discrete floor, and six (6) quality assurance quality control (QA/QC) duplicate samples. The soil quality results and the lateral limits of the excavation are shown on Figure LL-18-2, *Loon Lake Snow Dump Conditions After Remediation*.

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with collecting and analyzing soil were implemented during the remediation of the Loon Lake snow dump area, including the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical replicates. Relative percent differences (RpD) have been calculated and compiled in Table LL-18-2 for forty-five (45) on-site field screened duplicates, six (6) analytical laboratory duplicates, three (3) analytical laboratory replicates for a total of fifty-four (54) QA/QC sample sets for lead and zinc concentrations.

Fifty (50) of the sample results and their duplicate/replicate results either returned results below the practical quantitation limit, in which case the RpD value has been identified as “na” (not applicable) or they returned acceptable RpDs below the site specific objective of 50%. . Two on-site field screened duplicates, one analytical laboratory duplicate and one of the analytical replicates returned RpDs greater than the objective, 50%.

The variance between the sample and its duplicate or replicate is indicative of sample heterogeneity likely due to the presence of trace amounts of concentrated lead or zinc dust in the sample. Therefore, the metal QA/QC samples from the Loon Lake snow dump area serve to document the variable nature of the metal concentrations in the soil.

Discussion

The seven discrete samples were collected and submitted for laboratory analysis of lead and zinc from six composite sample areas collected in the same area and results were as follows:

Summary of Discrete Sample Results compared to the corresponding Composite Sample Results

Composite Sample ID	Lead (mg/kg)	Zinc (mg/kg)	Discrete Sample ID	Lead (mg/kg)	Zinc (mg/kg)
LL-11737-F-C	680	1780	LL-11423-F-D	73	170
LL-11740-F-C	680	1740	LL-11462-F-D	294	835
LL-11740-F-C	680	1740	LL-11463-F-D	1620	4430
LL-11941-F-C	1940	7460	LL-11502-F-D	<100	210
LL-11954-F-C	310	734	LL-11532-F-D	810	2280
LL-12075-F-C	<50	108	LL-12076-F-D	<100	95
LL-12084-F-C	<100	221	LL-12085-F-D	<100	6

Seventy (70) of the seventy one (71) confirmatory soil sample results from the Loon Lake snow dump area meet the SQROs for lead and zinc. One analytical laboratory duplicate sample (LL-12319-F-Q) returned lead concentrations of 2200 mg/kg, which is greater than the SQRO for lead (2,000 mg/kg). Ten soil samples were analyzed for addition metals. Arsenic concentrations ranged from <10 mg/kg to 14 mg/kg and barium concentrations ranged from 357 mg/kg to 994 mg/kg. The generic Canadian Council of Ministers of the Environment (CCME) Canadian Environmental Quality Guidelines (CEQG) for Parkland land use is 12 mg/kg arsenic and 500 mg/kg barium in soil. The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results,* are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of arsenic and barium greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of arsenic and barium concentrations in those samples in listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Arsenic and Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Arsenic	12	<5	15.1	12	11 +/- 2.7	13	12.25
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of arsenic and barium remaining within the footprint of the Loon Lake snow dump after remediation are within the range of the background concentrations. The presence of arsenic and barium concentrations in soil above the generic CCME guidelines for Parkland land use is therefore attributed to natural background mineralogy. In addition, the immobile nature of the arsenic and barium encountered on site was also demonstrated in the 1999 ESA leachate analysis that returned arsenic and barium concentrations at levels less than the detection limit and they were therefore not identified as a contaminants of concern in the Polaris Mine ESA.

The confirmation samples supported by the QA/QC samples from the Loon Lake snow dump area provide confidence that the remediation of the area complies with the SQROs.

CONCLUSIONS

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former Loon Lake snow dump area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was

undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:DL:gc

ATTACHMENTS

Tables

Table LL-18-1: Loon Lake Snow Dump Remediation Confirmation Soil Samples – Metals
Table LL-18-2: Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure LL-18-1: Loon Lake Snow Dump Conditions Before Remediation
Figure LL-18-2: Loon Lake Snow Dump Conditions After Remediation

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11423-F-D	LL-11462-F-D	LL-11463-F-D	LL-11502-F-D	LL-11532-F-D	LL-11753-F-Q	LL-11605-F-C	LL-11606-F-C
				Date Sampled	8-Jul-04	8-Jul-04	8-Jul-04	8-Jul-04	8-Jul-04	8-Jul-04	21-Jun-04	21-Jun-04
				ALS File Number	U5050	U5050	U5050	U5836	U5836	U5836	U5050	U5050
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	106	297	1724	59	792	duplicate of	160	209
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	315	848	7123	285	3654	LL-11532-F-D	705	941
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	-	-	-	-	-	8.7	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	**13**	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	**723**	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	1.8	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	11	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	7	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	29	-
Lead	T-Pb	2000	-	mg/kg	73	294	1620	<100	810	930	160	140
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	0.12	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	37	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	82	-
Zinc	T-Zn	10000	-	mg/kg	170	835	4430	210	2280	2370	507	390

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11607-F-C	LL-11608-F-C	LL-11609-F-C	LL-11610-F-C	LL-11611-F-C	LL-11612-F-C	LL-11613-F-C	LL-11614-F-C
				Date Sampled	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04
				ALS File Number	U5050	U5050	U5050	U5050	U5050	U5050	U5050	U5050
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	212	71	206	235	210	308	149	85
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	939	396	628	910	612	1216	475	407
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	-	-	-	-	-	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	170	<100	160	200	150	170	110	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	540	160	464	584	460	413	335	269

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11615-F-C	LL-11616-F-C	LL-11617-F-C	LL-11618-F-C	LL-11709-F-Q	LL-11619-F-C	LL-11620-F-C	LL-11621-F-C
				Date Sampled	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04	21-Jun-04
				ALS File Number	U5050	U5050	U5050	U5050	U5050	U5050	U5050	U5050
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	152	75	210	278	duplicate of	54	34	103
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	651	302	715	995	LL-11618-F-C	349	198	429
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	-	-	-	-	-	8.8	-
Metals					-	-						
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	**13**	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	423	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	<1	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	10	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	7	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	29	-
Lead	T-Pb	2000	-	mg/kg	105	<100	150	250	300	110	<100	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	0.16	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	39	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	80	-
Zinc	T-Zn	10000	-	mg/kg	296	191	435	723	880	138	110	162

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11622-F-C	LL-11623-F-C	LL-11697-F-C	LL-11698-F-C	LL-11699-F-C	LL-11737-F-C	LL-11738-F-C	LL-11739-F-C
				Date Sampled	21-Jun-04	21-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04
				ALS File Number	U5050	U5050	U5223	U5223	U5223	U5050	U5050	U5050
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	67	81	1397	1372	772	-	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	362	393	5028	6364	3564	-	-	-
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	-	-	-	-	-	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<100	110	1360	1400	700	680	210	150
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	141	344	3150	3560	2220	1780	267	355

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11740-F-C	LL-11741-F-C	LL-11742-F-Q	LL-11800-F-C	LL-11802-F-C	LL-11939-F-C	LL-11941-F-C	LL-11944-F-C
				Date Sampled	28-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04	28-Jun-04	8-Jul-04	8-Jul-04	8-Jul-04
				ALS File Number	U5050	U5050	U5050	U5223	U5223	U5836	U5836	U5615r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	-	duplicate of	1106	1364	1131	1460	384
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	-	LL-11741-F-C	5174	8307	3256	5613	1031
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	7.9	-	-	-	8.4	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	-	<10	-	-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	-	487	-	-	-	**695**	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	-	-	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	-	8.9	-	-	-	7.3	-	-
Chromium	T-Cr	-	64	mg/kg	-	10	-	-	-	10	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	5	-	-	-	<4	-	-
Copper	TCu	-	63	mg/kg	-	24	-	-	-	19	-	-
Lead	T-Pb	2000	-	mg/kg	680	1010	1210	1150	1880	970	1940	255
Mercury	T-Hg	-	7	mg/kg	-	0.08	-	-	-	0.07	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	-	-	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	-	26	-	-	-	21	-	-
Selenium	T-Se	-	1	mg/kg	-	<4	-	-	-	<4	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	<4	-	-	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	-	62	-	-	-	49	-	-
Zinc	T-Zn	10000	-	mg/kg	1740	2970	3520	2940	7660	2590	7460	650

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-11946-F-C	LL-11954-F-C	LL-12051-F-C	LL-12052-F-C	LL-12054-F-C	LL-12055-F-C	LL-12056-F-C	LL-12319-F-Q
				Date Sampled	8-Jul-04	8-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04
				ALS File Number	U5836	U5836	U6365r	U6365r	U6365r	U6365r	U6365r	U6365r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	1588	403	1327	1266	494	374	1697	duplicate of
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	6141	1699	3979	3717	1424	1112	4846	LL-12056-F-C
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	8.3	-	-	-	-	-	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	10	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	**906**	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	3.5	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	14	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	5	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	19	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	1690	490	1140	1340	310	380	1980	**2200**
Mercury	T-Hg	-	7	mg/kg	-	0.07	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	25	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	<4	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	<4	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	75	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	9410	1280	2760	3380	734	976	3020	4100

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-12061-F-C	LL-12063-F-C	LL-12064-F-C	LL-12065-F-C	LL-12066-F-C	LL-12075-F-C	LL-12076-F-D	LL-12077-F-C
				Date Sampled	25-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04	25-Jul-04	29-Jul-04	29-Jul-04	29-Jul-04
				ALS File Number	U6365r	U6365r	U6365r	U6365r	U6530rr	U6530rr	U6530rr	U6530rr
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	141	111	355	487	-	70	-	160
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	566	463	1153	1425	-	206	-	451
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					7.3	-	-	-	-	-	-	7.8
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	-	-	-	<20
Arsenic	T-As	-	12	mg/kg	**13**	-	-	-	-	-	-	**12**
Barium	T-Ba	-	500	mg/kg	**730**	-	-	-	-	-	-	**670**
Beryllium	T-Be	-	4[d]	mg/kg	<1	-	-	-	-	-	-	<1
Cadmium	T-Cd	-	10	mg/kg	1.4	-	-	-	-	-	-	<1
Chromium	T-Cr	-	64	mg/kg	15	-	-	-	-	-	-	13
Cobalt	T-Co	-	50[d]	mg/kg	7	-	-	-	-	-	-	6
Copper	TCu	-	63	mg/kg	32	-	-	-	-	-	-	28
Lead	T-Pb	2000	-	mg/kg	140	<100	450	670	104	<50	<100	<100
Mercury	T-Hg	-	7	mg/kg	0.13	-	-	-	-	-	-	0.10
Molybdenum	T-Mo	-	10[d]	mg/kg	<8	-	-	-	-	-	-	<8
Nickel	T-Ni	-	50	mg/kg	44	-	-	-	-	-	-	34
Selenium	T-Se	-	1	mg/kg	<14	-	-	-	-	-	-	<4
Silver	T-Ag	-	20[d]	mg/kg	<4	-	-	-	-	-	-	<4
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	-	-	-	<10
Vanadium	T-V	-	130	mg/kg	98	-	-	-	-	-	-	91
Zinc	T-Zn	10000	-	mg/kg	409	406	1510	1210	1190	108	95.2	266

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump							
				Sample ID	LL-12078-F-C	LL-12079-F-Q	LL-12080-F-C	LL-12081-F-C	LL-12084-F-C	LL-12085-F-D	LL-12104-F-C	LL-12105-F-C
				Date Sampled	29-Jul-04	29-Jul-04	29-Jul-04	29-Jul-04	29-Jul-04	29-Jul-04	2-Aug-04	2-Aug-04
				ALS File Number	U6530rr	U6530rr	U6530rr	U6530rr	U6530rr	U6530rr	U6826rr	U6826rr
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	180	duplicate of	172	106	149	-	168	329
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	564	LL-12078-F-C	482	295	432	-	455	463
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**							
pH					-	-	-	-	-	-	8.1	-
Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	10	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	357	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	1.2	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	14	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	12	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	26	-
Lead	T-Pb	2000	-	mg/kg	<100	120	100	100	<100	<100	150	250
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	0.11	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	46	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	<8	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	47	-
Zinc	T-Zn	10000	-	mg/kg	261	357	341	328	221	6.4	367	654

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-1. Loon Lake Snow Dump Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump						
				Sample ID	LL-12110-F-C	LL-12128-F-C	LL-12135-F-Q	LL-12136-F-C	LL-12137-F-C	LL-12138-F-C	LL-12139-F-C
				Date Sampled	2-Aug-04	5-Aug-04	5-Aug-04	8-Aug-04	8-Aug-04	8-Aug-04	8-Aug-04
				ALS File Number	U6826rr	U6770(1)	U6770(1)	U6898	U6898	U6898	U6898
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	139	81	duplicate of	378	408	397	420
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	417	142	LL-12128-F-C	1206	1417	1524	1443
Parameter		**Site Specific**	**CEQG(PL)[c]**	**Units**	**Analytical Results**						
pH					-	-	-	-	-	-	-
Metals											
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	**12**	-	-	-	**14**	-	-
Barium	T-Ba	-	500	mg/kg	**994**	-	-	-	442	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<1	-	-	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	1	-	-	-	2.1	-	-
Chromium	T-Cr	-	64	mg/kg	21	-	-	-	10	-	-
Cobalt	T-Co	-	50[d]	mg/kg	7	-	-	-	9	-	-
Copper	TCu	-	63	mg/kg	29	-	-	-	29	-	-
Lead	T-Pb	2000	-	mg/kg	74	<100	<100	182	180	159	210
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8	-	-	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	40	-	-	-	46	-	-
Selenium	T-Se	-	1	mg/kg	<6	-	-	-	<8	-	-
Silver	T-Ag	-	20[d]	mg/kg	<4	-	-	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	104	-	-	-	75	-	-
Zinc	T-Zn	10000	-	mg/kg	312	89	148	518	637	460	656

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guideline were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter. for a given parameter.

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump								
				Sample ID	LL-9-I-D	LL-20-I-D	LL-31-I-D	LL-45-I-D	LL-52-I-D	LL-58-I-D	LL-70-I-D	LL-73-1-W-D	LL-75-2-W-D
				Duplicate ID	LL-86-Q	LL-87-Q	LL-88-Q	LL-89-Q	LL-90-Q	LL-91-Q	LL-92-Q	LL-93-Q	LL-94-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		2765	2250	610	530	461	2493	122	4435	74
Duplicate Result	mg/kg	70	350		2636	2534	481	627	529	2372	320	4734	73
RpD	%				5%	12%	24%	17%	14%	5%	na	7%	na
Zinc (Zn)													
Sample Result	mg/kg	150	750		9669	9729	2734	2247	1155	9569	783	24843	431
Duplicate Result	mg/kg	150	750		9135	10463	1862	2452	1506	9039	1318	24653	456
RpD	%				6%	7%	38%	9%	26%	6%	**51%**	1%	na
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	%												
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	%												

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee			Location	Loon Lake Snow Dump								
			Sample ID	LL-79-2-W-D	LL-83-3-F-D	LL-11427-F-D	LL-11432-F-D	LL-11441-F-D	LL-11452-F-D	LL-11462-F-D	LL-11508-F-D	LL-11518-F-D
			Duplicate ID	LL-95-Q	LL-96-Q	LL-10508-F-Q	LL-11704-F-Q	LL-11705-F-Q	LL-11706-F-Q	LL-11701-F-Q	LL-11702-F-Q	LL-11703-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**								
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350	222	70	536	74	126	5039	300	1717	1597
Duplicate Result	mg/kg	70	350	350	23	513	57	134	4166	310	1708	1824
RpD	%			na	na	4%	na	na	19%	na	0%	13%
Zinc (Zn)												
Sample Result	mg/kg	150	750	689	478	1892	205	494	27038	1196	5079	6055
Duplicate Result	mg/kg	150	750	1108	536	2087	241	519	22632	830	5271	6584
RpD	%			47%	na	10%	16%	5%	18%	36%	4%	8%
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	-	-	-	-	-	-	-	-	-
RpD	%											
Zinc (Zn)												
Sample Result	mg/kg	2	10	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10	-	-	-	-	-	-	-	-	-
RpD	%											
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	-	-	-	-	-	-	-	-	-
RpD	%											
Zinc (Zn)												
Sample Result	mg/kg	2	10	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10	-	-	-	-	-	-	-	-	-
RpD	%											

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump								
				Sample ID	LL-11530-F-D	LL-11532-F-D	LL-11609-F-C	LL-11618-F-C	LL-11741-F-C	LL-11800-F-C	LL-11800-F-C	LL-11946-F-C	LL-12050-F-C
				Duplicate ID	LL-11700-F-Q	LL-11753-F-Q	LL-11708-F-Q	LL-11709-F-Q	LL-11742-F-Q	QC# 393918	LL-11719-F-Q	QC# 396124	LL-12318-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		1327	-	206	279	-	-	1106	-	4284
Duplicate Result	mg/kg	70	350		1169	-	263	302	-	-	1264	-	4167
RpD	%				13%		na	na			13%		3%
Zinc (Zn)													
Sample Result	mg/kg	150	750		5302	-	828	996	-	-	5174	-	16091
Duplicate Result	mg/kg	150	750		5321	-	1109	999	-	-	5661	-	14077
RpD	%				0%		29%	0%			9%		13%
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	810	-	250	1010	-	-	-	-
Duplicate Result	mg/kg	100	500		-	930	-	300	1210	-	-	-	-
RpD	%					14%		na	18%				
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	2280	-	723	2970	-	-	-	-
Duplicate Result	mg/kg	2	10		-	2370	-	880	3520	-	-	-	-
RpD	%					4%		20%	17%				
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	1150	-	1690	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	2230	-	2390	-
RpD	%									**64%**		34%	
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	2940	-	9410	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	4250	-	6060	-
RpD	%									36%		43%	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump								
				Sample ID	LL-12052-F-C	LL-12053-F-C	LL-12054-F-C	LL-12056-F-C	LL-12057-F-C	LL-12058-F-C	LL-12059-F-C	LL-12061-F-C	LL-12062-F-C
				Duplicate ID	LL-12323-F-Q	LL-12327-F-Q	LL-12320-F-Q	LL-12319-F-Q	LL-12325-F-Q	LL-12329-F-Q	LL-12328-F-Q	LL-12326-F-Q	LL-12316-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		1266	3250	494	1697	3566	2936	3106	141	3621
Duplicate Result	mg/kg	70	350		1287	3300	408	1393	3513	3573	2633	182	4531
RpD	%				2%	2%	19%	20%	1%	20%	16%	na	22%
Zinc (Zn)													
Sample Result	mg/kg	150	750		3717	11998	1424	4846	14783	11141	10875	566	14985
Duplicate Result	mg/kg	150	750		4091	15473	1231	4725	15669	14330	10524	605	17555
RpD	%				10%	25%	15%	3%	6%	25%	3%	na	16%
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	1980	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	2200	-	-	-	-	-
RpD	%							11%					
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	3020	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	4100	-	-	-	-	-
RpD	%							30%					
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	%												

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Loon Lake Snow Dump								
				Sample ID	LL-12063-F-C	LL-12064-F-C	LL-12065-F-C	LL-12077-F-C	LL-12078-F-C	LL-12080-F-C	LL-12082-F-C	LL-12111-F-C	LL-12128-F-C
				Duplicate ID	LL-12324-F-Q	LL-12317-F-Q	LL-12322-F-Q	QC# 399317	LL-12079-F-Q	LL-12335-F-Q	LL-12083-F-Q	LL-12112-F-Q	LL-12135-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		111	355	487	-	180	173	3290	3300	82
Duplicate Result	mg/kg	70	350		150	345	469	-	172	162	5912	3279	108
RpD	%				na	na	4%		na	na	**57%**	1%	na
Zinc (Zn)													
Sample Result	mg/kg	150	750		463	1153	1425	-	564	482	10060	11102	142
Duplicate Result	mg/kg	150	750		564	1197	1681	-	601	415	16436	10186	98
RpD	%				na	4%	16%		na	na	48%	9%	na
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	<100	-	-	-	<100
Duplicate Result	mg/kg	100	500		-	-	-	-	120	-	-	-	<100
RpD	**%**								na				na
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	261	-	-	-	89
Duplicate Result	mg/kg	2	10		-	-	-	-	357	-	-	-	148
RpD	**%**								31%				**50%**
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	<100	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	<100	-	-	-	-	-
RpD	%							na					
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	266	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	267	-	-	-	-	-
RpD	%							0%					

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table LL-18-2. Loon Lake Snow Dump Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee			Location	Loon Lake Snow Dump				
			Sample ID	LL-12136-F-C	LL-12137-F-C	LL-12138-F-C	LL-12138-F-C	LL-12139-F-C
			Duplicate ID	LL-12357-F-Q	LL-12358-F-Q	LL-12134-F-Q	LL-12359-F-Q	LL-12360-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**				
On Site Field Screening Duplicates								
Lead (Pb)								
Sample Result	mg/kg	70	350	378	408	159	398	420
Duplicate Result	mg/kg	70	350	435	436	<100	396	398
RpD	%			14%	7%	na	1%	6%
Zinc (Zn)								
Sample Result	mg/kg	150	750	1206	1417	460	1524	1443
Duplicate Result	mg/kg	150	750	1339	1381	87	1568	1391
RpD	%			10%	3%	na	3%	4%
Analytical Laboratory Duplicates								
Lead (Pb)								
Sample Result	mg/kg	100	500	-	-	-	-	-
Duplicate Result	mg/kg	100	500	-	-	-	-	-
RpD	%							
Zinc (Zn)								
Sample Result	mg/kg	2	10	-	-	-	-	-
Duplicate Result	mg/kg	2	10	-	-	-	-	-
RpD	%							
Analytical Laboratory Replicates								
Lead (Pb)								
Sample Result	mg/kg	100	500	-	-	-	-	-
Duplicate Result	mg/kg	100	500	-	-	-	-	-
RpD	%							
Zinc (Zn)								
Sample Result	mg/kg	2	10	-	-	-	-	-
Duplicate Result	mg/kg	2	10	-	-	-	-	-
RpD	%							

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

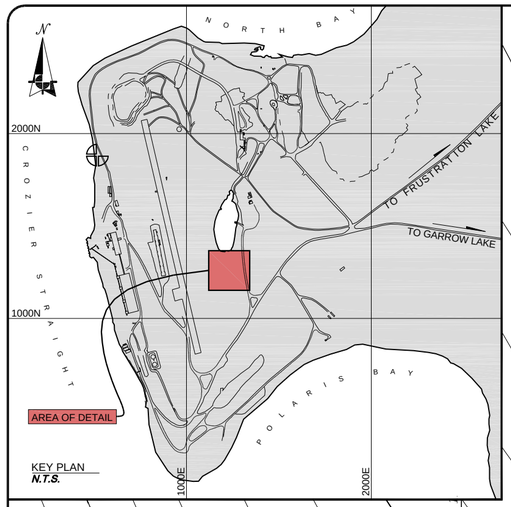

LOON LAKE

SNOW DUMP

ROAD

1043 1044 1045 1046 1047 1048 1049 1050 1051 1052 1053 1054 1055 1056 1057 1058 1059 1060

1100 1200 1300

LL-62 LL-61 LL-60 LL-59 LL-58 LL-57
LL-63 LL-35 LL-34 LL-84 LL-33 LL-85 LL-32 LL-31
LL-64 LL-83 LL-26 LL-27 LL-28 LL-29 LL-30
LL-65 LL-39 LL-25 LL-24 LL-82 LL-23 LL-22 LL-81 LL-80 LL-21
LL-66 LL-40 LL-76 LL-16 LL-17 LL-77 LL-18 LL-19 LL-20
LL-67 LL-41 LL-15 LL-14 LL-13 LL-12 LL-79 LL-11
LL-68 LL-42 LL-75 LL-6 LL-7 LL-8 LL-9 LL-78 LL-10 LL-52
LL-69 LL-74 LL-43 LL-5 LL-73 LL-4 LL-3 LL-72 LL-2 LL-1 LL-71 LL-51
LL-70 LL-44 LL-45 LL-46 LL-47 LL-48 LL-49 LL-50



LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)
- FIELD SCREENING SURFACE SAMPLE (2003/2004 ESA)
- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- FIELD SCREENING RESULTS USING NITON XRF ANALYZER WITH LEAD CONCENTRATIONS IN SOIL <1,500 MG/KG AND/OR ZINC CONCENTRATIONS IN SOIL <8,500 MG/KG
- FIELD SCREENING RESULTS USING NITON XRF ANALYZER WITH LEAD CONCENTRATIONS IN SOIL >=1,500 MG/KG AND/OR ZINC CONCENTRATIONS IN SOIL >=8,500 MG/KG

SOURCE OF DRAWING:

CONTOURS APPROXIMATE, DIGITIZED AND TRANSFORMED FROM BECHTEL FIGURES.

DRAWING INFORMATION:


REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–LL–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

LOON LAKE SNOW DUMP CONDITIONS BEFORE REMEDIATION

Gartner Lee

FIGURE NO. LL-18-1

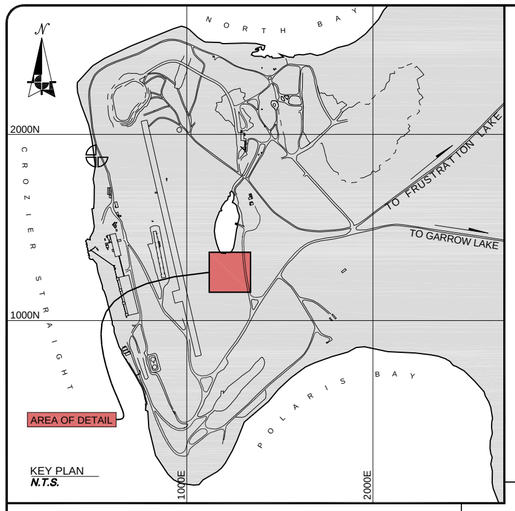


KEY PLAN
N.T.S.

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
LL-11423-F-D	73	170
LL-11462-F-D	294	835
LL-11463-F-D	1620	4430
LL-11502-F-D	<100	210
LL-11532-F-D	810	2280
LL-11753-F-Q duplicate of LL-11532-F-D	930	2370
LL-11605-F-C	160	507
LL-11606-F-C	140	390
LL-11607-F-C	170	540
LL-11608-F-C	<100	160
LL-11609-F-C	160	464
LL-11610-F-C	200	584
LL-11611-F-C	150	460
LL-11612-F-C	170	413
LL-11613-F-C	110	335
LL-11614-F-C	<100	269
LL-11615-F-C	105	296
LL-11616-F-C	<100	191
LL-11617-F-C	150	435
LL-11618-F-C	250	723
LL-11709-F-Q duplicate of LL-11618-F-C	300	880
LL-11619-F-C	110	138
LL-11620-F-C	<100	110
LL-11621-F-C	<100	162
LL-11622-F-C	<100	141
LL-11623-F-C	110	344
LL-11697-F-C	1360	3150
LL-11698-F-C	1400	3560
LL-11699-F-C	700	2220
LL-11737-F-C	680	1780
LL-11738-F-C	210	267
LL-11739-F-C	150	355
LL-11740-F-C	680	1740
LL-11741-F-C	1010	2970
LL-11742-F-Q duplicate of LL-11741-F-C	1210	3520
LL-11800-F-C	1150	2940
LL-11802-F-C	1880	7660
LL-11939-F-C	970	2590
LL-11941-F-C	1940	7460
LL-11944-F-C	255	650
LL-11946-F-C	1690	9410
LL-11954-F-C	490	1280
LL-12051-F-C	1140	2760
LL-12052-F-C	1340	3380
LL-12054-F-C	310	734
LL-12055-F-C	380	976
LL-12056-F-C	1980	3020
LL-12319-F-Q duplicate of LL-12056-F-C	**2200**	4100
LL-12061-F-C	140	409
LL-12063-F-C	<100	406
LL-12064-F-C	450	1510
LL-12065-F-C	670	1210
LL-12066-F-C	104	1190
LL-12075-F-C	<50	108
LL-12076-F-D	<100	95
LL-12077-F-C	<100	266
LL-12078-F-C	<100	261
LL-12079-F-Q duplicate of LL-12078-F-C	120	357
LL-12080-F-C	100	341
LL-12081-F-C	100	328
LL-12084-F-C	<100	221
LL-12085-F-D	<100	6
LL-12104-F-C	150	367
LL-12105-F-C	250	654
LL-12110-F-C	74	312
LL-12128-F-C	<100	89.1
LL-12135-F-Q duplicate of LL-12128-F-C	<100	148
LL-12136-F-C	182	518
LL-12137-F-C	180	637
LL-12138-F-C	159	460
LL-12139-F-C	210	656

Bold	**Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

Lead	2000 mg/kg
Zinc	10000 mg/kg

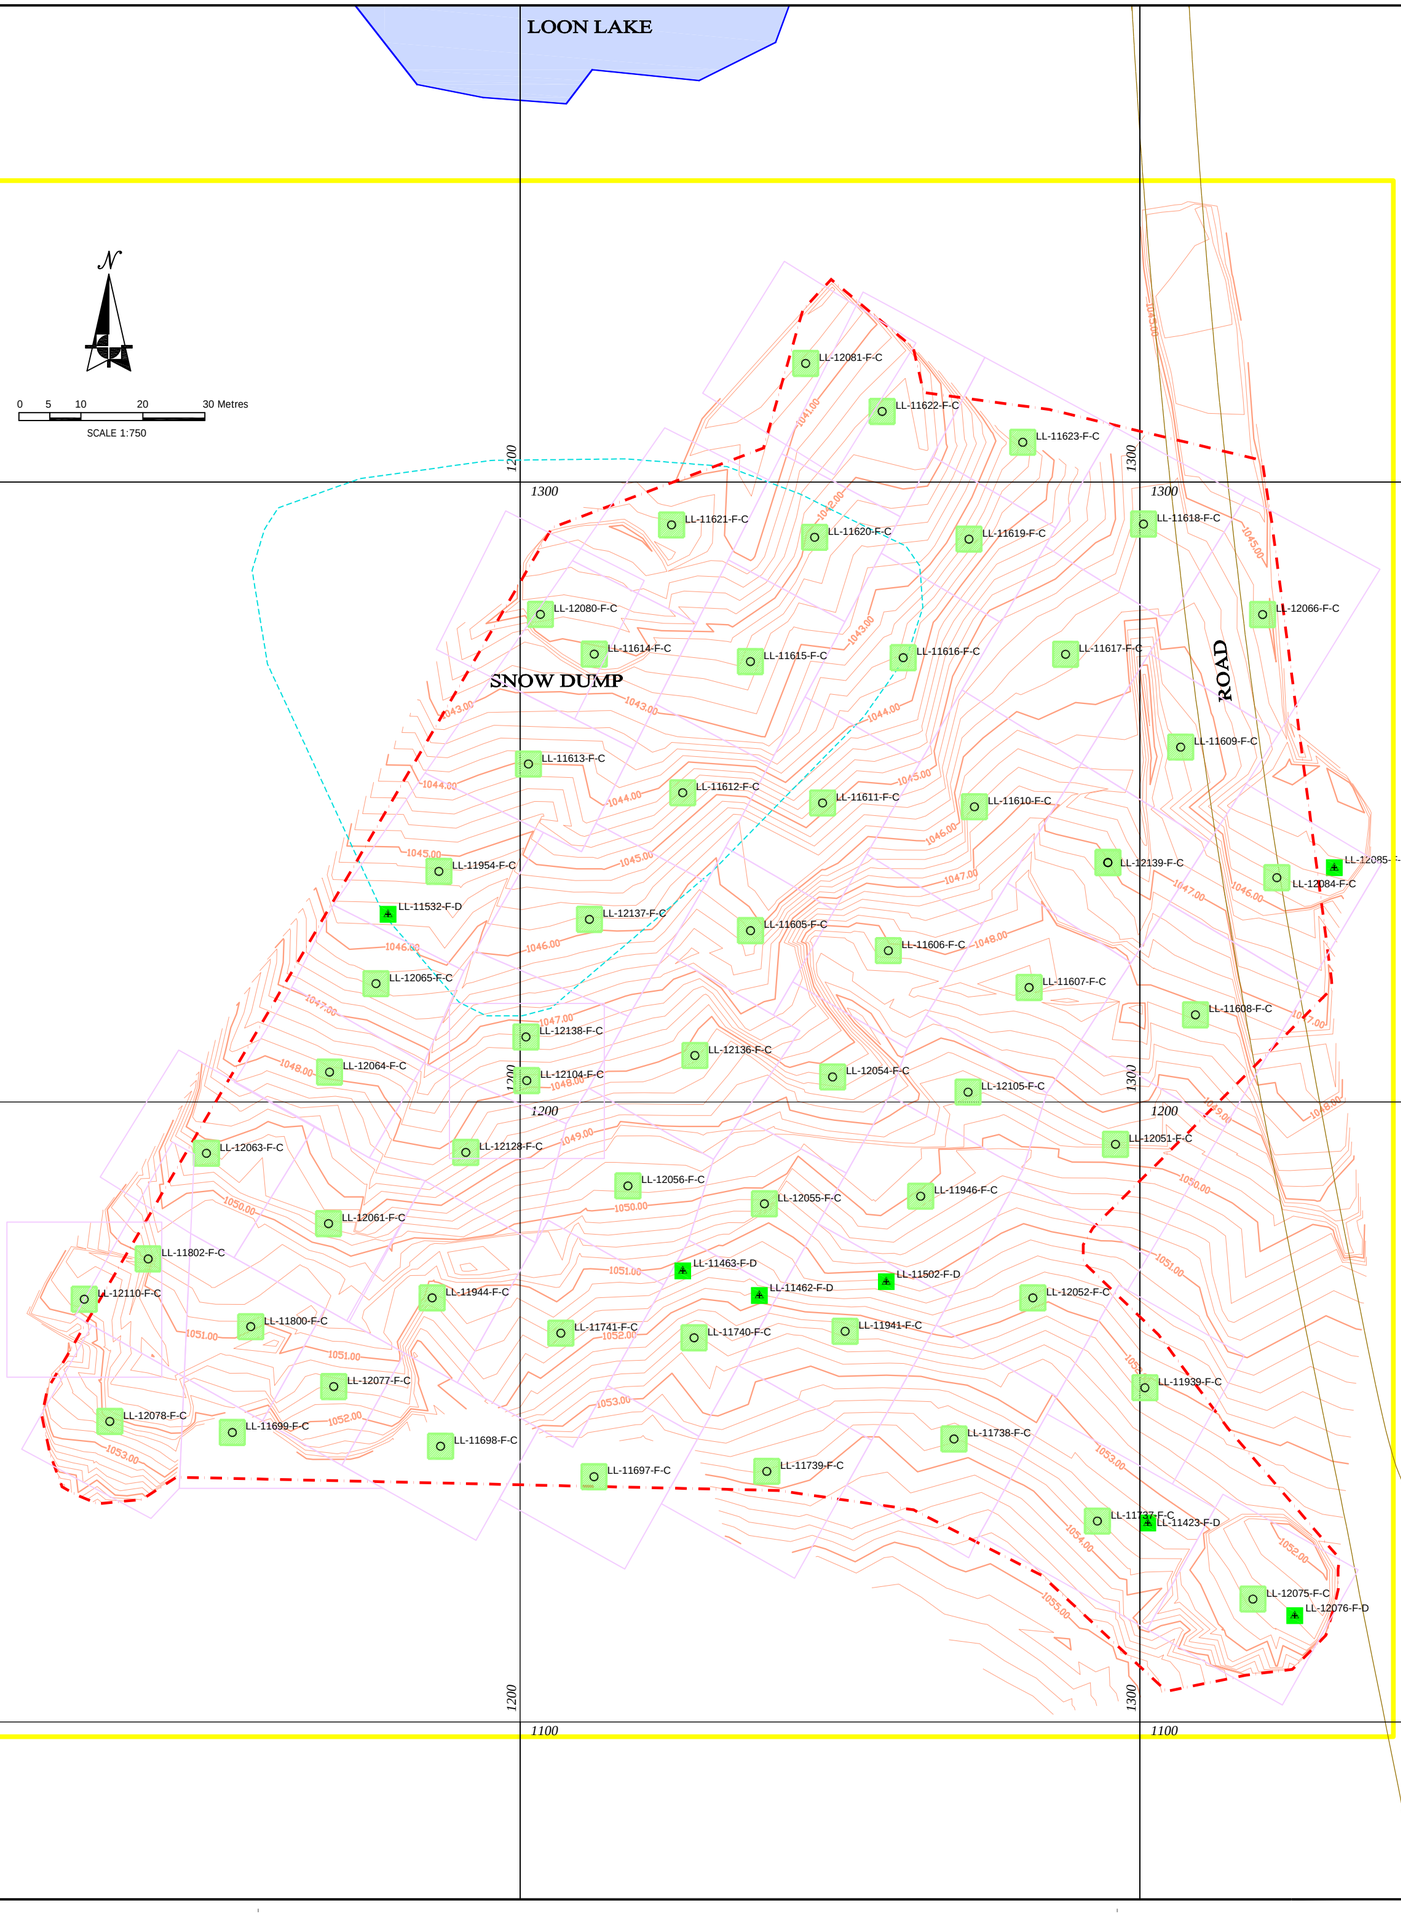

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

ESP–7–I–D
- AREA
- SAMPLE ID
- TYPE: C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA, WALL–5 SAMPLES ALONG 25m OF WALL; D= DISCRETE SAMPLE; Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
- LOCATION: F= FLOOR SAMPLE; I= INTERMEDIATE FLOOR SAMPLE; W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

SOURCE OF DRAWING:

CONTOURS APPROXIMATE, DIGITIZED AND TRANSFORMED FROM BECHTEL FIGURES.

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–LL–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

LOON LAKE SNOW DUMP CONDITIONS AFTER REMEDIATION

Gartner Lee

FIGURE NO. LL-18-2

Appendix H

Firehall

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: Firehall

BACKGROUND

The Firehall (shown as Area 21 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*) was located north of the former Process Barge.

The Firehall building was a steel building with a concrete floor that served as a storage facility for fire fighting gear and a water truck. An above ground fuel storage tank was located on the west wall of the Firehall building. The 1972 exploration decline portal was located 20 m north of the Firehall building. The rock removed from the 1972 exploration decline portal was stockpiled on the slope to the west. During operations, snow was dumped on the slope west of the exploration portal. A 100 man trailer camp was constructed to the north of the portal. An above ground fuel tank was located on the south side of the camp. Portions of the 100 man trailer camp served as a location for mine rescue and firefighting training during mine operations.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified metal and hydrocarbon contamination in the soil in the Firehall area. Twenty two samples, from fourteen test pits were analyzed for extractable petroleum hydrocarbons (EPH), Lead and Zinc during the ESA. The sample results indicated that elevated metal concentrations in the soil were present from surface to a depth of at least 1.2 m along the slope west of the exploration portal. Hydrocarbon contamination was detected at the south end of the 100 man trailer camp and adjacent to the west and north walls of the Firehall Building. Figure FH-21-1: *Firehall*

Conditions Before Remediation illustrates the sample results from the ESA, the area estimated following the ESA to be of concern for metal and hydrocarbon contamination, as well as the topography of the area prior to remediation.

METHODOLOGY

Delineation

The preliminary boundaries of the remediation area, as identified in the ESA as "Areas of Concern", were further delineated for excavation on the basis of field screening measurements obtained from twenty (20) boreholes drilled and sampled in 2003. The boreholes were advanced with an air rotary quarry drill and composite soil samples were collected over 0.6 m (2 foot) intervals to a maximum depth of 4.9 m. The soil samples were collected from the drill returns that accumulated at the mouth of the borehole. Following the collection of each sample the surface surrounding the borehole was cleared of the drill cuttings, and fresh snow was exposed.

The visual appearance, odour of the soil and field screening measurements obtained from the borehole samples were used to delineate the area to be excavated. Lead and Zinc field screening measurements were obtained using a Niton portable X-Ray Fluorescence (XRF) elemental analyzer in accordance with standard Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols. Hydrocarbon field screening measurements were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. Based on the results of the field screening GLL modified the extent of the area to be excavated as indicated by the "Limit of Remedial Excavation" shown on Figure FH-21-2.

Excavation

Excavation of the contaminated soils in the Firehall area commenced July 1, 2003 following the demolition of the 100 man trailer camp, but prior to the demolition of the Firehall building and the decommissioning of the access roads. In 2003 contaminated soil was excavated above the access road to the main portal and to within 15 m of west side of the Firehall building.

Excavation of contaminated soil in the Firehall area ceased September 8, 2003 when no more contaminated soil could be excavated without removal of the roads or additional buildings. Hydrocarbon contamination remained present in the east wall of the excavation adjacent to the Firehall building at this time. Plastic sheeting was placed along the east wall and a portion of the excavated area backfilled with clean soil in order to improve road access.

In 2004, the Firehall building was demolished and the access road to the main portal removed. Excavation of contaminated soil on the slope west of the exploration portal commenced April 28, 2004 and continued until field screening results indicated that the area would meet the Soil Quality Remediation Objectives (SQRO's) on June 30, 2004. The Firehall building was demolished on May 22, 2004. The excavation of the remaining contaminated soil at the former building commenced May 23, 2004 and was completed by July 6, 2004. The excavation at the former building extended westward until the plastic liner placed in 2003 was intersected.

Soil samples were collected across the floor of the excavation and along the walls. The visual appearance and odour of the soil along with the field screening measurements obtained with the PID and the XRF analyzer were used to further direct the excavation. All material excavated was disposed of in the mine workings in accordance with regulatory approvals. The limits of the excavation are shown on Figure FH-21-2: *Firehall Conditions After Remediation*.

Confirmation Sampling

Upon receipt of field screening results that indicated that the soil remaining in the excavation would meet the SQRO's, confirmation soil samples were collected. The excavation area was subdivided into individual composite sampling areas approximately 25 m by 25 m or less as required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation. Composite samples were created by collecting four or five evenly spaced allocates of soil with in the individual composite sample area. A single allocate of soil from a specific point is a discrete sample.

The soil samples were collected at the excavation limits and submitted to ALS Environmental for analysis of EPH, metals and Polycyclic Aromatic Hydrocarbons (PAH). Additional excavation was undertaken in areas where the laboratory analytical results did not meet the SQRO's and confirmatory samples at the base of excavation. Upon receipt of the analytical results that met the SQRO's for EPH, Lead and Zinc the final excavation limits were surveyed.

ANALYTICAL RESULTS

Quality Assurance and Quality Control (QA/QC)

QA/QC measures associated with collecting and analyzing soil were implemented during the remediation of the Firehall area, including the comparison of on-site field screening samples, the submission of blind duplicates to the analytical laboratory, and the analysis of analytical

laboratory replicates. Relative percent differences (RpDs) have been calculated and compiled in Table FH-21-04 for four (4) analytical laboratory duplicates and four (4) analytical laboratory replicates for hydrocarbon concentrations and Table FH-21-05 for twenty seven (27) field screening duplicates, three (3) analytical laboratory duplicates and six (6) analytical laboratory replicates for Lead and Zinc concentrations for a total of forty four (44) QA/QC samples.

Forty two (42) of the sample sets either returned results below the practical quantitation limit, in which case the RpD value has been identified as "na" (not applicable) or the sample result and its duplicate/replicate result had an acceptable RpD below the site specific remediation objective of 50%. One analytical laboratory duplicate and one analytical laboratory replicate returned RpDs greater than the objective. The variance between these samples and their duplicate/replicate is considered indicative of sample heterogeneity, especially at low concentration levels of Zinc as compared to the SQRO's. The metal QA/QC samples from the Firehall area serve to document the variable nature of the metal concentrations in the soil at the Polaris Mine.

Discussion

Analytical laboratory results for EPH, metals and PAH are summarized in Tables FH-21-01, FH-21-02 and FH-21-03 respectively, along with approved Polaris Mine SQRO's for petroleum hydrocarbons and metals. A total of forty four (44) remediation confirmation soil samples were submitted from the footprint of the area excavated area as follows: nineteen (19) composite floor samples, eighteen (18) composite wall samples, four (4) discrete samples and three (3) Quality Assurance and Quality Control (QA/QC) samples. The soil quality results and lateral limits of the excavation are shown on Figure FH-21-02: *Firehall Conditions After Remediation*.

Discrete samples (for EPH, Lead and Zinc) were collected in addition to the composite sample to discern the homogeneity of the sample area. The table below compares discrete samples to the individual composite sample areas they represented. The results show a variable nature in the metal concentrations and a homogeneity in the hydrocarbon concentrations. These results generally conform to the QA/QC sample data.

Summary of Discrete Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	Lead mg/kg	Zinc mg/kg	EPH C_{10}-C_{19} mg/kg	EPH C_{19}-C_{32} Mg/kg	Discrete Sample ID	Lead mg/kg	Zinc mg/kg	EPH C_{10}-C_{19} mg/kg	EPH C_{19}-C_{32} mg/kg
FH-28-F-C	998	7,890	<200	<200	FH-27-F-D	474	4550	<200	<200
FH-11135-W-C	1,190	7,770	210	<200	FH-11136-W-D	<100	122	420	<200
FH-11344-W-C	250	923	370	<200	FH-11345-W-D	<100	257	320	<200
FH-11922-F-C	<100	169	240	320	FH-11907-F-D	<100	137	<200	270

Thirty four (34) hydrocarbon samples were analyzed for EPH. Of this set, four randomly selected samples were extracted for PAH. Forty one (41) metals samples were submitted for analysis of Lead and Zinc. Of this set, three randomly selected samples were analyzed for total metals.

All the remediation confirmation samples results from the Firehall area meet the SQRO's for EPH, Lead and Zinc. All the samples analyzed for PAH returned values below the generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for parkland land use. One of the three samples analyzed for total metals returned a Barium concentration of 667 mg/kg, which is greater than the generic CCME CEQG for parkland land use of 500 mg/kg Barium in soil.

The presence of Barium concentrations in the soil above the generic CCME guidelines for parkland land use is attributed to natural background mineralogy. Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone. This is demonstrated through soil samples as described below.

Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results,* are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of Barium greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of Barium concentrations in those samples listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of Barium remaining within the footprint of the Firehall area after remediation are within the range of the background concentrations. In addition, the immobile nature of the Barium encountered on site was demonstrated in the ESA leachate test results that returned Barium concentrations at levels less than the detection limit and it was therefore not identified as a contaminant of concern in the ESA.

The confirmatory samples supported by the QA/QC samples from the Firehall area provide confidence that the remediation of the area complies with the SQRO's.

CONCLUSION

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the former Firehall area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgment in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is

not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Brenda Bolton, B.A., B.Sc.
Environmental Geologist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:BB:gc

ATTACHMENTS

Tables

Table FH-21-1	Firehall Remediation Confirmation Soil Samples – Hydrocarbons
Table FH-21-2	Firehall Remediation Confirmation Soil Samples – Metals
Table FH-21-3	Firehall Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table FH-21-4	Firehall Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons
Table FH-21-5	Firehall Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure FH-21-1	Firehall Conditions Before Remediation
Figure FH-21-2	Firehall Conditions After Remediation

Table FH-21-1. Firehall Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Fire Hall						
		Sample ID	FH-27-F-D	FH-28-F-C	FH-104-F-D	FH-10958-F-C	FH-11016-W-C	FH-11124-W-C	FH-11126-F-C
		Date Sampled	09-Jul-03	09-Jul-03	05-Aug-03	26-Jun-04	01-Jun-04	31-May-04	01-Jun-04
		ALS File Number	T1369	T1369	T2589	U4054r	U4137	U4137	U4137
		Field Screen (ppm)[b]	85	60	-		55	40	60
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	240	910	<200	420	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	760	<200
LEPH[c]	1000	mg/kg	-	-	240	-	<200	-	<200
HEPH[c]	1000	mg/kg	-	-	<200	-	<200	-	<200

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FH-21-1. Firehall Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Fire Hall						
		Sample ID	FH-10472-F-Q	FH-11135-W-C	FH-11136-W-D	FH-11209-F-C	FH-11275-F-C	FH-11344-W-C	FH-11370-W-Q
		Date Sampled	31-May-04	01-Jun-04	01-Jun-04	02-Jun-04	31-May-04	09-Jun-04	09-Jun-04
		ALS File Number	duplicate of	U4137	U4137	U4269r	U4137	U4484	duplicate of
		Field Screen (ppm)[b]	FH-11126-F-C	60	145	70	40	30	FH-11344-W-C
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	210	440	780	460	370	770
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	230	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FH-21-1. Firehall Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Fire Hall						
		Sample ID	FH-11345-W-D	FH-11346-W-C	FH-11347-F-C	FH-11348-W-C	FH-11349-F-C	FH-11478-W-C	FH-11479-W-C
		Date Sampled	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	15-Jun-04	15-Jun-04
		ALS File Number	U4484	U4484	U4484	U4484	U4484	U4704r	U4704r
		Field Screen (ppm)[b]	50	45	50	25	15	25	25
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	320	970	490	340	270	270	210
EPH C_{19}-C_{32}	1000	mg/kg	<200	230	<200	<200	<200	500	460
LEPH[c]	1000	mg/kg	-	-	490	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	<200	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FH-21-1. Firehall Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Fire Hall						
		Sample ID	FH-11572-W-C	FH-11635-W-C	FH-11735-W-C	FH-11736-F-C	FH-11764-F-C	FH-11765-F-Q	FH-11803-W-C
		Date Sampled	21-Jun-04	23-Jun-04	21-Jun-04	21-Jun-04	05-Jul-04	05-Jul-04	28-Jun-04
		ALS File Number	U4948	U5050	U4948	U4948	U5597r	duplicate of	U5223
		Field Screen (ppm)[b]	20	20	5	-	-	FH-11764-F-C	20
Parameter	**Site Specific**	**Units**	**Analytical Results**						
Extractable Hydrocarbons									
EPH C_{10}-C_{19}	1000	mg/kg	<200	220	<200	550	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	430	<200	<200	320	390	300
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use as .

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FH-21-1. Firehall Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Fire Hall					
		Sample ID	FH-11805-W-C	FH-11862-F-C	FH-11863-F-C	FH-11864-F-C	FH-11907-F-D	FH-11922-F-C
		Date Sampled	29-Jun-04	30-Jun-04	30-Jun-04	30-Jun-04	06-Jul-04	06-Jul-04
		ALS File Number	U5223	U5353r	U5353r	U5353r	U5597r	U5597r
		Field Screen (ppm)[b]	-	-	-	-	15	-
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	230	<200	240
EPH C_{19}-C_{32}	1000	mg/kg	370	<200	<200	400	270	350
LEPH[c]	1000	mg/kg	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table FH-21-2. Firehall Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Firehall								
				Sample ID	FH-27-F-D	FH-28-F-C	FH-105-F-C	FH-111-W-C	FH-112-116-F-C	FH-117-121-W-C	FH-160-F-C	FH-163-W-C	FH-10958-F-C
				Date Sampled	09-Jul-03	09-Jul-03	07-Aug-03	07-Aug-03	07-Aug-03	07-Aug-03	15-Aug-03	20-Aug-03	26-Jun-04
				ALS File Number	T1369	T1369	T2886	T2886	T2886	T2886	T3069	T3179	U4054r
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	-	-	270	199	-	-	116	52	-
				Field Screen Zn (ppm)[b]	-	-	1467	513	-	-	548	448	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**								
pH		-	-	-	-	-	-	-	-	-	-	-	-
Total Metals													
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	474	998	<200	<200	<200	514	212	148	300
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	4550	7890	883	791	145	793	428	940	4500

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-2. Firehall Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Firehall							
				Sample ID	FH-11016-W-C	FH-11124-W-C	FH-11126-F-C	FH-10472-F-Q	FH-11135-W-C	FH-11136-W-D	FH-11209-F-C	FH-11275-F-C
				Date Sampled	01-Jun-04	31-May-04	01-Jun-04	01-Jun-04	01-Jun-04	01-Jun-04	02-Jun-04	31-May-04
				ALS File Number	U4137	U4137	U4137	U4137	U4137	U4137	U4269r	U4137
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	100	382	123	duplicate of	731	21	258	144
				Field Screen Zn (ppm)[b]	508	1253	894	FH-11126-F-C	4003	123	1285	566
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	-	-	8.34	-	-	-	-	-
Total Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<20	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	<10	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	452	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<1	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	1.2	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	<4	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<4	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	3	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	230	1160	150	180	1190	<100	160	260
Mercury	T-Hg	-	6.6	mg/kg	-	-	<0.05	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<8	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	<10	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	<4	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	<4	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	<10	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	20	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	2230	2450	474	1610	7770	122	884	802

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-2. Firehall Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Firehall							
				Sample ID	FH-11344-W-C	FH-11370-W-Q	FH-11345-W-D	FH-11346-W-C	FH-11347-F-C	FH-11348-W-C	FH-11349-F-C	FH-11478-W-C
				Date Sampled	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	09-Jun-04	15-Jun-04
				ALS File Number	U4484	U4484	U4484	U4484	U4484	U4484	U4484	U4704r
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	240	duplicate of	112	489	287	317	320	-
				Field Screen Zn (ppm)[b]	1100	FH-11344-W-C	610	1812	917	1882	1010	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	-	-	-	-	8.68	-	-	-
Total Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	<20	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	<10	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	455	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	<1	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	4.5	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	<4	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	<4	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	3	-	-	-
Lead	T-Pb	2000	-	mg/kg	250	240	<100	460	180	480	230	<100
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	-	<0.05	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	<8	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	<10	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	<4	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	<4	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	<10	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	18	-	-	-
Zinc	T-Zn	10000	-	mg/kg	923	917	254	1880	1370	1770	1180	225

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-2. Firehall Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Firehall							
				Sample ID	FH-11479-W-C	FH-11572-W-C	FH-11635-W-C	FH-11666-W-C	FH-11667-W-C	FH-11668-F-C	FH-11735-W-C	FH-11736-F-C
				Date Sampled	15-Jun-04	21-Jun-04	23-Jun-04	25-Jun-04	25-Jun-04	25-Jun-04	21-Jun-04	21-Jun-04
				ALS File Number	U4704r	U4948	U5050	U5223	U5223	U5223	U4948	U4948
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	-	-	32	72	75	57	200	-
				Field Screen Zn (ppm)[b]	-	-	203	281	243	208	901	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	-	-	-	8.02	-	-	-	-
Total Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<10	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	9.4	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	**667**	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<0.5	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	0.61	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	12	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	7	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	30	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	180	300	<50	54	65	<50	200	<100
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	0.118	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	4	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	38	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<3	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<2	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<5	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	85	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	388	2190	56.5	135	195	142	704	25.7

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-2. Firehall Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	Firehall							
				Sample ID	FH-11764-F-C	FH-11765-F-Q	FH-11862-F-C	FH-11863-F-C	FH-11864-F-C	FH-11873-F-C	FH-11907-F-D	FH-11922-F-C
				Date Sampled	05-Jul-04	05-Jul-04	30-Jun-04	30-Jun-04	30-Jun-04	05-Jul-04	06-Jul-04	06-Jul-04
				ALS File Number	U5597r	U5597r	U5353r	U5353r	U5353r	U5597r	U5597r	U5597r
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	-	duplicate of	-	-	-	-	92	-
				Field Screen Zn (ppm)[b]	-	FH-11764-F-C	-	-	-	-	249	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**							
pH		-	-	-	-	-	-	-	-	-	-	-
Total Metals												
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	140	120	<100	<100	190	310	<100	<100
Mercury	T-Hg	-	6.6	mg/kg	-	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	386	280	23.5	71.5	572	165	137	169

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-3. Firehall Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	Firehall			
		Sample ID	FH-104-F-D	FH-11016-W-C	FH-11126-F-C	FH-11347-F-C
		Date Sampled	05-Aug-03	01-Jun-04	01-Jun-04	09-Jun-04
		ALS File Number	T2589	U4137	U4137	U4484
		Field Screen (ppm)[b]	-	55	60	50
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**			
Polycyclic Aromatic Hydrocarbons						
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	0.07	<0.05	<0.05	<0.2
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table FH-21-4. Firehall Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee				Location	Firehall							
				Sample ID	FH-11017-W-C	FH-11123-F-C	FH-11126-F-C	FH-11344-W-C	FH-11349-F-C	FH-11738-W-C	FH-11764-F-C	FH-11764-F-C
				Duplicate ID	QC# 389244	QC# 389245	FH-10472-W-Q	FH-11370-W-Q	QC# 390735	QC# 392657	FH-11765-F-Q	QC# 395247
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
Analytical Laboratory Duplicates												
EPH C_{10}-C_{19}												
Sample Result	mg/kg	200	1000		-	-	<200	370	-	-	<200	<200
Duplicate Result	mg/kg	200	1000		-	-	<200	770	-	-	<200	250
RpD	**%**						na	na			na	na
EPH C_{19}-C_{32}												
Sample Result	mg/kg	200	1000		-	-	<200	<200	-	-	320	320
Duplicate Result	mg/kg	200	1000		-	-	<200	<200	-	-	390	450
RpD	**%**						na	na			na	na
Analytical Laboratory Replicates												
EPH C_{10}-C_{19}												
Sample Result	mg/kg	200	1000		<200	1460	-	-	270	<200	-	-
Duplicate Result	mg/kg	200	1000		<200	1890	-	-	270	<200	-	-
RpD	**%**				na	26%			na	na		
EPH C_{19}-C_{32}												
Sample Result	mg/kg	200	1000		<200	520	-	-	<200	<200	-	-
Duplicate Result	mg/kg	200	1000		<200	460	-	-	<200	<200	-	-
RpD	**%**				na	na			na	na		

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table FH-21-5. Firehall Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Firehall								
				Sample ID	FH-BH-2-4-C	FH-BH-2-7-C	FH-BH-5-3-C	FH-BH-7-4-C	FH-BH-8-8-C	FH-BH-9-2-C	FH-BH-10-1-C	FH-BH-11-4-C	FH-BH-12-2-C
				Duplicate ID	FH-BH-2-4-Q	FH-BH-2-9-Q	FH-BH-5-10-Q	FH-BH-7-10-Q	FH-BH-8-11-Q	FH-BH-9-8-Q	FH-BH-10-9-Q	FH-BH-11-8-Q	FH-BH-12-10-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)					na								
Sample Result	mg/kg	70	350		152	20	20	20	485	2419	1450	40	54
Duplicate Result	mg/kg	70	350		121	20	20	32	418	2109	1829	51	80
RpD	%				na	na	na	na	15%	14%	23%	na	na
Zinc (Zn)													
Sample Result	mg/kg	150	750		411	60	60	610	3120	13299	5459	431	287
Duplicate Result	mg/kg	150	750		418	225	60	598	3328	12800	6349	171	303
RpD	%				na	na	na	na	6%	4%	15%	na	na
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	%												
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-
RpD	%												

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table FH-21-5. Firehall Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Firehall								
				Sample ID	FH-BH-13-2-C	FH-BH-14-6-C	FH-BH-15-1-C	FH-BH-15-3-C	FH-BH-18-3-C	FH-BH-18-7-C	FH-59-W-D	FH-97-F-C	FH-105-F-C
				Duplicate ID	FH-BH-13-6-Q	FH-BH-14-7-Q	FH-BH-15-7-Q	FH-BH-15-8-Q	FH-BH-18-8-Q	FH-BH-18-9-Q	FH-165-W-Q	FH-98-F-Q	FH-105-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		1160	67	374	2680	40	130	6860	285	270
Duplicate Result	mg/kg	70	350		994	53	287	2290	34	108	6264	318	272
RpD	%				15%	na	na	16%	na	na	9%	na	na
Zinc (Zn)													
Sample Result	mg/kg	150	750		6829	225	1550	27699	404	577	37016	1764	1467
Duplicate Result	mg/kg	150	750		5978	214	1160	25498	347	465	37923	1102	1396
RpD	%				13%	na	29%	8%	na	na	2%	46%	5%
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-	-
RpD	%												
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-
RpD	%												
Zinc (Zn)													
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-
RpD	%												

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table FH-21-5. Firehall Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Firehall								
				Sample ID	FH-110-W-D	FH-111-W-C	FH-135-W-D	FH-145-W-D	FH-158-F-D	FH-11126-F-C	FH-11344-W-C	FH-11764-F-C	FH-11764-F-C
				Duplicate ID	FH-110-W-Q	QC# 350292	FH-139-W-Q	FH-148-W-Q	FH-158-F-Q	FH-10472-W-Q	FH-11370-W-Q	FH-11765-F-Q	QC# 395247
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		204	199	12790	11203	55	-	-	-	-
Duplicate Result	mg/kg	70	350		190	195	13627	7220	65	-	-	-	-
RpD	%				na	na	6%	43%	na				
Zinc (Zn)													
Sample Result	mg/kg	150	750		593	513	72354	72692	304	-	-	-	-
Duplicate Result	mg/kg	150	750		603	455	61522	54744	684	-	-	-	-
RpD	%				na	na	16%	28%	na				
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	150	250	140	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	180	240	120	-
RpD	%									18%	4%	15%	
Zinc (Zn)													
Sample Result	mg/kg	2	10		-	-	-	-	-	474	923	386	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	1610	917	280	-
RpD	%									**109%**	1%	32%	
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	<200	-	-	-	-	-	-	140
Duplicate Result	mg/kg	100	500		-	232	-	-	-	-	-	-	120
RpD	%					na							15%
Zinc (Zn)													
Sample Result	mg/kg	3	15		-	791	-	-	-	-	-	-	386
Duplicate Result	mg/kg	3	15		-	1720	-	-	-	-	-	-	342
RpD	%					**74%**							12%

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table FH-21-5. Firehall Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	Firehall							
				Sample ID	FH-11017-W-C	FH-11123-F-C	FH-11349-F-C	FH-11726-F-D	FH-11668-F-C	FH-11691-W-D	FH-11580-F-D	FH-11738-W-C
				Duplicate ID	QC# 389244	QC# 389245	QC# 390735	FH-11711-F-Q	FH-11716-F-Q	FH-11718-W-Q	FH-11720-F-Q	QC# 392657
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350		-	-	-	45	57	37	24	-
Duplicate Result	mg/kg	70	350		-	-	-	25	77	55	30	-
RpD	%							na	na	na	na	
Zinc (Zn)												
Sample Result	mg/kg	150	750		-	-	-	147	208	220	205	-
Duplicate Result	mg/kg	150	750		-	-	-	187	219	375	179	-
RpD	%							na	na	na	na	
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-
RpD	%											
Zinc (Zn)												
Sample Result	mg/kg	2	10		-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	2	10		-	-	-	-	-	-	-	-
RpD	%											
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		120	1390	230	-	-	-	-	200
Duplicate Result	mg/kg	100	500		<100	1500	240	-	-	-	-	180
RpD	%				na	8%	0					11%
Zinc (Zn)												
Sample Result	mg/kg	3	15		552	4270	1180	-	-	-	-	704
Duplicate Result	mg/kg	3	15		376	4140	992	-	-	-	-	533
RpD	%				38%	3%	17%					28%

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

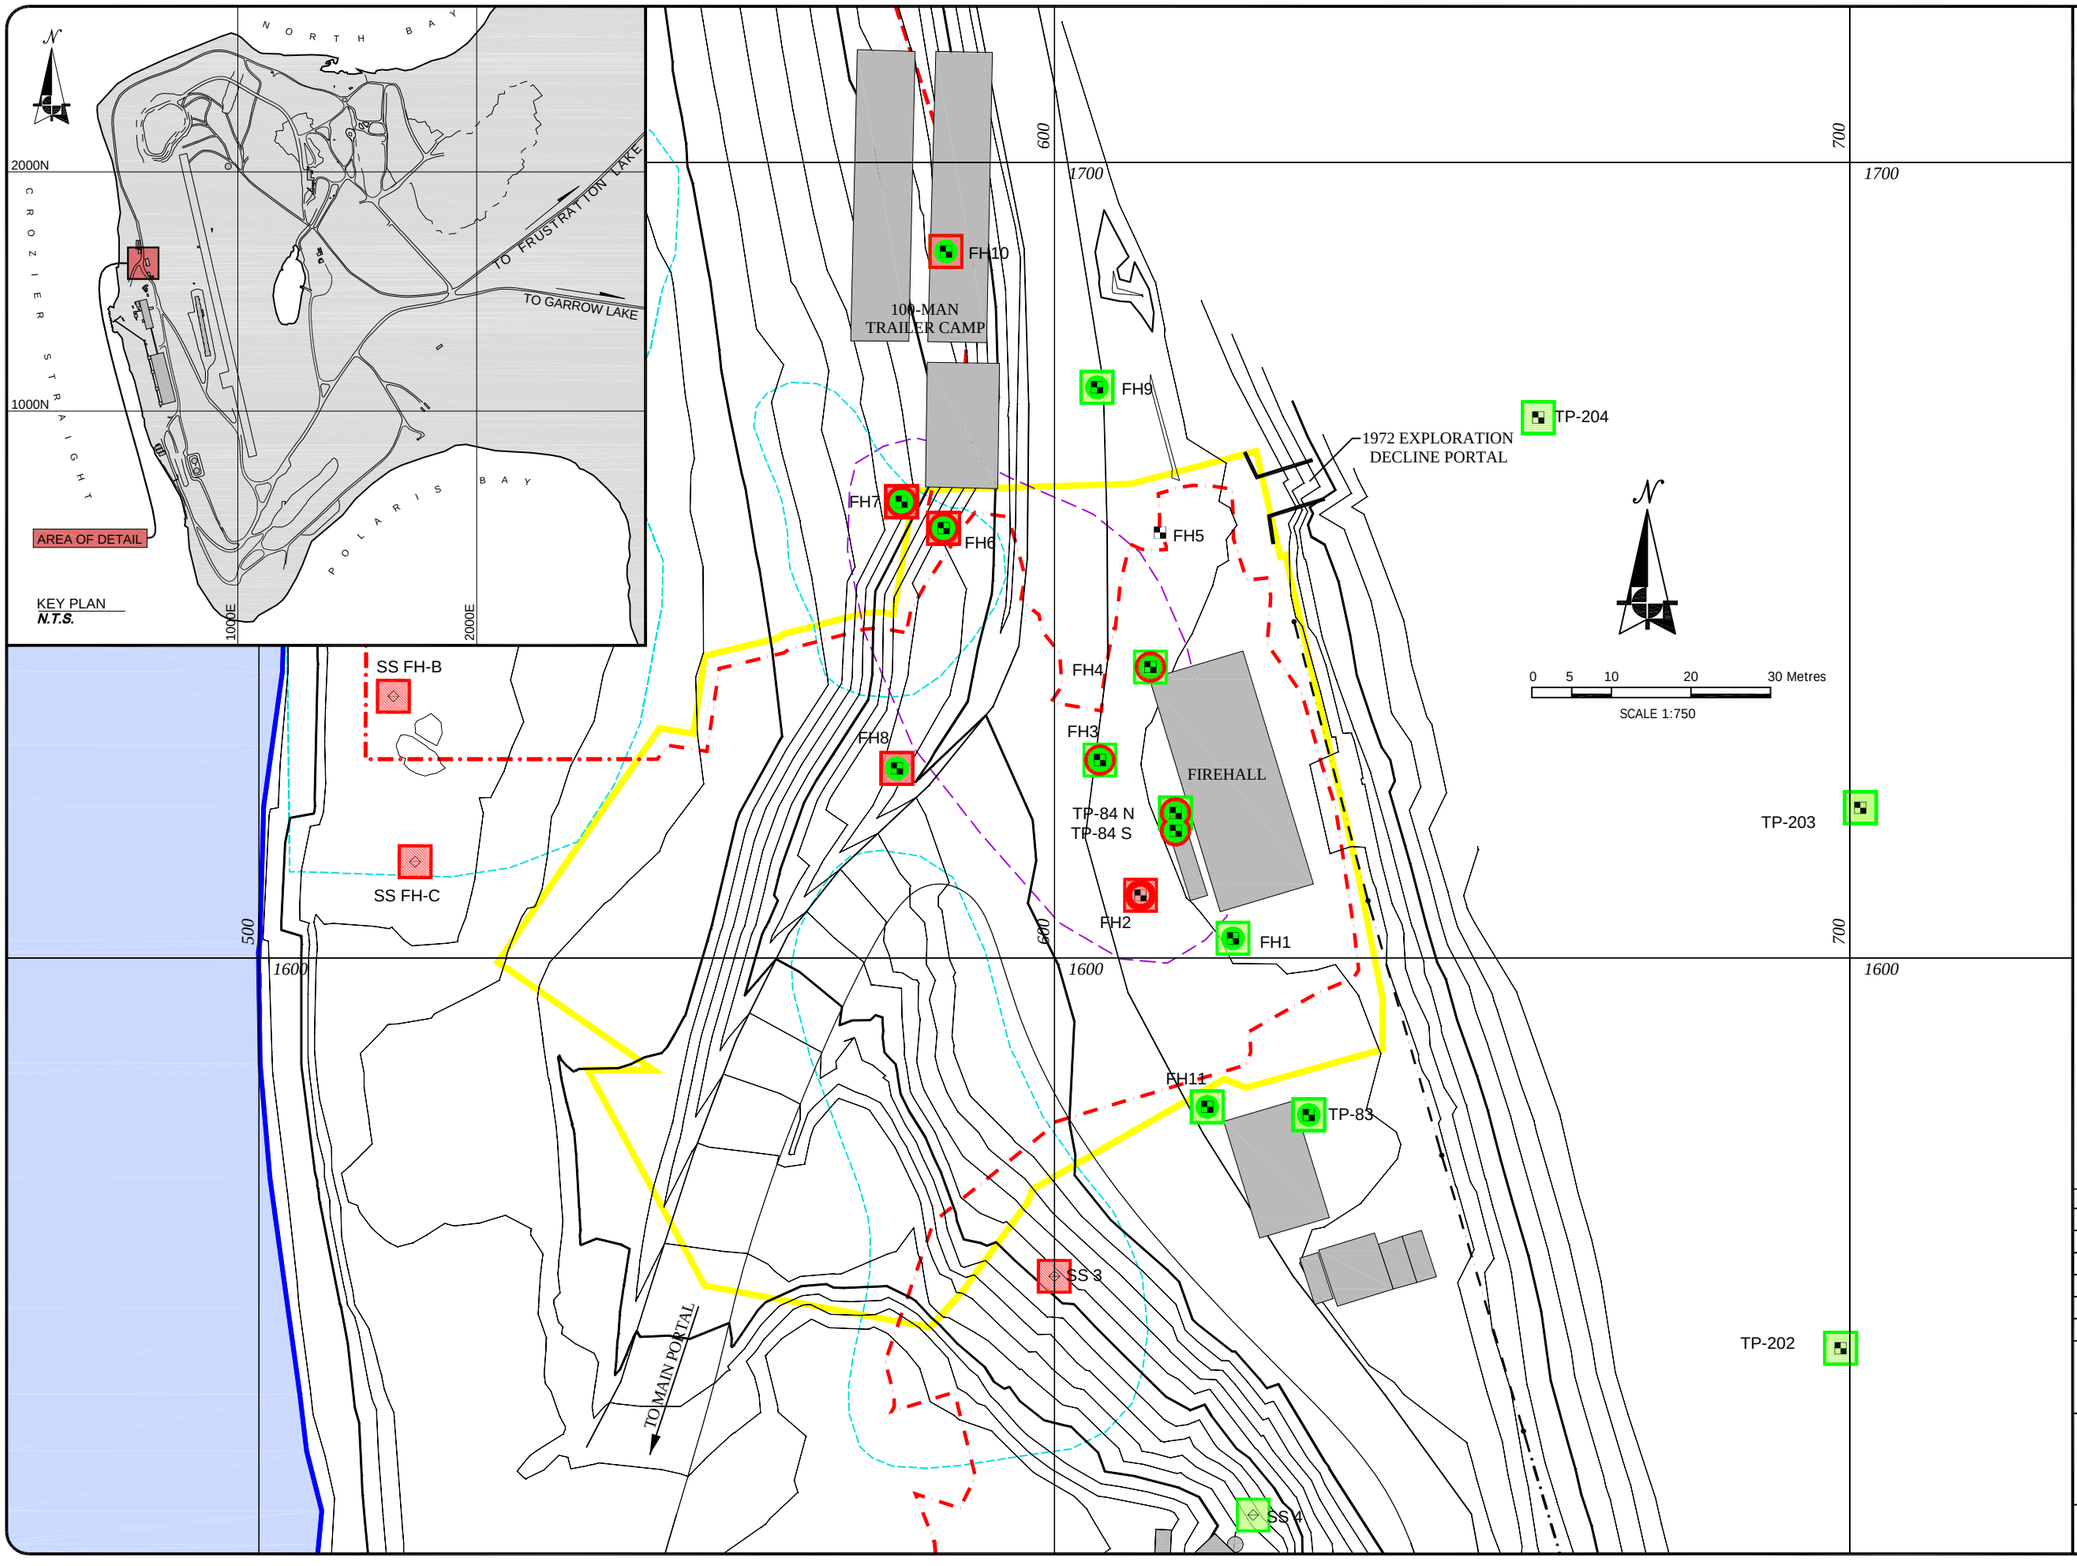

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20-6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)

- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)

- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS


DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–FH–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

FIREHALL CONDITIONS BEFORE REMEDIATION

Gartner Lee

Figure No. **FH-21-1**

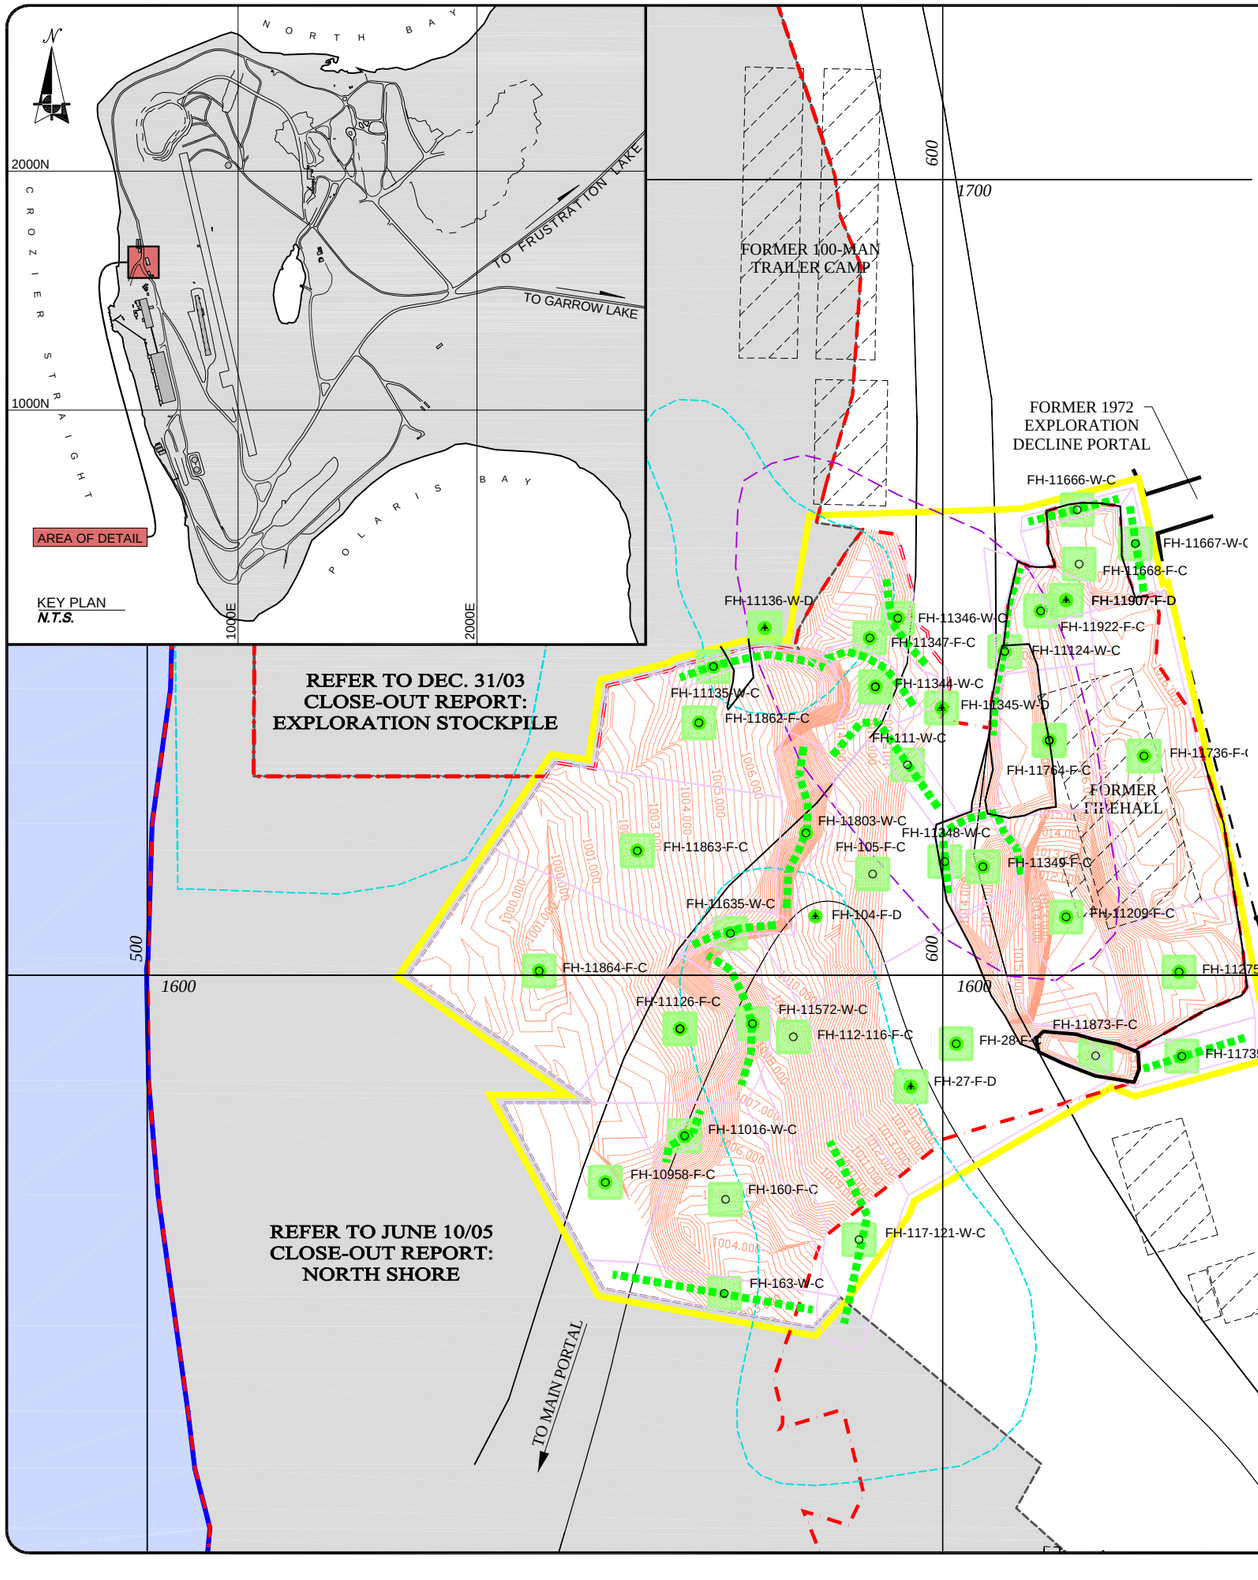


Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
FH-105-F-C	<200	883
FH-111-W-C	<200	791
FH-112-116-F-C	<200	145
FH-117-121-W-C	514	793
FH-160-F-C	212	428
FH-163- W-C	148	940
FH-28-F	998	7890
FH-10472-W-Q duplicate of FH-11126-F-C	180	1610
FH-11016-W-C	230	2230
FH-11017-W-C	120	552
FH-11124-W-C	1160	2450
FH-11126-F-C	150	474
FH-11135-W-C	1190	7770
FH-11209-F-C	160	884
FH-11275-F-C	260	802
FH-11344-W-C	250	923
FH-11346-W-C	460	1880
FH-11347-F-C	180	1370
FH-11348-W-C	480	1770
FH-11349-F-C	230	1180
FH-11370-W-Q duplicate of FH-11344-W-C	240	917
FH-11478-W-C	<100	225
FH-11479-W-C	180	388
FH-11572-W-C	300	2190
FH-11635-W-C	<50	56.5
FH-11666-W-C	54	135
FH-11667-W-C	65	195
FH-11668-F-C	<50	142
FH-11735-W-C	200	704
FH-11736-F-C	<100	25.7
FH-11764-F-C	140	386
FH-11765-F-Q duplicate of FH-11764-F-C	120	280
FH-11862-F-C	<100	23.5
FH-11863-F-C	<100	71.5
FH-11864-F-C	190	572
FH-11873-F-C	310	165
FH-11922-F-C	<100	169

Confirmation Sample ID	EPH C10-C19 mg/kg	EPH C19-C32 mg/kg
FH-27-F	<200	<200
FH-28-F	<200	<200
FH-104-F-C	240	<200
FH-10472-W-Q duplicate of FH-11126-F-C	<200	<200
FH-11016-W-C	<200	<200
FH-11017-W-C	<200	<200
FH-11019-W-C	230	<200
FH-11124-W-C	420	760
FH-11126-F-C	<200	<200
FH-11134-F-C	290	<200
FH-11135-W-C	210	<200
FH-11136-W-D	440	<200
FH-11209-F-C	780	230
FH-11275-F-C	460	<200
FH-11279-F-C	<200	260
FH-11344-W-C	370	<200
FH-11345-W-D	320	<200
FH-11346-W-C	970	230
FH-11347-F-C	490	<200
FH-11348-W-C	340	<200
FH-11349-F-C	270	<200
FH-11370-W-Q duplicate of FH-11334-W-C	770	<200
FH-11478-W-C	270	500
FH-11479-W-C	210	460
FH-11572-W-C	<200	<200
FH-11635-W-C	220	430
FH-11735-W-C	<200	<200
FH-11736-F-C	550	<200
FH-11764-F-C	<200	320
FH-11765-F-Q duplicate of FH-11764-F-C	<200	390
FH-11803-W-C	<200	300
FH-11805-W-C	<200	370
FH-11862-F-C	<200	<200
FH-11863-F-C	<200	<200
FH-11864-F-C	230	400
FH-11907-F-D	<200	270
FH-11922-F-C	240	350

Bold — **Concentration greater than or equal to the Polaris Mine SQROs**

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg



LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

AREA – SAMPLE ID – ESP–7–I–D

TYPE:
- C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL
- D= DISCRETE SAMPLE
- Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE

LOCATION:
- F= FLOOR SAMPLE
- I= INTERMEDIATE FLOOR SAMPLE
- W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- *EPH – EXTRACTABLE PETROLEUM HYDROCARBONS
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–FH–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

FIREHALL CONDITIONS AFTER REMEDIATION

Gartner Lee

Figure No. **FH-21-2**

Appendix I

South Shore

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: South Shore

BACKGROUND

The South Shore area surrounded the former concentrate storage shed and extended west to Crozier Strait (shown as Area 25 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*). Rock fill was used to level and expand the shoreline an additional 15 m (approximately) into Crozier Strait during construction. During the operation of the mine, the South Shore area was used as a storage yard for shipping containers. Several roads and a fuel line, that extended from the dock to the tank farm, crossed the area.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified metal contamination in the soil surrounding the concentrate shed on the South Shore. Two surface samples were collected, thirty one (31) test pits excavated and two (2) boreholes drilled during the ESA. The sample results indicated that elevated metal concentrations in the soil was limited to the upper 0.3 m between the south end of the concentrate storage shed and the shore. Between the north end of the concentrate storage shed and the shore elevated metal concentrations were encountered from surface to a depth of at least 1.5 m. No indication of hydrocarbon contamination was encountered during the ESA. The sample locations and an indication of results are shown on Figure SS-25-1: S*outh Shore Conditions Before Remediation*.

The sources of contaminate were attributed to lead and zinc concentrates being dispersed by wind and vehicle tracking from the concentrate storage shed and the conveyor to the shiploader at the dock. In addition, fill brought in to expand the shoreline during the construction and to repair eroded areas during the operation of the mine occasionally contained mineralized rock from near the ore zone and it was determined that it was to be excavated as part of the remedial work.

METHODOLOGY

Delineation

The preliminary boundaries of the remediation area, as identified in the ESA as "Areas of Concern" were not further delineated prior to excavation commencing along the shoreline in 2004. In 2004, further delineation of the remedial area was undertaken at the north end of the former concentrate storage shed by drilling eight boreholes and collecting field screening samples. The drill results determined that the metal contamination was bound vertically by bedrock at depths ranging from 0.3 m to 1.0 m below pre-excavation grades. Lead and zinc field screening measurements were obtained using a Niton portable X-Ray Fluorescence (XRF) elemental analyzer in accordance with standard Gartner Lee Limited (GLL) and Teck Cominco Limited (TCL) sampling procedures and protocols.

Excavation

The excavation of the South Shore area occurred from June 11, 2003 to October 23, 2003 and then again from April 19, 2004 to July 23, 2004. Material from the South Shore area was initial broken up for excavation utilising a ripper tooth attached to an excavator or onto the back of the D8 and D10 bulldozers. An excavator bucket was used to pick up the loosed material within the excavation, stockpile it and then load it onto trucks.

In 2003, a strip approximately 45 m wide from the dock cells to within 60 m of the foldaway buildings following the shoreline was removed. A berm was maintained between the ocean and the excavated area. The berm provided protection from the ocean flooding the area being excavated, as well as minimizing erosion in the marine foreshore area. Removal of the berm took place in May 2004 during periods of low tide. At this time ice still bound the foreshore and interaction with the marine foreshore was therefore reduced. Daily turbidity and Total Suspended Solids (TSS) levels were monitored prior to, during and immediately following periods of work in the foreshore in accordance with approved site procedures and protocols. Excavation activities were halted and mitigation measures implemented as required to address potential sediment releases into the marine environment.

In 2004, excavation occurred north and south of the former concentrate storage shed. During excavation at the north end of the concentrate storage shed, hydrocarbon contaminated soil was encountered. One source of hydrocarbon contamination originated at the fuel coupling located down slope of the road east of the barge (1313N, 680E). The contamination was found to have migrated downhill towards the gully that contained the conveyor-way from the barge to the concentrate shed. At this point the hydrocarbon contamination continued down gradient into the barge area. A second source of hydrocarbon contamination was located at a bend in the fuel line near the concentrate conveyor to the shiploader (1298N, 622E). Hydrocarbon contamination from this point source was found to have migrated down gradient towards the barge.

To direct the excavation activities, soil samples were collected across the floor excavation limits in accordance with standard GLL and TCL sampling procedures and protocols. Samples were field screened for metals using the XRF analyzer and for hydrocarbons using the portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. Additional excavation was undertaken where sample results indicated the lead and zinc or hydrocarbon concentrations were greater than the Polaris Mine Soil Quality Remediation Objectives (SQRO's).

The final limits of the excavation areas are shown on Figure SS-25-2: *South Shore Conditions After Remediation*. The material excavated was disposed in the mine workings in accordance with regulatory approvals.

Confirmation Sampling

Upon receipt of field screening results that indicated that the soil remaining in the excavation would meet the SQRO's, confirmation soil samples were collected. The excavation area was subdivided into individual composite sampling areas approximately 25 m by 25 m or less as required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation.

Soil samples were collected at the excavation limits and submitted to ALS Environmental for analysis of Extractable Petroleum Hydrocarbons (EPH), metals and Polycyclic Aromatic Hydrocarbons (PAH). Additional excavation was undertaken in areas that did not meet the SQRO's and additional confirmatory samples taken upon completion of excavation. Upon receipt of the analytical results that met the SQRO's the final excavation limits were surveyed.

ANALYTICAL RESULTS

Analytical laboratory results for EPH, metals and PAH are summarized in Tables SS-25-1, SS-25-2 and SS-25-3 along with the approved Polaris Mine SQRO's for petroleum hydrocarbons and metals. A total of four (4) hydrocarbon and one hundred fifty seven (157) metals remediation confirmation samples were submitted from the South Shore area. All of the hydrocarbon remediation confirmation samples were composite floor samples. Of the metals remediation confirmation samples there were one hundred sixteen (116) composite floors, nineteen (19) discrete floors, four (4) composite walls, one (1) discrete wall, and seventeen (17) quality assurance quality control (QA/QC) samples. The soil quality results and lateral limits of the excavation are shown on Figure SS-25-2.

Quality Assurance and Quality Control (QA/QC)

Relative percent differences (RpDs) have been calculated and compiled in Table SS-25-4 for thirty-one (31) field screening duplicates, seventeen (17) analytical laboratory duplicates and seventeen (17) analytical laboratory replicates for a total of sixty-five (65) QA/QC samples.

Sixty (60) of the sample results and their duplicate/replicate results returned RpDs below the practical quantitation limit (PQL), in which case the RpD value has been identified as "na" (not applicable), or returned acceptable RpDs, below the site specific remediation protocol of 50%. One on-site field screened duplicate and four of the analytical laboratory duplicates returned RpDs greater than the objective. The variance between these samples and their duplicates is considered indicative of sample heterogeneity, especially at low concentration levels of lead and zinc as compared to the SQRO's. The metal QA/QC samples from the South Shore area serve to document the variable nature of the metal concentrations in the soil at the Polaris Mine.

Polaris Mine Soil Quality Remediation Objectives

All of the hydrocarbon remediation confirmation samples returned results below the Polaris Mines SQRO's for EPH and PAH. All of the metal remediation confirmation composite samples returned results below the Polaris Mine SQRO's for lead and zinc. One of the twenty discrete samples, (sample Shore-11987-F-D), returned a lead concentration of 2,600 mg/kg which is greater than the SQRO of 2,000 mg/kg. The lead exceedance is less than two times the SQRO and is therefore in accordance with the approved site remedial protocol that stipulates "that contaminant concentrations in any residual soils will not exceed twice the SQRO's".

Discrete samples were collected to discern the homogeneity of the sample area for lead and zinc. The table below shows a comparison of discrete samples versus the composite areas they represented.

Summary of Discrete Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	Lead (mg/kg)	Zinc (mg/kg)	Discrete Sample ID	Lead (mg/kg)	Zinc (mg/kg)
Shore-52-F-C	135	645	Shore-59-F-D	<100	273
Shore-77-F-C	166	527	Shore-79-F-D	279	1220
Shore-76-F-C	121	365	Shore-78-F-D	202	967
Shore-56-F-C	225	991	Shore-466-F-D	1790	7800
Shore-54-F-C	208	1100	Shore-462-F-D	300	1530
Shore-146-F-C	553	1330	Shore-144-F-D	256	1360
Shore-11303-F-C	1170	3130	Shore-10775-F-D	220	526
Shore-10821-F-C	560	861	Shore-10779-F-D	680	1190
Shore-11368-F-C	310	1630	Shore-10947-F-D	310	1740
Shore-11308-F-C	270	1380	Shore-10956-F-D	210	1510
Shore-11747-F-C	290	822	Shore-11317-F-D	<100	241
Shore-11366-F-C	310	1380	Shore-11338-F-D	270	1290
Shore-11744-F-C	<50	101	Shore-11565-F-D	<50	69
Shore-11669-F-C	180	467	Shore-11649-F-D	319	1220
Shore-11364-F-C	110	747	Shore-11722-F-D	232	1340
Shore-11747-F-C	290	822	Shore-11854-F-D	<100	114
Shore-11998-F-C	<100	51	Shore-11964-F-D	320	934
Shore-11485-F-C	610	3020	Shore-11987-F-D	**2600**	4400
Shore-11821-F-C	228	616	Shore-11988-F-D	210	424
Shore-12074-W-C	93	361	Shore-12071-W-D	295	473

Generic Federal Soil Quality Guidelines for Parkland Land Use

A total of twenty (20) randomly selected samples were analysed for total metals as follows: fourteen (14) composite samples, five (5) discrete samples and one Quality Assurance and Quality Control sample.

Barium concentrations ranged from 192 mg/kg to 1,100 mg/kg. Sixteen (16) of the samples exceeded the generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for parkland land use of 500 mg/kg Barium in soil. One sample with a Barium concentration of 608 mg/kg returned an Arsenic concentration of 15 mg/kg, which exceeds generic CCME CEQG for parkland land use of 12 mg/kg Arsenic in soil. Cadmium concentrations ranged from 1.4 mg/kg to 17.8 mg/kg. The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone. Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling*

Results, are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations of arsenic and barium greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of arsenic and barium concentrations in those samples in listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Arsenic and Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Arsenic	12	<5	15.1	12	11 +/- 2.7	13	12.25
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of arsenic and barium remaining within the footprint of the South Shore area after remediation are within the range of the background concentrations. In addition, the immobile nature of the Arsenic and Barium encountered on site was demonstrated in the ESA leachate test results that returned Arsenic and Barium concentrations at levels less than the detection limit and they were therefore not identified as a contaminants of concern in the ESA.

Two (2) of the discrete samples (Shore-466-F-D and Shore-11987-F-D) exceeded the CCME CEQG parkland land use of 10 mg/kg Cadmium in soil (Sample Shore-11987-F-D also returned lead concentrations greater than the SQRO). Cadmium was not identified as a contaminant of concern based on the total metal analyses and leachate test results conducted during the ESA. Given the immobile nature of the Cadmium encountered on site, as demonstrated by the leachate results, the relatively low level of concentrations (less than twice the generic CCME guidelines for Parkland land use) and the lack of elevated concentrations being detected in the composite samples, no further remedial excavation work is considered necessary.

The confirmatory samples supported by the QA/QC samples from the South Shore area provide confidence that the remediation of the area complies with the SQRO's.

CONCLUSIONS

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the South Shore area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Ltd. and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

AL:DL:gc

ATTACHMENTS

Tables

Table SS-25-1:	South Shore Remediation Confirmation Soil Samples – Hydrocarbons
Table SS-25-2:	South Shore Remediation Confirmation Soil Samples – Metals
Table SS-25-3:	South Shore Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table SS 25-4:	South Shore Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure SS-25-1:	South Shore Conditions Before Remediation
Figure SS-25-2:	South Shore Conditions After Remediation

Table SS-25-1. South Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	South Shore			
		Sample ID	Shore-7-F-C	Shore-11860-F-C	Shore-11861-F-C	Shore-12037-F-C
		Date Sampled	23-Jun-03	29-Jun-04	29-Jun-04	23-Jul-04
		ALS File Number	S9893	U5353R	U5353R	U6364
		Field Screen (ppm)[b]	-	-	-	5
Parameter	**Site Specific**	**Units**	**Analytical Results**			
Extractable Hydrocarbons						
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	310	590
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	590
HEPH[c]	1000	mg/kg	-	-	-	<200

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The aaproved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore						
				Sample ID	Shore-4-F-C	Shore-5-F-C	Shore-6-F-C	Shore-8-F-C	Shore-10-F-C	Shore-50-F-C	Shore-51-F-C
				Date Sampled	24-Jun-03	24-Jun-03	24-Jun-03	24-Jun-03	24-Jun-03	19-Jul-03	19-Jul-03
				ALS File Number	S9893	S9893	S9893	S9893	S9893	T1801	T1801
				Field Screen Pb (ppm)[b]	563	607	353	403	298	627	586
				Field Screen Zn (ppm)[b]	3347	3379	2440	1979	1610	2370	2418
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	487	643	496	1970	1050	500	267
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	2690	3170	3760	4670	2660	2470	1420

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-52-F-C	Shore-54-F-C	Shore-56-F-C	Shore-57-F-C	Shore-58-F-C	Shore-59-F-D	Shore-60-F-C
				Date Sampled	19-Jul-03	19-Jul-03	19-Jul-03	19-Jul-03	19-Jul-03	19-Jul-03	19-Jul-03
				ALS File Number	T1801	T1801	T1801	T1801	T1801	T1801	T1801
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	287	353	280	203	234	174	282
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	874	1294	985	288	516	620	1465
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	135	208	225	137	154	<100	484
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	645	1100	991	448	265	273	3150

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-61-F-C	Shore-53-F-Q	Shore-74-F-C	Shore-75-F-C	Shore-76-F-C	Shore-77-F-C	Shore-78-F-D
				Date Sampled	19-Jul-03	19-Jul-03	22-Jul-03	22-Jul-03	23-Jul-03	22-Jul-03	22-Jul-03
				ALS File Number	T1801	T1801	T1888	T1888	T1888	T1888	T1888
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	212	duplicate of	485	675	271	259	309
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	816	Shore-61-F-C	1826	4195	826	805	1114
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<100	<100	453	437	121	116	202
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	431	495	5590	4300	365	527	967

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-79-F-D	Shore-80-F-C	Shore-72-F-Q	Shore-81-F-C	Shore-82-F-C	Shore-83-F-C	Shore-85-F-C
				Date Sampled	22-Jul-03	22-Jul-03	22-Jul-03	25-Jul-03	25-Jul-03	25-Jul-03	25-Jul-03
				ALS File Number	T1888	T1888	T1888	T2135r	T2135r	T2135r	T2135r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	308	-	duplicate of	210	255	382	271
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	1308	-	Shore-80-F-C	763	654	1322	1004
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	8.11	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	**1100**	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	2	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	10	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	11	-	-	-
Lead	T-Pb	2000	-	mg/kg	279	346	471	127	195	1060	123
Mercury	T-Hg	-	7	mg/kg	-	-	-	<0.05	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	15	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<4	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	40	-	-	-
Zinc	T-Zn	10000	-	mg/kg	1220	1050	1640	547	970	4160	462

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore						
				Sample ID	Shore-86-F-C	Shore-84-F-Q	Shore-87-F-C	Shore-89-F-C	Shore-90-F-C	Shore-96-F-C	Shore-109-F-C
				Date Sampled	25-Jul-03	25-Jul-03	25-Jul-03	29-Jul-03	29-Jul-03	28-Jul-03	03-Aug-03
				ALS File Number	T2135r	T2135r	T2135r	T2239	T2239	T2239	T2587
				Field Screen Pb (ppm)[b]	156	duplicate of	190	487	803	1066	442
				Field Screen Zn (ppm)[b]	272	Shore-86-F-C	760	1747	5172	5568	2691
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<100	214	<200	253	165	1040	159
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	120	812	578	791	1810	4710	912

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore						
				Sample ID	Shore-110-F-C	Shore-108-F-Q	Shore-111-F-C	Shore-112-F-C	Shore-114-F-C	Shore-115-F-C	Shore-120-F-C
				Date Sampled	03-Aug-03	03-Aug-03	03-Aug-03	08-Aug-03	13-Aug-03	13-Aug-03	13-Aug-03
				ALS File Number	T2587	T2587	T2587	T2588	T3191	T3191	T3069
				Field Screen Pb (ppm)[b]	844	duplicate of	268	766	1157	641	630
				Field Screen Zn (ppm)[b]	3480	Shore-110-F-C	635	4027	5525	1910	4061
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	676	717	<100	987	394	543	1030
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	2410	2530	279	3760	2570	1910	8910

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-122-F-C	Shore-124-F-C	Shore-125-F-C	Shore-127-F-C	Shore-142-F-C	Shore-144-F-D	Shore-146-F-C
				Date Sampled	16-Aug-03	13-Aug-03	13-Aug-03	16-Aug-03	18-Aug-03	17-Aug-03	18-Aug-03
				ALS File Number	T3069	T3191	T3191	T3069	T3069	T3069	T3069
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	568	1242	182	527	178	447	691
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	3144	4487	1046	2169	1336	1956	2559
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	8.56	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<20	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	<10	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	**509**	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<1	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	3	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	4	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<4	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	6	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	755	856	236	677	114	256	553
Mercury	T-Hg	-	7	mg/kg	-	-	<0.50	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<8	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	<10	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	<3	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	<4	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	<10	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	18	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	3640	2930	1180	2350	351	1360	1330

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-143-F-Q	Shore-156-F-C	Shore-157-F-C	Shore-158-F-C	Shore-159-F-C	Cshed-401-F-C	Cshed-402-F-C
				Date Sampled	17-Aug-03	18-Aug-03	18-Aug-03	18-Aug-03	18-Aug-03	12-Sep-03	12-Sep-03
				ALS File Number	T3069	T3069	T3069	T3069	T3069	T4071	T4071
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	duplicate of	-	-	-	-	149	231
				Field Screen Zn (ppm)[b]	Shore-146-F-C	-	-	-	-	1339	2898
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	8.07	-	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	<10	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	**675**	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	5	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	6	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	<4	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	12	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	428	369	197	152	282	327	227
Mercury	T-Hg	-	7	mg/kg	-	0.12	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	10	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	<3	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	<4	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	30	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	1270	1870	1030	572	1100	2140	3050

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore						
				Sample ID	Shore-411-F-C	Shore-429-F-C	Shore-436-F-C	Shore-420-F-Q	Shore-437-F-C	Shore-462-F-D	Shore-466-F-D
				Date Sampled	23-Sep-03	23-Sep-03	07-Oct-03	23-Sep-03	08-Oct-03	19-Oct-03	19-Oct-03
				ALS File Number	T4504	T4900	T5345	T4504	T5345	T5735	T5735
				Field Screen Pb (ppm)[b]	547	664	402	duplicate of	746	317	659
				Field Screen Zn (ppm)[b]	2721	2837	2045	Shore-436-F-Q	2671	1477	4138
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	8.22	-	-	7.91	8.38
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<30	-	-	<20	<20
Arsenic	T-As	-	12	mg/kg	-	-	<20	-	-	<10	<10
Barium	T-Ba	-	500	mg/kg	-	-	**987**	-	-	**889**	392
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<2	-	-	<1.0	<1.0
Cadmium	T-Cd	-	10	mg/kg	-	-	5	-	-	4	**17.8**
Chromium	T-Cr	-	64	mg/kg	-	-	8	-	-	8.3	6.6
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<6	-	-	<4.0	<4.0
Copper	TCu	-	63	mg/kg	-	-	13	-	-	12.3	22.4
Lead	T-Pb	2000	-	mg/kg	910	1170	411	485	994	300	1790
Mercury	T-Hg	-	7	mg/kg	-	-	<0.05	-	-	<0.050	<0.050
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<20	-	-	<8.0	<8.0
Nickel	T-Ni	-	50	mg/kg	-	-	<20	-	-	14	11
Selenium	T-Se	-	1	mg/kg	-	-	<4	-	-	<2.0	<2.0
Silver	T-Ag	-	20[d]	mg/kg	-	-	<6	-	-	<4.0	<4.0
Tin	T-Sn	-	50[d]	mg/kg	-	-	<20	-	-	<10	<10
Vanadium	T-V	-	130	mg/kg	-	-	35	-	-	29.9	17.6
Zinc	T-Zn	10000	-	mg/kg	3440	2390	2740	2510	5430	1530	7800

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore						
				Sample ID	Shore-482-F-C	Shore-484-F-C	Shore-485-F-C	Shore-486-F-C	Shore-502-F-C	Shore-503-F-C	Shore-504-F-C
				Date Sampled	20-Oct-03	20-Oct-03	20-Oct-03	20-Oct-03	23-Oct-03	23-Oct-03	23-Oct-03
				ALS File Number	T5735	T5735	T5735	T5735	T5790	T5790	T5790
				Field Screen Pb (ppm)[b]	-	-	-	-	-	-	-
				Field Screen Zn (ppm)[b]	-	-	-	-	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH		-	-	-	-	-	8.6	-	-	-	-
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<20	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	<10	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	274	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<1.0	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	5.6	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	<4.0	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<4.0	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	7.7	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	890	940	620	290	<50	580	120
Mercury	T-Hg	-	7	mg/kg	-	-	<0.050	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<8.0	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	<10	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	<2.0	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	<4.0	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	<10	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	8.7	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	3980	2300	2260	1510	90.4	1610	754

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-10647-F-C	Shore-10747-F-C	Shore-10775-F-D	Shore-10779-F-D	Shore-10820-F-C	Shore-10849-F-Q
				Date Sampled	13-May-04	13-May-04	31-May-04	23-May-04	24-May-04	24-May-04
				ALS File Number	U3898r	U3969r	U4137	U4484	U3969r	U3969r
				Field Screen Pb (ppm)[b]	-	-	147	336	-	duplicate of
				Field Screen Zn (ppm)[b]	-	-	752	771	-	Shore-10820-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	12.3	-	-	8.37	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	<10	-	-	<10	-
Barium	T-Ba	-	500	mg/kg	-	467	-	-	**718**	-
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	-	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	1.4	-	-	1.4	-
Chromium	T-Cr	-	64	mg/kg	-	6	-	-	5	-
Cobalt	T-Co	-	50[d]	mg/kg	-	<4	-	-	<4	-
Copper	TCu	-	63	mg/kg	-	7	-	-	7	-
Lead	T-Pb	2000	-	mg/kg	577	220	220	680	520	520
Mercury	T-Hg	-	7	mg/kg	-	<0.05	-	-	<0.05	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	-	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	<10	-	-	11	-
Selenium	T-Se	-	1	mg/kg	-	<4	-	-	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	<4	-	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	<10	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	24	-	-	22	-
Zinc	T-Zn	10000	-	mg/kg	2890	524	526	1190	566	719

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-10821-F-C	Shore-10947-F-D	Shore-10956-F-D	Shore-11220-F-C	Shore-11221-F-C	Shore-11222-F-C
				Date Sampled	24-May-04	28-May-04	28-May-04	04-Jun-04	04-Jun-04	04-Jun-04
				ALS File Number	U3969r	U4484	U4484	U4269r	U4269r	U4269r
				Field Screen Pb (ppm)[b]	-	231	250	-	-	-
				Field Screen Zn (ppm)[b]	-	1300	1478	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	8.38	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	<10	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	**989**	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	2.4	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	8	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	<4	-
Copper	TCu	-	63	mg/kg	-	-	-	-	10	-
Lead	T-Pb	2000	-	mg/kg	560	310	210	340	270	300
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	<0.05	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	12	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	43	-
Zinc	T-Zn	10000	-	mg/kg	861	1740	1510	1010	699	1030

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11223-F-C	Shore-11486-F-Q	Shore-11229-F-C	Shore-11232-F-C	Shore-11303-F-C	Shore-11304-F-C
				Date Sampled	15-Jun-04	15-Jun-04	15-Jun-04	15-Jun-04	31-May-04	31-May-04
				ALS File Number	U4704	U4704	U4704	U4704	U4137	U4137
				Field Screen Pb (ppm)[b]	-	duplicate of	-	-	-	-
				Field Screen Zn (ppm)[b]	-	Shore-11223-F-C	-	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	8.32	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	<20	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	<10	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	**678**	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<1	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	2	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	7	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<4	-	-	-	-	-
Copper	TCu	-	63	mg/kg	9	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	550	650	230	500	1170	160
Mercury	T-Hg	-	7	mg/kg	<0.05	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<8	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	12	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	<4	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	<4	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	<10	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	30	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	494	415	2340	649	3130	1630

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11305-F-C	Shore-11309-F-Q	Shore-11306-F-C	Shore-11307-F-C	Shore-11308-F-C	Shore-11317-F-D
				Date Sampled	31-May-04	31-May-04	31-May-04	31-May-04	31-May-04	08-Jun-04
				ALS File Number	U4137	U4137	U4137	U4137	U4137	U5353r
				Field Screen Pb (ppm)[b]	-	duplicate of	-	-	-	62
				Field Screen Zn (ppm)[b]	-	Shore-11305-F-C	-	-	-	435
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	<40
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	<200
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	**706**
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	<1
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	<4
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	8
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	<4
Copper	TCu	-	63	mg/kg	-	-	-	-	-	11
Lead	T-Pb	2000	-	mg/kg	130	170	320	220	270	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	<8
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	11
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	<100
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	<4
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	<20
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	48
Zinc	T-Zn	10000	-	mg/kg	527	486	1640	843	1380	241

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11338-F-D	Shore-11364-F-C	Shore-11366-F-C	Shore-11367-F-C	Shore-11368-F-C	Shore-11369-F-Q
				Date Sampled	09-Jun-04	15-Jun-04	08-Jun-04	08-Jun-04	08-Jun-04	08-Jun-04
				ALS File Number	U4484	U4704	U4484	U4484	U4484	U4484
				Field Screen Pb (ppm)[b]	209	-	-	-	-	duplicate of
				Field Screen Zn (ppm)[b]	1384	-	-	-	-	Shore-11368-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	8.5	-	7.93	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<20	-	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	<10	-	<10	-
Barium	T-Ba	-	500	mg/kg	-	-	**991**	-	**924**	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<1	-	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	4	-	4.4	-
Chromium	T-Cr	-	64	mg/kg	-	-	7	-	13	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<4	-	5	-
Copper	TCu	-	63	mg/kg	-	-	14	-	23	-
Lead	T-Pb	2000	-	mg/kg	270	110	310	250	310	210
Mercury	T-Hg	-	7	mg/kg	-	-	<0.05	-	0.057	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<8	-	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	13	-	26	-
Selenium	T-Se	-	1	mg/kg	-	-	<4	-	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	<4	-	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	<10	-	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	44	-	66	-
Zinc	T-Zn	10000	-	mg/kg	1290	747	1380	2570	1630	1370

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11470-F-C	Shore-11471-F-C	Shore-11472-F-C	Shore-11473-F-C	Shore-11474-F-C	Shore-11475-F-C
				Date Sampled	15-Jun-04	15-Jun-04	15-Jun-04	15-Jun-04	15-Jun-04	15-Jun-04
				ALS File Number	U4781	U4781	U4781	U4781	U4781	U4781
				Field Screen Pb (ppm)[b]	50	39	66	31	53	67
				Field Screen Zn (ppm)[b]	314	280	263	190	284	309
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	8.51	-	-	-	-	8.46
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	<10	-	-	-	-	<10
Arsenic	T-As	-	12	mg/kg	10	-	-	-	-	9
Barium	T-Ba	-	500	mg/kg	**1090**	-	-	-	-	**813**
Beryllium	T-Be	-	4[d]	mg/kg	<0.5	-	-	-	-	<0.5
Cadmium	T-Cd	-	10	mg/kg	0.61	-	-	-	-	0.53
Chromium	T-Cr	-	64	mg/kg	14	-	-	-	-	11
Cobalt	T-Co	-	50[d]	mg/kg	7	-	-	-	-	6
Copper	TCu	-	63	mg/kg	30	-	-	-	-	25
Lead	T-Pb	2000	-	mg/kg	<50	<50	59	<50	<50	<50
Mercury	T-Hg	-	7	mg/kg	0.116	-	-	-	-	0.099
Molybdenum	T-Mo	-	10[d]	mg/kg	4	-	-	-	-	<4
Nickel	T-Ni	-	50	mg/kg	40	-	-	-	-	33
Selenium	T-Se	-	1	mg/kg	<2	-	-	-	-	<2
Silver	T-Ag	-	20[d]	mg/kg	<2	-	-	-	-	<2
Tin	T-Sn	-	50[d]	mg/kg	<5	-	-	-	-	<5
Vanadium	T-V	-	130	mg/kg	84	-	-	-	-	69
Zinc	T-Zn	10000	-	mg/kg	163	127	180	112	105	139

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11585-F-Q	Shore-11476-F-C	Shore-11485-F-C	Shore-11565-F-D	Shore-11573-F-C	Shore-11575-F-C
				Date Sampled	15-Jun-04	15-Jun-04	15-Jun-04	15-Jun-04	21-Jun-04	21-Jun-04
				ALS File Number	U4781	U4781	U4704	U5353r	U4948	U4948
				Field Screen Pb (ppm)[b]	duplicate of	72	-	141	467	99
				Field Screen Zn (ppm)[b]	Shore-11475-F-C	259	-	174	2149	936
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<50	<50	610	<50	<100	130
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	142	118	3020	69	287	336

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore					
				Sample ID	Shore-11576-F-C	Shore-11597-F-C	Shore-11630-F-C	Shore-11631-F-C	Shore-11649-F-D	Shore-11669-F-C
				Date Sampled	21-Jun-04	19-Jun-04	22-Jun-04	22-Jun-04	15-Jun-04	25-Jun-04
				ALS File Number	U4948	U4948	U5223	U5223	U5353r	U5050
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	494	445	55	57	270	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	721	3086	157	189	843	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	250	660	<50	<50	319	180
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	330	3930	82.4	103	1220	467

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11670-F-C	Shore-11671-F-C	Shore-11672-F-C	Shore-11676-F-C	Shore-11695-F-C	Shore-11722-F-D
				Date Sampled	25-Jun-04	25-Jun-04	25-Jun-04	26-Jun-04	28-Jun-04	23-Jun-04
				ALS File Number	U5050	U5050	U5050	U5223	U5223	U5050
				Field Screen Pb (ppm)[b]	-	-	-	207	106	244
				Field Screen Zn (ppm)[b]	-	-	-	779	459	1561
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	78	230	450	190	150	232
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	198	1050	694	509	466	1340

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11743-F-C	Shore-11744-F-C	Shore-11746-F-C	Shore-11747-F-C	Shore-11767-F-C	Shore-11768-F-Q
				Date Sampled	15-Jun-04	15-Jun-04	02-Jul-04	02-Jul-04	07-Jul-04	07-Jul-04
				ALS File Number	U5353r	U5353r	U5353r	U5353r	U5615r	U5615r
				Field Screen Pb (ppm)[b]	-	-	-	-	-	duplicate of
				Field Screen Zn (ppm)[b]	-	-	-	-	-	Shore-11767-F-C
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<40	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<200	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	**805**	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	<4	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	10	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4	-	-
Copper	TCu	-	63	mg/kg	-	-	-	17	-	-
Lead	T-Pb	2000	-	mg/kg	<50	<50	380	290	480	520
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	18	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<100	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<20	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	57	-	-
Zinc	T-Zn	10000	-	mg/kg	67.6	101	1880	822	786	1050

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11816-F-C	Shore-11817-F-Q	Shore-11818-F-C	Shore-11821-F-C	Shore-11822-F-C	Shore-11854-F-D
				Date Sampled	27-Jun-04	27-Jun-04	27-Jun-04	30-Jun-04	30-Jun-04	02-Jul-04
				ALS File Number	U5223	U5223	U5223	U5353r	U5353r	U5353r
				Field Screen Pb (ppm)[b]	-	duplicate of	-	380	262	-
				Field Screen Zn (ppm)[b]	-	Shore-11816-F-C	-	1719	1006	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	<40
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	<200
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	**513**
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	<1
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	<4
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	11
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	8
Copper	TCu	-	63	mg/kg	-	-	-	-	-	32
Lead	T-Pb	2000	-	mg/kg	<50	<50	<50	228	203	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	<8
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	38
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	<100
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	<4
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	<20
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	82
Zinc	T-Zn	10000	-	mg/kg	96.8	157	63.8	616	610	114

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11860-F-C	Shore-11861-F-C	Shore-11964-F-D	Shore-11987-F-D	Shore-11778-F-Q	Shore-11988-F-D
				Date Sampled	29-Jun-04	29-Jun-04	15-Jul-04	13-Jul-04	13-Jul-04	13-Jul-04
				ALS File Number	U5353r	U5353r	U6440	U5836	U5836	U5836
				Field Screen Pb (ppm)[b]	-	-	-	170	duplicate of	175
				Field Screen Zn (ppm)[b]	-	-	-	299	Shore-11987-F-D	576
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	8.73	8.58	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	<20	<20	-
Arsenic	T-As	-	12	mg/kg	-	-	-	<10	**15**	-
Barium	T-Ba	-	500	mg/kg	-	-	-	192	**608**	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	<1	<1	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	**11.4**	1.4	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	5	12	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	<4	8	-
Copper	TCu	-	63	mg/kg	-	-	-	7	30	-
Lead	T-Pb	2000	-	mg/kg	<200	<200	320	**2600**	140	210
Mercury	T-Hg	-	7	mg/kg	-	-	-	<0.05	0.119	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	<8	<8	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	<10	38	-
Selenium	T-Se	-	1	mg/kg	-	-	-	<4	<4	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	<4	<4	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	<10	<10	-
Vanadium	T-V	-	130	mg/kg	-	-	-	26	86	-
Zinc	T-Zn	10000	-	mg/kg	49.2	134	934	4400	365	424

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee		Polaris Mine Soil Quality Remediation Objectives[a]		Location	South Shore					
				Sample ID	Shore-11779-F-Q	Shore-11996-F-C	Shore-11997-F-Q	Shore-11998-F-C	Shore-11999-F-Q	Shore-12000-F-C
				Date Sampled	13-Jul-04	15-Jul-04	15-Jul-04	15-Jul-04	15-Jul-04	15-Jul-04
				ALS File Number	U5830	U6440	U6440	U6440	U6440	U6440
				Field Screen Pb (ppm)[b]	duplicate of	515	duplicate of	-	duplicate of	-
				Field Screen Zn (ppm)[b]	Shore-11988-F-D	2405	Shore-11996-F-C	-	Shore-11998-F-C	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<100	<100	<100	<100	280	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	207	36	39	51	363	179

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore					
				Sample ID	Shore-12001-F-C	Shore-12002-F-C	Shore-12003-F-C	Shore-12037-F-C	Shore-12067-W-C	Shore-12071-W-D
				Date Sampled	18-Jul-04	18-Jul-04	18-Jul-04	23-Jul-04	26-Jul-04	26-Jul-04
				ALS File Number	U6530r	U6530r	U6530r	U6364	U6530r	U6530r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	773	693	896	250	1248	540
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	1208	1306	1530	1652	2064	1074
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**					
pH		-	-	-	-	-	-	-	-	-
Total Metals										
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	279	244	314	<100	537	295
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	331	321	403	462	760	473

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-2. South Shore Area Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	South Shore		
				Sample ID	Shore-12072-W-C	Shore-12073-W-C	Shore-12074-W-C
				Date Sampled	28-Jul-04	28-Jul-04	28-Jul-04
				ALS File Number	U6530r	U6530r	U6530r
		Polaris Mine Soil Quality Remediation Objectives[a]		Field Screen Pb (ppm)[b]	194	293	-
				Field Screen Zn (ppm)[b]	590	1290	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**		
pH		-	-	-	-	-	-
Total Metals							
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-
Copper	TCu	-	63	mg/kg	-	-	-
Lead	T-Pb	2000	-	mg/kg	<50	94	93
Mercury	T-Hg	-	7	mg/kg	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-
Zinc	T-Zn	10000	-	mg/kg	134	298	361

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS-25-3. South Shore Area Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons (PAHs)

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	South Shore
		Sample ID	Shore-12037-F-C
		Date Sampled	7/23/2004
		ALS File Number	U6364
		Field Screen (ppm)[b]	5
Parameter	**CEQG [b]**	**Units**	**Analytical Results**
Polycyclic Aromatic Hydrocarbons			
Acenaphthene	-	mg/kg	<0.06
Acenaphthylene	-	mg/kg	<0.05
Anthracene	-	mg/kg	<0.05
Benz(a)anthracene	1[c]	mg/kg	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05
Benzo(b)fluoranthene	1[c]	mg/kg	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05
Benzo(k)fluoranthene	1[c]	mg/kg	<0.05
Chrysene	-	mg/kg	<0.05
Dibenz(a,h)anthracene	1[c]	mg/kg	<0.05
Fluoranthene	-	mg/kg	<0.05
Fluorene	-	mg/kg	0.128
Indeno(1,2,3,-c,d)pyrene	1[c]	mg/kg	<0.05
Napthalene	0.6	mg/kg	0.177
Phenanthrene	5[c]	mg/kg	0.074
Pyrene	10[c]	mg/kg	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore							
				Sample ID	Shore-5-F-C	Shore-6-F	Shore-55-F	Shore-61-F-C	Shore-71-W-D	Shore-77-F	Shore-80-F-C	Shore-84-F-Q
				Duplicate ID	Shore 45-F-Q	QC# 342557	QC# 346418	Shore-53-F-Q	Shore-107-W-Q	QC# 346792	Shore-72-F-Q	QC# 347684
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350		607	-	-	-	4925	-	-	-
Duplicate Result	mg/kg	70	350		530	-	-	-	3635	-	-	-
RpD	%				13%				30%			
Zinc (Zn)												
Sample Result	mg/kg	150	750		3379	-	-	-	53208	-	-	-
Duplicate Result	mg/kg	150	750		3318	-	-	-	40596	-	-	-
RpD	%				2%				27%			
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		-	-	-	<100	-	-	346	-
Duplicate Result	mg/kg	100	500		-	-	-	<100	-	-	471	-
RpD	%							na			na	
Zinc (Zn)												
Sample Result	mg/kg	3	15		-	-	-	431	-	-	1050	-
Duplicate Result	mg/kg	3	15		-	-	-	495	-	-	1640	-
RpD	%							14%			44%	
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		-	496	2040	-	-	166	-	214
Duplicate Result	mg/kg	100	500		-	1360	1290	-	-	143	-	201
RpD	%					na	45%			na		na
Zinc (Zn)												
Sample Result	mg/kg	3	15		-	3760	6160	-	-	527	-	812
Duplicate Result	mg/kg	3	15		-	4850	4020	-	-	568	-	779
RpD	%					25%	42%			7%		4%

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore							
				Sample ID	Shore-86-F-C	Shore-110-F-C	Shore-122-I-C	Shore-126-F-C	Shore-127-F-C	Shore-143-F-C	Shore-159-F-C	Shore-418-F-C
				Duplicate ID	Shore-84-F-Q	Shore-108-F-Q	QC# 351114	Shore 31-F-Q	Shore 32-F-Q	Shore 146-F-Q	QC# 351116	Shore 43-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**							
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350		156	-	-	857	527	-	-	720
Duplicate Result	mg/kg	70	350		273	-	-	727	843	-	-	446
RpD	%				na			16%	46%			0
Zinc (Zn)												
Sample Result	mg/kg	150	750		272	-	-	4948	2169	-	-	10133
Duplicate Result	mg/kg	150	750		845	-	-	4230	2441	-	-	5775
RpD	%				na			16%	12%			1
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		<100	676	-	-	-	428	-	-
Duplicate Result	mg/kg	100	500		214	717	-	-	-	553	-	-
RpD	%				na	6%				na		
Zinc (Zn)												
Sample Result	mg/kg	3	15		120	2410	-	-	-	1270	-	-
Duplicate Result	mg/kg	3	15		812	2530	-	-	-	1330	-	-
RpD	%				**148%**	5%				5%		
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500		-	-	755	-	-	-	282	-
Duplicate Result	mg/kg	100	500		-	-	932	-	-	-	283	-
RpD	%						21%				na	
Zinc (Zn)												
Sample Result	mg/kg	3	15		-	-	3640	-	-	-	1100	-
Duplicate Result	mg/kg	3	15		-	-	3310	-	-	-	1120	-
RpD	%						9%				0	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-419-F-C	Shore-436-F-C	Shore482-F-C	Shore-10204-BH-C	Shore-10205-BH-C	Shore-10779-F-D	Shore-10820-F-C
				Duplicate ID	Shore 44-F-Q	Shore-420-F-Q	QC# 361123	Shore-10216-BH-Q	Shore-10217-BH-Q	QC# 390728	Shore-10849-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		1083	-	-	43	373	-	-
Duplicate Result	mg/kg	70	350		494	-	-	57	459	-	-
RpD	%				**75%**			na	21%		
Zinc (Zn)											
Sample Result	mg/kg	150	750		7514	-	-	336	1437	-	-
Duplicate Result	mg/kg	150	750		6527	-	-	248	1481	-	-
RpD	%				14%			na	3%		
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	411	-	-	-	-	520
Duplicate Result	mg/kg	100	500		-	485	-	-	-	-	520
RpD	%					na					0
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	2740	-	-	-	-	566
Duplicate Result	mg/kg	3	15		-	2510	-	-	-	-	719
RpD	%					9%					0
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	890	-	-	680	-
Duplicate Result	mg/kg	100	500		-	-	1070	-	-	790	-
RpD	%						18%			0	
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	3980	-	-	1190	-
Duplicate Result	mg/kg	3	15		-	-	4450	-	-	1110	-
RpD	%						11%			0	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-11220-F-C	Shore-11223-F-C	Shore-11229-F-C	Shore-11303-F-C	Shore-11305-F-C	Shore-11317-F-D	Shore-11339-F-D
				Duplicate ID	QC# 389862	Shore-11486-F-Q	QC# 391524	QC# 389243	Shore-11309-F-Q	QC# 394459	Shore-10491-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		-	-	-	-	-	-	240
Duplicate Result	mg/kg	70	350		-	-	-	-	-	-	227
RpD	%										na
Zinc (Zn)											
Sample Result	mg/kg	150	750		-	-	-	-	-	-	1423
Duplicate Result	mg/kg	150	750		-	-	-	-	-	-	1807
RpD	%										0
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	550	-	-	130	-	-
Duplicate Result	mg/kg	100	500		-	650	-	-	170	-	-
RpD	%					17%			na		
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	494	-	-	527	-	-
Duplicate Result	mg/kg	3	15		-	415	-	-	486	-	-
RpD	%					17%			8%		
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		340	-	230	1170	-	<100	-
Duplicate Result	mg/kg	100	500		340	-	220	1530	-	<100	-
RpD	%				na		na	0		na	
Zinc (Zn)											
Sample Result	mg/kg	3	15		1010	-	2340	3130	-	241	-
Duplicate Result	mg/kg	3	15		925	-	2180	2690	-	547	-
RpD	%				9%		0	0		na	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-11343-F-D	Shore-11353-F-D	Shore-11368-F-C	Shore-11400-F-D	Shore-11402-F-D	Shore-11475-F-C	Shore-11576-F-C
				Duplicate ID	Shore-10492-F-Q	Shore-10493-F-Q	Shore-11369-F-Q	Shore-10494-F-Q	Shore-11750-F-Q	Shore-11585-F-Q	QC# 392656
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		866	195	-	6697	356	-	-
Duplicate Result	mg/kg	70	350		1110	246	-	8796	357	-	-
RpD	%				25%	na		0	0%		
Zinc (Zn)											
Sample Result	mg/kg	150	750		22435	351	-	28062	637	-	-
Duplicate Result	mg/kg	150	750		22790	349	-	36829	543	-	-
RpD	%				2%	na		0	na		
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	310	-	-	<50	-
Duplicate Result	mg/kg	100	500		-	-	210	-	-	<50	-
RpD	%						na			na	
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	1630	-	-	139	-
Duplicate Result	mg/kg	3	15		-	-	1370	-	-	142	-
RpD	%						17%			2%	
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	-	-	-	-	250
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	160
RpD	%										na
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	-	-	-	-	330
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	203
RpD	%										na

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-11641-F-D	Shore-11649-F-D	Shore-11659-F-D	Shore-11670-F-C	Shore-11676-F-C	Shore-11767-F-C	Shore-11816-F-C
				Duplicate ID	Shore-11713-F-Q	Shore-11715-F-Q	Shore-11717-F-Q	QC# 393170	QC# 393917	Shore-11768-F-Q	Shore-11817-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		69	270	220	-	190	-	-
Duplicate Result	mg/kg	70	350		94	351	246	-	210	-	-
RpD	%				na	na	na		na		
Zinc (Zn)											
Sample Result	mg/kg	150	750		491	843	716	-	509	-	-
Duplicate Result	mg/kg	150	750		367	1122	824	-	603	-	-
RpD	%				na	0	na		na		
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	-	-	-	480	<50
Duplicate Result	mg/kg	100	500		-	-	-	-	-	520	<50
RpD	%									na	na
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	-	-	-	786	97
Duplicate Result	mg/kg	3	15		-	-	-	-	-	1050	157
RpD	%									29%	0
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	-	78	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	77	-	-	-
RpD	%							na			
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	-	198	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	229	-	-	-
RpD	%							na			

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-11821-F-C	Shore-11987-F-D	Shore-11988-F-D	Shore-11996-F-C	Shore-11997-F-Q	Shore-11998-F-C	Shore-12002-F-C
				Duplicate ID	QC# 394458	Shore-11778-F-Q	Shore-11779-F-Q	Shore-11997-F-Q	QC# 399152	Shore-11999-F-Q	QC# 399318
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		-	-	-	-	-	-	-
Duplicate Result	mg/kg	70	350		-	-	-	-	-	-	-
RpD	%										
Zinc (Zn)											
Sample Result	mg/kg	150	750		-	-	-	-	-	-	-
Duplicate Result	mg/kg	150	750		-	-	-	-	-	-	-
RpD	%										
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	2600	210	<100	-	<100	-
Duplicate Result	mg/kg	100	500		-	140	<100	<100	-	280	-
RpD	%					na	na	na		na	
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	4400	424	36	-	51	-
Duplicate Result	mg/kg	3	15		-	365	207	39	-	363	-
RpD	%					**169%**	**69%**	6%		**151%**	
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		228	-	-	-	<100	-	244
Duplicate Result	mg/kg	100	500		314	-	-	-	<100	-	246
RpD	%				na				na		na
Zinc (Zn)											
Sample Result	mg/kg	3	15		616	-	-	-	39	-	321
Duplicate Result	mg/kg	3	15		653	-	-	-	38	-	321
RpD	%				na				na		na

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore						
				Sample ID	Shore-12013-S-D	Shore-12014-S-D	Shore-12015-S-D	Shore-12016-S-D	Shore-12017-S-D	Shore-12018-S-D	Shore-12019-S-D
				Duplicate ID	Shore-12308-S-Q	Shore-12309-S-Q	Shore-12310-S-Q	Shore-12311-S-Q	Shore-12312-S-Q	Shore-12313-S-Q	Shore-12314-S-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**						
On Site Field Screening Duplicates											
Lead (Pb)											
Sample Result	mg/kg	70	350		5544	9553	1748	3408	1027	2093	3702
Duplicate Result	mg/kg	70	350		5309	9221	1675	3600	883	1966	4679
RpD	%				0	0	4%	5%	15%	6%	0
Zinc (Zn)											
Sample Result	mg/kg	150	750		15801	28170	5867	18193	3276	5249	7894
Duplicate Result	mg/kg	150	750		15546	27128	5381	18453	3023	4838	9938
RpD	%				0	0	9%	1%	8%	8%	0
Analytical Laboratory Duplicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-
RpD	%										
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-
RpD	%										
Analytical Laboratory Replicates											
Lead (Pb)											
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-
RpD	%										
Zinc (Zn)											
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-
RpD	%										

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

Table SS 25-4. South Shore Area Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	South Shore					
				Sample ID	Shore-12020-S-D	Shore-12067-W-C	Shore-12068-W-C	Shore-12069-W-C	Shore-12070-W-C	Shore-12071-W-D
				Duplicate ID	Shore-12315-S-Q	Shore-12332-W-Q	Shore-12331-W-Q	Shore-12333-W-Q	Shore-12330-W-Q	Shore-12334-W-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**					
On Site Field Screening Duplicates										
Lead (Pb)										
Sample Result	mg/kg	70	350		2242	1248	2854	988	5756	540
Duplicate Result	mg/kg	70	350		2260	1404	3338	1168	4778	846
RpD	%				0	0	16%	17%	19%	44%
Zinc (Zn)										
Sample Result	mg/kg	150	750		4594	2064	6241	2061	8968	1074
Duplicate Result	mg/kg	150	750		4946	2354	6160	2239	7451	1631
RpD	%				0	0	1%	8%	18%	41%
Analytical Laboratory Duplicates										
Lead (Pb)										
Sample Result	mg/kg	100	500		-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-
RpD	%									
Zinc (Zn)										
Sample Result	mg/kg	3	15		-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-
RpD	%									
Analytical Laboratory Replicates										
Lead (Pb)										
Sample Result	mg/kg	100	500		-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-
RpD	%									
Zinc (Zn)										
Sample Result	mg/kg	3	15		-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-
RpD	%									

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na *RpD value is not applicable because one or both results are less than the PQL.*

RpD *Relative Percent Difference = (Difference/Average)*100.*

PQL *Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL *Method Detection Limit of analysis.*

BH-7
SS 13
SS TL1
TP-207
TP-18
BH-6
TP-12
TP-4
BH-8
TP-38
TP-3
TP-2
TP-208
SS20-6
SS20-5
TP-20
SS 21
TP-1
BH-10
TP-19
SS 12
TP-21
SS 14
TP-37
TP-26
TP-209
TP-36
BH-9
SS 6
TP-25
TP-39
TP-151
TP-35
TP-23
SS 22
TP-24
TP-150
TP-34
TP-149
SS TL3
TP-40
TP-27
SS 23
SS 28
TP-33
TP-148
TP-41
SS TL5
SHORELINE
TP-147
TP-32
TP-155
SS 26
TP-42
TP-154
TP-146
TP-28
TP-31
TP-29
TP-145
TP-30
TP-144
TP-152
TP-143
TP-153
SS FW-B
F-16
SS FW-A
F-17
FSD-2
F-15
F-4
FSD-1
F-3
F-14
TP-43
F-5

500 600 700 800
1300 1200 1100 1000 900

C R O Z I E R S T R A I T

N

0 5 10 20 30 Metres
SCALE 1:750

KEY PLAN
N.T.S.

N O R T H B A Y
P O L A R I S B A Y
TO FRUSTRATION LAKE
TO GARROW LAKE
AREA OF DETAIL
2000N
1000N
100E
2000E

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)
- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)
- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

SOURCE OF DRAWING:
-

DRAWING INFORMATION:	
REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–SS–M1–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

SOUTH SHORE CONDITIONS BEFORE REMEDIATION

Gartner Lee

FIGURE NO. SS-25-1

REFER TO JUNE 10/05 CLOSE-OUT REPORT: DOCK AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: BARGE AREA

REFER TO DEC. 31/03 CLOSE-OUT REPORT: CONCENTRATE STORAGE SHED AREA

REFER TO JUNE 10/05 CLOSE-OUT REPORT: FOLDAWAY BUILDINGS


Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
Shore-4-F-C	487	2690
Shore-5-F-C	643	3170
Shore-6-F-C	496	3760
Shore-8-F-C	1970	4670
Shore-10-F-C	1050	2660
Shore-50-F-C	500	2470
Shore-51-F-C	267	1420
Shore-52-F-C	135	645
Shore-54-F-C	208	1100
Shore-56-F-C	225	991
Shore-57-F-C	137	448
Shore-58-F-C	154	265
Shore-59-F-D	<100	273
Shore-60-F-C	484	3150
Shore-61-F-C	<100	431
Shore-53-F-Q duplicate of Shore-61-F-C	<100	495
Shore-74-F-C	453	5590
Shore-75-F-C	437	4300
Shore-76-F-C	121	365
Shore-77-F-C	116	527
Shore-78-F-D	202	967
Shore-79-F-D	279	1220
Shore-80-F-C	346	1050
Shore-72-F-Q duplicate of Shore-80-F-C	471	1640
Shore-81-F-C	127	547
Shore-82-F-C	195	970
Shore-83-F-C	1060	4160
Shore-85-F-C	123	462
Shore-86-F-C	<100	120
Shore-84-F-Q duplicate of Shore-86-F-C	214	812
Shore-87-F-C	<200	578
Shore-89-F-C	253	791
Shore-90-F-C	165	1810
Shore-96-F-C	1040	4710
Shore-109-F-C	159	912
Shore-110-F-C	676	2410
Shore-108-F-Q duplicate of Shore-110-F-C	717	2530
Shore-111-F-C	<100	279
Shore-112-F-C	987	3760
Shore-114-F-C	394	2570
Shore-115-F-C	543	1910
Shore-120-F-C	1030	8910
Shore-122-F-C	755	3640
Shore-124-F-C	856	2930
Shore-125-F-C	236	1180
Shore-127-F-C	677	2350
Shore-142-F-C	114	351
Shore-144-F-D	256	1360
Shore-146-F-C	553	1330
Shore-143-F-Q duplicate of Shore-146-F-C	428	1270
Shore-156-F-C	369	1870
Shore-157-F-C	197	1030
Shore-158-F-C	152	572
Shore-159-F-C	282	1100
Cshed-401-F-C	327	2140
Cshed-402-F-C	227	3050
Shore-411-F-C	910	3440
Shore-429-F-C	1170	2390
Shore-436-F-C	411	2740
Shore-420-F-Q duplicate of Shore-436-F-C	485	2510
Shore-437-F-C	994	5430
Shore-462-F-D	300	1530
Shore-466-F-D	1790	7800
Shore-482-F-C	890	3980
Shore-484-F-C	940	2300
Shore-485-F-C	620	2260
Shore-486-F-C	290	1510
Shore-502-F-C	<50	90.4
Shore-503-F-C	580	1610
Shore-504-F-C	120	754
Shore-10647-F-C	577	2890
Shore-10747-F-C	220	524
Shore-10775-F-D	220	526
Shore-10779-F-D	680	1190
Shore-10820-F-C	520	566
Shore-10849-F-Q duplicate of Shore-10820-F-C	520	719
Shore-10821-F-C	560	861
Shore-10947-F-D	310	1740
Shore-10956-F-D	210	1510
Shore-11220-F-C	340	1010
Shore-11221-F-C	270	699
Shore-11222-F-C	300	1030
Shore-11223-F-C	550	494
Shore-11486-F-Q duplicate of Shore-11223-F-C	650	415
Shore-11229-F-C	230	2340
Shore-11232-F-C	500	649
Shore-11303-F-C	1170	3130
Shore-11304-F-C	160	1630
Shore-11305-F-C	130	527
Shore-11309-F-Q duplicate of Shore-11305-F-C	170	486
Shore-11306-F-C	320	1640
Shore-11307-F-C	220	843
Shore-11308-F-C	270	1380
Shore-11317-F-D	<100	241
Shore-11338-F-D	270	1290
Shore-11364-F-C	110	747
Shore-11366-F-C	310	1380
Shore-11367-F-C	250	2570
Shore-11368-F-C	310	1630
Shore-11369-F-Q duplicate of Shore-11368-F-C	210	1370
Shore-11470-F-C	<50	163
Shore-11471-F-C	<50	127
Shore-11472-F-C	59	180
Shore-11473-F-C	<50	112
Shore-11474-F-C	<50	105
Shore-11475-F-C	<50	139
Shore-11585-F-Q duplicate of Shore-11475-F-C	<50	142
Shore-11476-F-C	<50	118
Shore-11485-F-C	610	3020
Shore-11565-F-D	<50	69
Shore-11573-F-C	<100	287
Shore-11575-F-C	130	336
Shore-11576-F-C	250	330
Shore-11597-F-C	660	3930
Shore-11630-F-C	<50	82.4
Shore-11631-F-C	<50	103
Shore-11649-F-D	319	1220
Shore-11669-F-C	180	467
Shore-11670-F-C	78	198
Shore-11671-F-C	230	1050
Shore-11672-F-C	450	694
Shore-11676-F-C	190	509
Shore-11695-F-C	150	466
Shore-11722-F-D	232	1340
Shore-11743-F-C	<50	67.6
Shore-11744-F-C	<50	101
Shore-11746-F-C	380	1880
Shore-11747-F-C	290	822
Shore-11767-F-C	480	786
Shore-11768-F-Q duplicate of Shore-11767-F-C	520	1050
Shore-11816-F-C	<50	96.8
Shore-11817-F-Q duplicate of Shore-11816-F-C	<50	157
Shore-11818-F-C	<50	63.8
Shore-11821-F-C	228	616
Shore-11822-F-C	203	610
Shore-11854-F-D	<100	114
Shore-11860-F-C	<200	49.2
Shore-11861-F-C	<200	134
Shore-11964-F-D	320	934
Shore-11987-F-D	**2600**	4400
Shore-11778-F-Q duplicate of Shore-11987-F-D	140	365
Shore-11988-F-D	210	424
Shore-11779-F-Q duplicate of Shore-11988-F-D	<100	207
Shore-11996-F-C	<100	36.3
Shore-11997-F-Q duplicate of Shore-11996-F-C	<100	38.7
Shore-11998-F-C	<100	50.9
Shore-11999-F-Q duplicate of Shore-11998-F-C	280	363
Shore-12000-F-C	<100	179
Shore-12001-F-C	279	331
Shore-12002-F-C	244	321
Shore-12003-F-C	314	403
Shore-12037-F-C	<100	462
Shore-12067-W-C	537	760
Shore-12071-W-D	295	473
Shore-12072-W-C	<50	134
Shore-12073-W-C	94	298
Shore-12074-W-C	93	361

Confirmation Sample ID	EPH C10-C19 mg/kg	EPH C19-C32 mg/kg
Shore-7-F-C	<200	<200
Shore-11860-F-C	<200	<200
Shore-11861-F-C	310	<200
Shore-12037-F-C	590	<200

Bold — Concentration greater than or equal to the Polaris Mine SQROs

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

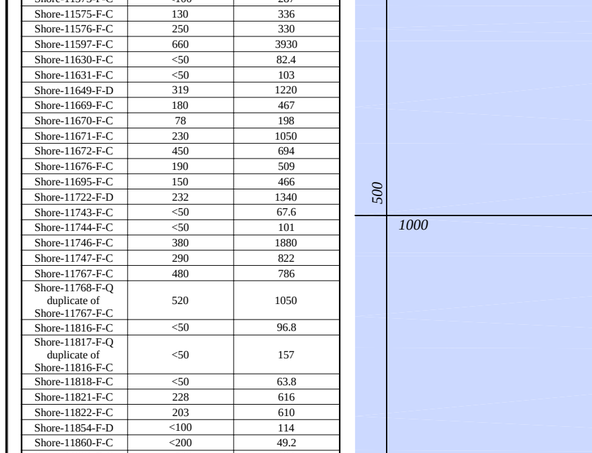

KEY PLAN
N.T.S.

0 5 10 20 30 Metres
SCALE 1:750

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

ESP–7–I–D
- AREA
- SAMPLE ID
- TYPE: C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA; WALL–5 SAMPLES ALONG 25m OF WALL; D= DISCRETE SAMPLE; Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
- LOCATION: F= FLOOR SAMPLE; I= INTERMEDIATE FLOOR SAMPLE; W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- *EPH – EXTRACTABLE PETROLEUM HYDROCARBONS
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

SOURCE OF DRAWING:

-

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–SS–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

SOUTH SHORE CONDITIONS AFTER REMEDIATION

Gartner Lee

FIGURE NO. SS-25-2

Appendix J

North Shore

June 10, 2005

Mr. Bruce Donald
Teck Cominco Limited
Bag 2000
Kimberley, BC V1A 3E1

Dear Mr. Donald:

Re: 40137 – Polaris Mine Operations Contaminated Soil Remediation
Close Out Report: North Shore

BACKGROUND

The North Shore area (shown as Area 26 on Figure 1: *Contaminated Soils Remediation Progress Plan, December 31, 2003* and on Figure 2: *Contaminated Soils Remediation Progress Plan, December 31, 2004*) is located north of the sewer line and dock along Crozier Strait. The area was bound by the sewage line to the south, the exploration stockpile to the north and the firehall and main portal to the east.

The North Shore area housed a temporary shop, an ore stockpile and contained part of the berthing lagoon excavated to float the Process Barge into place during the construction of the mine. The temporary shop was located in front of the main portal, and was used to service equipment during the development of the underground workings. A cofferdam was constructed across the entrance to the lagoon, the sea water was pumped out and the excavation backfilled once the Process Barge was in place. Rock obtained from the mine workings was used to backfill the berthing lagoon and to build up the shoreline during the construction and to repair eroded areas during the operation of the mine.

The Environmental Site Assessment (ESA) conducted in 1999 and 2000 identified metal contamination at the North Shore. Three (3) surface samples were collected, one (1) test pit excavated and three (3) boreholes drilled during the ESA. The sample results indicated that elevated metal concentrations were present from surface up to a depth of at least 1.5 m in the backfilled areas. Metals contamination was observed in boreholes and test pit samples. No indication of hydrocarbon contamination was encountered during the ESA. Figure NS-26-01: *North Shore Conditions Before Remediation* illustrates the original topography of the area as well as the sample results from the ESA.

METHODOLOGY

Delineation

Between July 6, 2003 and July 8, 2003, the preliminary boundary of the area to be remediated, identified in the ESA as an "Area of Concern" was further delineated for excavation through the collection and analysis of field screening samples from twenty six (26) boreholes advanced with an air rotary quarry drill. Gartner Lee Limited (GLL) sampled the soil in accordance with standard GLL and Teck Cominco Limited (TCL) sampling procedures and protocols. Three hundred fifty nine (359) composite samples were collected from the boreholes. Each hole was drilled until bedrock was encountered; depths ranged from 1.0 m to 9.5 m and composite soil samples were collected over 0.5 m intervals. The soil samples were collected from the drill returns that accumulated at the mouth of the borehole. Following the collection of each sample the surface surrounding the borehole was cleared of the drill cuttings.

The visual appearance, odour of the soil and field screening measurements obtained from the borehole samples were used to delineate the area to be excavated. Based on the results of the field screening sampling, GLL modified the boundaries of the area to be remediated and directed excavation. The field screening measurements for hydrocarbons were obtained using a portable photo-ionization detector (PID) to measure the concentrations of organic vapours in the headspace of the sample bags. Metals concentrations were analysed using a Niton portable X-Ray Fluorescence (XRF) elemental analyzer. Field screening results from the drilling indicated that both metal and hydrocarbon contamination was present in sub-areas at depths ranging from 1.0 m to 4.5 m. No hydrocarbon contamination was encountered within 25 m of the shoreline.

Excavation

The excavation of the North Shore area started in August 2003 and it was completed in July 2004. In 2003, excavation of metal contaminated soil commenced adjacent to the shoreline. A berm, approximately 10 m wide was left intact between the ocean and the excavation to limit the interaction with the foreshore environment. The berm provided protection from the ocean flooding the worksite as well as protection from the water washing fine sand and silt into the marine environment. Total suspended solids (TSS) levels were monitored daily during periods of work in the foreshore along the shoreline at predetermined stations in accordance with approved site procedures and protocols.

The excavation was left open over the winter months and work recommenced in the spring of 2004. Removal of the berm took place in July 2004 while ice still bound the marine foreshore and interaction with the marine foreshore was minimal.

To direct the excavation activities, soil samples were collected across the excavation area in accordance with standard GLL and TCL sampling procedures and protocols. Field screening using the PID for hydrocarbons and the XRF analyzer for Lead and Zinc was used to determine where additional excavation was required to meet the Site Quality Remediation Objectives (SQRO). Excavation of the North Shore was completed on July 10, 2004. The limits of the excavation are shown on Figure NS-26-02: *North Shore Conditions After Remediation*. This material was disposed of in the underground mine working in accordance with regulatory approvals.

Confirmation Sampling

Upon receipt of field screening results that indicated that the soil remaining in the excavation would meet the SQROs confirmation soil samples were collected. The excavation area was sub divided into individual composite sampling areas approximately 25 m x 25 m or less as required to cover the area to be sampled. Wall samples were composited over a length of 25 m on the wall of the excavation. Composite samples were created by collecting four or five evenly spaced allocates of soil with in the individual composite sample area. A single allocate of soil from a specific point is a discrete sample.

The soil samples were collected at the excavation limits and submitted to ALS Environmental (ALS) for Extractable Petroleum Hydrocarbons (EPH), Polycyclic Aromatic Hydrocarbons (PAH) and metals. Additional excavation was undertaken in areas where the laboratory analytical results did not meet the Soil Quality Remediation Objectives (SQROs) and additional confirmatory samples were taken upon completion of excavation. Upon receipt of analytical results that met the SQROs the final excavation limits were surveyed.

ANALYTICAL RESULTS

Analytical laboratory results for EPH, metals and PAH are summarised in Tables NS-26-1, NS-26-2 and NS-26-3 along with the approved Polaris Mine SQRO's for petroleum hydrocarbons and metals. A total of thirty eight (38) hydrocarbon remediation confirmation samples were submitted from the North Shore area: twenty four (24) composite floor samples, seven (7) discrete samples, and seven (7) quality assurance quality control (QA/QC) samples. Of the metals remediation confirmation samples there were fifty four (54) confirmation samples submitted: thirty four (34) composite floor samples, thirteen (13) discrete samples, two (2) composite wall samples, and five (5) quality assurance quality control (QA/QC) samples. The soil quality results and lateral limits of the excavation are shown on Figure NS-26-2.

Quality Assurance/Quality Control (QA/QC)

Relative percent differences have been calculated and compiled in Table NS-26-4 for EPH and Table NS-26-5 for Lead and Zinc. There are a total of seven (7) analytical laboratory duplicates and four (4) analytical laboratory duplicates for EPH. Of the metals, there are twenty three (23) onsite field screened duplicates, nine (9) analytical laboratory duplicates, and six (6) analytical laboratory replicates for a total forty nine (49) QA/QC samples.

Forty seven (47) of the sample results and their duplicate/replicate results returned RpDs below the practical quantitation limit (PQL), in which case the RpD value has been identified as "na" (not applicable), or returned acceptable RpDs, below the site specific remediation protocol of 50%. Two analytical laboratory duplicates returned RpDs greater than the objective for Lead. The variance between the sample and its duplicate is considered indicative of sample heterogeneity, especially at low concentrations of Lead.

Polaris Mine Soil Quality Remediation Objectives

Twenty four (24) hydrocarbon remediation confirmation composite samples and thirty six (36) metal remediation confirmation composite samples were collected across the floor and the wall of the excavation. All of the remediation confirmation composite samples returned results below the Polaris Mines SQRO's for EPH. Two (2) remediation confirmation composite samples returned results above the Polaris Mine SQRO's for Lead and/or Zinc. Shore-10135-F-C had a Lead concentration of 2320 mg/kg and Shore-10588-F-C had a Lead concentration of 2,140 mg/kg and a Zinc concentration of 10,700 mg/kg. The exceedances are less than two times the SQRO. The SQRO's for Lead and Zinc are 2,000 mg/kg and 10,000 mg/kg respectively. The approved site-specific remedial objectives allow for minor exceedances in a small percentage of the confirmatory sample area, as long as the concentration is less than twice the remedial target.

Discrete samples were collected in addition to the composite samples to discern the homogeneity of the sample areas represented by the composite samples. The results are shown on the tables below and generally confirm that there is reasonable homogeneity within the sample areas with the exception of EPH C_{19}-C_{32} and Zinc concentrations in sample Shore-10800-F-D.

Summary of Discrete Hydrocarbon Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	EPH_{10-19} (mg/kg)	EPH_{19-32} (mg/kg)	Discrete Sample ID	EPH_{10-19} (mg/kg)	EPH_{19-32} (mg/kg)
Shore-10051-F-C	<200	<200	Shore-10042-F-D	<200	<200
Shore-10082-F-C	<200	<200	Shore-10073-F-D	<200	<200
Shore-10080-F-C	<200	<200	Shore-10076-F-D	220	<200
Shore-10080-F-C	<200	<200	Shore-10079-F-D	<200	<200
Shore-10846-F-C	640	490	Shore-10794-F-D	370	460
Shore-10845-F-C	940	370	Shore-10800-F-D	**1180**	**1010**

Summary of Discrete Metals Sample Results Compared to Corresponding Composite Sample Results

Composite Sample ID	Lead (mg/kg)	Zinc (mg/kg)	Discrete Sample ID	Lead (mg/kg)	Zinc (mg/kg)
Shore-10051-F-C	<150	19	Shore-10042-F-D	<150	31
Shore-10082-F-C	<150	16	Shore-10073-F-D	<150	9
Shore-10080-F-C	<150	8	Shore-10076-F-D	<150	7
Shore-10080-F-C	<150	8	Shore-10079-F-D	<150	7
Shore-10134-F-C	<150	11	Shore-10116-F-D	160	623
Shore-10846-F-C	<100	153	Shore-10794-F-D	<100	72
Shore-10845-F-C	140	387	Shore-10800-F-D	230	1190

Generic Federal Soil Quality Guidelines for Parkland Land Use

Eight (8) hydrocarbon samples were analysed for polycyclic aromatic hydrocarbons (PAH) and eight (8) metal samples were analyzed for total metals. The PAH results were below the generic Canadian Council of Ministers of Environment (CCME) Canadian Environmental Quality Guideline (CEQG) for Parkland Land use. Three confirmation samples returned Barium concentrations greater than the CCME CEQG for Parkland Land use of 500 mg/kg for Barium in soil. Barium concentrations in the samples analyzed from the North Shore ranged from 286 mg/kg to 727 mg/kg. The CCME recognizes that local geological conditions may result in elevated background levels of metals above the guidelines.

Barium is a common mineral associated with lead sulphides, and it is found in cavities in limestone and dolostone. Soil samples collected during the 2004 vegetation sampling program at Polaris, as documented in the November 24, 2004 Memorandum *2004 Vegetation Sampling Results,* are considered to be representative of background conditions. Samples were collected at the following intervals surface to 0.01 m, 0.01 m to 0.05 m, and 0.05 m to 0.1 m. Concentrations

of barium greater than generic CCME CEQG Parkland land use were detected in each interval. The variability of barium concentrations in those samples is listed in the following table.

Summary of 2004 Background Area Soil Concentrations of Barium

Parameter	n	Minimum Concentration (mg/kg)	Maximum Concentration (mg/kg)	Median Concentration (mg/kg)	Mean Concentration (mg/kg +/-SD)	90th Percentile (mg/kg)	75th Percentile (mg/kg)
Barium	12	228	2140	1185	1249 +/-518	1986	1560

n = number of samples.

SD = standard deviation.

The concentrations of Barium remaining within the footprint of the North Shore area after remediation are within the range of the background concentrations. In addition, the immobile nature of the Barium encountered on site was demonstrated in the ESA leachate test results that returned Barium concentrations at levels less than the detection limit and it was therefore not identified as a contaminant of concern in the ESA.

The confirmatory samples supported by the QA/QC samples from the North Shore area provide confidence that the remediation of the North Shore complies with the SQRO's.

CONCLUSION

Based on confirmatory sampling consistent with good practice and the approved site specific sampling procedures and protocols, the remediation of the North Shore area has been completed to meet the Polaris Mine remedial targets, as documented in the approved Polaris Mine Decommissioning and Remediation Plan, March 2001.

LIMITATIONS

This report has been prepared by Gartner Lee Limited and the information in this report is intended for the use of Teck Cominco Metals Ltd. during the decommissioning and reclamation program at the Polaris Mine Site. Any use which a third party makes of this report, or any reliance on or decisions made on the basis of the information in this report is the responsibility of such third parties. Gartner Lee Limited accepts no responsibility for damages, if any, suffered by the third party, based on the use of or reliance on any information contained in this report.

The scope of Gartner Lee Limited's work was limited to that described in this report. The confirmation of environmental conditions at the site of the remedial work is based on sampling at

specific wall and floor locations within the excavation limits. Gartner Lee Limited has used judgement in the interpretation of the available information but subsurface physical and/or chemical characteristics may vary between or beyond sampling locations. Gartner Lee Limited is not a guarantor of the environmental condition of the site but warrants only that its work was undertaken and its report prepared in a manner consistent with the level of skill and diligence normally exercised by competent environmental professionals practicing in the Nunavut Territory.

Yours very truly,
GARTNER LEE LIMITED

Dennis Lu, B.Sc.
Field Scientist

Arlene Laudrum, P.Geol.
Remediation Supervisor, Polaris Mine Project

Dr. Dennis Gregor, P.Geol.
Senior Reviewer, Senior Aquatic Scientist

AL:DL:gc

ATTACHMENTS

Tables

Table NS-25-1:	North Shore Remediation Confirmation Soil Samples – Hydrocarbons
Table NS-25-2:	North Shore Remediation Confirmation Soil Samples – Metals
Table NS-25-3:	North Shore Remediation Confirmation Soil Samples – Polycyclic Aromatic Hydrocarbons (PAHs)
Table NS 25-4:	North Shore Quality Assurance and Quality Control Remediation Soil Samples – Hydrocarbons
Table NS 25-5:	North Shore Quality Assurance and Quality Control Remediation Soil Samples – Metals

Figures

Figure NS-25-1:	North Shore Conditions Before Remediation
Figure NS-25-2:	North Shore Conditions After Remediation

Table NS-26-1. North Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore							
		Sample ID	Shore-10042-F-D	Shore-10051-F-C	Shore-10062-F-C	Shore-10073-F-D	Shore-10076-F-D	Shore-10079-F-D	Shore-10080-F-C	Shore-10081-F-C
		Date Sampled	13-Apr-04	13-Apr-04	13-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04
		ALS File Number	U4484	U2687	U2687	U4484	U2688R	U2688R	U2688R	U2688R
		Field Screen (ppm)[b]	35	-	-	50	60	45	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	<200	220	<200	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	<200	<200
LEPH[c]	1000	mg/kg	-	-	-	-	-	<200	<200	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	<200	<200	-

Bold *Concentration exceeds the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table NS-26-1. North Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore							
		Sample ID	Shore-10082-F-C	Shore-10131-F-C	Shore-10132-F-C	Shore-10133-F-C	Shore-10136-F-Q	Shore-10286-F-C	Shore-10491-F-C	Shore-10794-F-D
		Date Sampled	15-Apr-04	20-Apr-04	20-Apr-04	20-Apr-04	20-Apr-04	28-Apr-04	06-May-04	24-May-04
		ALS File Number	U2688R	U2778r	U2778R	U2778R	U5597r	U3083	U3342	U3969R
		Field Screen (ppm)[b]	-	-	-	-	-	-	-	65
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	<200	870	810	<200	<200	<200	<200	370
EPH C_{19}-C_{32}	1000	mg/kg	<200	<200	<200	<200	<200	<200	460	460
LEPH[c]	1000	mg/kg	-	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	-	-	-	-	-	-	-	-

Bold *Concentration exceeds the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table NS-26-1. North Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore							
		Sample ID	Shore-10800-F-D	Shore-10845-F-C	Shore-10846-F-C	Shore-10850-F-Q	Shore-10847-F-C	Shore-10848-F-Q	Shore-11171-F-C	Shore-11755-F-C
		Date Sampled	24-May-04	24-May-04	24-May-04	24-May-04	24-May-04	24-May-04	04-Jun-04	06-Jul-04
		ALS File Number	U3969R	U3969R	U3969R	duplicate of Shore-10846-F-C	U3969R	duplicate of Shore-10847-F-C	U4269R	U5597R
		Field Screen (ppm)[b]	70	-	-		-		-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	**1180**	940	640	840	580	510	900	<200
EPH C_{19}-C_{32}	1000	mg/kg	**1010**	370	490	510	430	410	990	<200
LEPH[c]	1000	mg/kg	**1180**	-	640	-	-	-	-	-
HEPH[c]	1000	mg/kg	**1010**	-	490	-	-	-	-	-

Bold *Concentration exceeds the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table NS-26-1. North Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore							
		Sample ID	Shore-11757-F-C	Shore-11823-F-C	Shore-11824-F-C	Shore-11748-F-Q	Shore-11825-F-C	Shore-11909-F-C	Shore-11938-F-C	Shore-12144-F-D
		Date Sampled	08-Jul-04	30-Jun-04	30-Jun-04	30-Jun-04	30-Jun-04	06-Jul-04	07-Jul-04	12-Aug-04
		ALS File Number	U5615R	U5353R	U5353R	duplicate of Shore-11824-F-C	U5353R	U5597R	U5615R	U7283
		Field Screen (ppm)[b]	-	5	5		5	-	-	-
Parameter	**Site Specific**	**Units**	**Analytical Results**							
Extractable Hydrocarbons										
EPH C_{10}-C_{19}	1000	mg/kg	220	<200	220	<200	270	<200	210	230
EPH C_{19}-C_{32}	1000	mg/kg	<200	340	400	350	450	290	370	410
LEPH[c]	1000	mg/kg	220	-	-	-	-	-	-	-
HEPH[c]	1000	mg/kg	<200	-	-	-	-	-	-	-

Bold *Concentration exceeds the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table NS-26-1. North Shore Remediation Confirmation Soil Samples - Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore					
		Sample ID	Shore-12156-F-C	Shore-12159-F-Q	Shore-12157-F-C	Shore-12161-F-Q	Shore-12158-F-C	Shore-12160-F-Q
		Date Sampled	12-Aug-04	12-Aug-04	12-Aug-04	12-Aug-04	12-Aug-04	12-Aug-04
		ALS File Number	U7283	duplicate of Shore-12156-F-C	U7283	duplicate of Shore-12157-F-C	U7283	duplicate of Shore-12158-F-C
		Field Screen (ppm)[b]	-		-		-	
Parameter	**Site Specific**	**Units**	**Analytical Results**					
Extractable Hydrocarbons								
EPH C_{10}-C_{19}	1000	mg/kg	<200	<200	<200	290	<200	<200
EPH C_{19}-C_{32}	1000	mg/kg	<200	240	<200	520	240	<200
LEPH[c]	1000	mg/kg	<200	-	<200	-	<200	-
HEPH[c]	1000	mg/kg	<200	-	<200	-	240	-

Bold *Concentration exceeds the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The approved Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on the Yukon Territorial Contaminated Sites Regulation for Parkland (PL) Land Use.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Light Extractable Petroleum Hydrocarbons (LEPH) and Heavy Extractable Petroleum Hydrocarbons (HEPH) are determined by subtracting Polycyclic Aromatic Hydrocarbons (PAH) from Extractable Petroleum Hydrocarbons (EPH), therefore use of the EPH remediation objective is conservative.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-510-F-C	Shore-10000-F-D	Shore-10001-F-D	Shore-10042-F-D	Shore-10051-F-C	Shore-10062-F-C	Shore-10073-F-D
				Date Sampled	28-Oct-03	28-Oct-03	28-Oct-03	13-Apr-04	13-Apr-04	13-Apr-04	15-Apr-04
				ALS File Number	T6195	U3083	U3083	U2687	U2687	U2687	U2688R
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	294	370	27	-	-	27
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	1867	1869	296	-	-	207
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH											
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	1090	720	1250	<150	<150	<150	<150
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	8850	2850	1730	31.1	18.6	150	9.2

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-10076-F-D	Shore-10079-F-D	Shore-10080-F-C	Shore-10081-F-C	Shore-10082-F-C	Shore-10116-F-D	Shore-10131-F-C
				Date Sampled	15-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04	15-Apr-04	20-Apr-04
				ALS File Number	U2688R	U2688R	U2688R	U2688R	U2688R	U2778R	U2778r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	24	28	-	-	-	137	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	150	163	-	-	-	1302	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH											
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<150	<150	<150	<150	<150	<150	<150
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	7.4	7.1	8.2	125	15.5	623	168

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-10132-F-C	Shore-10133-F-C	Shore-10136-F-Q	Shore-10134-F-C	Shore-10135-F-C	Shore-10286-F-C	Shore-10314-F-D
				Date Sampled	20-Apr-04	20-Apr-04	18-Apr-04	18-Apr-04	18-Apr-04	28-Apr-04	04-May-04
				ALS File Number	U2778r	U2778r	U2778r	U2778r	U2778r	U3083	U4484
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	-	duplicate of	-	-	-	366
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	-	Shore-10133-F-C	-	-	-	2344
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH					8.76						
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	<30	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	<15	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	318	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	<2	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	<2	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	<6	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	<6	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	<3	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	<150	<150	<150	<150	**2320**	<150	1390
Mercury	T-Hg	-	7	mg/kg	<0.050	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	<12	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	<15	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	<6	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	<6	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	<15	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	14	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	177	677	479	10.5	7210	23	5830

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-10360-F-C	Shore-10582-F-C	Shore-10583-F-C	Shore-10584-F-C	Shore-10585-F-C	Shore-10586-F-C	Shore-10587-F-C
				Date Sampled	04-May-04	10-May-04	10-May-04	10-May-04	10-May-04	10-May-04	10-May-04
				ALS File Number	U3240	U3476r	U3476r	U3476r	U3476r	U3476r	U3476r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	-	-	-	-	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	-	-	-	-	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH											
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	150	<100	980	<100	340	440	<100
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	1230	81.7	5310	75.4	850	1500	563

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-10588-F-C	Shore-10794-F-D	Shore-10800-F-D	Shore-10845-F-C	Shore-10846-F-C	Shore-10850-F-Q	Shore-10847-F-C
				Date Sampled	10-May-04	24-May-04	24-May-04	24-May-04	24-May-04	24-Mau-04	24-May-04
				ALS File Number	U3476r	U3969R	U3969R	U3969r	U3969r	U3969r	U3969r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	-	29	161	-	-	duplicate of	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	-	182	649	-	-	Shore-1046-F-C	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH							8.80		8.95		
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	<20	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	-	-	<10	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	-	-	418	-	479	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	<1.0	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	2.3	-	<1	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	<4.0	-	<4	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	<4.0	-	<4	-	-
Copper	T-Cu	-	63	mg/kg	-	-	<2.0	-	<2	-	-
Lead	T-Pb	2000	-	mg/kg	**2140**	<100	230	140	<100	<100	<100
Mercury	T-Hg	-	7	mg/kg	-	-	<0.050	-	<0.050	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	<8.0	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	<10	-	<10	-	-
Selenium	T-Se	-	1	mg/kg	-	-	<4.0	-	<4	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	<4.0	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	<10	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	-	-	<10.6	-	12	-	-
Zinc	T-Zn	10000	-	mg/kg	**10700**	71.5	1190	387	153	460	159

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-10848-F-Q	Shore-11022-S-D	Shore-11171-F-C	Shore-11477-F-C	Shore-11757-F-C	Shore-11823-F-C	Shore-11824-F-C
				Date Sampled	24-May-04	09-May-04	04-Jun-04	15-Jun-04	08-Jul-04	30-Jun-04	30-Jun-04
				ALS File Number	U3969r	U4269r	U4269r	U4781	U5615R	U5353r	U5353r
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	duplicate of	-	-	78	-	-	297
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	Shore-10847-F-C	-	-	344	-	-	1388
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH									8.94		
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-		-	-	<20	-	-
Arsenic	T-As	-	12	mg/kg	-		-	-	<10	-	-
Barium	T-Ba	-	500	mg/kg	-		-	-	286	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-		-	-	<1	-	-
Cadmium	T-Cd	-	10	mg/kg	-		-	-	10	-	-
Chromium	T-Cr	-	64	mg/kg	-		-	-	5	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-		-	-	<4	-	-
Copper	T-Cu	-	63	mg/kg	-		-	-	6	-	-
Lead	T-Pb	2000	-	mg/kg	<100	1160	1230	121	320	170	<50
Mercury	T-Hg	-	7	mg/kg	-		-	-	<0.050	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-		-	-	<8	-	-
Nickel	T-Ni	-	50	mg/kg	-		-	-	<10	-	-
Selenium	T-Se	-	1	mg/kg	-		-	-	<4	-	-
Silver	T-Ag	-	20[d]	mg/kg	-		-	-	<4	-	-
Tin	T-Sn	-	50[d]	mg/kg	-		-	-	<10	-	-
Vanadium	T-V	-	130	mg/kg	-		-	-	30	-	-
Zinc	T-Zn	10000	-	mg/kg	186	3870	4460	214	3010	425	456

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore						
				ALS Sample ID	Shore-11748-F-Q	Shore-11825-F-C	Shore-11852-W-C	Shore-11853-W-C	Shore-11909-F-C	Shore-11938-F-C	Shore-12140-F-D
				Date Sampled	30-Jun-04	30-Jun-04	02-Jul-04	02-Jul-04	06-Jul-04	07-Jul-04	12-Aug-04
				ALS File Number	U5353r	U5353r	U5597r	U5597r	U5597r	U5615r	U7283
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	duplicate of	361	-	-	-	-	270
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	Shore-11824-F-C	773	-	-	-	-	456
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**						
pH											
Total Metals											
Antimony	T-Sb	-	20[d]	mg/kg	-	-	-	-	-	-	-
Arsenic	T-As	-	12	mg/kg	-	-	-	-	-	-	-
Barium	T-Ba	-	500	mg/kg	-	-	-	-	-	-	-
Beryllium	T-Be	-	4[d]	mg/kg	-	-	-	-	-	-	-
Cadmium	T-Cd	-	10	mg/kg	-	-	-	-	-	-	-
Chromium	T-Cr	-	64	mg/kg	-	-	-	-	-	-	-
Cobalt	T-Co	-	50[d]	mg/kg	-	-	-	-	-	-	-
Copper	T-Cu	-	63	mg/kg	-	-	-	-	-	-	-
Lead	T-Pb	2000	-	mg/kg	243	<50	<100	<100	<100	140	410
Mercury	T-Hg	-	7	mg/kg	-	-	-	-	-	-	-
Molybdenum	T-Mo	-	10[d]	mg/kg	-	-	-	-	-	-	-
Nickel	T-Ni	-	50	mg/kg	-	-	-	-	-	-	-
Selenium	T-Se	-	1	mg/kg	-	-	-	-	-	-	-
Silver	T-Ag	-	20[d]	mg/kg	-	-	-	-	-	-	-
Tin	T-Sn	-	50[d]	mg/kg	-	-	-	-	-	-	-
Vanadium	T-V	-	130	mg/kg	-	-	-	-	-	-	-
Zinc	T-Zn	10000	-	mg/kg	557	106	241	228	82.3	447	1330

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.

b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-2. North Shore Remediation Confirmation Soil Samples - Metals

Gartner Lee				Location	North Shore				
				ALS Sample ID	Shore-12144-F-D	Shore-12156-F-C	Shore-12159-F-Q	Shore-12157-F-C	Shore-12158-F-C
				Date Sampled	12-Aug-04	12-Aug-04	12-Aug-04	12-Aug-04	12-Aug-04
				ALS File Number	U7283	U7283	U7283	U7283	U7283
		Polaris Mine Soil Quality		Field Screen Pb (ppm)[b]	235	-	duplicate of	-	-
		Remediation Objectives[a]		Field Screen Zn (ppm)[b]	726	-	Shore-12156-F-C	-	-
Parameter		**Site Specific**	**CEQG (PL)[c]**	**Units**	**Analytical Results**				
pH						8.5	9	8.82	8.68
Total Metals									
Antimony	T-Sb	-	20[d]	mg/kg	-	<20	<20	<20	<20
Arsenic	T-As	-	12	mg/kg	-	<10	<10	<10	<10
Barium	T-Ba	-	500	mg/kg	-	**719**	643	**499**	**727**
Beryllium	T-Be	-	4[d]	mg/kg	-	<1	<1	<1	<1
Cadmium	T-Cd	-	10	mg/kg	-	2	<1	<1	1
Chromium	T-Cr	-	64	mg/kg	-	10	9	9	10
Cobalt	T-Co	-	50[d]	mg/kg	-	<4	<4	<4	<4
Copper	T-Cu	-	63	mg/kg	-	14	12	14	13
Lead	T-Pb	2000	-	mg/kg	470	270	<100	<100	170
Mercury	T-Hg	-	7	mg/kg	-	0.065	0.059	0.062	0.065
Molybdenum	T-Mo	-	10[d]	mg/kg	-	<8	<8	<8	<8
Nickel	T-Ni	-	50	mg/kg	-	20	15	16	18
Selenium	T-Se	-	1	mg/kg	-	<9	<9	<7	<10
Silver	T-Ag	-	20[d]	mg/kg	-	<4	<4	<4	<4
Tin	T-Sn	-	50[d]	mg/kg	-	<10	<10	<10	<10
Vanadium	T-V	-	130	mg/kg	-	50	51	51	57
Zinc	T-Zn	10000	-	mg/kg	1840	494	83.5	64.3	223

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:
"<" = Less than analytical method detection limit.
"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and expsoure pathways.
b) Field screening results are measured using a Niton Xli 700 Series portable X-Ray Fluorescence (XRF) elemental analyser.
c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.
d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-3. North Shore Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore				
		ALS Sample ID	Shore-10079-F-D	Shore-10080-F-C	Shore-10800-F-D	Shore-10846-F-C	Shore-11757-F-C
		Date Sampled	15/04/2004	4/15/2004	24-May-04	5/24/2004	7/8/2004
		ALS File Number	U2688R	U2688R	U3969r	U3969r	U5615r
		Field Screen (ppm)[b]	45	-	70	-	-
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**				
Polycyclic Aromatic Hydrocarbons							
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.06	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	<0.06	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	0.106	0.332	<0.08	<0.08	0.188
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-3. North Shore Remediation Confirmation Soil Samples - Polycyclic Aromatic Hydrocarbons

Gartner Lee	Polaris Mine Soil Quality Remediation Objectives[a]	Location	North Shore		
		ALS Sample ID	Shore-12156-F-C	Shore-12157-F-C	Shore-12158-F-C
		Date Sampled	12-Aug-04	12-Aug-04	12-Aug-04
		ALS File Number	U7283	U7283	U7283
		Field Screen (ppm)[b]	-	-	-
Parameter	**CEQG (PL)[c]**	**Units**	**Analytical Results**		
Polycyclic Aromatic Hydrocarbons					
Acenaphthene	-	mg/kg	<0.04	<0.04	<0.04
Acenaphthylene	-	mg/kg	<0.05	<0.05	<0.05
Anthracene	-	mg/kg	<0.05	<0.05	<0.05
Benz(a)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05
Benzo(a)pyrene	0.7	mg/kg	<0.05	<0.05	<0.05
Benzo(b)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05
Benzo(g,h,I)perylene	-	mg/kg	<0.05	<0.05	<0.05
Benzo(k)fluoranthene	1[d]	mg/kg	<0.05	<0.05	<0.05
Chrysene	-	mg/kg	<0.05	<0.05	<0.05
Dibenz(a,h)anthracene	1[d]	mg/kg	<0.05	<0.05	<0.05
Fluoranthene	-	mg/kg	<0.05	<0.05	<0.05
Fluorene	-	mg/kg	<0.05	<0.05	<0.05
Indeno(1,2,3,-c,d)pyrene	1[d]	mg/kg	<0.05	<0.05	<0.05
Napthalene	0.6	mg/kg	<0.05	<0.05	<0.05
Phenanthrene	5[d]	mg/kg	<0.05	<0.05	<0.05
Pyrene	10[d]	mg/kg	<0.05	<0.05	<0.05

Bold *Concentration greater than or equal to the Soil Quality Remediation Objective (SQRO) for the Polaris Mine Site.*

Notes:

"<" = Less than analytical method detection limit.

"-" = Analysis not conducted, or no guideline.

a) The Soil Quality Remediation Objectives (SQROs) for the Polaris Mine Site are based on Canadian Council of Ministers of the Environment (CCME) standards and guidelines. The CCME provides criteria based on land use activities and applies the most strigent criteria based on site-specific receptors and exposure pathways.

b) Field screening results are measured based on a 'dry headspace' method using a combustible gas meter calibrated to a hexane standard.

c) Canadian Environmental Quality Guidelines (CEQG) for Parkland (PL) Land Use. The site-specific factors used for determining the soil quality guidelines were: soil ingestion, soil contact and nutrient cycling.

d) Interim Remediation Criterion. Soil Quality Guidelines based on the CCME soil protocol have not yet been developed for a given parameter.

Table NS-26-4. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee			Location	North Shore					
			Sample ID	Shore-10133-F-C	Shore-10846-F-C	Shore-10847-F-C	Shore-11824-F-C	Shore-12156-F-C	Shore-12157-F-C
			Duplicate ID	Shore-10136-F-Q	Shore-10850-F-Q	Shore-10848-F-Q	Shore-11748-F-Q	Shore-12159-F-Q	Shore-12161-F-Q
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**					
Analytical Laboratory Duplicates									
Extractable Hydrocarbons									
EPH C_{10}-C_{19}									
Sample Result	mg/kg	200	1000	<200	640	580	220	<200	<200
Duplicate Result	mg/kg	200	1000	<200	840	510	<200	<200	290
RpD	**%**			na	na	na	na	na	na
EPH C_{19}-C_{32}									
Sample Result	mg/kg	200	1000	<200	490	430	400	<200	<200
Duplicate Result	mg/kg	200	1000	<200	510	410	350	240	520
RpD	**%**			na	na	na	na	na	na
Analytical Laboratory Replicates									
Extractable Hydrocarbons									
EPH C_{10}-C_{19}									
Sample Result	mg/kg	200	1000						
Duplicate Result	mg/kg	200	1000						
RpD	**%**								
EPH C_{19}-C_{32}									
Sample Result	mg/kg	200	1000						
Duplicate Result	mg/kg	200	1000						
RpD	**%**								

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table NS-26-4. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Hydrocarbons

Gartner Lee			Location	North Shore				
			Sample ID	Shore-12158-F-C	Shore-10081-F-C	Shore-10131-F-C	Shore-11938-F-C	Shore-12158-F-C
			Duplicate ID	Shore-12160-F-Q	QC# 383542	QC# 383928	QC# 395282	QC# 402626
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**				
Analytical Laboratory Duplicates								
Extractable Hydrocarbons								
EPH C_{10}-C_{19}								
Sample Result	mg/kg	200	1000	<200				
Duplicate Result	mg/kg	200	1000	<200				
RpD	**%**			na				
EPH C_{19}-C_{32}								
Sample Result	mg/kg	200	1000	240				
Duplicate Result	mg/kg	200	1000	<200				
RpD	**%**			na				
Analytical Laboratory Replicates								
Extractable Hydrocarbons								
EPH C_{10}-C_{19}								
Sample Result	mg/kg	200	1000		<200	870	210	<200
Duplicate Result	mg/kg	200	1000		<200	700	<200	<200
RpD	**%**				na	na	na	na
EPH C_{19}-C_{32}								
Sample Result	mg/kg	200	1000		<200	<200	370	240
Duplicate Result	mg/kg	200	1000		<200	<200	340	200
RpD	**%**				na	na	na	na

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL.*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table NS-26-5. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	North Shore								
				Sample ID	Shore-10081-F-C	Shore-10101-F-D	Shore-10102-F-D	Shore-10103-F-D	Shore-10104-F-D	Shore-10105-F-D	Shore-10106-F-D	Shore-10131-F-C	Shore-10133-F-C
				Duplicate ID	QC# 383542	Shore-10149-F-Q	Shore-10150-F-Q	Shore-10151-F-Q	Shore-10152-F-Q	Shore-10153-F-Q	Shore-10154-F-Q	QC# 383928	Shore-10136-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350		-	30	10	17	22	31	25	-	-
Duplicate Result	mg/kg	70	350		-	139	317	32	609	695	719	-	-
RpD	**%**					na	na	na	na	na	na		
Zinc (Zn)													
Sample Result	mg/kg	150	750		-	136	213	118	103	178	150	-	-
Duplicate Result	mg/kg	150	750		-	537	1455	398	1577	2329	4199	-	-
RpD	**%**					na	na	na	na	na	na		
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	<150
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	<150
RpD	**%**												na
Zinc (Zn)						-							
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-	-	677
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-	-	479
RpD	**%**												34%
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500		<150	-	-	-	-	-	-	<150	-
Duplicate Result	mg/kg	100	500		<150	-	-	-	-	-	-	<150	-
RpD	**%**				na							na	
Zinc (Zn)													
Sample Result	mg/kg	3	15		125	-	-	-	-	-	-	168	-
Duplicate Result	mg/kg	3	15		97	-	-	-	-	-	-	129	-
RpD	**%**				25%							26%	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL..*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table NS-26-5. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee	Location			North Shore								
	Sample ID			Shore-10147-W-D	Shore-10585-F-C	Shore-10779-F-D	Shore-10846-F-C	Shore-10847-F-C	Shore-11220-F-C	Shore-11317-F-D	Shore-11477-F-C	Shore-11821-F-C
	Duplicate ID			Shore-10148-W-Q	QC# 386677	QC# 390728	Shore-10850-F-Q	Shore-10848-F-Q	QC# 389862	QC# 394459	QC# 391813	QC# 394458
Parameter	**Units**	**MDL**	**PQL**	**Analytical Results**								
On Site Field Screening Duplicates												
Lead (Pb)												
Sample Result	mg/kg	70	350	267	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	70	350	272	-	-	-	-	-	-	-	-
RpD	**%**			na								
Zinc (Zn)												
Sample Result	mg/kg	150	750	1508	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	150	750	1519	-	-	-	-	-	-	-	-
RpD	**%**			1%								
Analytical Laboratory Duplicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	-	680	<100	<100	340	<100	-	228
Duplicate Result	mg/kg	100	500	-	-	790	<100	<100	340	<100	-	314
RpD	**%**					15%	n/a	n/a	0%	na		32%
Zinc (Zn)												
Sample Result	mg/kg	3	15	-	-	1190	153	159	1010	241	-	616
Duplicate Result	mg/kg	3	15	-	-	1110	460	186	925	547	-	653
RpD	**%**					7%	**100%**	16%	9%	78%		6%
Analytical Laboratory Replicates												
Lead (Pb)												
Sample Result	mg/kg	100	500	-	340	-	-	580	-	-	121	-
Duplicate Result	mg/kg	100	500	-	310	-	-	510	-	-	91	-
RpD	**%**				na			13%			na	
Zinc (Zn)												
Sample Result	mg/kg	3	15	-	850	-	-	430	-	-	214	-
Duplicate Result	mg/kg	3	15	-	827	-	-	410	-	-	209	-
RpD	**%**				3%			5%			2%	

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL..*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table NS-26-5. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	North Shore									
				Sample ID	Shore-11824-F-C	Shore-11938	Shore-12140-F-D	Shore-12141-F-D	Shore-12142-F-D	Shore-12143-F-D	Shore-12144-F-D	Shore-12145-F-D	Shore-12146-F-D
				Duplicate ID	Shore-11748-F-Q	QC# 395282	Shore-12361-F-Q	Shore-12362-F-Q	Shore-12363-F-Q	Shore-12364-F-Q	Shore-12365-F-Q	Shore-12366-F-Q	Shore-12367-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**								
On Site Field Screening Duplicates													
Lead (Pb)													
Sample Result	mg/kg	70	350	-	-	270	263	171	292	235	269	78
Duplicate Result	mg/kg	70	350	-	-	296	294	214	258	246	233	92
RpD	**%**					na	na	na	na	na	na	na
Zinc (Zn)													
Sample Result	mg/kg	150	750	-	-	456	549	353	750	726	894	165
Duplicate Result	mg/kg	150	750	-	-	897	530	549	908	522	428	83
RpD	**%**					na	na	na	19%	na	na	na
Analytical Laboratory Duplicates													
Lead (Pb)													
Sample Result	mg/kg	100	500	<50	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	243	-	-	-	-	-	-	-	-
RpD	**%**			n/a								
Zinc (Zn)													
Sample Result	mg/kg	3	15	456	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15	557	-	-	-	-	-	-	-	-
RpD	**%**			20%								
Analytical Laboratory Replicates													
Lead (Pb)													
Sample Result	mg/kg	100	500	-	140	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500	-	130	-	-	-	-	-	-	-
RpD	**%**				na							
Zinc (Zn)													
Sample Result	mg/kg	3	15	-	447	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15	-	399	-	-	-	-	-	-	-
RpD	**%**				11%								

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL..*

Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

Table NS-26-5. North Shore Quality Assurance and Quality Control Remediation Soil Samples - Metals

Gartner Lee				Location	North Shore									
				Sample ID	Shore-12147-F-D	Shore-12148-F-D	Shore-12149-F-D	Shore-12150-F-D	Shore-12151-F-D	Shore-12152-F-D	Shore-12153-F-D	Shore-12154-F-D	Shore-12155-F-D	Shore-12156-F-C
				Duplicate ID	Shore-12368-F-Q	Shore-12369-F-Q	Shore-12370-F-Q	Shore-12371-F-Q	Shore-12372-F-Q	Shore-12373-F-Q	Shore-12374-F-Q	Shore-12375-F-Q	Shore-12376-F-Q	Shore-12159-F-Q
Parameter	**Units**	**MDL**	**PQL**		**Analytical Results**									
On Site Field Screening Duplicates														
Lead (Pb)														
Sample Result	mg/kg	70	350		95	110	92	100	128	108	90	88	98	-
Duplicate Result	mg/kg	70	350		109	106	104	119	88	116	130	91	108	-
RpD	**%**				na	na	na	na	na	na	na	na	na	
Zinc (Zn)														
Sample Result	mg/kg	150	750		120	155	138	167	149	55	107	97	185	-
Duplicate Result	mg/kg	150	750		156	117	182	130	136	162	116	47	169	-
RpD	**%**				na	na	na	na	na	na	na	na	na	
Analytical Laboratory Duplicates														
Lead (Pb)														
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-	270
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-	<100
RpD	**%**													na
Zinc (Zn)														
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-	494
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-	84
RpD	**%**													**142%**
Analytical Laboratory Replicates														
Lead (Pb)														
Sample Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	100	500		-	-	-	-	-	-	-	-	-	-
RpD	**%**													
Zinc (Zn)														
Sample Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-	-
Duplicate Result	mg/kg	3	15		-	-	-	-	-	-	-	-	-	-
RpD	**%**													

Bold *RpD Value is greater than or equal to 50% and the concentrations of both samples are greater than the PQL..*


Notes:

na RpD value is not applicable because one or both results are less than the PQL.

*RpD Relative Percent Difference = (Difference/Average)*100.*

*PQL Practical Quantitation Limit = 5 * Method Detection Limit (MDL).*

MDL Method Detection Limit of analysis.

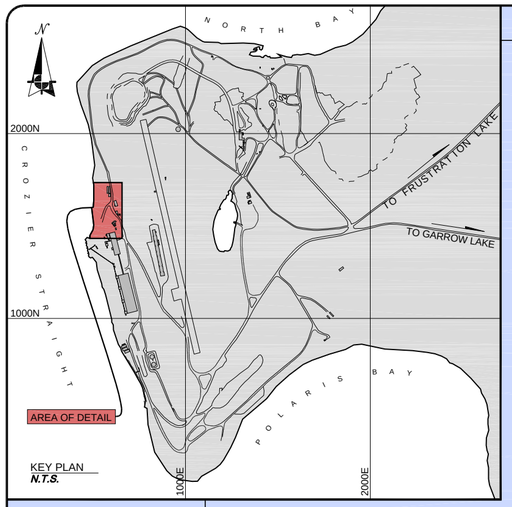

100-MAN TRAILER CAMP
FH10
FH9
TP-204
FH7
FH6
FH5
SS FH-A
SS FH-B
SS FH-C
FH4
FH3
FH8
FIREHALL
TP-84 N
TP-84 S
TP-203
FH2
FH1
FH11
TP-83
TO FIREHALL
SS 3
SS 4
BH-3
TP-202
BH-2
MAIN PORTAL
TP-14
BH-4
TP-8
SS 10
TP-9
TP-7
TP-15
TP-22
BARGE
BH-1
TP-16
TP-6
BH-5
TP-11
TP-10
TP-17

LEGEND:

- LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS BEFORE REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS BEFORE REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- FH5 — TEST PIT (1999/2000 ESA)
- SS20–6 — SURFACE SAMPLE (1999/2000 ESA)

ZINC CONCENTRATION IN SOILS (1999 & 2000 DATA)
- 0–1000 PPM
- 1000–5000 PPM
- 5000–10,000 PPM
- >10,000 PPM

LEAD CONCENTRATION IN SOILS (1999 & 2000 DATA)
- 0–1,000 PPM
- 1,000–2,000 PPM
- > 2,000 PPM

EPH CONCENTRATION IN SOILS (1999 & 2000 DATA)
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL LESS THAN 1,000 mg/kg
- EPH 10–19 OR EPH 19–32 CONCENTRATION IN SOIL GREATER THAN OR EQUAL TO 1,000 mg/kg

*EPH – EXTRACTABLE PETROLEUM HYDROCARBONS

SOURCE OF DRAWING:

DRAWING INFORMATION:


REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–NS–M1–01.DWG
REVISION:	0


POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

NORTH SHORE CONDITIONS BEFORE REMEDIATION

Gartner Lee

FIGURE NO. NS-26-1

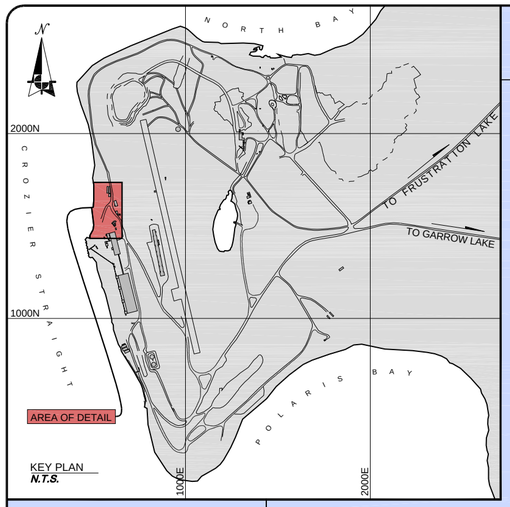

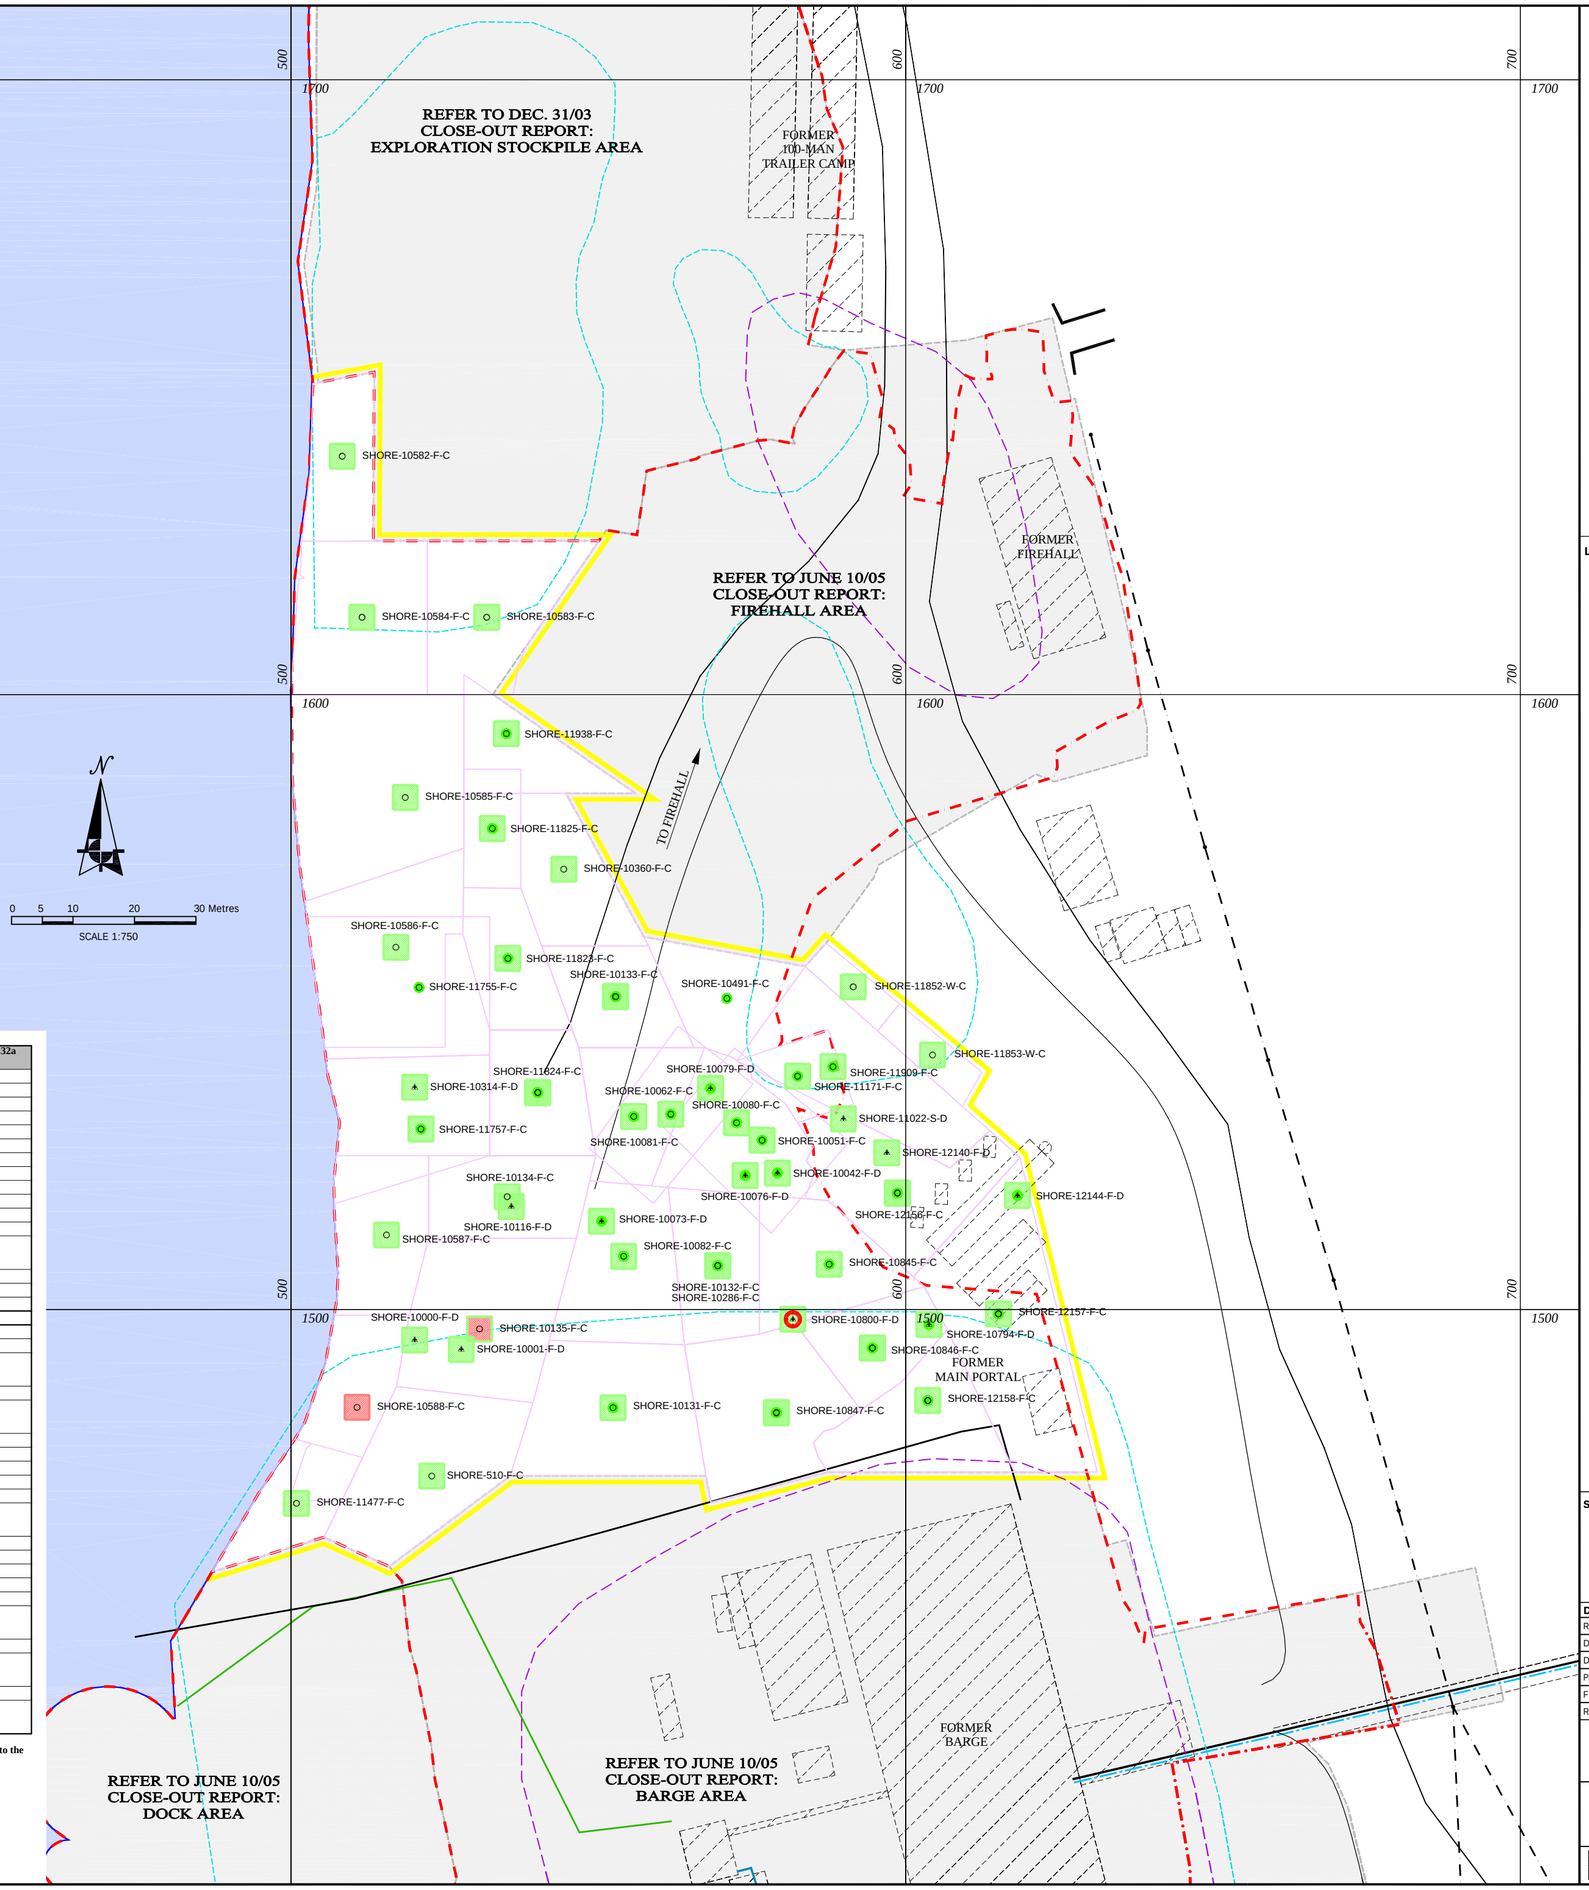

Confirmation Sample ID	Lead mg/kg	Zinc mg/kg
Shore-510-F-C	1090	8850
Shore-10000-F-D	720	2850
Shore-10001-F-D	1250	1730
Shore-10042-F-D	<150	31.1
Shore-10051-F-C	<150	18.6
Shore-10062-F-C	<150	150
Shore-10073-F-D	<150	9.2
Shore-10076-F-D	<150	7.4
Shore-10079-F-D	<150	7.1
Shore-10080-F-C	<150	8.2
Shore-10081-F-C	<150	125
Shore-10082-F-C	<150	15.5
Shore-10116-F-D	160	623
Shore-10131-F-C	<150	168
Shore-10132-F-C	<150	177
Shore-10133-F-C	<150	677
Shore-10136-F-Q duplicate of Shore-10133-F-C	<150	479
Shore-10134-F-C	<150	10.5
Shore-10135-F-C	**2320**	7210
Shore-10286-F-C	<150	23
Shore-10314-F-D	1390	5830
Shore-10360-F-C	150	1230
Shore-10582-F-C	<100	81.7
Shore-10583-F-C	980	5310
Shore-10584-F-C	<100	75.4
Shore-10585-F-C	340	850
Shore-10586-F-C	440	1500
Shore-10587-F-C	<100	563
Shore-10588-F-C	**2140**	**10700**
Shore-10794-F-D	<100	71.5
Shore-10800-F-D	230	1190
Shore-10845-F-C	140	387
Shore-10846-F-C	<100	153
Shore-10850-F-Q duplicate of Shore-10846-F-C	<100	460
Shore-10847-F-C	<100	159
Shore-10848-F-Q duplicate of Shore-10847-F-C	<100	186
Shore-11022-S-D	1160	3870
Shore-11171-F-C	1230	4460
Shore-11477-F-C	121	214
Shore-11757-F-C	320	3010
Shore-11823-F-C	170	425
Shore-11824-F-C	<50	456
Shore-11748-F-Q duplicate of Shore-11824-F-C	243	557
Shore-11825-F-C	<50	106
Shore-11852-W-C	<100	241
Shore-11853-W-C	<100	228
Shore-11909-F-C	<100	82.3
Shore-11938-F-C	140	447
Shore-12140-F-D	410	1330
Shore-12144-F-D	470	1840
Shore-12156-F-C	270	494
Shore-12159-F-Q duplicate of Shore-12156-F-C	<100	83.5
Shore-12157-F-C	<100	64.3
Shore-12158-F-C	170	223

Confirmation Sample ID	EPH C10-C19a mg/kg	EPH C19-C32a mg/kg
Shore-10042-F-D	<200	<200
Shore-10051-F-C	<200	<200
Shore-10062-F-C	<200	<200
Shore-10073-F-D	<200	<200
Shore-10076-F-D	220	<200
Shore-10079-F-D	<200	<200
Shore-10080-F-C	<200	<200
Shore-10081-F-C	<200	<200
Shore-10082-F-C	<200	<200
Shore-10131-F-C	870	<200
Shore-10132-F-C	810	<200
Shore-10133-F-C	<200	<200
Shore-10136-F-Q duplicate of Shore-10133-F-C	<200	<200
Shore-10286-F-C	<200	<200
Shore-10491-F-C	<200	460
Shore-10794-F-D	370	460
Shore-10800-F-D	**1180**	**1010**
Shore-10845-F-C	940	370
Shore-10846-F-C	640	490
Shore-10850-F-Q duplicate of Shore-10846-F-C	840	510
Shore-10847-F-C	580	430
Shore-10848-F-Q duplicate of Shore-10847-F-C	510	410
Shore-11171-F-C	900	990
Shore-11755-F-C	<200	<200
Shore-11757-F-C	220	<200
Shore-11823-F-C	<200	340
Shore-11824-F-C	220	400
Shore-11748-F-Q duplicate of Shore-11824-F-C	<200	350
Shore-11825-F-C	270	450
Shore-11909-F-C	<200	290
Shore-11938-F-C	210	370
Shore-12144-F-D	230	410
Shore-12156-F-C	<200	<200
Shore-12159-F-Q duplicate of Shore-12156-F-C	<200	240
Shore-12157-F-C	<200	<200
Shore-12161-F-Q duplicate of Shore-12157-F-C	290	520
Shore-12158-F-C	<200	240
Shore-12160-F-Q duplicate of Shore-12158-F-C	<200	<200

Bold — Concentration greater than or equal to the Polaris Mine SQROs

Soil Quality Remediation Objectives (SQROs)

EPH C10-C19	1000 mg/kg
EPH C19-C32	1000 mg/kg
Lead	2000 mg/kg
Zinc	10000 mg/kg

LEGEND:

- FORMER LOCATION OF BUILDING
- SHORE LINE
- ROADS
- TAILINGS LINE
- TAILINGS LINE (FORMER)
- FUEL LINE
- GROUND WIRE
- SEWER LINE
- GROUND CONTOURS AFTER REMEDIATION (m) – MAJOR (1.0m)
- GROUND CONTOURS AFTER REMEDIATION (m) – MINOR (0.2m)
- AREA BOUNDARY
- LIMIT OF REMEDIAL EXCAVATION
- AREA OF CONCERN FOR HYDROCARBON CONTAMINATION FROM THE 1999–2000 ESA
- AREA OF CONCERN FOR METALS CONTAMINATION FROM THE 1999–2000 ESA
- OVERHEAD POWER LINE
- POWER POLE
- COMPOSITE CONFIRMATORY FLOOR OR WALL SAMPLE
- DISCRETE CONFIRMATION OR WALL SAMPLE

SAMPLE NAMING CONVENTION

ESP–7–I–D
- ESP = AREA
- 7 = SAMPLE ID
- I = LOCATION
- D = TYPE
  - C= COMPOSITE SAMPLE FLOOR–5 SAMPLES IN A 25x25m AREA WALL–5 SAMPLES ALONG 25m OF WALL
  - D= DISCRETE SAMPLE
  - Q= DUPLICATED QUALITY ASSURANCE/ QUALITY CONTROL SAMPLE
  - F= FLOOR SAMPLE
  - I= INTERMEDIATE FLOOR SAMPLE
  - W= WALL SAMPLE

- SOIL SAMPLE FROM EXCAVATION CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- SOIL SAMPLE FROM EXCAVATION CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32
- *EPH – EXTRACTABLE PETROLEUM HYDROCARBONS
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 10,000 mg/kg ZINC
- SAMPLE CONTAINS GREATER THAN OR EQUAL TO 2,000 mg/kg LEAD
- SAMPLE CONTAINS LESS THAN 10,000 mg/kg ZINC
- SAMPLE CONTAINS LESS THAN 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS GREATER THAN 1,000 mg/kg EPH 10–19 OR EPH 19–32 AND/OR GREATER THAN 10,000 mg/kg ZINC OR 2,000 mg/kg LEAD
- AREA OF WALL COMPOSITE SAMPLE CONTAINS LESS THAN 1,000 mg/kg EPH 10–19 AND EPH 19–32 AND/OR LESS THAN 10,000 mg/kg ZINC AND 2,000 mg/kg LEAD

SOURCE OF DRAWING:

DRAWING INFORMATION:

REVIEWED BY:	AL
DRAWN BY:	CHARONE
DATE ISSUED:	ISSUED – JUNE 10, 2005
PROJECT NUMBER:	40–137
FILE NAME:	40137–NS–M2–01.DWG
REVISION:	0

POLARIS MINE
CONTAMINATED SITE REMEDIATION
LITTLE CORNWALLIS ISLAND, NUNAVUT

NORTH SHORE CONDITIONS AFTER REMEDIATION

Gartner Lee

FIGURE NO. NS-26-2

APPENDIX 7

HAZARDOUS MATERIALS

Gartner Lee Limited

to: Bruce Donald, P.Eng, Reclamation Manager, Teck Cominco Limited
From: Arlene Laudrum, P.Geol., Remediation Supervisor, Polaris Mine Project
Date: November 24, 2004
ref: 40137
re: **Non-PCBs Light Ballasts, Polaris Mine**

This memo is written to confirm that there were no polychlorinated biphenyl (PCB) containing capacitors in the light ballasts in the accommodation complex, auxiliary trailers or buildings that were demolished in 2003 and 2004.

During the Environmental Site Assessment (ESA) conducted by Gartner Lee Limited in 1999 and 2000 the Maintenance Superintendent and the Electrical Superintendent were interviewed and purchase orders for equipment checked with suppliers in order to confirm that there was no PCB containing equipment at the Polaris Mine. The interviews and purchase order reviews indicated that there was no PCB containing equipment on site. In addition, samples were collected and analyzed for PCBs from electrical transformers. The results of the analysis verified that there were no PCB containing electrical transformers on site.

However, no documentation generated during the ESA specifically discusses the absence of PCB containing light ballasts. Therefore, during the final stages of demolition the capacitor nameplates on twenty-seven (27) lamp ballasts from the accommodation complex, auxiliary trailers and outbuilding buildings were documented to confirm that no PCB containing capacitors were present.

The sample set presented in the following table verifies that no ballasts contained PCBs, as based on Environment Canada Environmental Protection Series Report EPS 2/CC/2 (revised) August 1991 entitled *Identification of Lamp Ballasts Containing PCBs*.

Capacitor Manufacture	Date Code	Manufacture Date	Product Label Statement	Interpretation
Advance	08-19-96	August 19, 1996	NO PCB's	Non-PCB is clearly marked on the capacitor. Advance ballasts manufactured from 1979 onwards do not contain PCB capacitors.
Advance	08-19-96	August 19, 1996	NO PCB's	
Alliance Ballasts	1901	January 1991	NO PCB's	Non-PCB is clearly marked on the capacitor.
Alliance Ballasts	1901	January 1991	NO PCB's	

Capacitor Manufacture	Date Code	Manufacture Date	Product Label Statement	Interpretation
CGE	0805	May 1980		CGE Ballasts manufactured from March 1978 onwards do not contain PCB capacitors.
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	0805	May 1980		
CGE	1809	September 1981		
CGE	0804	April 1980		
CGE	4812	December 1984		
CGE	5810	October 1985		
CGE	0805	May 1980		
CGE	0801	January 1980		
MagneTek	C 92	March 1992	NO PCB's	Non-PCB is clearly marked on the capacitor. MagneTek ballasts manufactured after July 1980 do not contain PCB capacitors
MagneTek	C 92	March 1992	NO PCB's	
MagneTek	C 92	March 1992	NO PCB's	
MagneTek	C 92	March 1992	NO PCB's	
MagneTek	C 92	March 1992	NO PCB's	
Phillips	?		NO PCB's	Non-PCB is clearly marked on the capacitor.
Sola Ballasts	E95	May 1995		Any ballast manufactured by Solo in 1980 or later does not contain PCBs.
Sola Ballasts	E95	May 1995		

In summary, the samples of light ballasts collected during demolition confirm that no PCB containing capacitors were present at the Polaris Mine site during mine demolition.

Arlene Laudrum, P.Geol.
Senior Geologist
GARTNER LEE LIMITED

AL:gc

APPENDIX 8

MISCELLANEOUS WATER AND SOIL SAMPLES

COLLECTED FROM SITE

ALS Environmental

CHEMICAL ANALYSIS REPORT

Date:	October 22, 2004
ALS File No.	U7585
Report On:	TC-03-03 Soil Analysis
Report To:	**Azimuth Consulting Group Inc.** 218 - 2902 West Broadway Vancouver, BC V6K 2G8
Attention:	**Mr. Patrick Allard**
Received:	September 1, 2004

ALS ENVIRONMENTAL
per:

Andre Langlais, M.Sc. - Project Chemist
Frederick Chen, B.Sc. - Section Coordinator

ALS CANADA LTD.
1988 Triumph Street, Vancouver, BC Canada V5L 1K5
Phone: 604-253-4188 Fax: 604-253-6700 Website: www.alsenviro.com

A Campbell Brothers Limited Company

File No. U7585

RESULTS OF ANALYSIS - Sediment/Soil

Sample ID				G Lake	G Bay-int
Sample Date				04-08-26	04-08-26
ALS ID				*1*	*2*
Physical Tests					
pH				7.97	
Total Metals					
Antimony	T-Sb			<10	<20
Arsenic	T-As			11.0	<10
Barium	T-Ba			984	711
Beryllium	T-Be			0.59	<1.0
Cadmium	T-Cd			3.01	<1.0
Chromium	T-Cr			18.6	15.1
Cobalt	T-Co			4.7	<4.0
Copper	T-Cu			28.1	15.1
Lead	T-Pb			71	<100
Mercury	T-Hg			0.070	<0.050
Molybdenum	T-Mo			<4.0	<8.0
Nickel	T-Ni			32.2	20
Selenium	T-Se			<2.0	<4.0
Silver	T-Ag			<2.0	<4.0
Tin	T-Sn			<5.0	<10
Vanadium	T-V			59.3	57.2
Zinc	T-Zn			1160	101
Organic Parameters					
Total Organic Carbon		C		4.61	
Particle Size					
Gravel	(>2.00mm)		(%)	<0.10	0.80
Sand	(2.00mm - 0.063mm)		(%)	2.30	48.1
Silt	(0.063mm - 4um)		(%)	71.7	40.1
Clay	(<4um)		(%)	26.0	11.0

Results are expressed as milligrams per dry kilogram except where noted.
< = Less than the detection limit indicated.
Total Organic Carbon results are expressed as percent, dry weight basis.

A Campbell Brothers Limited Company

File No. U7585

Appendix 1 - METHODOLOGY

Outlines of the methodologies utilized for the analysis of the samples submitted are as follows

pH in Soil

This analysis is carried out in accordance with procedures described in "Soil Sampling and Methods of Analysis" (CSSS). The procedure involves mixing the air-dried sample with deionized/distilled water. The pH of the solution is then measured using a standard pH probe. A one to two ratio of sediment to water is used for mineral soils and a one to ten ratio is used for highly organic soils.

Metals in Sediment/Soil

This analysis is carried out using procedures from CSR Analytical Method 8 "Strong Acid Leachable Metals (SALM) in Soil", BC Ministry of Environment, Lands and Parks, 26 June 2001, and procedures adapted from "Test Methods for Evaluating Solid Waste", SW-846 Method 3050B or Method 3051, United States Environmental Protection Agency (EPA). The sample is manually homogenized, dried at 60 degrees Celsius, sieved through a 2 mm (10 mesh) sieve, and a representative subsample of the dry material is weighed. The sample is then digested at 90 degrees Celsius for 2 hours by either hotplate or block digester using a 1:1 ratio of concentrated nitric and hydrochloric acids. Instrumental analysis is by atomic absorption/fluorescence spectrophotometry (EPA Method 7000 series), inductively coupled plasma - optical emission spectrophotometry (EPA Method 6010B), and/or inductively coupled plasma - mass spectrometry (EPA Method 6020).

Method Limitation: This method is not a total digestion technique. It is a very strong acid digestion that is intended to dissolve those metals that may be environmentally available. By design, elements bound in silicate structures are not normally dissolved by this procedure as they are not usually mobile in the environment.

Recommended Holding Time:

Sample:	6 months (Hg = 28 days)
Extract:	6 months (Hg = 28 days, Sb & Sn = 7 days)
Reference:	BCMELP

For more detail see ALS Environmental "Collection & Sampling Guide"

Total Carbon, Total Organic Carbon and Inorganic Carbon in Sediment/Soil

This analysis is carried out in accordance with U.S. EPA Method 9060A (Publ. # SW-846 3rd ed., Washington, DC 20460). Total Carbon is determined by high temperature oxidation of carbon to carbon dioxide which is then measured by means of a nondispersive infrared analyzer. Inorganic Carbon is determined by reaction with phosphoric acid to convert all carbonates to carbon dioxide which is also measured by means of a nondispersive infrared analyzer. Total Organic Carbon is determined as the difference between Total and Inorganic Carbons.

Recommended Holding Time:

A Campbell Brothers Limited Company

Appendix 1 - METHODOLOGY - Continued

Sample: 14 days
Reference: Puget
For more detail see ASL "Collection & Sampling Guide"

Particle Size Distribution in Sediment/Soil

This analysis is carried out using a method adapted for Fisheries and Environment Canada, Ottawa, described in Walton, 1978. The procedure involves oven-drying and sample pre-treatment to remove organics, prior to using standard sieves for the sand and silt fractions and the pipette method for the clay fraction.

Laboratory Location: Pacific Soil Analysis Inc., Richmond (Subcontract)

Results contained within this report relate only to the samples as submitted.

This Chemical Analysis Report shall only be reproduced in full, except with the written approval of ALS Environmental.

End of Report

A Campbell Brothers Limited Company

ALS Environmental

CHEMICAL ANALYSIS REPORT

Date:	September 29, 2004
ALS File No.	U8363
Report On:	Polaris/ TC-03-03 Water Analysis
Report To:	**Azimuth Consulting Group Inc.** 218 - 2902 West Broadway Vancouver, BC V6K 2G8
Attention:	**Mr. Randy Baker**
Received:	September 20, 2004

ALS ENVIRONMENTAL
per:

Leanne Harris, B.Sc. - Project Chemist
Andre Langlais, M.Sc. - Project Chemist

File No. U8363

RESULTS OF ANALYSIS - Water

Sample ID	F-FRUST-TSS-12200
Sample Date	04-09-03
Sample Time	17:00
ALS ID	*1*

Physical Tests

Total Suspended Solids	3.3

Results are expressed as milligrams per litre except where noted.

A Campbell Brothers Limited Company

File No. U8363

Appendix 1 - METHODOLOGY

Outlines of the methodologies utilized for the analysis of the samples submitted are as follows

Solids in Water

This analysis is carried out using procedures adapted from APHA Method 2540 "Solids". Solids are determined gravimetrically. Total dissolved solids (TDS) and total suspended solids (TSS) are determined by filtering a sample through a glass fibre filter, TDS is determined by evaporating the filtrate to dryness at 180 degrees celsius, TSS is determined by drying the filter at 104 degrees celsius. Total solids are determined by evaporating a sample to dryness at 104 degrees celsius. Fixed and volatile solids are determined by igniting a dried sample residue at 550 degrees celsius.

Recommended Holding Time:
Sample: 7 days
Reference: APHA
For more detail see ALS Environmental "Collection & Sampling Guide"

Results contained within this report relate only to the samples as submitted.

This Chemical Analysis Report shall only be reproduced in full, except with the written approval of ALS Environmental.

End of Report

A Campbell Brothers Limited Company

APPENDIX 9

PROJECT COST REPORT

POLARIS MINE DECOMMISSIONING, RECLAMATION AND MONITORING COST ESTIMATE
END OF RECLAMATION PHASE COST UPDATE

	BUDGET		Estimate to Complete		End of Project PROJECT COST	
	By Code	Subtotals	By Code	Subtotals	By Code	Subtotals
DEMOLITION & RECLAMATION (BARE COSTS)						
MINE EQUIPMENT REMOVAL						
Hazardous Materials Removal	35,845				853	
Mine Refrigeration Plant	145,525				25,639	
Mobile & Mine Equipment	2,919				12,981	
Remove Salvaged Mine Equipment	20,754				-	
Misc Sub Contract Costs	45,957				28,540	
		$ 251,000		$ -		$ 68,013
MINE ACCESS SEALING						
Seal Mine Portals	60,000				20,992	
		$ 60,000		$ -		$ 20,992
CONCENTRATOR BUILDING						
Miscellaneous Materials	22,092				-	
Mill Equipment Clean-Up - Fuels	16,398				-	
Mill Equipment Clean-Up	99,900				40,613	
Hazardous Materials Removal	151,117				94,553	
Barge Demolition	608,592				443,526	
Misc Process Equipment Demolition & Removal	197,432				183,317	
Misc Sub Contract Costs	88,469				84,794	
		$ 1,184,000		$ -		$ 846,803
CONCENTRATE STORAGE STRUCTURE & EQUIPMENT						
Concentrate Storage Equipment Clean-Up	26,117				1,905	
Conveyors	67,600				8,421	
Concentrate Storage Structure & Equipment	555,283				93,654	
		$ 649,000		$ -		$ 103,980
SHIP LOADER & CONVEYOR						
Conveyors	50,000				24,592	
		$ 50,000		$ -		$ 24,592
DOCK & SHORELINE						
Dock & Shoreline Reclamation	869,000				837,739	
		$ 869,000		$ -		$ 837,739
THICKENER & TAILINGS LINES						
Hazardous Materials Removal	22,577				16,452	
Tailings Thickener	377,423				106,677	
		$ 400,000		$ -		$ 123,129
GARROW LAKE						
Garrow Lake Siphons & Lake Drawdown	120,391				195,965	
Dam/Spillway Modifications	95,467				269,662	
Escalation Allowance	3,142				-	
		$ 219,000		$ -		$ 465,627
CRF PLANT STRUCTURE & EQUIPMENT						
CRF Plant Equipment Clean-Up	7,002				1,040	
CRF Plant Equipment Removal	17,533				9,406	
CRF Plant Buildings Demolition	130,455				23,497	
Misc Sub Contract Costs	11,010				46,766	
		$ 166,000		$ -		$ 80,709
ACCOMMODATION COMPLEX STRUCTURE & EQUIPMENT						
Accommodation Complex Building Demolition	249,000				72,318	
		$ 249,000		$ -		$ 72,318
FUEL STORAGE & HANDLING EQUIPMENT						
Miscellaneous Materials	3,681				4,904	
Purge & Decommission Fuel Tanks	53,404				341,959	
Hazardous Materials Removal	50,645				547,319	
Fuel Pumping & Distribution Systems	87,270				11,173	
		$ 195,000		$ -		$ 905,355
BUILDINGS & CONTAINERS						
Miscellaneous Materials	1,323				-	
Misc Warehouse / Shipping Equipment	1,221				3,292	
Misc Buildings Demolition	250,456				100,053	
		$ 253,000		$ -		$ 103,345
MISC CONTRACTOR LABOUR						
Unallocated Labour	133,000				2,310	
		$ 133,000		$ -		$ 2,310
GENERAL SITE GRADING						
Hazardous Materials Removal	44,719				90,114	
General Site Grading & Reclamation	7,129		200,000		702,089	
Escalation Allowance	4,152				-	
		$ 56,000		$ 200,000		$ 792,203

POLARIS MINE DECOMMISSIONING, RECLAMATION AND MONITORING COST ESTIMATE
END OF RECLAMATION PHASE COST UPDATE

	BUDGET		Estimate to Complete		End of Project PROJECT COST	
	By Code	Subtotals	By Code	Subtotals	By Code	Subtotals
LANDFILL RECLAMATION						
Landfill Reclamation	432,000				821,746	
		$ 432,000		$ -		$ 821,746
CONTAMINATED SOILS - CLEANUP						
Metals & Hydrocarbon Contaminated Soils Cleanup & Disposal	366,623				2,627,104	
Hydrocarbon Contaminated Soils (By Polaris)	6,097				13,131	
Metals Contaminated Soils (By Polaris)	173,605				52,382	
U/G Handling & Disposal Of Contaminated Soils	48,675				1,012,154	
		$ 595,000		$ -		$ 3,704,771
QUARRIES & MINE SURFACE RECLAMATION (EARTHWORK)						
Backfill & Re-Contouring	263,000				273,711	
		$ 263,000		$ -		$ 273,711
MISC. DEMOLITION & CLEAN-UP						
Misc Unallocated Clean-Up / Demo	380,000				-	
		$ 380,000		$ -		$ -
EQUIPMENT PURCHASE/RENTAL						
Contractor Equipment Rental	5,274,900				5,216,572	
Contractor Misc Equipment Purchase	719,407				432,906	
Escalation Allowance	59,693				-	
		$ 6,054,000		$ -		$ 5,649,478
MISC. SERVICES & SUPPLIES						
Misc Purchased Materials / Supplies	235,333				536,124	
Escalation Allowance	19,667				-	
		$ 255,000		$ -		$ 536,124
FUEL						
Fuel Supply	3,294,536				4,216,186	
Fuel Taxes (Heating & Power Generation)	68,677				-	
Fuel Taxes (Equipment)	467,343				713,101	
Escalation Allowance	157,444				-	
		$ 3,988,000		$ -		$ 4,929,287
MAINTENANCE OF EQUIPMENT & FACILITIES						
Mobile Equip Maintenance	1,296,759				7,682,560	
Building Maintenance	506,923				2,136,535	
Escalation Allowance	101,318				-	
		$ 1,905,000		$ -		$ 9,819,095
PRE - PURCHASED EQUIPMENT (BY COMINCO)						
Construction Equipment - Purchase (By Owner)	541,000				893,766	
		$ 541,000		$ -		$ 893,766
CONTRACTOR'S FIELD SUPPORT & SUPPLIES						
TRANSPORTATION (SHIPPING)						
Packing & Preparation	85,326				-	
Shipping Costs	948,661				3,411,970	
Escalation Allowance	78,013				-	
		$ 1,112,000		$ -		$ 3,411,970
CONTRACTOR MOB, DEMOB & SUPERVISION						
Contractor Mob/Demob	61,883				208,747	
Contractor Supervisory/Admin Personnel	2,127,339				3,758,445	
Safety Services & Supplies	36,000				521,604	
Misc Temporary Services / Modifications	223,824				1,007,843	
Escalation Allowance	13,954				-	
		$ 2,463,000		$ -		$ 5,496,639
MISC. SERVICES & SUPPLIES						
Communications & TV	374,000				256,412	
Escalation Allowance	31,000				-	
		$ 405,000		$ -		$ 256,412
ACCOMODATIONS						
Catering	1,487,166				2,153,968	
Escalation Allowance	122,834				-	
		$ 1,610,000		$ -		$ 2,153,968
TRAVEL & PERSONNEL						
Travel (Airfares & Expenses)	1,552,881				4,683,561	
Travel Premium - Revised Rotation Schedule	1,072,773				-	
Misc Personnel Transport	72,274				391,547	
Escalation Allowance	575,072				-	
		$ 3,273,000		$ -		$ 5,075,108

POLARIS MINE DECOMMISSIONING, RECLAMATION AND MONITORING COST ESTIMATE
END OF RECLAMATION PHASE COST UPDATE

	BUDGET		Estimate to Complete		End of Project PROJECT COST	
	By Code	Subtotals	By Code	Subtotals	By Code	Subtotals
CONTRACTOR INDIRECTS						
HO MOB & DEMOB SUPPORT						
Mob & Demob	1,912,000				1,912,376	
		$ 1,912,000		$ -		$ 1,912,376
CONTRACTOR MANAGEMENT SUPPORT						
Personnel	3,928,932				3,928,932	
Safety & First Aid Personnel to Provide Overlap	184,068				183,644	
		$ 4,113,000		$ -		$ 4,112,576
OTHER CONTRACTOR INDIRECTS						
Contractor's General Indirects	4,952,000				7,470,401	
		$ 4,952,000		$ -		$ 7,470,401
ENGINEERING / PROJECT MANAGEMENT						
ENVIRONMENTAL SITE ASSESMENT						
Environmental Consultants - Site Assesment	275,787				354,711	
Site Assessment - Unallocated	207,874				105,263	
Escalation Allowance	2,339				-	
		$ 486,000		$ -		$ 459,974
CLOSURE PLAN						
Environmental Consultants - Closure Plan	415,772				372,272	
Escalation Allowance	2,228				-	
		$ 418,000		$ -		$ 372,272
ENGINEERING / SPECIAL CONSULTANTS						
Design Consultants - Dock / Loadout	1,316				1,320	
Design Consultants - Tailings / Garrow Lake	3,520				3,515	
Design Consultants - Dock / Loadout	79,684				65,354	
Design Consultants - Tailings / Garrow Lake	54,780				45,328	
Sitework & Demolition Procedures - Design Services	18,300				46,825	
Escalation Allowance	2,400				-	
		$ 160,000		$ -		$ 162,342
PROJECT MANAGEMENT CONSULTANT (HO STAFF)						
Project Management - Salaries	411,069				1,289,847	
Project Management - Reimb Expenses	100,000				85,492	
Escalation Allowance	31,931				-	
		$ 543,000		$ -		$ 1,375,339
CONSTRUCTION MANAGEMENT (FIELD STAFF)						
Construction Management - Salaries	2,142,878				1,915,004	
Escalation Allowance	179,122				-	
		$ 2,322,000		$ -		$ 1,915,004
ENVIRONMENTAL TESTING AND SAMPLING						
Environmental Reclamation Supervision - Staff	337,123				1,038,747	
Escalation Allowance	29,550				-	
Environmental Reclamation Supervision - Testing	330,000				171,498	
Additional Sampling and Consultant Services (MMER)	0				354,386	
Escalation Allowance	26,327				-	
		$ 723,000		$ -		$ 1,564,631
OWNER'S COSTS						
SALARIES & EXPENSES						
Teck Cominco HO Proj Mgmnt (Staff Lab)	374,631				476,911	
Teck Cominco HO Proj Mgmnt (Misc Material & Exp)	199,149				221,031	
Escalation Allowance	34,220				-	
		$ 608,000		$ -		$ 697,942
OVERHEAD / HO SUPPORT						
Land Leases, Licences	175,000				96,979	
Miscellaneous Permits	45,000				16,889	
Insurance	445,900				319,459	
Property Taxes	495,000				180,412	
Home Office General Admin (Labour & Exp)	722,384				16,700	
Public Relations	74,292				58,718	
Legal	57,540				48,421	
Escalation Allowance	168,560				-	
Misc Owner's Overhead	6,324				13,882	
		$ 2,190,000		$ -		$ 751,460
GENERAL ADMIN						
Closure Management - Polaris Personnel	54,000				-	
Escalation Allowance	2,880				-	
Closure Wrap Up	5,120				-	
		$ 62,000		$ -		$ -
POST RECLAMATION COSTS (2005 - 2011)						
SITE MONITORING AND HOLDING COSTS						
Annual Post Closure Environmental Monitoring (2005 to 2011)	510,000		510,000		510,000	
Final Sampling Program, Data Evaluation and Reporting in 2011	160,000		160,000		160,000	
Land Lease/Licence costs from 2005 to 2011	126,000		126,000		126,000	
Property Taxes - 2005 to 2011	70,000		70,000		70,000	
Escalation Allowance	135,000		135,000		135,000	
		$ 1,001,000		$ 1,001,000		$ 1,001,000
UNALLOCATED						
Uncoded Forecast Cost Adjustments (Net)	-		-		-	
		$ -		$ -		$ -
TOTAL DECOMMISSIONING / RECLAMATION & MONITORING COSTS		**$ 47,500,000**		**$ 1,201,000**		**$ 69,264,507**

APPENDIX 10

RECORD of DEBRIS

PLACED INTO

LITTLE RED DOG QUARRY LANDFILL

APPENDIX 9

RECORD OF DEBRIS PLACED

INTO

LITTLE RED DOG QUARRY

PLACEMENT OF DEBRIS INTO LRD QUARRY LANDFILL

2004 - Final Report

DRAWINGS OF DEBRIS PLACEMENT

Relatively little debris was placed into Little Red Dog Quarry Landfill (LRDQL) during 2004. Demolition of the two largest structures on the site had been previously completed in 2003 (the Concentrate Storage Building and Barge). While a number of buildings were demolished, Apart from the Accommodations Complex the other buildings were relatively small. Structures demolished in 2004 included the Accommodations Complex, Fuel Tank Farm, Foldaway Buildings (3), Cat Generator Building, the Dock Cells, and various storage containers and scrap equipment were the main sources of debris for 2004. The attached three drawings indicate the areas where debris was placed in the 1st Quarter, the 2nd Quarter and the 3rd Quarter (the end of the 3rd Quarter really represents the end of the project work which ended September 7th). The locations shown on the drawings represent the final placement locations and not temporary staging areas.

The drawings show the 5th and 6th Lifts (L5 and L6) of debris placed in the quarry. Each area is dated, for example'L6-2005-08' represents Lift 6, for the month of August 2005.

RECORD OF WASTE SOURCE/VOLUME AND TYPE


Following the placement drawings is a listing by day showing the source of the debris, type of debris, where it was hauled to, and the quantity of debris.

VERIFICATION OF HYDROCARBON REMOVAL

For equipment disposed of either in LRD or underground, each individual piece of equipment that contains hydrocarbons (or other hazardous materials), under went removal of these substances before being disposed of. The mechanic doing the work completes the check sheet documenting that the equipment has been properly prepared for disposal. Copies of the equipment preparation sheets are attached.

PHOTOGRAPHIC RECORD

As specified in the Closure Plan, a photographic record of debris placement was maintained. Attached to this appendix are pictures of typical debris being placed in LRDQL. As there was less debris placed into LRDQL during the year, fewer pictures were taken than in the previously. Lack of light prevented pictures from being taken in January but there was essentially no building debris generated during January or February.

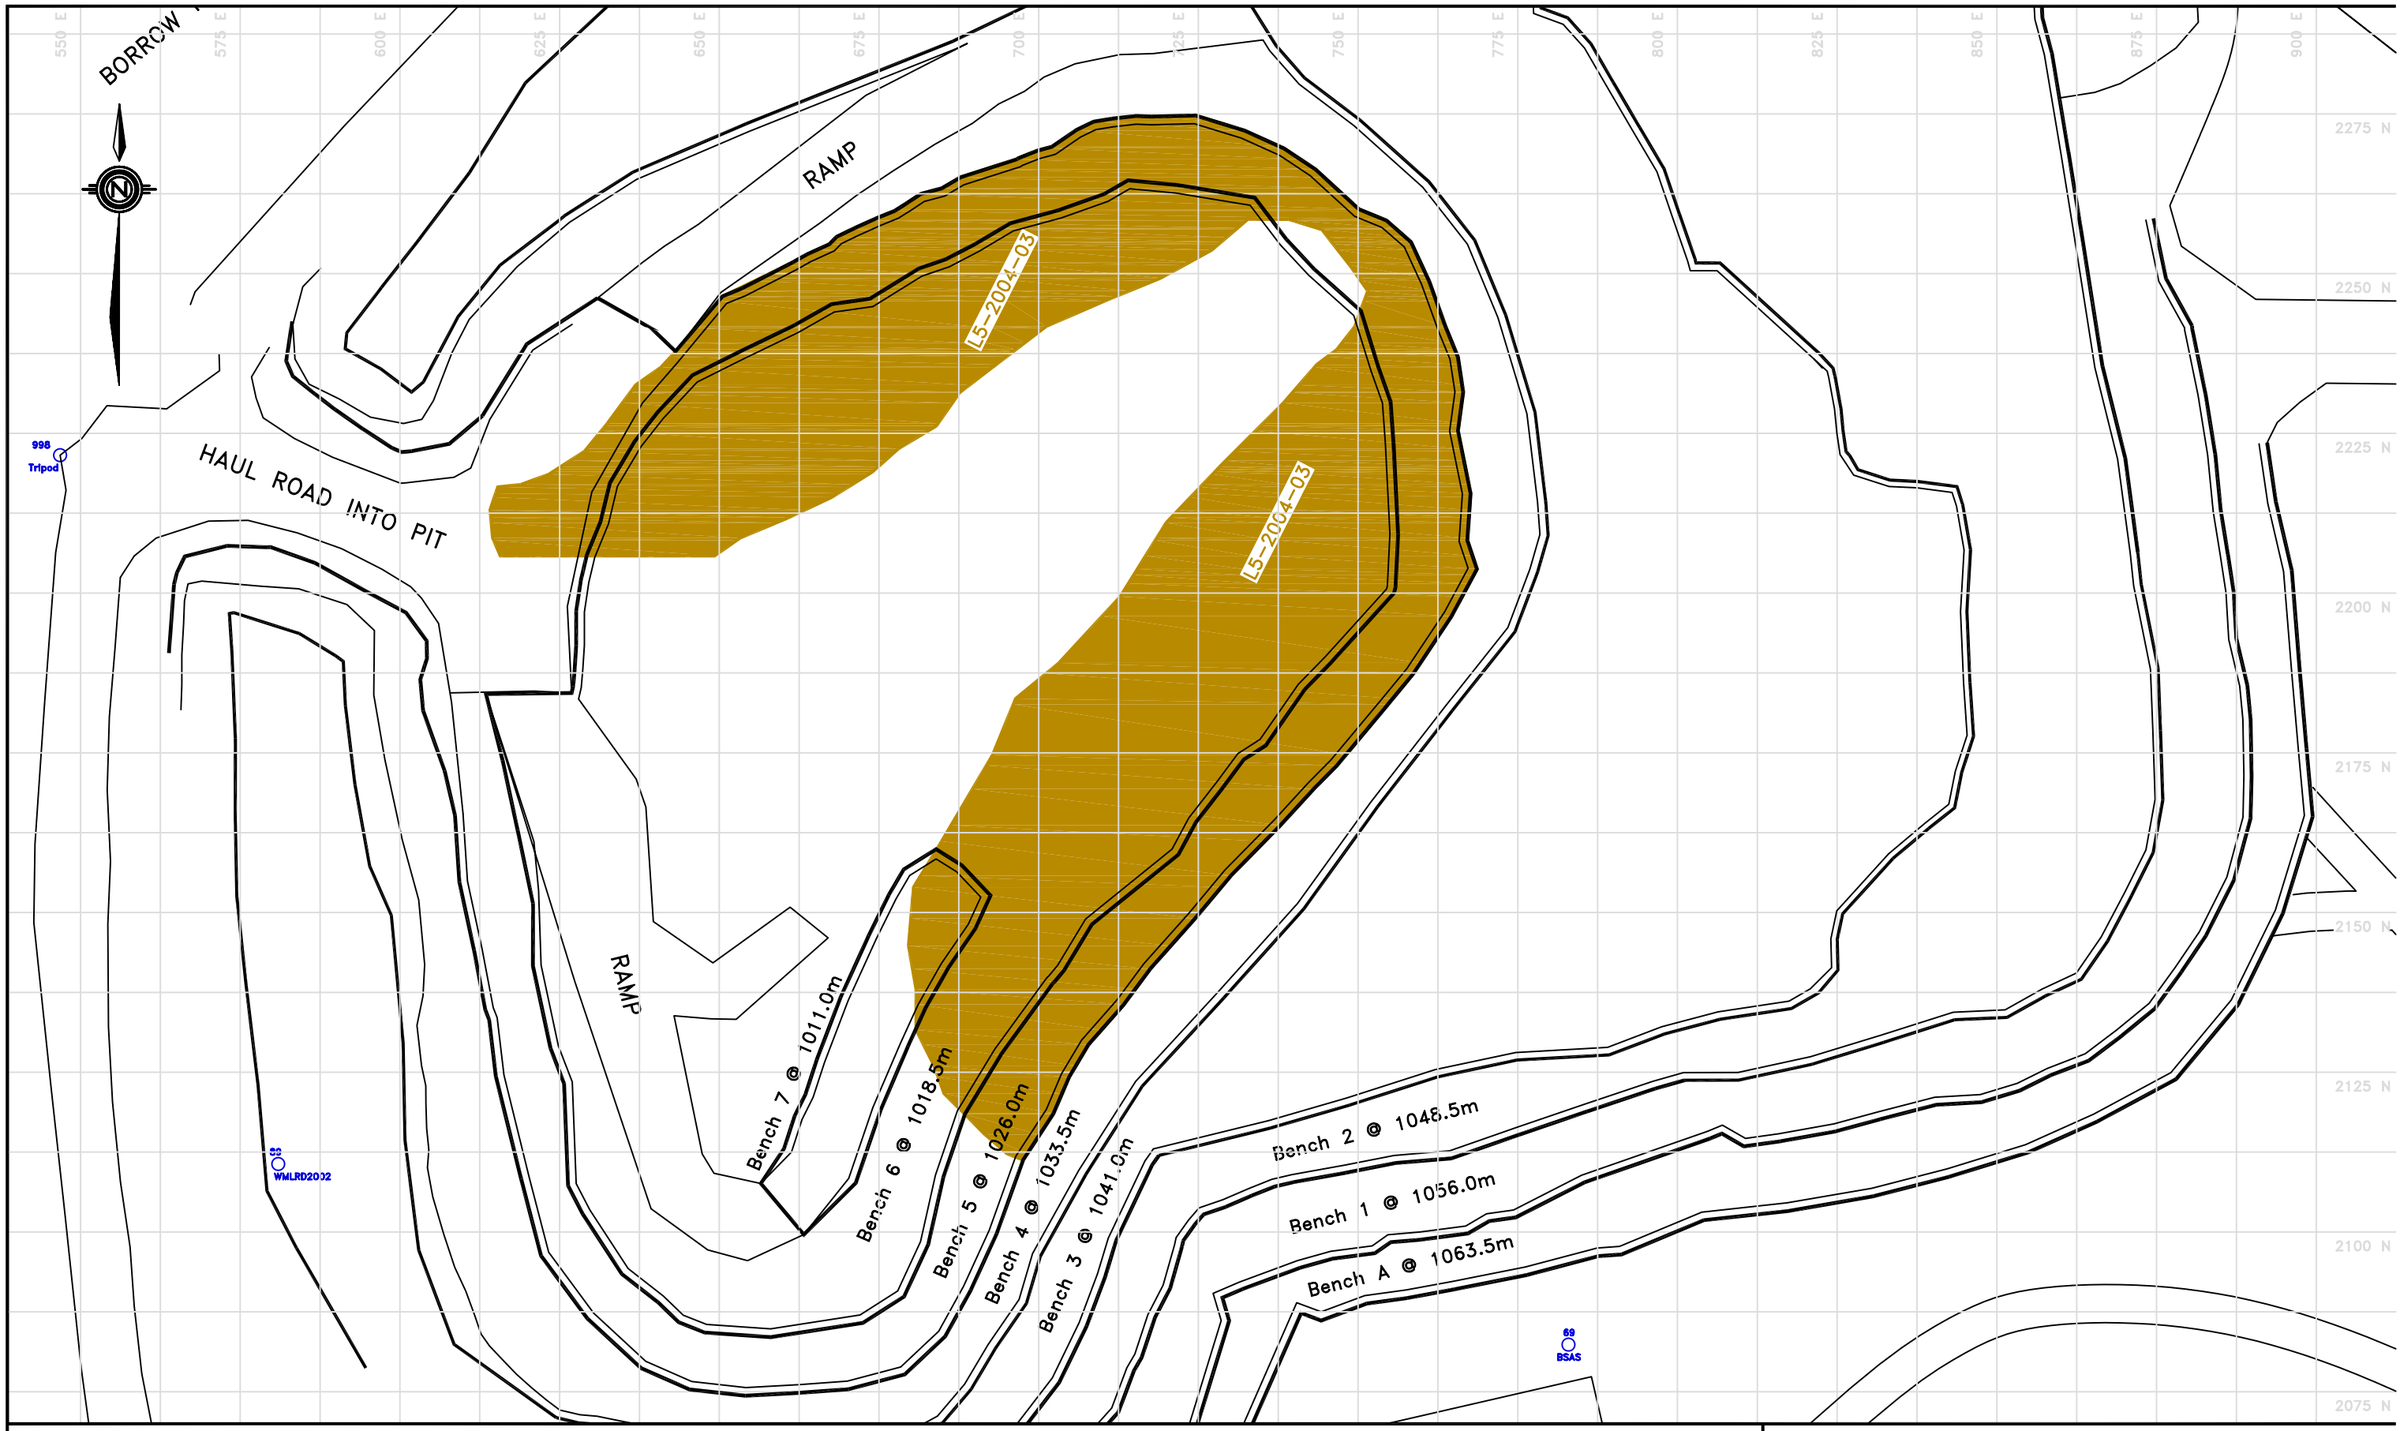

teckcominco

POLARIS PROJECT

LRD Quarry – LIFT 05

Demolition Debris Placement

DRAWN BY:	SCALE:	DATE:	DWG #:
TSF	NTS	MAR-2004	

BORROW

RAMP

HAUL ROAD INTO PIT

998
Tripod

L6-2004-05

L6-2004-04

L6-2004-06

RAMP

Bench 7 @ 1011.0m

Bench 6 @ 1018.5m

Bench 5 @ 1026.0m

Bench 4 @ 1033.5m

Bench 3 @ 1041.0m

Bench 2 @ 1048.5m

Bench 1 @ 1056.0m

Bench A @ 1063.5m

68
WMLRD2002

69
BSAS

550 E 575 E 600 E 625 E 650 E 675 E 700 E 725 E 750 E 775 E 800 E 825 E 850 E 875 E 900 E

2275 N 2250 N 2225 N 2200 N 2175 N 2150 N 2125 N 2100 N 2075 N

teckcominco

POLARIS PROJECT

LRD Quarry – LIFT 06

Demolition Debris Placement

DRAWN BY:	SCALE:	DATE:	DWG #:
TSF	NTS	JUN–2004	

R:\37 – RECLAMATION PLANNING/37.02 Contaminated Soil/LRD Debris Placement

BORROW

RAMP

HAUL ROAD INTO PIT

998
Tripod

L6-2004-05

L6-2004-04

L6-2004-08

L6-2004-07

L6-2004-06

RAMP

Bench 7 @ 1011.0m

Bench 6 @ 1018.5m

Bench 5 @ 1026.0m

Bench 4 @ 1033.5m

Bench 3 @ 1041.0m

Bench 2 @ 1048.5m

Bench 1 @ 1056.0m

Bench A @ 1063.5m

WMLRD2002

BSAS

550 E 575 E 600 E 625 E 650 E 675 E 700 E 725 E 750 E 775 E 800 E 825 E 850 E 875 E 900 E

2275 N 2250 N 2225 N 2200 N 2175 N 2150 N 2125 N 2100 N 2075 N

teckcominco

POLARIS PROJECT

LRD Quarry – LIFT 06

Demolition Debris Placement

DRAWN BY:	SCALE:	DATE:	DWG #:
TSF	NTS	DEC–2004	

R:\37 – RECLAMATION PLANNING/37.02 Contaminated Soil/LRD Debris Placement

POLARIS MINE DEBRIS DISPOSAL IN LITTLE RED DOG QUARRY LANDFILL - 2004

Date	Origin	Disposal	Material	Quantity (m3)
8-Mar-04	Garrow Dam	L-R-D	Frozen Core	185
10-Mar-04	Garrow Dam	L-R-D	Frozen Core	180
14-Mar-04	Foldaway	L-R-D	Steel	6
27-Mar-04	Garrow Dam [stockpile]	L-R-D	Sand/Gravel	72
30-Mar-04	Garrow Dam	L-R-D	Frozen Core	585
6-Apr-04	Garrow Dam [stockpile]	L-R-D	Frozen Core	57
7-Apr-04	Garrow Dam [stockpile]	L-R-D	Frozen Core	312
8-Apr-04	Garrow Dam [stockpile]	L-R-D	Frozen Core	859
9-Apr-04	Garrow Dam [stockpile]	L-R-D	Frozen Core	106
11-Apr-04	Barge	L-R-D	Debris	117
13-Apr-04	Dock	L-R-D	Steel	45
14-Apr-04	Shoreline	L-R-D	Debris	10
20-Apr-04	Accommodation	L-R-D	Debris	20
20-Apr-04	Shoreline	L-R-D	Steel	18
23-Apr-04	Burn Pit	L-R-D	Steel	10
25-Apr-04	Dock	L-R-D	Sheet Pile	78
26-Apr-04	Incinerator	L-R-D	Snow w/ debris	60
27-Apr-04	Foldaway	L-R-D	Debris	10
27-Apr-04	Shoreline	L-R-D	Styrofoam	24
28-Apr-04	Foldaway	L-R-D	Snow w/ debris	270
29-Apr-04	Dock	L-R-D	Sheet Pile	36
29-Apr-04	Foldaway	L-R-D	Snow w/ debris	120
1-May-04	Fire Hall	L-R-D	Debris	10
2-May-04	Ball Field	L-R-D	Debris	10
4-May-04	Fire Hall	L-R-D	Snow w/ debris	40
5-May-04	Fire Hall	L-R-D	Snow w/ debris	110
6-May-04	Dock	L-R-D	Sheet Pile	90
12-May-04	Ball Field	L-R-D	Debris	29
13-May-04	Ball Field	L-R-D	Debris	10
14-May-04	Ball Field	L-R-D	Debris	10
14-May-04	Dock	L-R-D	Styrofoam	10
15-May-04	Dock	L-R-D	Debris	29
22-May-04	Fire Hall	L-R-D	Steel	442
25-May-04	Dock	L-R-D	Sheet Pile	284
29-May-04	L-R-D [notch]	L-R-D	Sand/Gravel	244
1-Jun-04	Ball Field	L-R-D	Debris	59
2-Jun-04	Foldaway	L-R-D	Debris	20
4-Jun-04	Foldaway	L-R-D	Debris	10
6-Jun-04	Foldaway	L-R-D	Debris	20
10-Jun-04	Dock	L-R-D	Sheet Pile	14
11-Jun-04	North Portal	L-R-D	Debris	10
11-Jun-04	Dock	L-R-D	Sheet Pile	18
12-Jun-04	Foldaway	L-R-D	Concrete	29
12-Jun-04	Foldaway	L-R-D	Steel	585
13-Jun-04	Foldaway	L-R-D	Concrete	128
13-Jun-04	Bone Yard	L-R-D	Debris	98
13-Jun-04	Foldaway	L-R-D	Steel	30
14-Jun-04	Bone Yard	L-R-D	Debris	10
15-Jun-04	Foldaway	L-R-D	Concrete	49
15-Jun-04	Foldaway	L-R-D	Steel	790
16-Jun-04	Foldaway	L-R-D	Debris	322
16-Jun-04	Dock	L-R-D	Sheet Pile	42
17-Jun-04	Foldaway	L-R-D	Concrete	199
19-Jun-04	CRF Plant	L-R-D	Debris	18

POLARIS MINE DEBRIS DISPOSAL IN LITTLE RED DOG QUARRY LANDFILL - 2004

Date	Origin	Disposal	Material	Quantity (m3)
21-Jun-04	Conc. Shed	L-R-D	Concrete	26
24-Jun-04	North Portal	L-R-D	Debris	10
24-Jun-04	Barge	L-R-D	Steel	144
25-Jun-04	Barge	L-R-D	Debris	72
25-Jun-04	Barge	L-R-D	Steel	180
26-Jun-04	Barge	L-R-D	Concrete	36
26-Jun-04	Barge	L-R-D	Debris	132
26-Jun-04	Barge	L-R-D	Steel	90
27-Jun-04	Barge	L-R-D	Concrete	388
27-Jun-04	Foldaway	L-R-D	Debris	59
27-Jun-04	Barge	L-R-D	Steel	560
28-Jun-04	Barge	L-R-D	Steel	18
30-Jun-04	Conc. Shed	L-R-D	Steel	98
1-Jul-04	Conc. Shed	L-R-D	Steel	29
2-Jul-04	Conc. Shed	L-R-D	Steel	176
3-Jul-04	Conc. Shed	L-R-D	Steel	38
4-Jul-04	Conc. Shed	L-R-D	Debris	29
4-Jul-04	Conc. Shed	L-R-D	Steel	20
5-Jul-04	Foldaway	L-R-D	Steel	14
6-Jul-04	Conc. Shed	L-R-D	Steel	77
7-Jul-04	Conc. Shed	L-R-D	Steel	98
8-Jul-04	Barge	L-R-D	Debris	10
11-Jul-04	Foldaway	L-R-D	Debris	127
12-Jul-04	Tank Farm	L-R-D	Steel	156
13-Jul-04	Tank Farm	L-R-D	Steel	254
15-Jul-04	Warehouse	L-R-D	Steel	78
16-Jul-04	Ball Field	L-R-D	Debris	20
17-Jul-04	Conc. Shed	L-R-D	Debris	38
18-Jul-04	Airstrip	L-R-D	Debris	10
19-Jul-04	Ball Field	L-R-D	Debris	10
19-Jul-04	Warehouse	L-R-D	Steel	16
20-Jul-04	North Portal	L-R-D	Debris	29
21-Jul-04	Bone Yard	L-R-D	Debris	82
22-Jul-04	Warehouse	L-R-D	Debris	57
23-Jul-04	Ball Field	L-R-D	Debris	29
23-Jul-04	Warehouse	L-R-D	Steel	113
27-Jul-04	Ball Field	L-R-D	Debris	10
29-Jul-04	North Portal	L-R-D	Steel	90
30-Jul-04	Main Portal	L-R-D	Steel	410
30-Jul-04	Conc. Shed	L-R-D	Tailing line	56
31-Jul-04	Garrow Dam	L-R-D	Steel	16
31-Jul-04	Conc. Shed	L-R-D	Tailing line	251
1-Aug-04	Main Portal	L-R-D	Debris	134
1-Aug-04	Bone Yard	L-R-D	Steel	156
3-Aug-04	Ball Field	L-R-D	Cement	294
3-Aug-04	Ball Field	L-R-D	Debris	39
3-Aug-04	Ball Field	L-R-D	Steel	42
5-Aug-04	Accommodation	L-R-D	Debris	8
5-Aug-04	Accommodation	L-R-D	Steel	314
6-Aug-04	Accommodation	L-R-D	Steel	1344
7-Aug-04	Accommodation	L-R-D	Debris	560
7-Aug-04	Accommodation	L-R-D	Steel	1283
8-Aug-04	Accommodation	L-R-D	Debris	530
8-Aug-04	Accommodation	L-R-D	Steel	958

POLARIS MINE DEBRIS DISPOSAL IN LITTLE RED DOG QUARRY LANDFILL - 2004

Date	Origin	Disposal	Material	Quantity (m3)
9-Aug-04	Accommodation	L-R-D	Debris	508
9-Aug-04	Barge	L-R-D	Steel	333
10-Aug-04	Accommodation	L-R-D	Debris	824
10-Aug-04	Accommodation	L-R-D	Steel	488
11-Aug-04	Accommodation	L-R-D	Debris	944
11-Aug-04	Accommodation	L-R-D	Steel	442
12-Aug-04	Accommodation	L-R-D	Debris	664
12-Aug-04	Accommodation	L-R-D	Steel	340
13-Aug-04	Accommodation	L-R-D	Debris	688
13-Aug-04	Incinerator	L-R-D	Steel	640
14-Aug-04	Accommodation	L-R-D	Concrete	120
14-Aug-04	Accommodation	L-R-D	Debris	512
14-Aug-04	Ball Field	L-R-D	Steel	80
15-Aug-04	Accommodation	L-R-D	Concrete	124
15-Aug-04	Accommodation	L-R-D	Debris	200
16-Aug-04	Water Tank	L-R-D	Debris	39
17-Aug-04	Accommodation	L-R-D	Concrete	116
17-Aug-04	Main Portal	L-R-D	Debris	91
17-Aug-04	Frustration Lake	L-R-D	Steel	16
18-Aug-04	Accommodation	L-R-D	Concrete	28
18-Aug-04	Shoreline	L-R-D	Debris	65
19-Aug-04	Ball Field	L-R-D	Debris	20
19-Aug-04	CRF Plant	L-R-D	Steel	78
20-Aug-04	North Portal	L-R-D	Debris	88
20-Aug-04	L-R-D	L-R-D	Rock / Stone	1400
20-Aug-04	Beach	L-R-D	Steel	36
21-Aug-04	CRF Plant	L-R-D	Debris	24
21-Aug-04	L-R-D	L-R-D	Rock / Stone	3634
21-Aug-04	Tank Farm	L-R-D	Steel	178
22-Aug-04	CRF Plant	L-R-D	Debris	26
22-Aug-04	L-R-D	L-R-D	Rock / Stone	5040
22-Aug-04	Tank Farm	L-R-D	Steel	54
23-Aug-04	L-R-D	L-R-D	Rock / Stone	7165
24-Aug-04	L-R-D	L-R-D	Rock / Stone	8514
25-Aug-04	L-R-D	L-R-D	Rock / Stone	4170
26-Aug-04	North Portal	L-R-D	Debris	8
26-Aug-04	L-R-D	L-R-D	Rock / Stone	3764
26-Aug-04	CRF Plant	L-R-D	Steel	128
27-Aug-04	L-R-D	L-R-D	Rock / Stone	1136
27-Aug-04	CRF Plant	L-R-D	Steel	64
28-Aug-04	Tank Farm	L-R-D	Debris	36
28-Aug-04	L-R-D	L-R-D	Rock / Stone	792
29-Aug-04	L-R-D	L-R-D	Rock / Stone	384
30-Aug-04	Water Tank	L-R-D	Steel	138
31-Aug-04	Ball Field	L-R-D	Debris	184
31-Aug-04	Water Tank	L-R-D	Steel	128
1-Sep-04	Ball Field	L-R-D	Debris	160
1-Sep-04	L-R-D [notch]	L-R-D	Sand/Gravel	1078
2-Sep-04	CRF Plant	L-R-D	Debris	92
2-Sep-04	L-R-D	L-R-D	Rock / Stone	2264
3-Sep-04	L-R-D	L-R-D	Rock / Stone	540

CHECK SHEETS

FOR

EQUIPMENT

BEING PREPARED

FOR

BURIAL

STATIONARY EQUIPMENT LUBR[illegible]T EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 29/04	Seasons	POZZUTEC 20	CEMENT AGGREGATOR	1,230 LT	UNDERGROUND	(CB)	[illegible]	

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Pola[redacted]in[illegible]site Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & [illegible]ractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
	TANK FARM	#2 SHORE TANK	DIESEL FUEL.		INCINERATOR		[signature]	[signature]
	Clone By	Smit Tank						
	TANK FARM	OLD GAS TANK Bent Horn Tank	WATER Bent Horn Crude Diesel		INCINERATOR		[signature]	[signature]

//freezy/snc/insert directory and file name here.xls

[redacted]

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
Aug 5,04	ACCOMODATIONS	GLYCOL PIPING	PROPYLENE		INCINERATOR			
		AND HEAT EXCHANGERS	GLYCOL					
Aug 6.04	ACCOMODATIONS	SEWAGE PUMP	OIL	3QTS	INCINERATOR			
Aug 6.04	ACCOMODATIONS	FW PUMP 1	N/A	SEALED	N/A			
		FW PUMP 2	N/A	〃	〃		〃	
		FW PUMP 3	N/A	〃	〃		〃	

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polar [redacted] Inc. Site Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Contractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 29/04		135 426 4/6 Truck			930 Level U/G	CB	PS	
		"	All oils		Incinerator	CB	PS	
		"	Fuel		"	CB	PS	
			~~air cooled~~ engine Coolant		"	CB	PS	
June 28/04		108 Scoop			930 level U/G	CB	PS	
		"	All oil			CB	PS	
		"	Fuel			CB	PS	
		"	~~air cooled~~ engine Coolant			CB	PS	

//freezy/snc/insert directory and file name here.xls

[redacted]

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Contractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
SEPT 17/03		250 TRUCK (LRD)	ALL OILS	30 litres	FUTURE INCINERATION	CB		
			FUEL	25 litres	" "	CB		
			Coolant	15 litres	" "	CB		
MAY 2/03		752 TOYOTA (LRD)	ALL OILS	5 litres	" "	CB		
			FUEL	13 litres	" "	CB		
			Coolant	6 litres	" "	CB		
JUNE 2/05		740 TOYOTA (LRD)	ALL OILS	5 litres	" "	CB		
			FUEL	17 litres	" "	CB		
			Coolant	7 litres	" "	CB		
JUNE 3/04		111 SCOOP (UG)	ALL OILS		" "	CB		
			FUEL		" "	CB		
			~~air cooled~~ ~~Coolant~~ engine		" "	CB		
JUNE 22/04		3 TOYOTA ENGINE BLOCK	ALL OILS	15 litres	" "	CB		
			Fuel lines	N/A	" "	CB		
JUNE 16/04		2 12 cylinder DEUTZ Engines	OILS	20 litres	" "	CB		

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Contractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 27/04		316 ANFO TRUCK			AB SCRAM U/G	CR	PS	
		"	ALL OILS		INCINERATOR	CR	PS	
			FUEL		"	CR	PS	
			COOLANT		"	CR	PS	
JUNE 30/04		ANFO - PLANT			U/G	CR	PS	
		" "	FUEL		INCINERATOR	CR	PS	
			ALL OIL		"	CR	PS	
June 25/04		152 JUMBO			AB SCRAM U/G	CR	PS	
		"	ALL OILS		INCINERATOR	CR	PS	
		"	FUELS		"	CR	PS	
		"	COOLANT		"	CR	PS	
June 30/04		133 426 U/G TRUCK			930 LEVEL U/G	CR	PS	
		"	ALL OILS		INCINERATOR	CR	PS	
		"	FUEL		"	CR	PS	
			COOLANT		"	CR	PS	
							PS	

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Pola[illegible]lin[illegible]site Demolition and Reclamation Project
Daily Activity Log and Disposal Record

Disposal location

SNC-LAVALIN Engineers & [illegible]ractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 4/04		763 TOYOTA (LRD)	ALL OILS	5 litres	FUTURE INCINERATOR	CB	PS	
			FUEL	12 litres	" "	CB	PS	
			Coolant	5 litres	" "	CB	PS	
June 4/04		753 TOYOTA (LRD)	ALL OILS	5 litres	" "	CB	PS	
			FUEL	12 litres	" "	CB	PS	
			Coolant	6 litres	" "	CB	PS	
APR 28/04		196 COMPRESSOR (LRD)	ALL OILS	14 litres	" "	CB	PS	
			Fuel	27 litres	" "	CB	PS	
			Coolant	10 litres	" "	CB	PS	
APR 28/04		964 WELDER (LRD)	FUEL	20 litres	" "	CB	PS	
			OIL	8 litres	" "	CB	PS	
SEPT 16/03		258 TRUCK (LRD)	ALL OILS	30 litres	" "	CB	PS	
			Fuel	40 litres	" "	CB	PS	
			Coolant	15 litres	" "	CB	PS	
June 5/04		700 TOYOTA	ALL OIL	5 litres	" "	CB	PS	
			FUEL	17 litres		CB	PS	
			coolant	6 litres		CB	PS	

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Pula... In-Site Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Contractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
MAY 31/02		206 W-20 CASE Loader (Sink Hole)	ALL OIL	4 Litres	Future Incinerati	CB	PS	
			FUEL	10 Litres	" "	CB	P	
			Coolant	5 litres	" "	CB	PS	
MAY 31/04		662 TOYOTA (LRD)	ALL OIL	4 litres	" "	CB	P	
			Fuel	5 GALS	" "	CB	P	
			Coolant	3 litres	" "	CB	P	
JUNE 4/04		659 TOYOTA (LRD)	ALL oils	4 litres	" "	CB	PS	
			FUEL	12 litres	" "	CB	PS	
			Coolant	3 litres	" "	CB	PS	
JUNE 5/04		655 TOYOTA (LRD)	ALL OILS	4 litres	" "	CB	PS	
			FUEL	7 litres	" "	CB	PS	
			Coolant	3 litres	" "	CB	PS	
JUNE 5/04		741 TOYOTA (LRD)	ALL oils	4 litres	" "	CB	PS	
			FUEL	10 litres	" "	CB	PS	
			Coolant	4 litres		CB	PS	
						—		

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

Disposal Facility

SNC-LAVALIN Engineers & Contractors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 7/04		746 TOYOTA (LRD)	ALL OILS	4 litres	" "	CB		
			FUEL	15 litres	" "	CB		
			Coolant	5 litres	" "	CB		
June 1/04		653 TOYOTA (LRD)	ALL OILS	4 litres	" "	CB		
			FUEL	8 litres	" "	CB		
			CoolanT	4 litres	" "	CB		
June 5/04		737 TOYOTA (LRD)	ALL OILS	5 litres	" "	CB		
			FUEL	15 litres	" "	CB		
			CoolanT	5 litres	" "	CB		
June 5/04		744 TOYOTA (LRD)	ALL OILS	5 litres	" "	CB		
			FUEL	17 litres	" "	CB		
			CoolanT	5 litres	" "	CB		
June 4/04		Dodge RAM TRUCK (LRD)	ALL OILS	8 litres	" "	CB		
			FUELS	23 litres	" "	CB		
			CoolanT	7 litres	" "	CB		

scanned June 22/05 S.V.D.

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	MAIN MINE ENTRANCE	#1 mine cooling unit	Freon 22	300 16's		Tundra		
		Serial # 5,651 · 723						
			10 gal. oil	10 gal.	incenerator	Tundra.		

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	main mine entrance	#2 mine cooling unit	Freon 22	400 lbs		Tundra		
		serial # 5.651.721						
			oil	10 gal.	incinerator.	Tundra.		

//freezy/snc/insert directory and file name here xls

Scanned June 22/05 C.V.Q.

Scanned June 22/05 E.V.D.

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
06/07/04	Main mine entrance	#3 mine Cooling Unit	Freon 22	400 lbs		Tundra		
		Serial # 5.651.724						
			10 gal. oil	10 gal.	incinerator	Tundra		

//freezy/snc/insert directory and file name here.xls

Scanned June 22/05 C.V.D.

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	MAIN mine entrance	#4 mine cooling unit	Freon 22	340 lbs		Tundra.		
		serial # 5.651.722						
			10gal oil	10gal.	incinerator	Tundra.		

//freezy/snc/insert directory and file name here xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Pula ...inesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & ...ructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
June 15/16/04	POWERHOUSE	#5 CAT GENERATOR	ALL OILS	820 LT	INCINERATOR	CB	PS	
	"	"	GLYCOL/WATER 60/40	410 LT	"	CB	PS	
		#6 CAT GENERATOR	ALL OILS	820 LT	"	CB	PS	
		"	GLYCOL/WATER 60/40	410 LT	"	CB	PS	
		Fuel lines on ENGINES	FUEL	205 LT	"	CB	PS	
	"	GLYCOL FROM HEATERS & PIPING	GLYCOL 50/50	205 LT	"	CB	PS	
	BENTHORN BUILDING	Fuel tank, lines	FUEL	205 LT	"	CB	PS	
		OILS & GLYCOL	OILS & GLYCOL	205 LT	"	CB	PS	
	TANK FARM BENTHORN TANK							

Scanned June 22/05 P.V.D.

//freezy/snc/insert directory and file name here.xls

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

29-04-04

UNIT #: 135 DATE OF DRAINING: 29-04-04

UNIT DESCRIPTION: JDT 426 U/G TRUCK

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	X	✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: JUNE 30th 04

DISPOSAL LOCATION: SENT TO NORTH PORTAL FOR U/G DISPOSAL

BENCH LEVEL:

U/G DRIFT LEVEL: 930-Level

SECTION:

Scanned June 22/05 C.R.D.

Claude Baillargeon
PAR Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 133 DATE OF DRAINING: 30-04-04

UNIT DESCRIPTION: TDT 426 U/G Driven

	OK	N/A
Battery	✓	
Cooler liquid		
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: JULY 1ST, 04

DISPOSAL LOCATION: SEND TO NORTH PORTAL FOR U/G DISPOSAL

BENCH LEVEL:

U/G DRIFT LEVEL: 930-Level

SECTION:

Scanned June 22/05 L.V.D.

Claude Baillargeon
per Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 152 DATE OF DRAINING: June 25/04

UNIT DESCRIPTION: ATLAS COPCO JUMBO

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

BATTERY - FIRE EXTINGUISHER + FIRE SUPPRESSION

DATE OF PLACEMENT: JUNE 25/04

DISPOSAL LOCATION: AB/SCRAM

BENCH LEVEL: 885

U/G DRIFT LEVEL: 885

SECTION: LOWER

Scanned June 22/05 L.V.D.

Claude Bourbonnais
FOR Jean Halle
General Foreman

Gan Lapointe
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: Auto-Plant DATE OF DRAINING: June 30/04
UNIT DESCRIPTION: _____

	OK	N/A
Battery		✓
Cooler liquid		
Differentiel housing oil		
Extinguisher	✓	
Fuel tank	✓	
Glycol		
Hydraulic hose oil	✓	
Hydraulic brake oil		
Hydraulic clutch oil		
Hydraulic control oil	✓	
Hydraulic cylinder oil		
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		
Power steering oil		
Transfer case oil		✓
Transmission oil		
Windshield washer		

List the parts removed from unit:
Both hoppers Removed & buried.

DATE OF PLACEMENT: June 30/04
DISPOSAL LOCATION: AB-SCRAM
BENCH LEVEL: 885
U/G DRIFT LEVEL: 885
SECTION: Lower

Scanned June 22/05 L.V.D.

Claude Baillargeon
for Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 316 DATE OF DRAINING: June 27/04

UNIT DESCRIPTION: ANFO TRUCK

	OK	N/A
Battery	✓	
Cooler liquid	✗	✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil		✓
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

Battery - FIRE EXTINGUISHER

DATE OF PLACEMENT: June 27/04
DISPOSAL LOCATION: ANFO PLANT Load-OUT
BENCH LEVEL: 960-RAMP
U/G DRIFT LEVEL: 950
SECTION:

Claude Bellavance
FOR Jean Halle
General Foreman

Jean Cayer
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 741 DATE OF DRAINING: June 5, 04

UNIT DESCRIPTION: Toyota truck

	OK	N/A
Battery	x	
Cooler liquid	x	
Differentiel housing oil	x	
Extinguisher	x	
Fuel tank	x	
Glycol		x
Hydraulic hose oil		x
Hydraulic brake oil		x
Hydraulic clutch oil		x
Hydraulic control oil		x
Hydraulic cylinder oil		x
Hydraulic oil (tank)		x
Motor oil	x	
Planetary gear drive oil		x
Power steering oil	x	
Transfer case oil	x	
Transmission oil	x	
Windshield washer	x	

List the parts removed from unit:

DATE OF PLACEMENT: June 5, 04
DISPOSAL LOCATION: Beach (salvage)
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Frédéric St-Hilaire
Mechanic

THE FOLLOWING IS A SUMMARY OF THE HYDRO CARIBOU UTILITY WAS DRAINED FROM THE VARIOUS SYSTEMS PRIOR TO DEMOLISHING THE CAT & BENTHORN BUILDINGS.

	CAT #5	CAT #6
COOLANT SYSTEM 60/40 GLYCOL/WATER	= 2x205LT	3x205LT
- LUBRICATING OIL FROM ENGINE & LINES	= 4x205LT	2x205LT
- DRAINED ALL FUEL LINES ON ENGINES AND BUILDING	=	1x205LT
- GLYCOL HEATERS AND PIPING (MIXTURE 50/50)	= 1x205LT	

BENTHORN BUILDING 8000 GALLON FUEL TANK, REDUCED LEVEL TO 16" PRIOR TO SHUTTING DOWN CATS #5 & 6. WE THAN PUMPED REMAINING FUEL TO FUEL TRUCK UNTIL TRANSFER PUMP LOST SUCTION. WE THAN RIGGED 8" FUEL TRANSFER LINE FROM SHORE TANKS TO B/H BUILDING. ALL FUEL & SLUDGE REMAINING IN TRANSFER LINE WAS PUSHED BY PIG TO B/H TANK. AFTER RETRIEVING THE PIG THE FUEL TANK CONTENTS WAS PUMPED TO 4x205 LT DRUMS. WHEN THE TRANSFER PUMP LOST SUCTION WE REMOVED THE MANHOLE ON THE SIDE OF TANK AND THE REMAINING SLUDGE (APPROXIMATELY 1½") WAS VACUUMED UP WITH THE VACUUM TRUCK. ALL FUEL LINES IN B/H BUILDING WERE DISASSEMBLED & DRAINED TO 205LT DRUMS APPROXIMATELY 2x205 LT DRUMS.

ALL FUEL, OIL & GLYCOL THAT WAS COLLECTED TO DRUMS WERE TAKEN TO INCINERATOR FOR PROPER DISPOSAL.

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 108 DATE OF DRAINING: 28 06-04

UNIT DESCRIPTION: _____

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

CUTTER

DATE OF PLACEMENT: 9

DISPOSAL LOCATION: SENT TO NORTH PORNAL FOR U/G DISPOSAL

BENCH LEVEL:

U/G DRIFT LEVEL: 930-Level

SECTION:

Claude Bilodeau
P.P. Jean Halle
General Foreman

Sylvain Vallieres
Mechanic

DANIEL Ouellette
draining operator

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record — MINE COOLING BUILDING

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
July 29/04	MINE COOLING	COMPRESSOR #1	OIL	15 gal approx	INCINERATOR			
July 29/04	MINE COOLING	COMPRESSOR #2	OIL	15 gal approx	INCINERATOR			
July 29/04	MINE COOLING	COMPRESSOR #3	OIL	15 gal approx	INCINERATOR			
July 29/04	MINE COOLING	COMPRESSOR #4	OIL	15 gal approx	INCINERATOR			

//freezy/snc/insert directory and file name here.xls

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 131 DATE OF DRAINING: 08-08-04

UNIT DESCRIPTION: MINE truck

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST 15.08.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: BENCH. 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

(Kent Robert)
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 112 DATE OF DRAINING: 09-08-04

UNIT DESCRIPTION: Mine scoop

	OK	N/A	
Battery	✓		
Cooler liquid		✓	
Differentiel housing oil	✓		
Extinguisher		✓	NONE
Fuel tank	✓		
Glycol		✓	
Hydraulic hose oil	✓		
Hydraulic brake oil	✓		
Hydraulic clutch oil	✓		
Hydraulic control oil	✓		
Hydraulic cylinder oil	✓		
Hydraulic oil (tank)	✓		
Motor oil	✓		
Planetary gear drive oil	✓		
Power steering oil		✓	
Transfer case oil	✓		
Transmission oil	✓		
Windshield washer		✓	

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST 15.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: BENCH. 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

(BENT Robert)
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 110 DATE OF DRAINING: 08/08.04.

UNIT DESCRIPTION: Mine Scoop

	OK	N/A
Battery	✓	
Cooler liquid		
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	✓
Transfer case oil		✓
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:
UNIT DRAIN BY KENT ROBERT AND JEAN GUY HALLE.

DATE OF PLACEMENT: AUGUST 15. 04
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: BENCH 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Jean Guy Halle
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 153 DATE OF DRAINING: 08-07-04

UNIT DESCRIPTION: CAMION DIESEL FIRE

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: July 16. 04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench. 05. 04.
U/G DRIFT LEVEL:
SECTION:

Jean Hallé
General Foreman

Louis Sylvaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 315 DATE OF DRAINING: 08-07-04

UNIT DESCRIPTION: CAMION BOME

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: July/16-04

DISPOSAL LOCATION: C.R.D.

BENCH LEVEL: Bench 05.

U/G DRIFT LEVEL:

SECTION:

Jean Hallé
General Foreman

Louis St Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 181 DATE OF DRAINING: 06-07-04

UNIT DESCRIPTION: COMPRESSEUR

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil		/
Hydraulic cylinder oil		/
Hydraulic oil (tank)		/
Motor oil	/	
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil		/
Transmission oil		/
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: 15/07.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 250 DATE OF DRAINING: 6-04-04

UNIT DESCRIPTION: CANION

	OK	N/A
Battery		
Cooler liquid		
Differentiel housing oil	X	
Extinguisher		
Fuel tank		
Glycol		
Hydraulic hose oil		
Hydraulic brake oil		
Hydraulic clutch oil		
Hydraulic control oil		
Hydraulic cylinder oil		
Hydraulic oil (tank)		
Motor oil		
Planetary gear drive oil		
Power steering oil		
Transfer case oil		
Transmission oil	X	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: 15/07. 04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: DRILL ORANGE 163 SOLO drill DATE OF DRAINING: 05-07-04

UNIT DESCRIPTION: _____

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

THE DRAINAGE AS BEEN FINISH. O/G BY. MECHANICS.

DATE OF PLACEMENT: AUGUST.

DISPOSAL LOCATION: MINE

BENCH LEVEL: _____

U/G DRIFT LEVEL: NORTH PORTAL DRIFT.

SECTION: _____

Jean Halle
General Foreman

Louis [illegible]
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 366 DATE OF DRAINING: AUGUST 08. 04.

UNIT DESCRIPTION: HARMER

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST 15. 04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: BENCH. 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 258 DATE OF DRAINING: 06-07-07

UNIT DESCRIPTION: CAMION

	OK	N/A
Battery		/
Cooler liquid		/
Differentiel housing oil	X	
Extinguisher		/
Fuel tank		/
Glycol		/
Hydraulic hose oil		/
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil		/
Hydraulic cylinder oil		/
Hydraulic oil (tank)		/
Motor oil		/
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil		/
Transmission oil		/
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: July 21. 04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench. 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 80 DATE OF DRAINING: 7-07-04

UNIT DESCRIPTION: CAMION ELEVATEUR

	OK	N/A
Battery	x	
Cooler liquid		x
Differentiel housing oil	x	
Extinguisher	x	
Fuel tank	x	
Glycol		x
Hydraulic hose oil	x	
Hydraulic brake oil	x	
Hydraulic clutch oil		x
Hydraulic control oil	x	
Hydraulic cylinder oil	x	
Hydraulic oil (tank)	x	
Motor oil	x	
Planetary gear drive oil	x	
Power steering oil	x	x
Transfer case oil	x	
Transmission oil	x	
Windshield washer		x

List the parts removed from unit:

DATE OF PLACEMENT: July.
DISPOSAL LOCATION: mine
BENCH LEVEL:
U/G DRIFT LEVEL: mine Ramp.
SECTION:

Jean Hallé
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 334 DATE OF DRAINING: 11-07-04

UNIT DESCRIPTION: NASSEL EXPLOSIF

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: July

DISPOSAL LOCATION: MINE

BENCH LEVEL:

U/G DRIFT LEVEL: MAIN DRIFT.

SECTION:

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 335 DATE OF DRAINING: 9-07-04

UNIT DESCRIPTION: NASSEL EXPLOSIF

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil	/	
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST

DISPOSAL LOCATION: MINE

BENCH LEVEL:

U/G DRIFT LEVEL: MAIN DRIFT

SECTION:

Jean Hallé
General Foreman

Louis St HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 255 DATE OF DRAINING: 19-07-04

UNIT DESCRIPTION: CAMION FORD

	OK	N/A
Battery	/	
Cooler liquid	/	
Differentiel housing oil	/	
Extinguisher		/
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil		/
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil		/
Power steering oil	/	
Transfer case oil		/
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: July 19.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 05.
U/G DRIFT LEVEL:
SECTION:

Jean Hallé
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 159 DATE OF DRAINING: 15-07-04

UNIT DESCRIPTION: DRILL

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil		X
Extinguisher	X	
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	
Hydraulic brake oil	X	
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil		X
Power steering oil	X	
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST
DISPOSAL LOCATION: MINE.
BENCH LEVEL: MAIN ROUTAL.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

LUC'S ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 964 DATE OF DRAINING: 15-07-04

UNIT DESCRIPTION: SCOOPTRAM

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil		X
Extinguisher		X
Fuel tank	X	
Glycol		X
Hydraulic hose oil		X
Hydraulic brake oil		X
Hydraulic clutch oil		X
Hydraulic control oil		X
Hydraulic cylinder oil		X
Hydraulic oil (tank)		X
Motor oil	X	
Planetary gear drive oil		X
Power steering oil		X
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

DATE OF PLACEMENT: July 24.04
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 05.
U/G DRIFT LEVEL:
SECTION:

Jean Hallé
General Foreman

Louis St-Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 963 DATE OF DRAINING: 21-07-04

UNIT DESCRIPTION: SOUDEUSE

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: July/24.04.
DISPOSAL LOCATION: L.T.R.P.
BENCH LEVEL: Bench 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Louis St Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: 24.07.04

UNIT DESCRIPTION: SCOOP

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST 15. 04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: BENCH. 05.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 364 DATE OF DRAINING: 30-07-04

UNIT DESCRIPTION: TRAMACK

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil	/	
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST
DISPOSAL LOCATION: MINE
BENCH LEVEL:
U/G DRIFT LEVEL: MAIN DRIFT.
SECTION:

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 230 DATE OF DRAINING: 1-08-04

UNIT DESCRIPTION: CAT V200B FORKLIFT

	OK	N/A
Battery	/	
Cooler liquid	/	
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		N
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil	/	
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: AUGUST

DISPOSAL LOCATION: MINE

BENCH LEVEL:

U/G DRIFT LEVEL: MAIN DRIFT.

SECTION:

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: 3-08-04

UNIT DESCRIPTION: DIAMON DRILL

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil		X
Extinguisher		X
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	X
Hydraulic brake oil		X
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil		X
Power steering oil		X
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: AUGUST 15. 04

DISPOSAL LOCATION: L.12.D

BENCH LEVEL: BENCH 5

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: 2-08-04

UNIT DESCRIPTION: SCOOP

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT:

DISPOSAL LOCATION: MINE

BENCH LEVEL:

U/G DRIFT LEVEL: MAIN DRIFT. (MAIN PORTAL)

SECTION:

Jean Halle
General Foreman

LOUIS SYLVAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: D-53 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Ford truck

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil		✓
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

Cossinco Keep The Truck For Further use.

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 198 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Compressor

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Hallie
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 387 DATE OF DRAINING: 18-08-04

UNIT DESCRIPTION: Height lift

	OK	N/A
Battery	✓	
Cooler liquid	✓	✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: I.R.P.
BENCH LEVEL: 5.
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: August 1/20.04.

UNIT DESCRIPTION: Service tank from the (Tank farm)

	OK	N/A
Battery		✓
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: August 31.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 5
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: 2 UNIT ON JULY = 16/04. 2 UNIT ON AUGUST / 25.04.

UNIT DESCRIPTION: Reefer from the Kitchen (4 unit)

	OK	N/A	
Battery	✓		
Cooler liquid		✓	
Differentiel housing oil		✓	
Extinguisher	✓		
Fuel tank	✓		→ 180 Gallon.
Glycol		✓	
Hydraulic hose oil		✓	
Hydraulic brake oil		✓	
Hydraulic clutch oil		✓	
Hydraulic control oil		✓	
Hydraulic cylinder oil		✓	
Hydraulic oil (tank)		✓	
Motor oil		✓	
Planetary gear drive oil		✓	
Power steering oil		✓	
Transfer case oil		✓	
Transmission oil		✓	
Windshield washer		✓	

List the parts removed from unit:

Some of the unit has been drain (2) at the L.R.D. By Tower Arctic, on August /13.04.
The one we have at Temporary camps has been drain By Yukon Quigley on August /25.04.
All the Reefer as been clean By John Singleton.

DATE OF PLACEMENT: 2 UNIT: AUGUST 14/04 - 2 UNIT ON AUGUST 25.04
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 5.
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: August 13 /04.

UNIT DESCRIPTION: Transformer frustration lake road

	OK	N/A
Battery		✓
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher		✓
Fuel tank		✓
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: August 15. 04.
DISPOSAL LOCATION: Bench 5 L.R.D.
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: South-west.

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 387 DATE OF DRAINING: 18-08-04

UNIT DESCRIPTION: Height Lift

	OK	N/A
Battery	✓	
Cooler liquid	~~✓~~	✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: I.R.D.
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 198 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Compressor

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: Q53 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Ford truck

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil		✓
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

Cossinco Keep The Truck For Further use.

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: 2-08-04

UNIT DESCRIPTION: SCOOP

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS SYLVAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: 3-08-04

UNIT DESCRIPTION: DIAMON DRILL

	OK	N/A
Battery	X	
Cooler liquid		A
Differentiel housing oil		X
Extinguisher		X
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	X
Hydraulic brake oil		X
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil		X
Power steering oil		X
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

_____
Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 230 DATE OF DRAINING: 1-08-04

UNIT DESCRIPTION: CAT V200B FORKLIFT

	OK	N/A
Battery	/	
Cooler liquid	/	
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		N
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil	/	
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 364 DATE OF DRAINING: 30-07-04

UNIT DESCRIPTION: TRAMACK

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: August 1/20.04.

UNIT DESCRIPTION: Service tank from the (Tank farm)

	OK	N/A
Battery		✓
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: August 31.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 5
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: 2 UNIT ON JULY = 16/04. 2 UNIT ON AUGUST / 25.04.

UNIT DESCRIPTION: Reefer from the Kitchen (4 unit)

	OK	N/A	
Battery	✓		
Cooler liquid		✓	
Differentiel housing oil		✓	
Extinguisher	✓		
Fuel tank	✓		→ 180 Gallon.
Glycol		✓	
Hydraulic hose oil		✓	
Hydraulic brake oil		✓	
Hydraulic clutch oil		✓	
Hydraulic control oil		✓	
Hydraulic cylinder oil		✓	
Hydraulic oil (tank)		✓	
Motor oil		✓	
Planetary gear drive oil		✓	
Power steering oil		✓	
Transfer case oil		✓	
Transmission oil		✓	
Windshield washer		✓	

List the parts removed from unit:

Some of the unit has been drain (2) at the L.R.D. By Tower Arctic, on August /13.04.
The one we have at Temporary camps has been drain By Yukon Quigley on August /25.04.
All the Reefer as been clean By John Singleton.

DATE OF PLACEMENT: 2 UNIT: AUGUST 14/04 - 2 UNIT ON AUGUST 25.04
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: Bench 5.
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: August 13 /04.

UNIT DESCRIPTION: Transformer frustration lake road

	OK	N/A
Battery		✓
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher		✓
Fuel tank		✓
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: August 15. 04.
DISPOSAL LOCATION: Bench 5 L.R.D.
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: South-west.

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 387 DATE OF DRAINING: 18-08-04

UNIT DESCRIPTION: Height Lift

	OK	N/A
Battery	✓	
Cooler liquid	~~✓~~	✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: I.R.D.
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 198 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Compressor

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: 28/08/04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL:
U/G DRIFT LEVEL:
SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: Q53 DATE OF DRAINING: 20-08-04

UNIT DESCRIPTION: Ford truck

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil		✓
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

Cossinco Keep The Truck For Further use.

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: 2-08-04

UNIT DESCRIPTION: SCOOP

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS SYLVAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: 3-08-04

UNIT DESCRIPTION: DIAMON DRILL

	OK	N/A
Battery	X	
Cooler liquid		A
Differentiel housing oil		X
Extinguisher		X
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	X
Hydraulic brake oil		X
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil		X
Power steering oil		X
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

_____
Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 230 DATE OF DRAINING: 1-08-04

UNIT DESCRIPTION: CAT V200B FORKLIFT

	OK	N/A
Battery	/	
Cooler liquid	/	
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		N
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil	/	
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 364 DATE OF DRAINING: 30-07-04

UNIT DESCRIPTION: TRAMACK

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: 24.07.04

UNIT DESCRIPTION: SCOOP

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 963 DATE OF DRAINING: 21-04-04

UNIT DESCRIPTION: SOUDEUSE

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 464 DATE OF DRAINING: 15-07-04

UNIT DESCRIPTION: SOUDEUSE

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil		X
Extinguisher		X
Fuel tank	X	
Glycol		X
Hydraulic hose oil		X
Hydraulic brake oil		X
Hydraulic clutch oil		X
Hydraulic control oil		X
Hydraulic cylinder oil		X
Hydraulic oil (tank)		X
Motor oil	X	
Planetary gear drive oil		X
Power steering oil		X
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Louis St-Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 159 DATE OF DRAINING: 15-07-04

UNIT DESCRIPTION: DRILL

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil		X
Extinguisher	X	
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	
Hydraulic brake oil	X	
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil		X
Power steering oil	X	
Transfer case oil		X
Transmission oil		X
Windshield washer		X

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Luis St HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 255 DATE OF DRAINING: 19-07-04

UNIT DESCRIPTION: CAMION FORD

	OK	N/A
Battery	/	
Cooler liquid	/	
Differentiel housing oil	/	
Extinguisher		/
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil		/
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil		/
Power steering oil	/	
Transfer case oil		/
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Hallé
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 335 DATE OF DRAINING: 9-07-04

UNIT DESCRIPTION: NASSEL EXPLOSIF

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil	/	
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Louis St-Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 334 DATE OF DRAINING: 11-07-04

UNIT DESCRIPTION: NASSEL EXPLOSIF

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Louis St Hilaire
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 30 DATE OF DRAINING: 7-07-04

UNIT DESCRIPTION: CAMION ÉLÉVATEUR

	OK	N/A
Battery	X	
Cooler liquid		X
Differentiel housing oil	X	
Extinguisher	X	
Fuel tank	X	
Glycol		X
Hydraulic hose oil	X	
Hydraulic brake oil	X	
Hydraulic clutch oil		X
Hydraulic control oil	X	
Hydraulic cylinder oil	X	
Hydraulic oil (tank)	X	
Motor oil	X	
Planetary gear drive oil	X	
Power steering oil	X	X
Transfer case oil	X	
Transmission oil	X	
Windshield washer		X

List the parts removed from unit:

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Hallé
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 258 DATE OF DRAINING: 06-07-04

UNIT DESCRIPTION: CAMION

	OK	N/A
Battery		/
Cooler liquid		/
Differentiel housing oil	X	
Extinguisher		/
Fuel tank		/
Glycol		/
Hydraulic hose oil		/
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil		/
Hydraulic cylinder oil		/
Hydraulic oil (tank)		/
Motor oil		/
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil		/
Transmission oil		/
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 366 DATE OF DRAINING: _____

UNIT DESCRIPTION: HARMER

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

_____ _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: DRILL ORANGE DATE OF DRAINING: 05-07-04

UNIT DESCRIPTION: _____

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Louis [illegible]
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 236 DATE OF DRAINING: 6-04-04

UNIT DESCRIPTION: CANOR Truck.

	OK	N/A
Battery		/
Cooler liquid		/
Differentiel housing oil	X	/
Extinguisher		/
Fuel tank		/
Glycol		/
Hydraulic hose oil		/
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil		/
Hydraulic cylinder oil		/
Hydraulic oil (tank)		/
Motor oil		/
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil		/
Transmission oil	X	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 181 DATE OF DRAINING: 06-07-04

UNIT DESCRIPTION: COMPRESSEUR

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol		/
Hydraulic hose oil	/	
Hydraulic brake oil		/
Hydraulic clutch oil		/
Hydraulic control oil		/
Hydraulic cylinder oil		/
Hydraulic oil (tank)		/
Motor oil	/	
Planetary gear drive oil		/
Power steering oil		/
Transfer case oil		/
Transmission oil		/
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 315 DATE OF DRAINING: 08-07-04

UNIT DESCRIPTION: CAMION BOME
Boom Truck

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

LOUIS ST HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 153 DATE OF DRAINING: 08-07-04

UNIT DESCRIPTION: CAMION NASSEL FIXE
Fixed Axle Truck.

	OK	N/A
Battery	/	
Cooler liquid		/
Differentiel housing oil	/	
Extinguisher	/	
Fuel tank	/	
Glycol	/	
Hydraulic hose oil	/	
Hydraulic brake oil	/	
Hydraulic clutch oil		/
Hydraulic control oil	/	
Hydraulic cylinder oil	/	
Hydraulic oil (tank)	/	
Motor oil	/	
Planetary gear drive oil	/	
Power steering oil		/
Transfer case oil	/	
Transmission oil	/	
Windshield washer		/

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Louis Sylvestre
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 110 DATE OF DRAINING: _____

UNIT DESCRIPTION: Mine Scoop

	OK	N/A
Battery	✓	
Cooler liquid		
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil		✓
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor ~~oil~~	✓	
Planetary gear drive oil	✓	
Power steering oil	✓	✓
Transfer case oil		✓
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: _____

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Halle
General Foreman

Jean Aug-Coulombe
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 112 DATE OF DRAINING: 09-08-04

UNIT DESCRIPTION: Mine scoop

	OK	N/A	
Battery	✓		
Cooler liquid		✓	
Differentiel housing oil	✓		
Extinguisher		✓	NONE
Fuel tank	✓		
Glycol		✓	
Hydraulic hose oil	✓		
Hydraulic brake oil	✓		
Hydraulic clutch oil	✓		
Hydraulic control oil	✓		
Hydraulic cylinder oil	✓		
Hydraulic oil (tank)	✓		
Motor oil	✓		
Planetary gear drive oil	✓		
Power steering oil		✓	
Transfer case oil	✓		
Transmission oil	✓		
Windshield washer		✓	

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 131 DATE OF DRAINING: 08-08-04

UNIT DESCRIPTION: MINE truck

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	✓	
Hydraulic cylinder oil	✓	
Hydraulic oil (tank)	✓	
Motor oil	✓	
Planetary gear drive oil	✓	
Power steering oil		✓
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: _____
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: August 20.04.

UNIT DESCRIPTION: Service tank from the (Tank farm)

	OK	N/A
Battery		✓
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: August 21.04.
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Halle
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: août 7/13/14/04

UNIT DESCRIPTION: Transformer frustration lake road

	OK	N/A
Battery		✓
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher		✓
Fuel tank		✓
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil		✓
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

_____

_____

_____

_____

DATE OF PLACEMENT: SEE DISPOSAL LOGS.

DISPOSAL LOCATION: _____

BENCH LEVEL: _____

U/G DRIFT LEVEL: _____

SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: _____ DATE OF DRAINING: _____

UNIT DESCRIPTION: Reefer from the Kitchen (4 unit)

	OK	N/A	
Battery	✓		
Cooler liquid		✓	
Differentiel housing oil		✓	
Extinguisher	✓		
Fuel tank	✓		→ 150 Gallon.
Glycol		✓	
Hydraulic hose oil		✓	
Hydraulic brake oil		✓	
Hydraulic clutch oil		✓	
Hydraulic control oil		✓	
Hydraulic cylinder oil		✓	
Hydraulic oil (tank)		✓	
Motor oil		✓	
Planetary gear drive oil		✓	
Power steering oil		✓	
Transfer case oil		✓	
Transmission oil		✓	
Windshield washer		✓	

List the parts removed from unit:

Some of the unit has been drain (2) at the L.Rid. By Tower Cretes, on August 13.04.
The one we have at Temporary camps has been drain By Yvan Duguay on August 25.04.
All the Reefer as been clean By John Singleton.

DATE OF PLACEMENT: See DISPOSAL Logs.
DISPOSAL LOCATION: _____
BENCH LEVEL: _____
U/G DRIFT LEVEL: _____
SECTION: _____

Jean Hallé
General Foreman

Jean Lavergne
Mechanic

Refrigerant Data Sheet

Date: 25/08/04

Type of Refrigerant: R-22

Amount of Refrigerant: 397 lbs

Location Recovered: mine cooling.

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

Refrigerant Data Sheet

Date: 25/08/04

Type of Refrigerant: R-22

Amount of Refrigerant: 643 16's

Location Recovered: Mine cooling.

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

Refrigerant Data Sheet

Date: Aug 31/04

Type of Refrigerant: R-22

Amount of Refrigerant: 241 kg

Location Recovered: Mine Cooling

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

Refrigerant Data Sheet

Date: 25/08/04

Type of Refrigerant: R-22

Amount of Refrigerant: 179 Kg

Location Recovered: mine cooling units & Accommodations units.

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

Refrigerant Data Sheet

Date: 25/08/04

Type of Refrigerant: R-22

Amount of Refrigerant: 313 16's

Location Recovered: mine Cooling.

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

Refrigerant Data Sheet

Date: 25/08/04

Type of Refrigerant: R-22

Amount of Refrigerant: 179 Kg

Location Recovered: mine cooling.

Technician: John F. Singleton, Tundra Site Services

Certificate Number: NF-2920

Contractor: SNC Lavalin Engineers and Constructors /Tundra Site Services

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	Main mine entrance	#2 mine cooling unit	Freon 22	400 lbs		Tundra		
		Serial # 5.651.721						
			Oil	10 gal.	incentorator.	Tundra.		

I/freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	Main mine entrance	#3 mine Cooling Unit	Freon 22	400 lbs		Tundra		
		Serial # 5.651.724						
			10gal. oil	10gal.	incenterator	Tundra		

//freezy/snc/insert directory and file name here.xls

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	MAIN MINE ENTRANCE	#1 MINE COOLING UNIT	FREON 22	300 16's		TUNDRA		
		SERIAL # 5.651 · 723						
			10 GAL. OIL	10 GAL.	INCENTORATOR	TUNDRA.		

STATIONARY EQUIPMENT LUBRICANT EVACUATION CHECKLIST

Cominco Polaris Minesite Demolition and Reclamation Project
Daily Activity Log and Disposal Record

SNC-LAVALIN Engineers & Constructors

Date	Origin Location	Equipment Description	Lubricant/Fluid Type	Quantity If Appl.	Disposal Location	Sub-Contractor	SLEC	Owner/Rep
16/07/04	MAIN mine entrance	#4 mine cooling unit	Freon 22	340 lbs		Tundra.		
		serial # 5.651.722						
			10gal. oil	10gal.	incenterator	Tundra.		

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 659
UNIT DESCRIPTION: TOYOTA

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil		✓
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:
ENGINE, TRANSMISSION, FUEL TANK, BRAKE + CLUTCH MASTER CYL.
DISPOSED OF IN L.R.D.

Claude Bellavance
For: Jean Halle
General Foreman

P. Markham.
Mechanic

PNB

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 258 DATE OF DRAINING: 16-09-03

UNIT DESCRIPTION: TRUCK

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher		✓
Fuel tank	✓	
Glycol	✓	✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		
Hydraulic cylinder oil		
Hydraulic oil (tank)	✓	
Motor oil	✓	✓
Planetary gear drive oil		✓
Power steering oil		
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

UNIT STRIPPED OF ALL MOTOR, DRIVE RELATED PARTS AND DISPOSED OF

List the parts removed from unit:

UNITS STILL BEING SCAVENGED FOR PARTS — OCT 1.03

DATE OF PLACEMENT: MARCH 15, 04

DISPOSAL LOCATION: L.R.P.

BENCH LEVEL: BENCH 5

U/G DRIFT LEVEL:

SECTION:

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 250 DATE OF DRAINING: 16-17/09/03

UNIT DESCRIPTION: TRUCK

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil		
Extinguisher		
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		
Hydraulic brake oil		
Hydraulic clutch oil		
Hydraulic control oil		
Hydraulic cylinder oil		
Hydraulic oil (tank)	✓	
Motor oil		✓
Planetary gear drive oil		
Power steering oil		
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		

List the parts removed from unit:
UNIT STILL BEING SCAVENGED FOR PARTS — OCT 1, 03

DATE OF PLACEMENT: MARCH 15, 04
DISPOSAL LOCATION: L.R.D. * RELOCATED @ BALL FIELD
BENCH LEVEL: BENCH 5
U/G DRIFT LEVEL:
SECTION:

JUNE 03, 04

Jean Halle
General Foreman

Mechanic

Scanned June 23/04

FNL

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 258 DATE OF DRAINING: 16-09-03

UNIT DESCRIPTION: TRUCK

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil	✓	
Extinguisher		✓
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		
Hydraulic cylinder oil		
Hydraulic oil (tank)	✓	
Motor oil	✓	✓
Planetary gear drive oil		✓
Power steering oil		
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer		✓

List the parts removed from unit:
UNITS STILL BEING SCAVENGED FOR PARTS — OCT 1.03 KH.

DATE OF PLACEMENT: MARCH 15, 04
DISPOSAL LOCATION: L.R.P. = * RELOCATED @ BALL FIELD
BENCH LEVEL: BENCH 5
U/G DRIFT LEVEL:
SECTION:
JUNE 03, 04

Jean Halle
General Foreman

Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 196 DATE OF DRAINING: APRIL 28, 04

UNIT DESCRIPTION: COMPRESSOR

	OK	N/A
Battery		✓
Cooler liquid	✓	
Differentiel housing oil		✓
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:
COMPRESSOR OIL (OK)

DATE OF PLACEMENT: APRIL 28, 04
DISPOSAL LOCATION: L.R.D.
BENCH LEVEL: 6
U/G DRIFT LEVEL:
SECTION:

Jean Halle / CLAUDE BAILLARGEON
General Foreman

FRÉDÉRIC ST-HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 964 DATE OF DRAINING: APRIL 28, 04

UNIT DESCRIPTION: WELDER MACHINE

	OK	N/A
Battery	✓	
Cooler liquid		✓
Differentiel housing oil		✓
Extinguisher		✓
Fuel tank	✓	
Glycol		✓
Hydraulic hose oil		✓
Hydraulic brake oil		✓
Hydraulic clutch oil		✓
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil		✓
Transfer case oil		✓
Transmission oil		✓
Windshield washer		✓

List the parts removed from unit:

DATE OF PLACEMENT: APRIL 29, 04
DISPOSAL LOCATION: L.R.O.
BENCH LEVEL: 6
U/G DRIFT LEVEL:
SECTION:

Scanned June 23/04

André Baillargeon
Jean Halle
General Foreman

FRÉDÉRIC ST-HILAIRE
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: TOYOTA BRUN 653 DATE OF DRAINING: 01/05/2004
UNIT DESCRIPTION: TOYOTA MUCK

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil AV OK AR OK	✓	
Extinguisher	—	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil	—	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	—	
Hydraulic cylinder oil	—	
Hydraulic oil (tank)	—	
Motor oil	✓	
Planetary gear drive oil	—	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

DATE OF PLACEMENT: MAY 03, 2004
DISPOSAL LOCATION: LRd
BENCH LEVEL: 6
U/G DRIFT LEVEL:
SECTION:

Scanned June 23/04

Jean Halle
General Foreman

JERRY
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 740 DATE OF DRAINING: 2/05/2004

UNIT DESCRIPTION: TOYOTA DYNA

	OK	N/A
Battery		
Cooler liquid	✓	
Differentiel housing oil DV	✓	
Extinguisher		✓
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil	✓	
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil	—	
Hydraulic cylinder oil	—	
Hydraulic oil (tank)	—	
Motor oil	✓	
Planetary gear drive oil	—	
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

DATE OF PLACEMENT: MAY 3rd, 2004
DISPOSAL LOCATION: LRD
BENCH LEVEL: 6
U/G DRIFT LEVEL:
SECTION:

Claude Baillargeon
Jean Halle
General Foreman

JERRY
Mechanic

Scanned June 23/04

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 059

UNIT DESCRIPTION: TOYOTA

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil		✓
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

ENGINE, TRANSMISSION, FUEL TANK, BRAKE + CLUTCH MASTER CYL.

Claude Bellavance
Jean Halle
General Foreman

P. Markham.
Mechanic

Scanned June 23/04

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 111 DATE OF DRAINING: June 3, 04

UNIT DESCRIPTION: Scoop

	OK	N/A
Battery	x	
Cooler liquid	x	
Differentiel housing oil	x	
Extinguisher	x	
Fuel tank	x	
Glycol		x
Hydraulic hose oil	x	
Hydraulic brake oil	x	
Hydraulic clutch oil		x
Hydraulic control oil	x	
Hydraulic cylinder oil	x	
Hydraulic oil (tank)	x	
Motor oil	x	
Planetary gear drive oil	x	
Power steering oil	x	
Transfer case oil	x	
Transmission oil	x	
Windshield washer		x

List the parts removed from unit:

DATE OF PLACEMENT: June 4, 04
DISPOSAL LOCATION: L-R-D
BENCH LEVEL: 6
U/G DRIFT LEVEL:
SECTION:

Jean Hallé
General Foreman

Frédéric St-Hilaire
Mechanic

MACHINE # 763 Toyota DATE: June 4, 2004 DRAINAGE OF MACHINES

MODEL # Toyota Landcruiser

	DRAINED	NONE	OUT
MOT OIL	✓		
ANTIFREEZ	✓		
HYD OIL	Steering	✓	
DIFF OIL	✓		
BRAKE OIL	✓		
BATTREY	Removed		✓
HOSES	✓		
FUEL TANK	✓		
NITROGEN		✓	
TRANNY	✓	✓	
TRANSFERCASE	✓		
Remove clutch	✓		

REMARKS MECH: Motorstech Paul Loosie

Removed front driveshaft, Radiator, steering reservoir, master brake cylinder, clutch reservoir, alternator, front grill, Heater Blower Housing, Alternator bracket

DRAINED Transmission and Transfer Case

7

Scanned June 23/04

MACHINE # 746 DATE: June 7, 2004 DRAINAGE OF MACHINES

MODEL #

	DRAINED	NONE	OUT
MOT OIL	✓		✓
ANTIFREEZ	✓		✓
HYD OIL	✓		✓
DIFF OIL	✓		✓
BRAKE OIL	✓		✓
BATTREY	✓		✓
HOSES	✓		✓
FUEL TANK	✓		✓
NITROGEN	✓		✓
TRANNY	✓		✓
TRANSFER CASE	✓		

REMARKS

MECH: Paul (Siakuluk) Okadlak

-Remove : Engine with transmission
: Brake master cylinder
: clutch master cylinders
: Radiator and reservoir
: steering pump and reservoir
:

Scanned June 23/04

DRAINAGE REPORT

TWO (2) DEUTZ 12 CYLINDER ENGINES.

BOTH THESE UNITS HAVE BEEN DRAIN OF ENGINE OILS.

DATE OF PLACEMENT: JUNE 16. 2004

DISPOSAL LOCATION: LRD

SNC SUPERVISOR

DRAINAGE REPORT

THREE TOYOTA ENGINE BLOCKS.

ALL THREE UNITS HAVE BEEN DRAIN OF ENGINE OILS.

DATE OF PLACEMENT: June 16, 2004

DISPOSAL LOCATION: LRD

SNC SUPERVISOR

Paul S

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 752
UNIT DESCRIPTION: TOYOTA.

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil		✓
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:
FUEL TANK REMOVED FROM VEHICLE, ALSO ENGINE, TRANS, CLUTCH & BRAKE MASTER CYL'S, POWER STEERING RES., & DIFFERENTIALS, FRONT AXLE HOUSING.
DISPOSED OF IN LRD

Brian Lowes
Jean Halle
General Foreman

P. Markham.
Mechanic

Scanned June 23/04

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 752
UNIT DESCRIPTION: TOYOTA

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
Fuel tank	✓	
Glycol	✓	
Hydraulic hose oil		✓
Hydraulic brake oil	✓	
Hydraulic clutch oil	✓	
Hydraulic control oil		✓
Hydraulic cylinder oil		✓
Hydraulic oil (tank)		✓
Motor oil	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:
FUEL TANK REMOVED FROM VEHICLE, ALSO ENGINE, TRANS, CLUTCH & BRAKE MASTER CYL'S, POWER STEERING RES., & DIFFERENTIALS, FRONT AXLE HOUSING.

Brian Powers
Jean Halle
General Foreman

P. Markham
Mechanic

EQUIPEMENTS INDUSTRIELS ROBERT LTEE
POLARIS MINE

DRAINING REPORT

The goal of this procedure is to remove most of the oil and other liquid from the unit before it goes to scrap to reduce fire and explosion hazard and eliminate environmental contamination.

UNIT #: 752
UNIT DESCRIPTION: TOYOTA

	OK	N/A
Battery	✓	
Cooler liquid	✓	
Differentiel housing oil	✓	
Extinguisher	✓	
	✓	
	✓	
		✓
lic brake oil	✓	
lic clutch oil	✓	
lic control oil		✓
lic cylinder oil		✓
		✓
	✓	
Planetary gear drive oil		✓
Power steering oil	✓	
Transfer case oil	✓	
Transmission oil	✓	
Windshield washer	✓	

List the parts removed from unit:

FUEL TANK REMOVED FROM VEHICLE, ALSO ENGINE, TRANS, CLUTCH & BRAKE MASTER CYL'S, POWER STEERING RES., & DIFFERENTIALS, FRONT AXLE HOUSING.

Brian Powers
Jean Halle
General Foreman

P. Markham
Mechanic

POLARIS MINE – 2004 1ST QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



March 4, 2004



March 29, 2004



March 29, 2004


POLARIS MINE – 2004 2ND QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



April 18, 2004



April 18, 2004

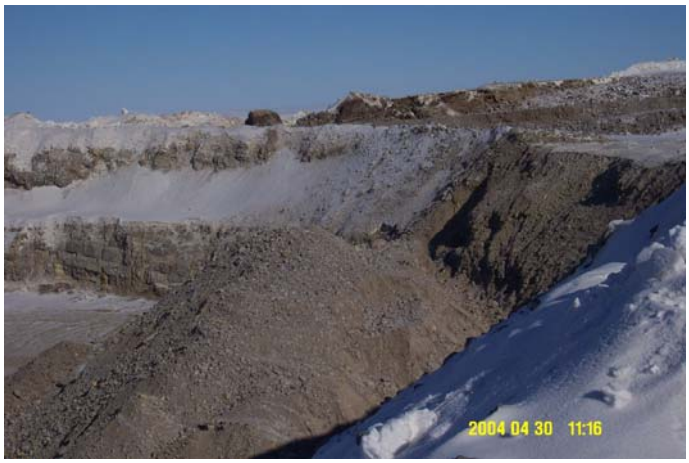

April 30, 2004

POLARIS MINE – 2004 2ND QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



April 30, 2004



April 30, 2004



May 5, 2004

POLARIS MINE – 2004 2ND QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



May 17, 2004



May 31, 2004



June 12, 2004

POLARIS MINE – 2004 2ND QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



June 12, 2004



June 12, 2004



June 24, 2004

POLARIS MINE – 2004 3rd QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



July 2, 2004



July 2, 2004



July 11, 2004

POLARIS MINE – 2004 3rd QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



July 30, 2004



July 30, 2004



August 7, 2004

POLARIS MINE – 2004 3rd QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



August 20, 2004



August 30, 2004



August 30, 2004

POLARIS MINE – 2004 3rd QUARTER DEBRIS PLACED INTO LRD QUARRY LANDFILL



September 7, 2004



September 7, 2004



September 7, 2004

APPENDIX 11

RECORD of CONTAMINATED SOILS EXCAVATED

AND

DISPOSAL LOCATIONS IN THE MINE

TABLE 1
POLARIS MINE - CONTAMINATED SOILS EXCAVATED
TO DECEMBER 31, 2004

[1]Contaminated Soil Locations	DRP Forecast Volumes To Be Excavated (m^3 in-situ volume)		[4]Estimated Volumes Excavated To Date (m^3 in-situ volume)		Estimated Volumes Excavated During 2004 (m^3 in-situ volume)		[3]Total Volumes Excavated (m^3 in-situ volume)	
	Hydrocarbons	Metals	Hydrocarbons	Metals	Hydrocarbons	Metals	Hydrocarbons	Metals
North Portal Pb Ore Stockpile Area	-	TBA	-	11,352	-	-	-	11,352
Fuel Bladder Storage Area	12,000	-	12,513	-	-	-	12,513	-
Old Crusher	-	TBA	-	1,079	-	-	-	1,079
Tails Thickener/ Tailings Lines	TBA	3,000	-	2,183	-	-	-	2,183
CRF Plant	100	-	40	-	-	-	40	-
Exploration Dump & Stockpile Area		TBA	-	11,028	-	10,607	-	21,635
Firehall Training Area	2,000		1,465	-	11,747	5,048	13,212	5,048
Concentrate Storage Shed Area	Note 2	Note 2	-	24,314	1,731	26,869	1,731	51,183
Barge Area	20,000	85,000	28,314	-	48,164	31,985	76,478	31,985
Dock Cells			12,210		3,519	8,481	15,729	8,481
Shoreline				44,645	-	(9,666)	-	34,979
Foldaway Buildings	2,000	-	628	110	15,946	161	16,574	271
Incinerator Area							4,390	6,110
Accommodation Building	500	-	-	-	1,800	-	1,800	-
Quonset Huts	TBA	-	-	-	-	-	-	-
Snow Dumps		3,500		1,641	-	14,000	-	15,641
Lube Storage / Tank Farm Area	-	-			3,150	-	3,150	-
June 2002 Fuel Spill	Note 3	-	-	-	580	-	580	-
Miscellaneous	-		-	-	628	110	628	110
TOTALS	36,600	91,500	55,170	96,352	87,265	87,595	146,825	190,057
TOTAL CONTAMINANTS		**128,100**		**151,522**		**174,860**		**336,882**

Notes:

Note 1 - Some area boundaries have changed from the 2003 4th Quarter report as volumes presented are based on surveyed data which has changed the definition of some of the areas.

Note 2 - DRP estimated metals contaminated soils in the Concentrate Storage Area and the Barge area together as one quantity.

Note 3 - this fuel spill ocurred after the DRP was issued so there was not estimate for it.

Note 4 - Total volumes are based on surveys of remediated areas.

Abreviations:

DRP - Decommissioning and Reclamation Plan

TBA - Areas identified in the DRP as being contaminated but no estimate of volumes were made as investigations were not completed.

TABLE 2
POLARIS MINE - CONTAMINATED SOILS HANDLING TO DECEMBER 31, 2004


HYDROCARBON CONTAMINATED SOILS		METALS CONTAMIANTED SOILS		TOTALS CONTAMINATED SOILS (M^3)		
LRDQL	MINE	LRDQL	MINE	LRDQL	MINE	TOTAL
0	146,844	80,324	109,774	80,324	256,618	336,942

NOTES:

Hydrocarbon Soils include Co-contaminated (Metals & Hydrocarbons)
LRDQL - refers to Little Red Dog Quarry Landfill
MINE - refers to the underground working of the mine

2200 N | 2100 N | 2000 N | 1900 N | 1800 N

1600 E | 1500 E | 1400 E

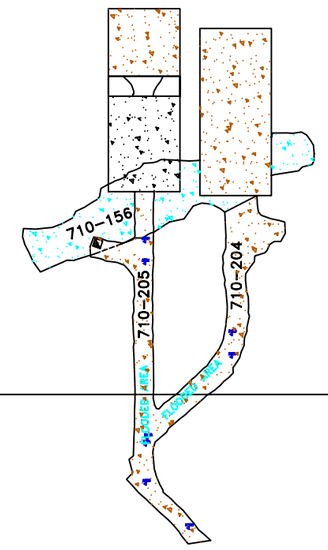

Sept 4 2003

Level flooded with Water from under the Barge excavation

MATERIALS PLACED UNDERGROUND

- NORMAL MINE BACKFILL FROM OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER MATERIALS STORAGE

1800 N

POLARIS MINE

DRAWN BY: J.A. | CHECKED BY:


REVISED BY: | DATE: | REVISION

710 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED

as of December 31, 2004

SCALE: 1:1500

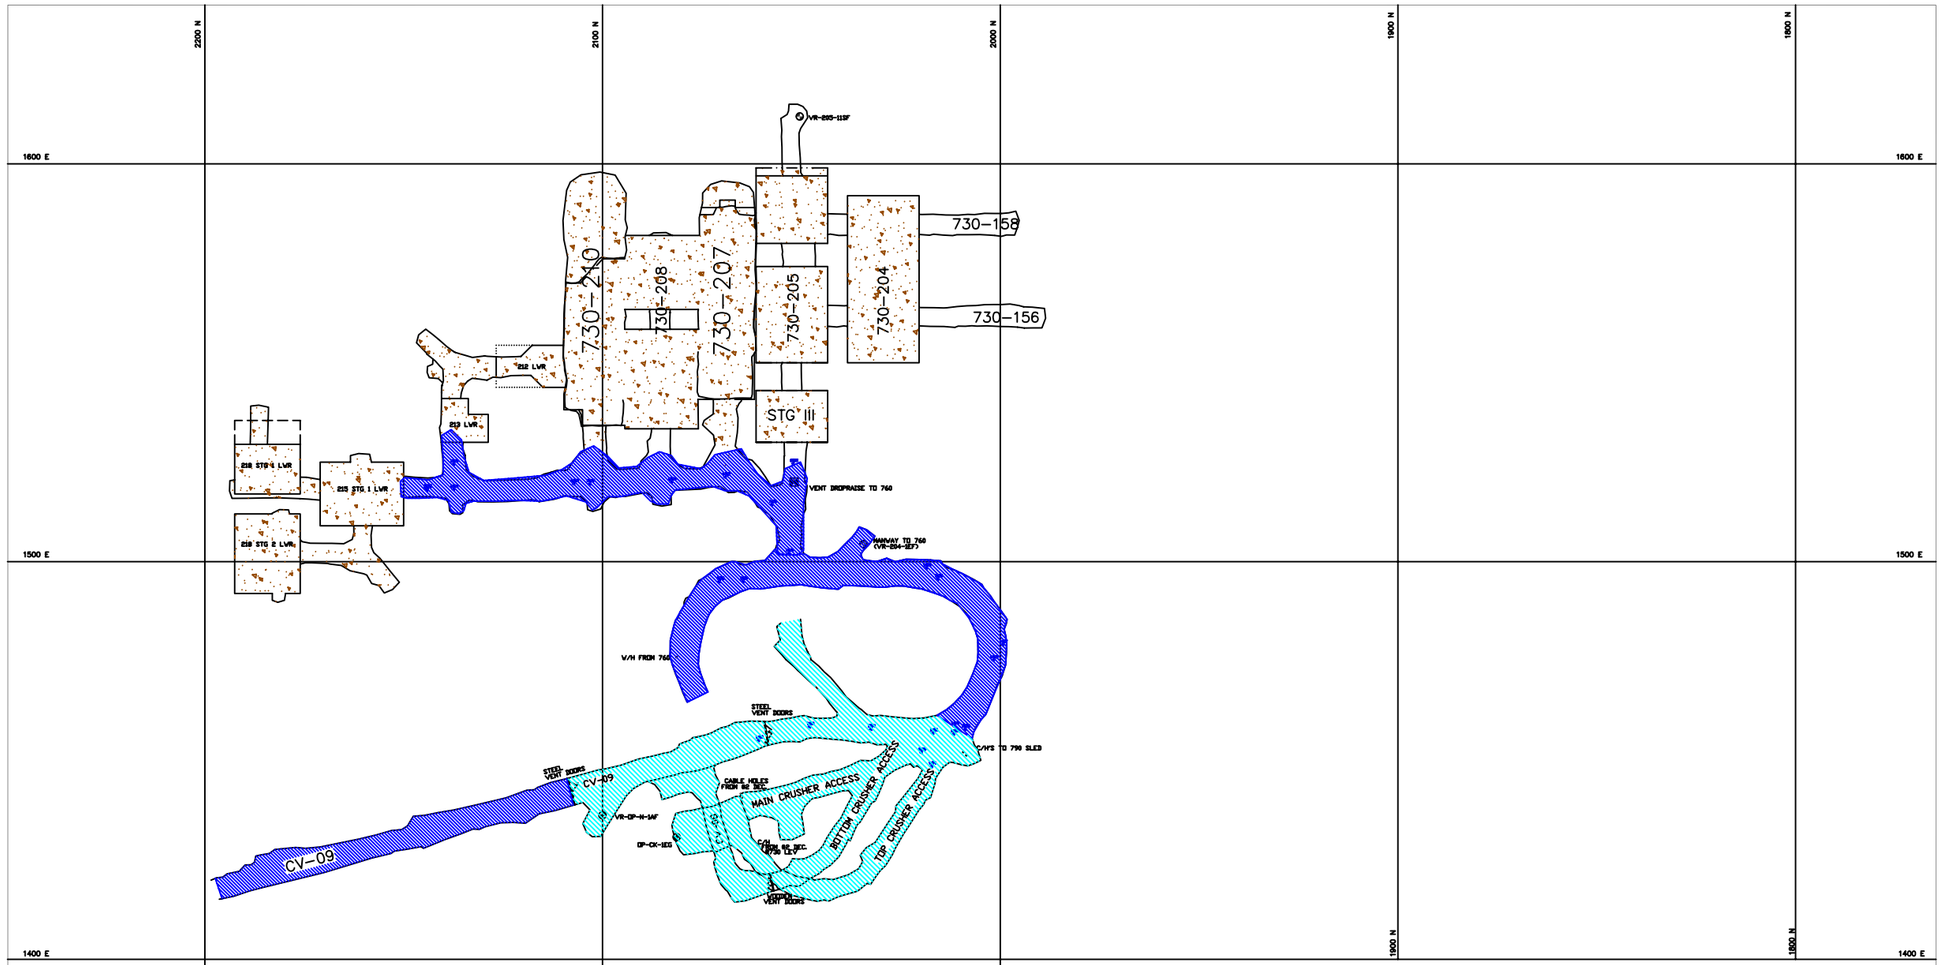

MATERIALS PLACED UNDERGROUND


- NORMAL MINE BACKFILL FROM OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER MATERIALS STORAGE


POLARIS MINE


DRAWN BY: J.A.	SCALE: 1:1500	
REVISED BY:	DATE:	REVISION


730 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

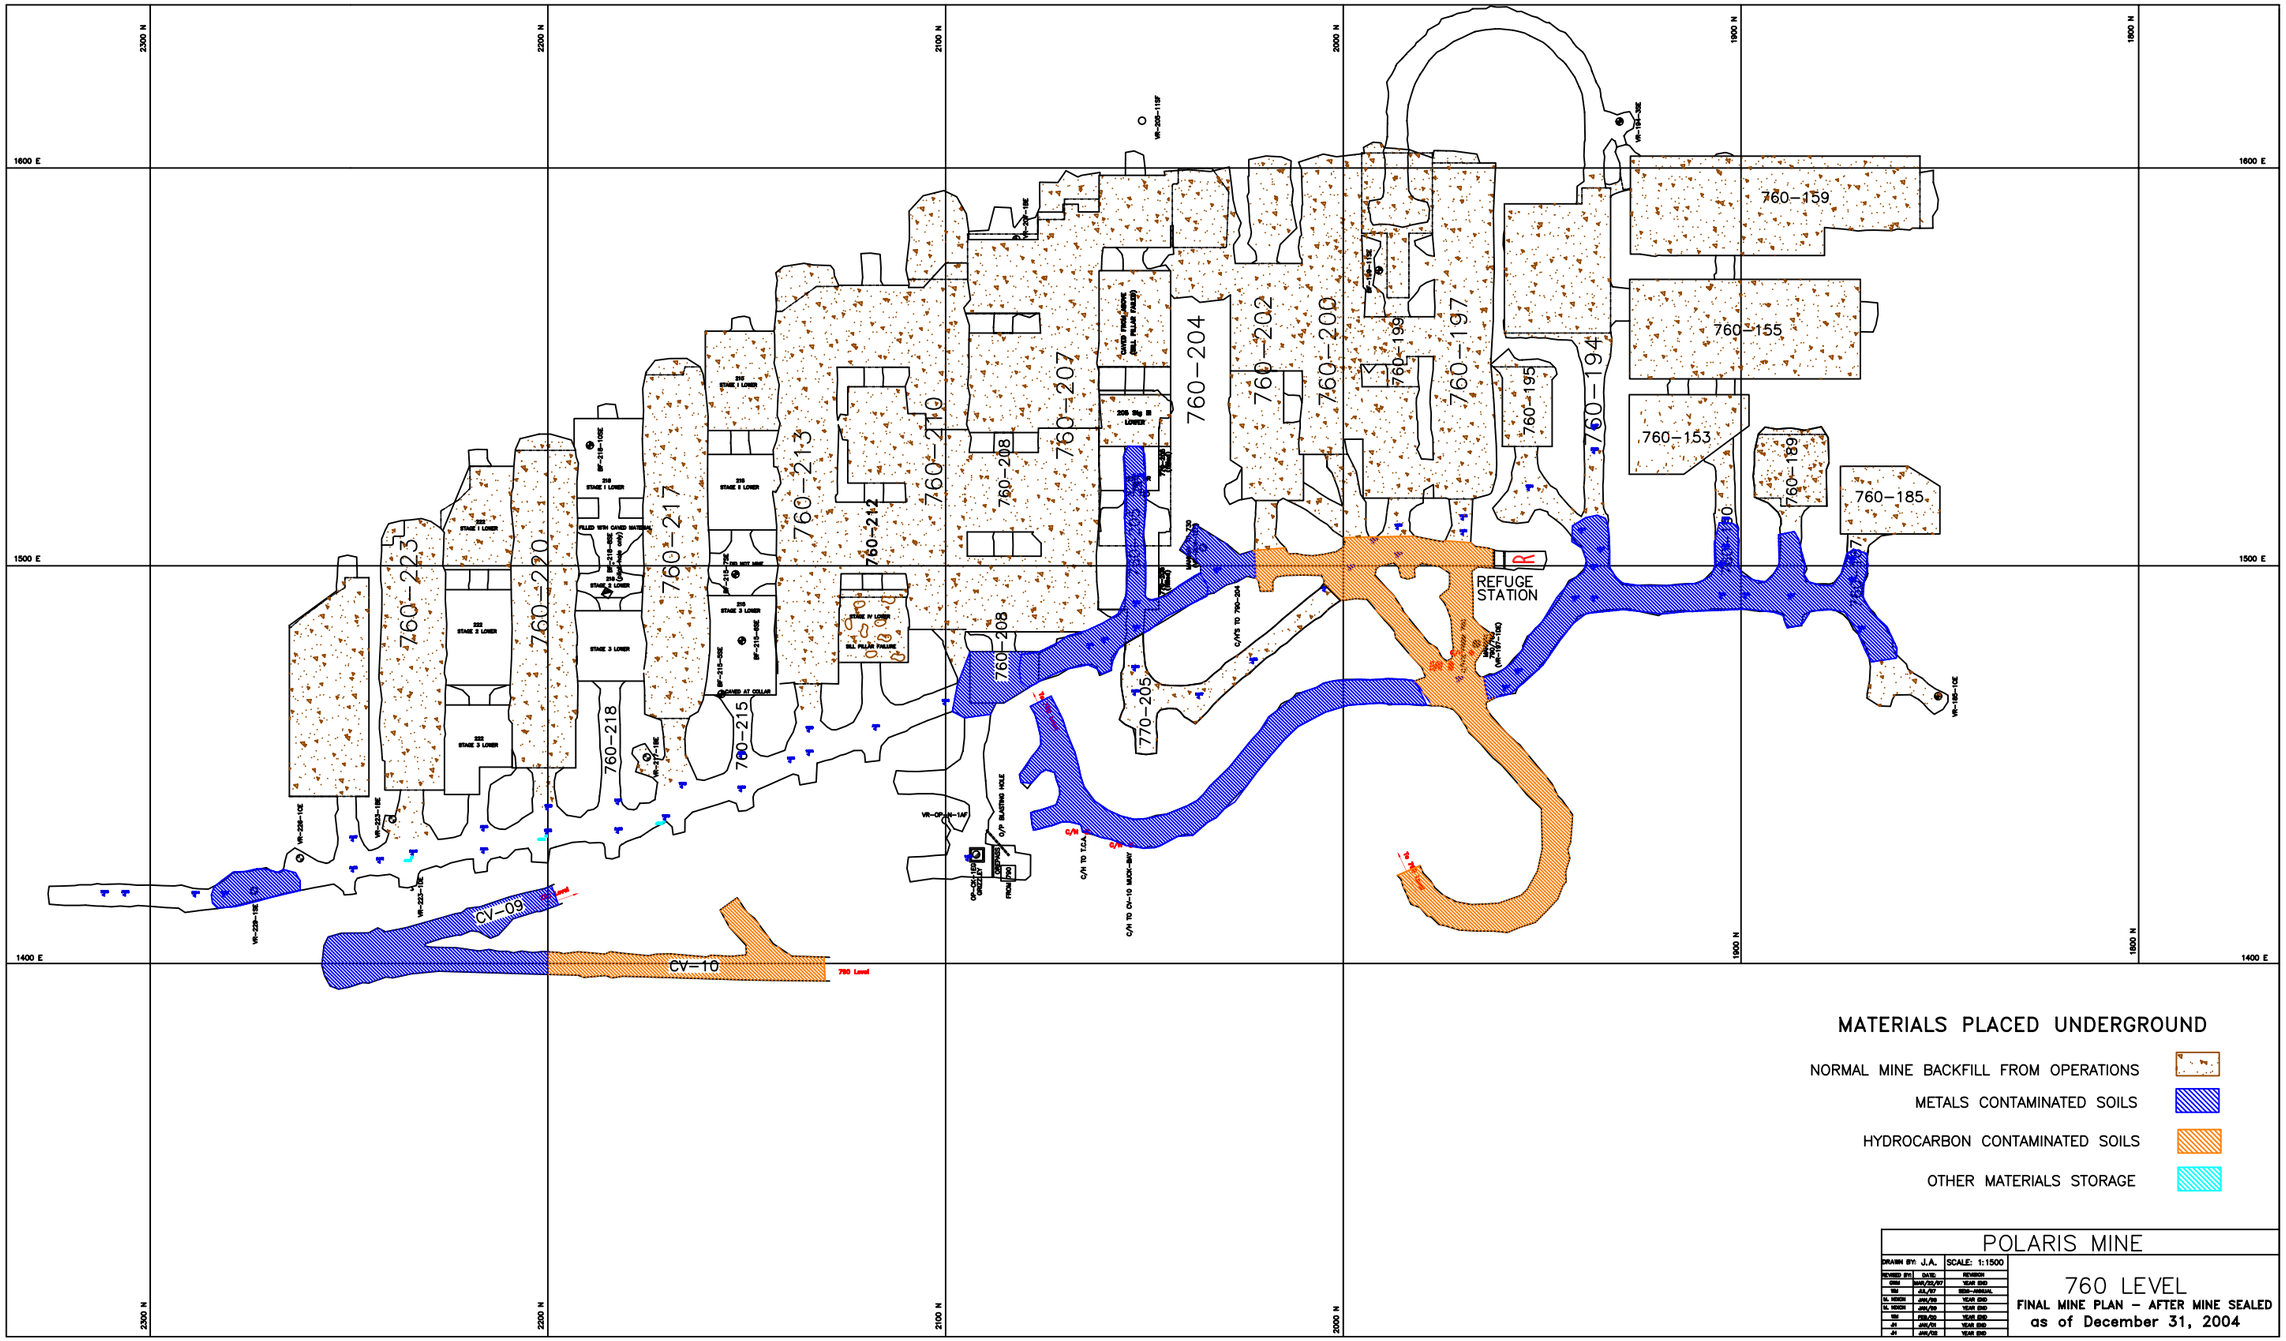
2300 N
2200 N
2100 N
2000 N
1900 N
1800 N
1600 E
1500 E
1400 E
760-159
760-155
760-153
760-189
760-185
760-194
760-195
760-197
760-199
760-200
760-202
760-204
760-207
760-208
760-210
760-212
760-213
760-217
760-218
760-220
760-223
770-205
770-215
REFUGE STATION
CV-09
CV-10
750 Level
C/A TO 760-204
C/A TO T.O.A.
C/A TO CH-10 MUCK-BAY
6FT ALUMINUM MAN DOOR
VENTILATION RAISE
VENTILATION RAISE (RAISE BORED)
VENTILATION RAISE (RAISE BORED)
VENTILATION RAISE (RAISE BORED)

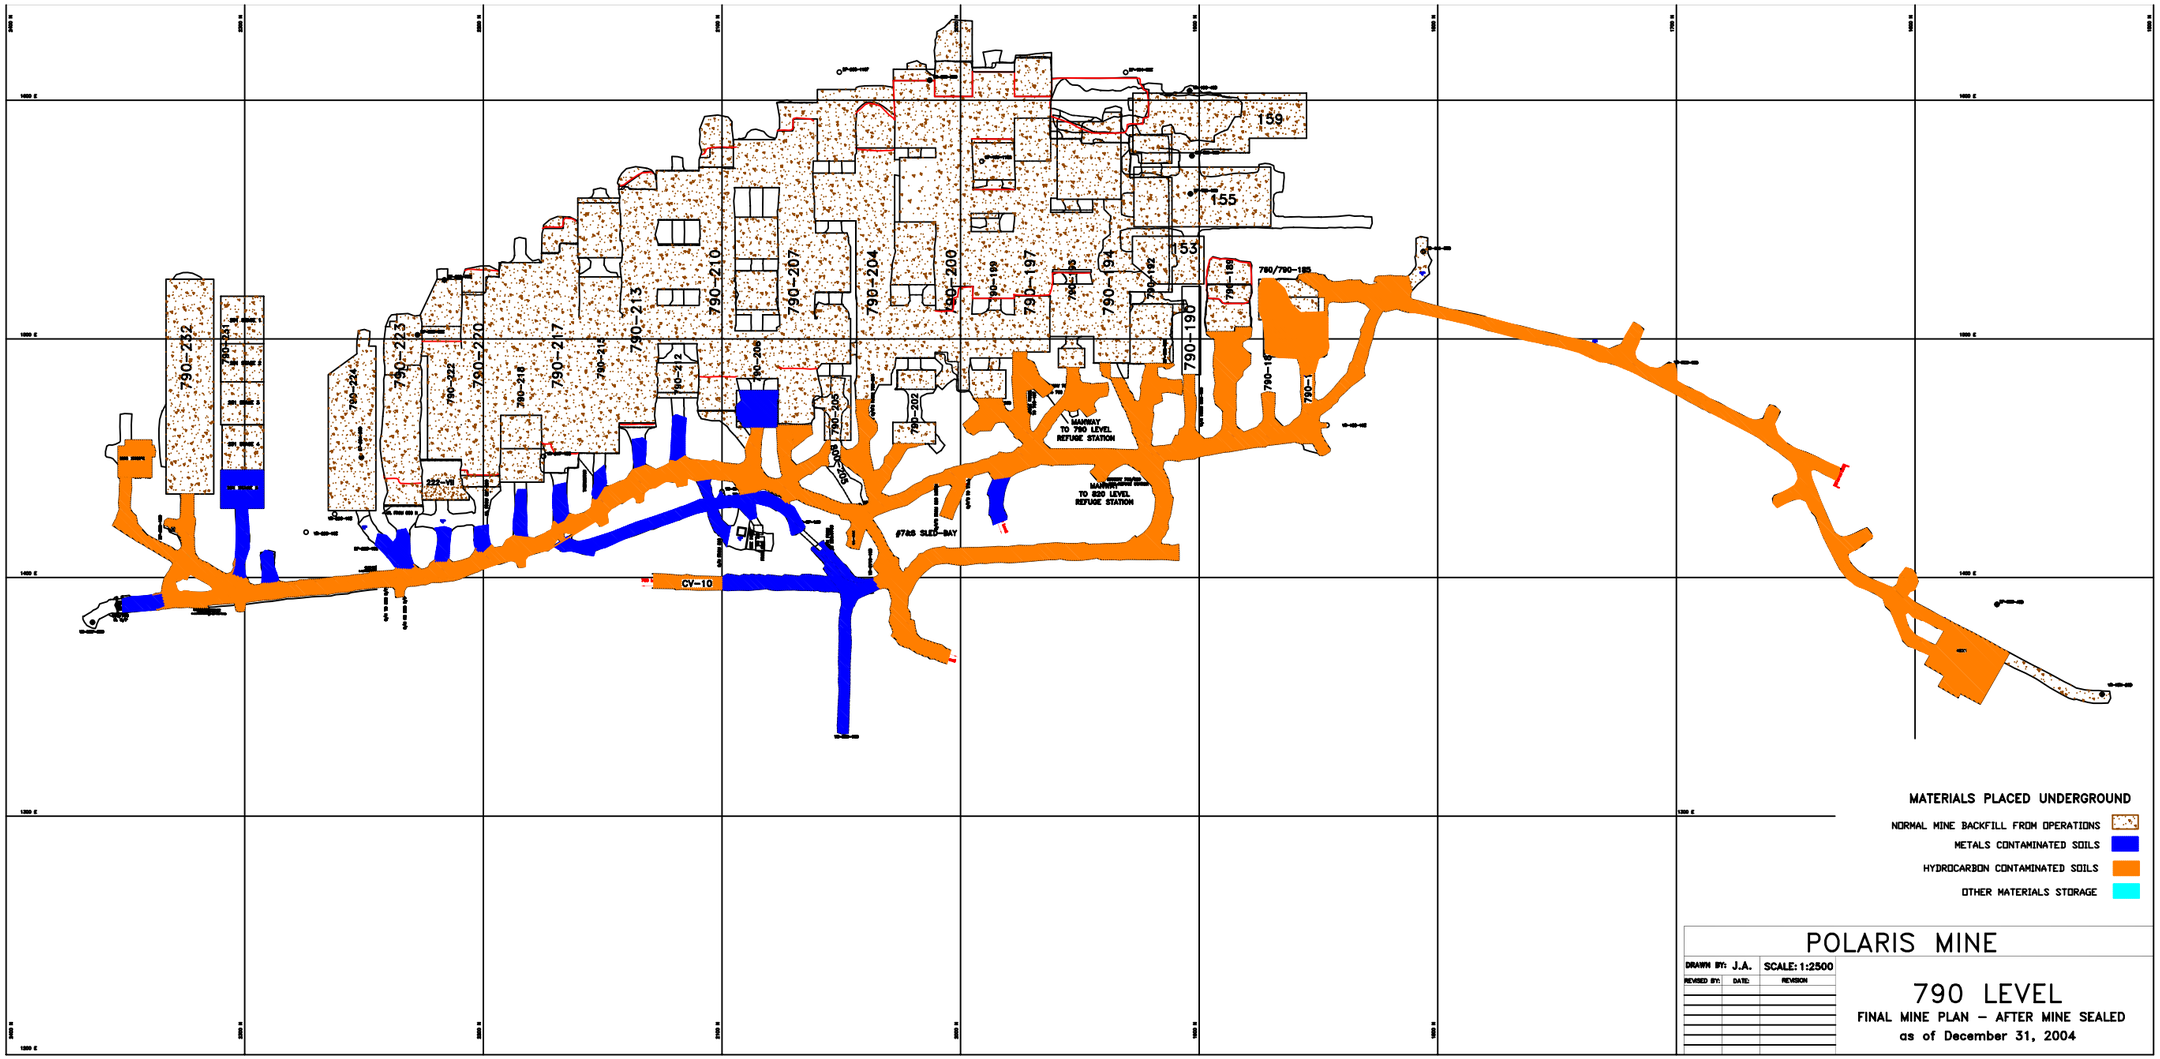
790-252
790-223
790-220
790-217
790-213
790-210
790-207
790-204
790-200
790-197
790-194
790-190
790-1
159
155
153
780/790-185
MANWAY
TO 790 LEVEL
REFUSE STATION
MANWAY
TO 820 LEVEL
REFUSE STATION
6785 SUMP
CV-10
MATERIALS PLACED UNDERGROUND
NORMAL MINE BACKFILL FROM OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER MATERIALS STORAGE
POLARIS MINE
DRAWN BY: J.A.
SCALE: 1:2500
REVISED BY:
DATE:
REVISION
790 LEVEL
FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

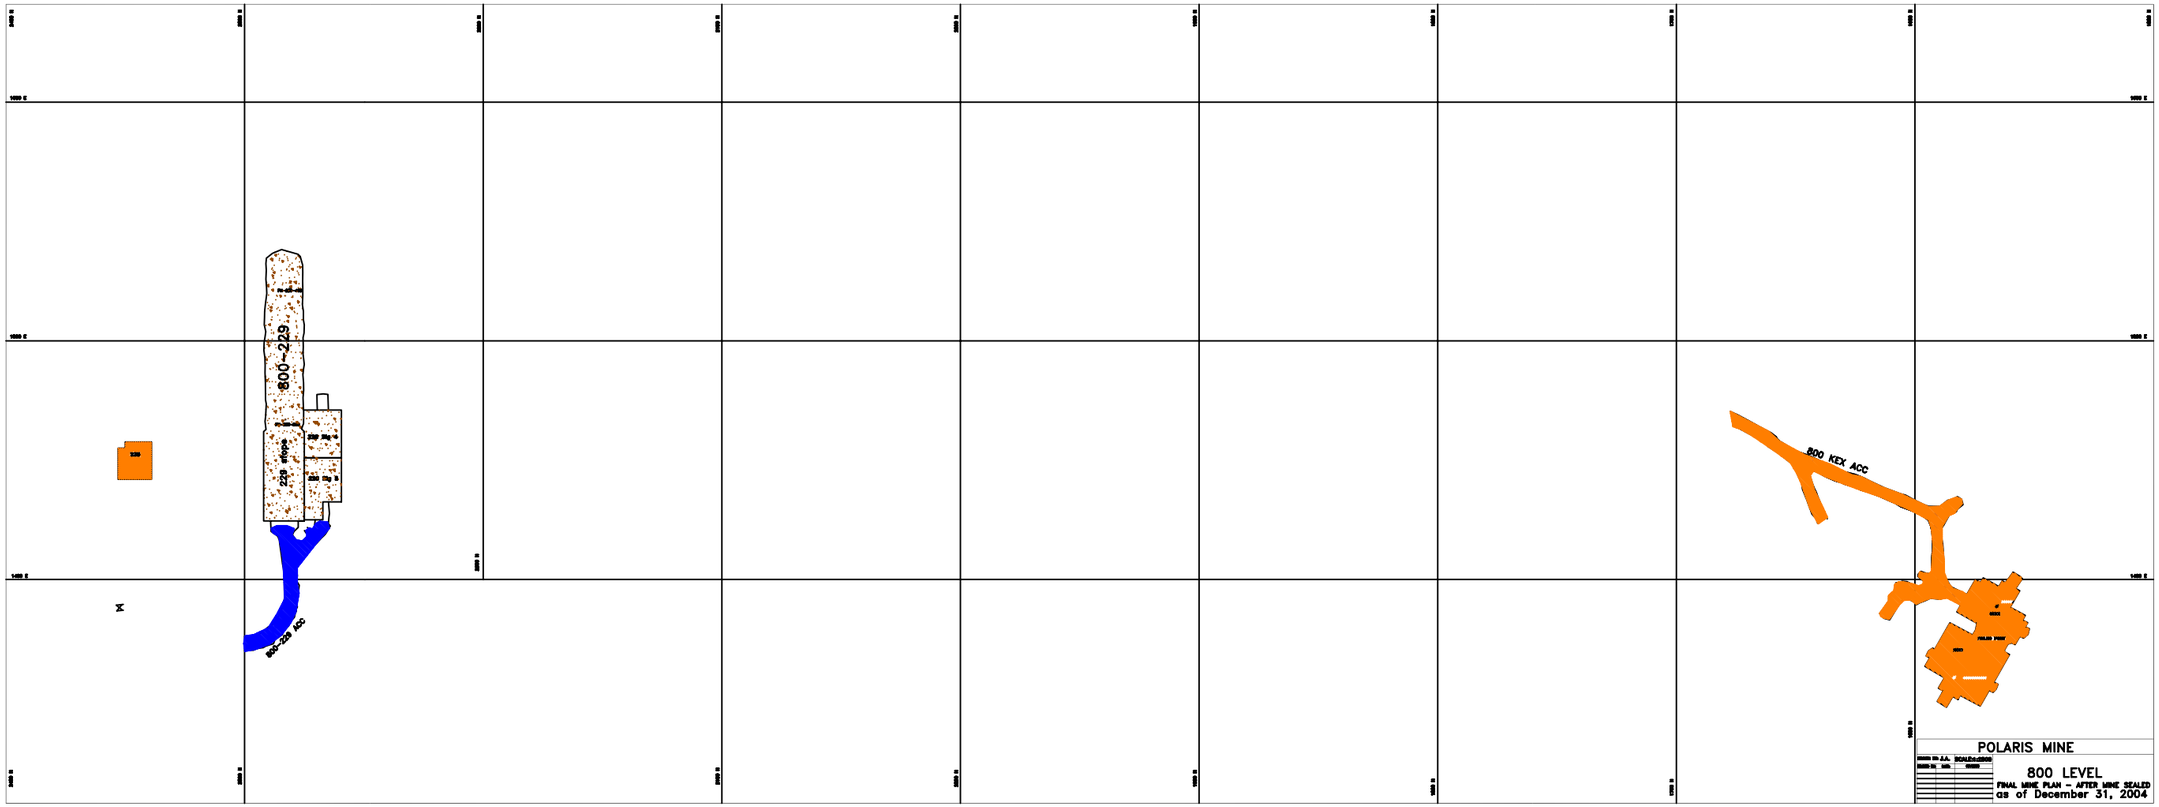
800-229
800-229 ACC
800 KEK ACC
POLARIS MINE
800 LEVEL
FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

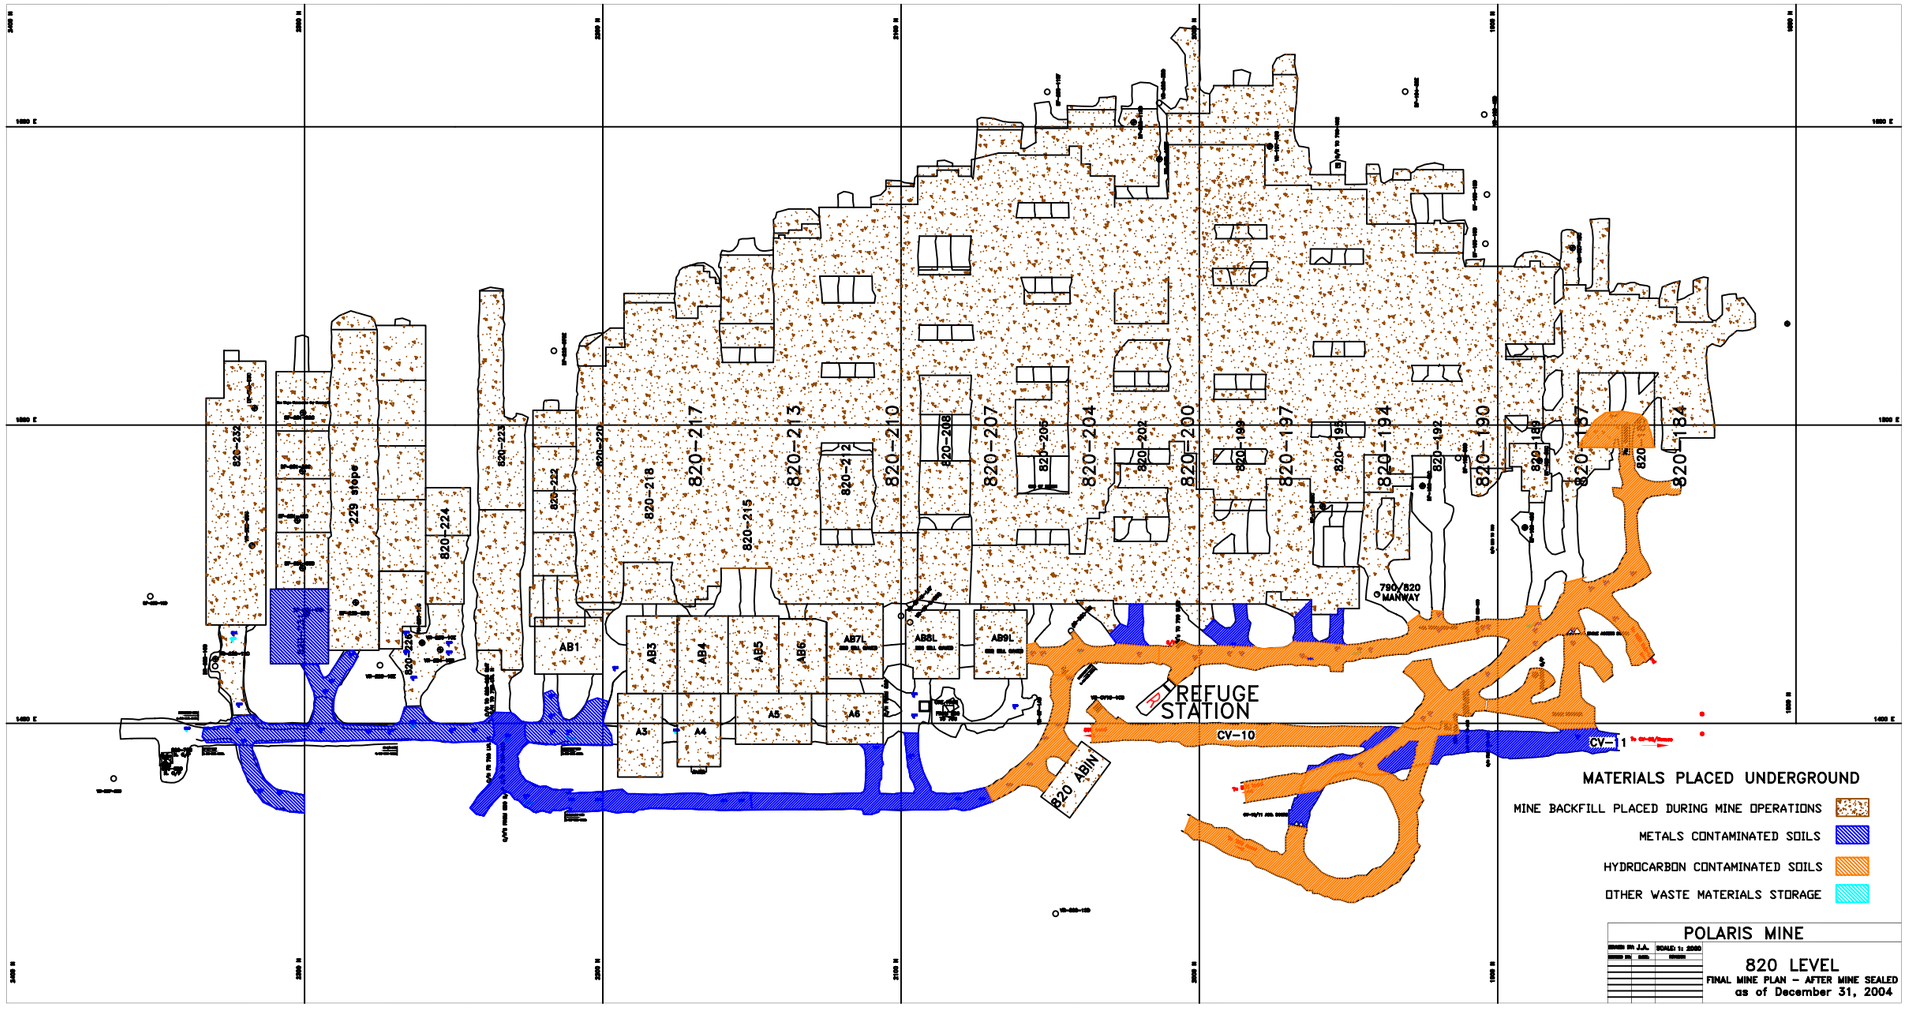
820-232
229 stope
820-224
820-223
820-222
820-220
820-218
820-217
820-215
820-213
820-212
820-210
820-208
820-207
820-205
820-204
820-202
820-200
820-198
820-197
820-195
820-194
820-192
820-190
820-189
820-187
820-184
790/820 MANWAY
AB1
AB3
AB4
AB5
AB6
AB7L
AB8L
AB9L
A3
A4
A5
A6
REFUGE STATION
CV-10
CV-1
820 ABIN
MATERIALS PLACED UNDERGROUND
MINE BACKFILL PLACED DURING MINE OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER WASTE MATERIALS STORAGE
POLARIS MINE
820 LEVEL
FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

2000 N
1900 N
1800 N
1700 N
1600 E
1500 E
1400 E

850/820–187
850/820–185
850/820–184
825–181
825–152
825–150
825–185
825–176
825–172
C/H FROM 850
CV–11
CV–12

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

POLARIS MINE

DRAWN BY: J.A.	SCALE 1:1250
REVISED BY:	DATE: / REVISION

825 SUBLEVEL

FINAL MINE PLAN – AFTER MINE SEALED

as of December 31, 2004

850 NORTH LEVEL

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

POLARIS MINE

850 LEVEL SOUTH

FINAL MINE PLAN – AFTER MINE SEALED

as of December 31, 2004

Mak Parts
Pump
Compressor
Hydraulic Pack

880–145
880–142
880–141
880–139
880–137
880–135
880 DUMP
125W
680–124W

NP–231
NP–229
NP–227
NP–142
NP–140

880–223
880–220
880–217
880–213
880–210
880–207
880–204
880–200
880–197
880–194
880–190
880–187
880–184
880–181

AB1 AB2 AB3 AB4 AB5 AB6 AB7 AB8 AB9 AB10 AB11 AB12 AB13 AB14 AB15 AB16 AB17 AB19 AB20

A STOPE
A/B UNDERCUT
B STOPE
B/C UNDERCUT

105–7
105–6

Tires, Steel & Pallets
Tailings Lines


SLED–BAY
LADDER UP TO REFUGE STATION
REFUGE STATION NEXT RIGHT

MATERIALS PLACED UNDERGROUND

- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE

POLARIS MINE

880 LEVEL SOUTH
FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

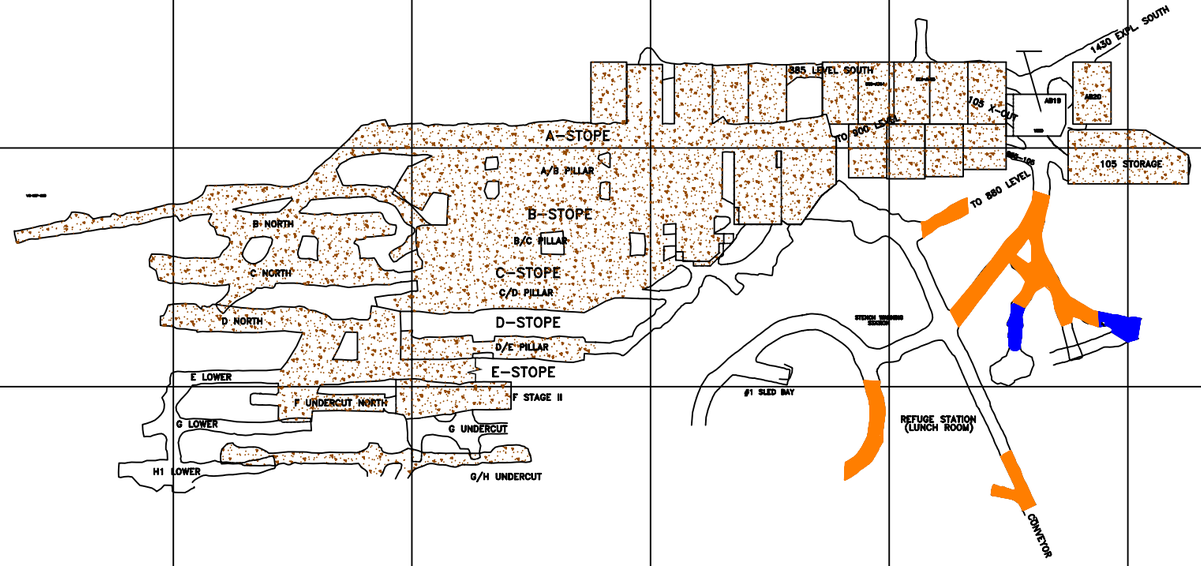

MATERIALS PLACED UNDERGROUND


- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE

POLARIS MINE

DRAWN BY: J.A.	SCALE:1:2500
REVISED BY:	DATE: / REVISION

885 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

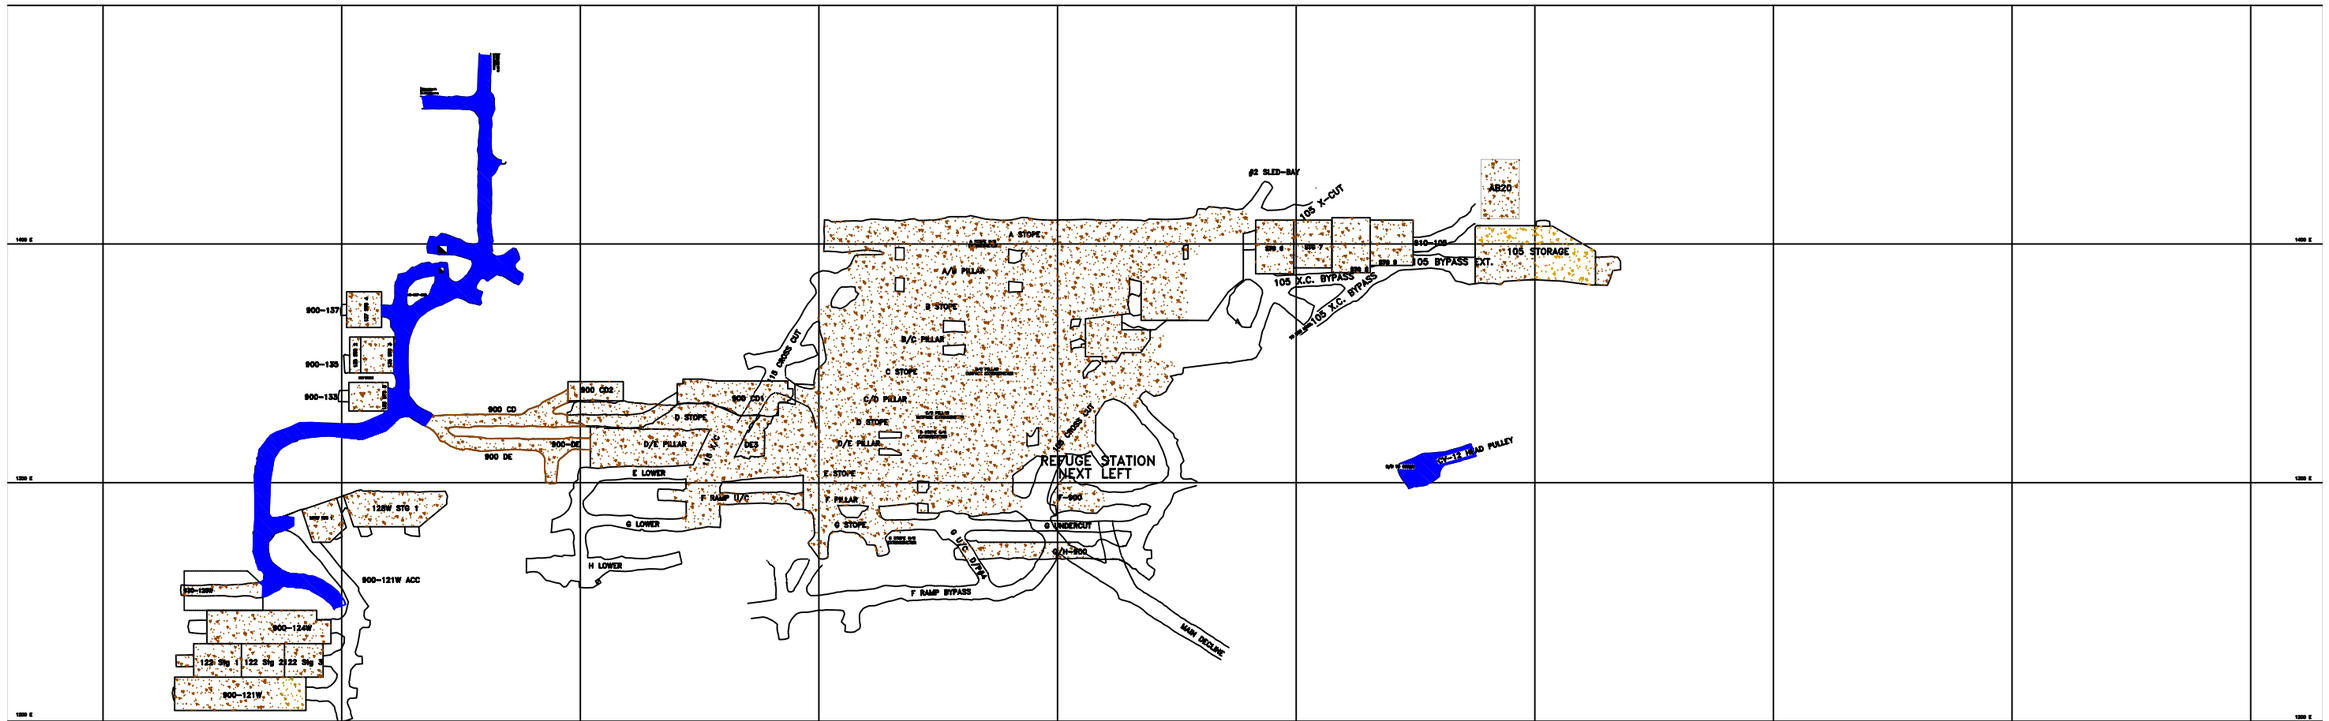

MATERIALS PLACED UNDERGROUND

- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE


POLARIS MINE

DRAWN BY: J.A. SCALE: 1:2500

DRAWN BY:	DATE:	REVISIONS

900 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

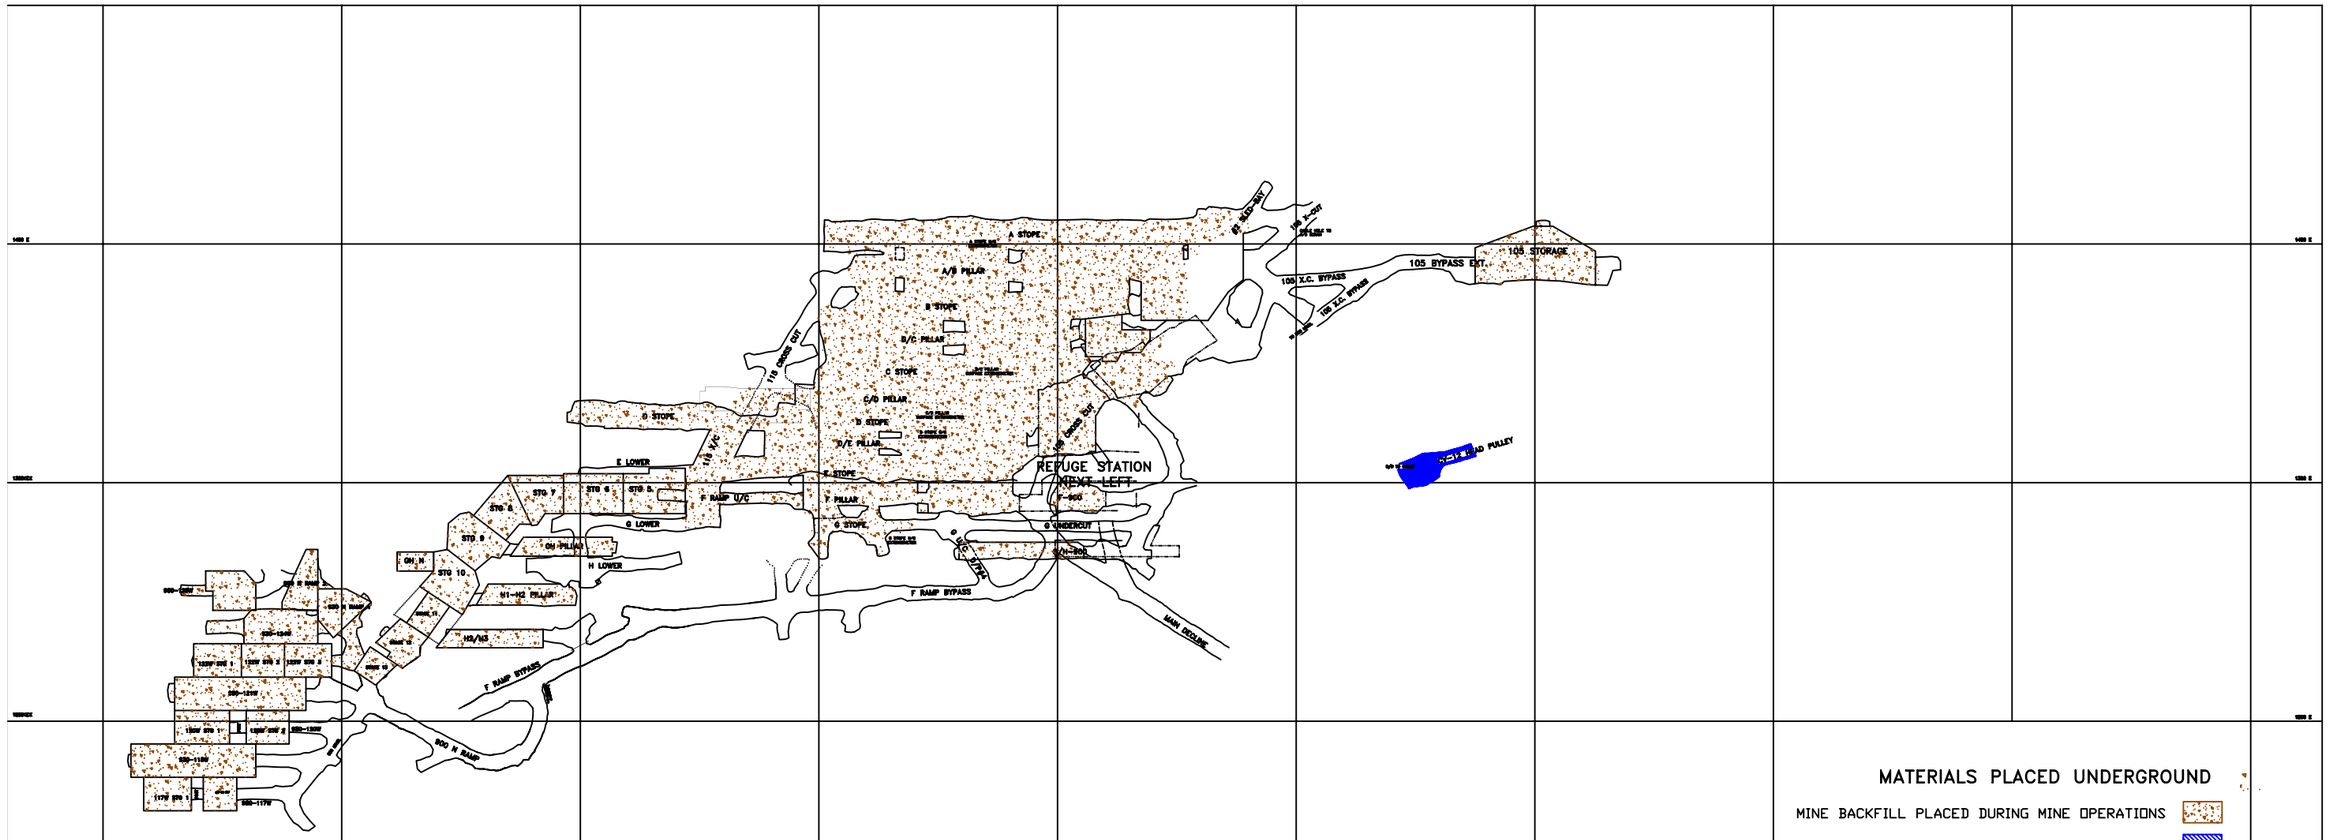

MATERIALS PLACED UNDERGROUND

- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE


POLARIS MINE

DRAWN BY: J.A. | SCALE: 1:2500

930 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED

as of December 31, 2004

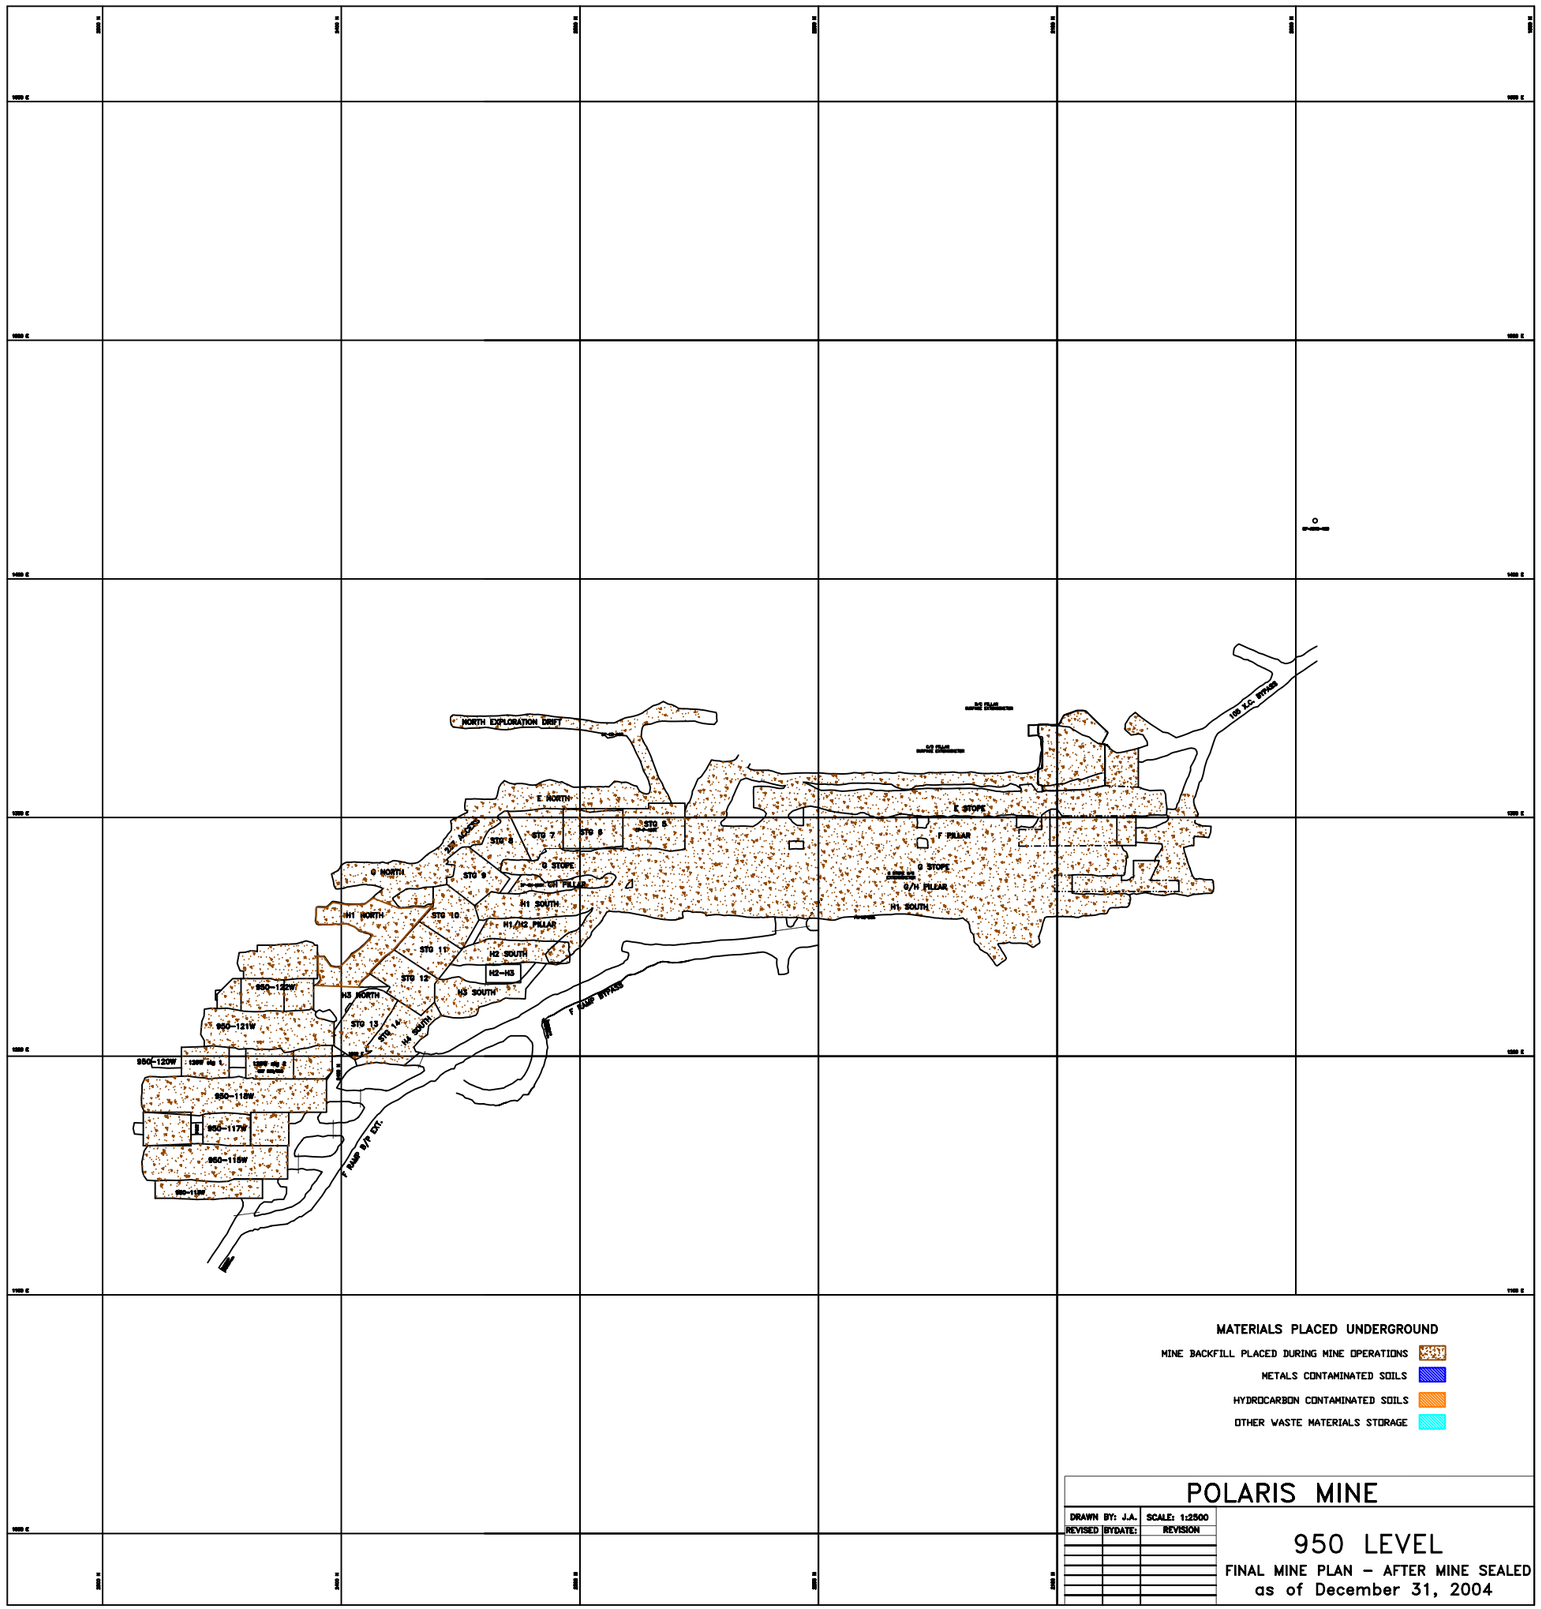

MATERIALS PLACED UNDERGROUND

- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE

POLARIS MINE

DRAWN BY: J.A.		SCALE: 1:2500
REVISED	BYDATE:	REVISION

950 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

2500 N
2500 N
2400 N
2300 N
2200 N
1300 E
1300 E
1200 E
1200 E
960 F
960–120W
960–118W
960–117W
960–115W
960–113W
Tailings Line Storage Area
1100 E
1100 E
2300 N
2500 N
2500 N
2400 N
2300 N

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

POLARIS MINE

DRAWN BY: MJH	SCALE: 1:1500
REVISED BY:	DATE:

960 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED
as of December 31, 2004

PORTAL PLUG

MACHINERY AND TELEPHONE POLES

NORTH PORTAL

ANFO PLANT

ø4 SLED-BAY

FUEL BAY (1000 GAL)

ANFO STORAGE

MAIN DECLINE

STEEL SETS

MACHINERY

BAGS OF LIME

CV-01 CONVEYOR

JUNE 2003 MELT WATER STORAGE AREA

COB #1

CV-02 CONVEYOR

MAIN DECLINE

MACHINERY

PORTAL PLUG

PORTAL PLUG

PORTAL PLUG

CV-03

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

POLARIS MINE

DRAWN BY: J.A. SCALE: NTS

REVISED BY	DATED	REVISION

980 LEVEL

FINAL MINE PLAN – AFTER MINE SEALED


as of December 31, 2004

APPENDIX 12

ROCK TEMPERATURES MEASURED

FROM THE

UNDERGROUND MINE WORKINGS

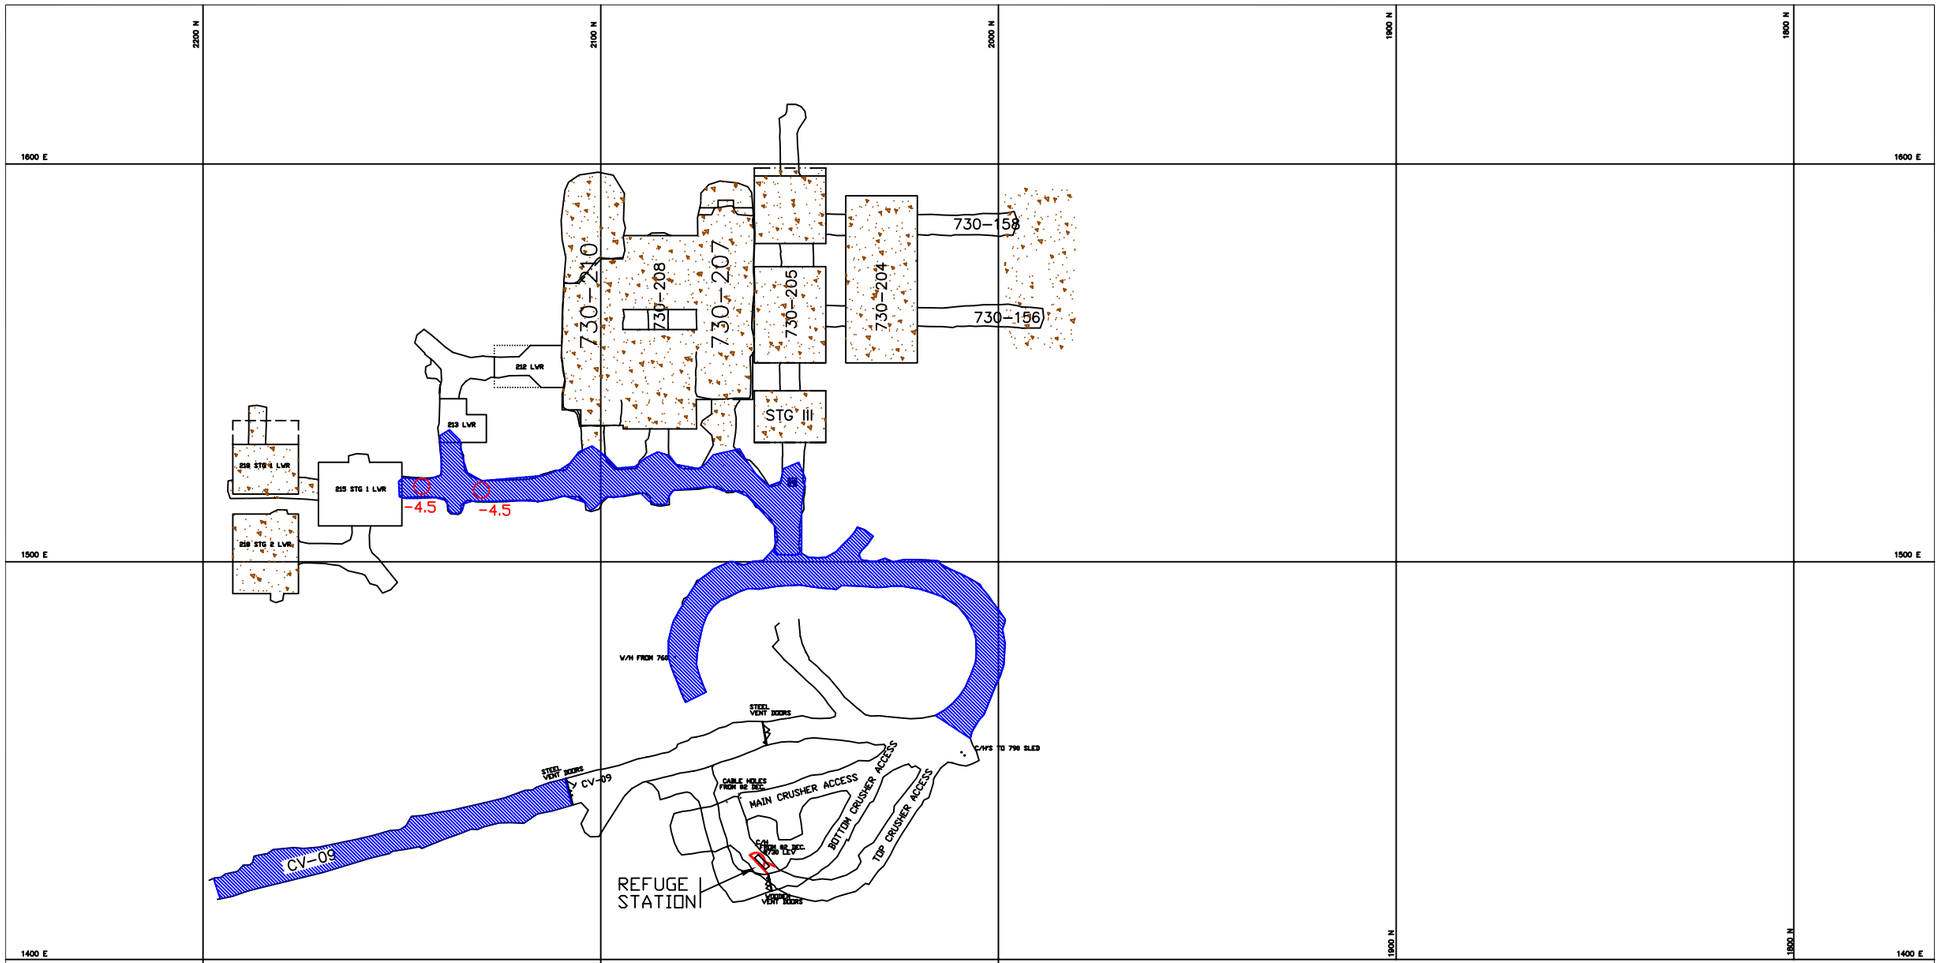

MATERIALS PLACED UNDERGROUND

NORMAL MINE BACKFILL FROM OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER MATERIALS STORAGE

ROCK TEMPERATURE -5.5

POLARIS MINE

DRAWN BY: J.A. SCALE: 1:500

REVISED BY:	DATE:	REVISION
GMM	MAR/02/07	YEAR END
NM	JUL/07	SEMI-ANNUAL
GL MINOR	JAN/08	YEAR END
GL MINOR	JAN/09	YEAR END
NM	FEB/09	YEAR END
NLB	JAN/01	YEAR END
JH	JAN/10	YEAR END

730 LEVEL

Contamination Placement as of December 31, 2003

2300 N
2200 N
2100 N
2000 N
1900 N
1800 N
1600 E
1500 E
1400 E

760-223
760-220
760-217
760-218
760-215
760-213
760-212
760-210
760-208
760-207
760-204
760-202
760-200
760-198
760-197
760-195
760-194
760-159
760-155
760-153
760-189
760-185
760-190
760-187
770-205
760-208
760-208

REFUGE STATION

CV-09
CV-10

-5.4

MATERIALS PLACED UNDERGROUND


NORMAL MINE BACKFILL FROM OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER MATERIALS STORAGE
ROCK TEMPERATURE -5.5

POLARIS MINE

DRAWN BY: J.A. SCALE: 1:500

REVISED BY	DATE	REVISION
GMH	MAR/22/97	YEAR END
TEC	JUL/97	SEMI-ANNUAL
N. HAMM	JAN/98	YEAR END
N. HAMM	JAN/99	YEAR END
TEC	FEB/99	YEAR END
JH	JAN/01	YEAR END
JH	JAN/02	YEAR END

760 LEVEL
Contamination Placement
as of December 31, 2003

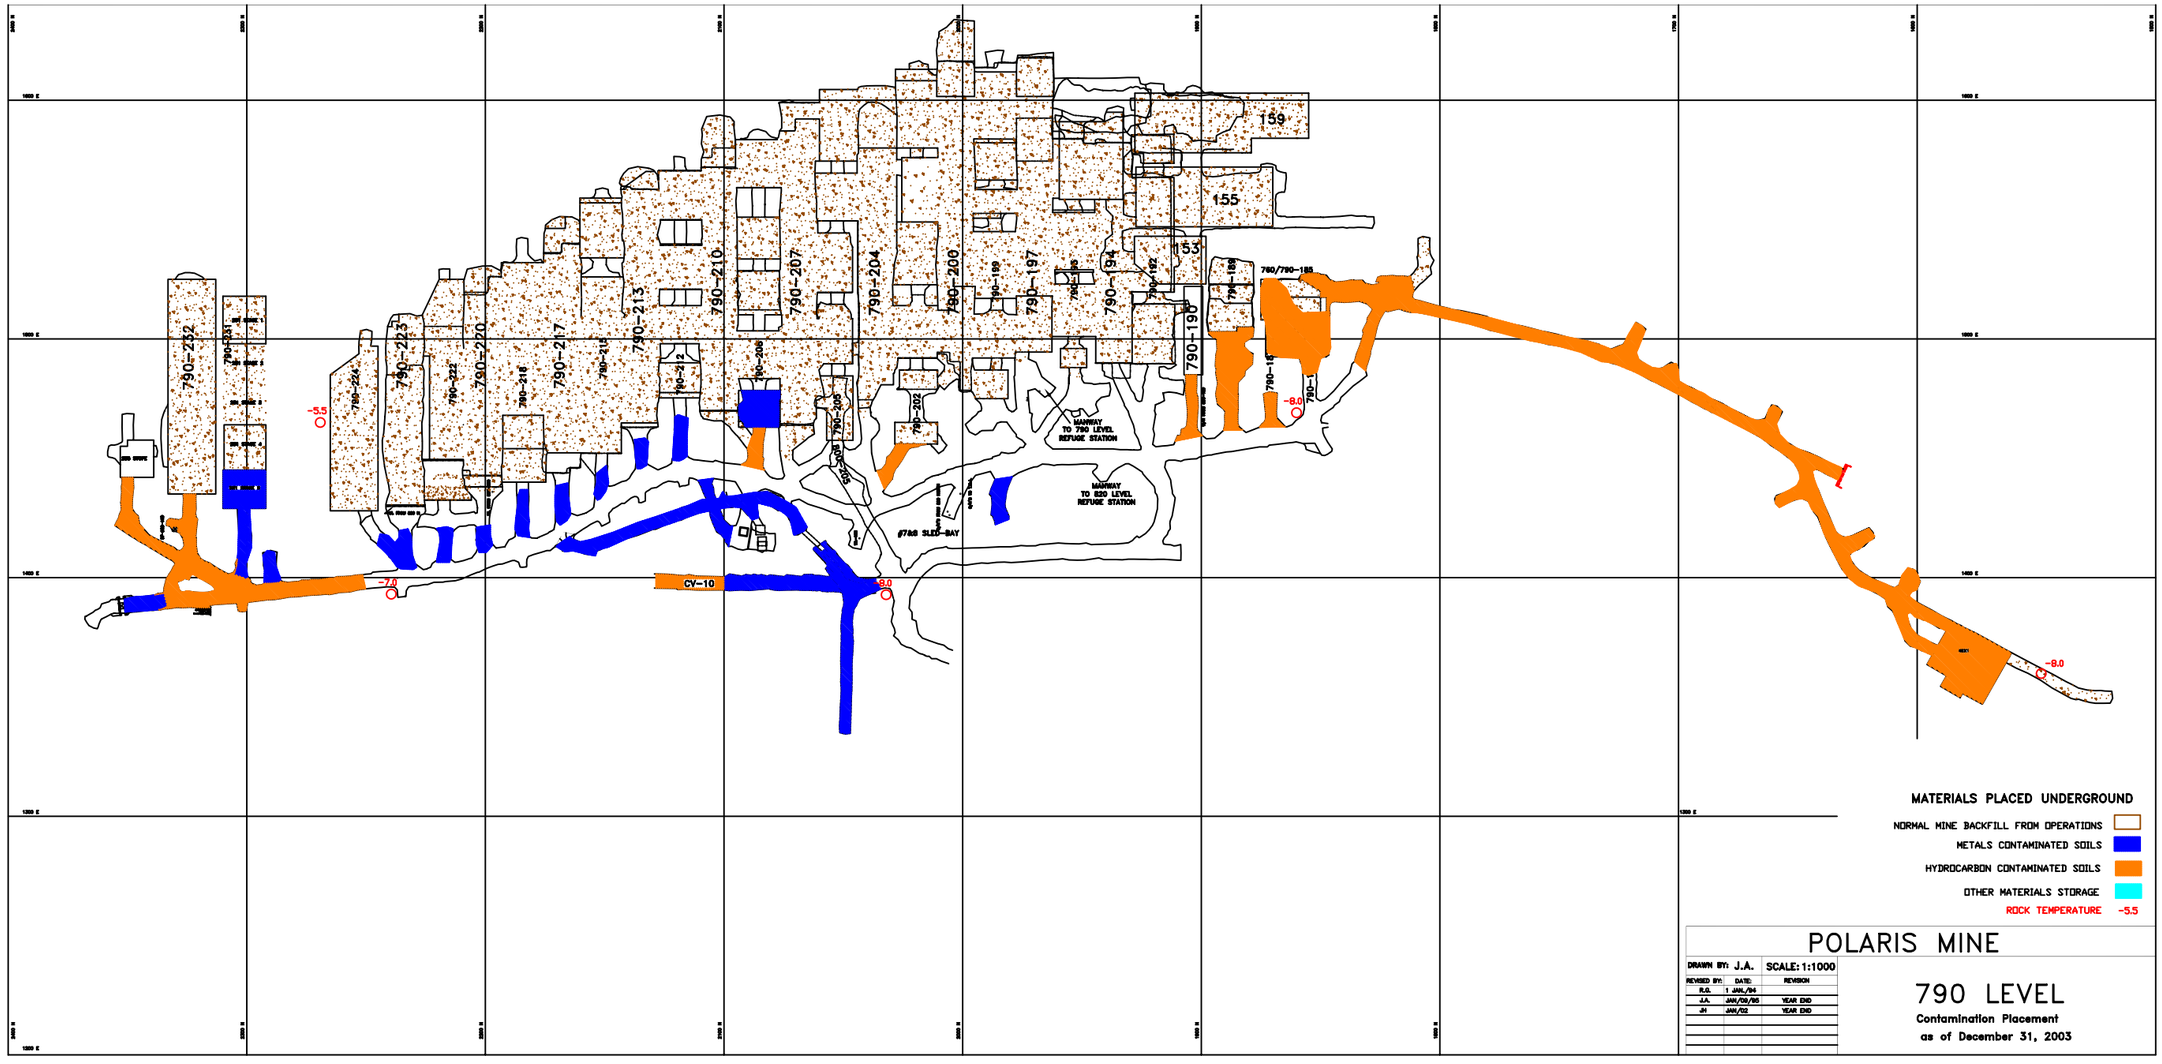


POLARIS MINE


DRAWN BY: J.A. | SCALE: 1:1000

REVISED BY:	DATE:	REVISION
R.G.	1 JAN./04	
J.A.	JAN/03/03	YEAR END
JH	JAN/02	YEAR END

790 LEVEL

Contamination Placement
as of December 31, 2003

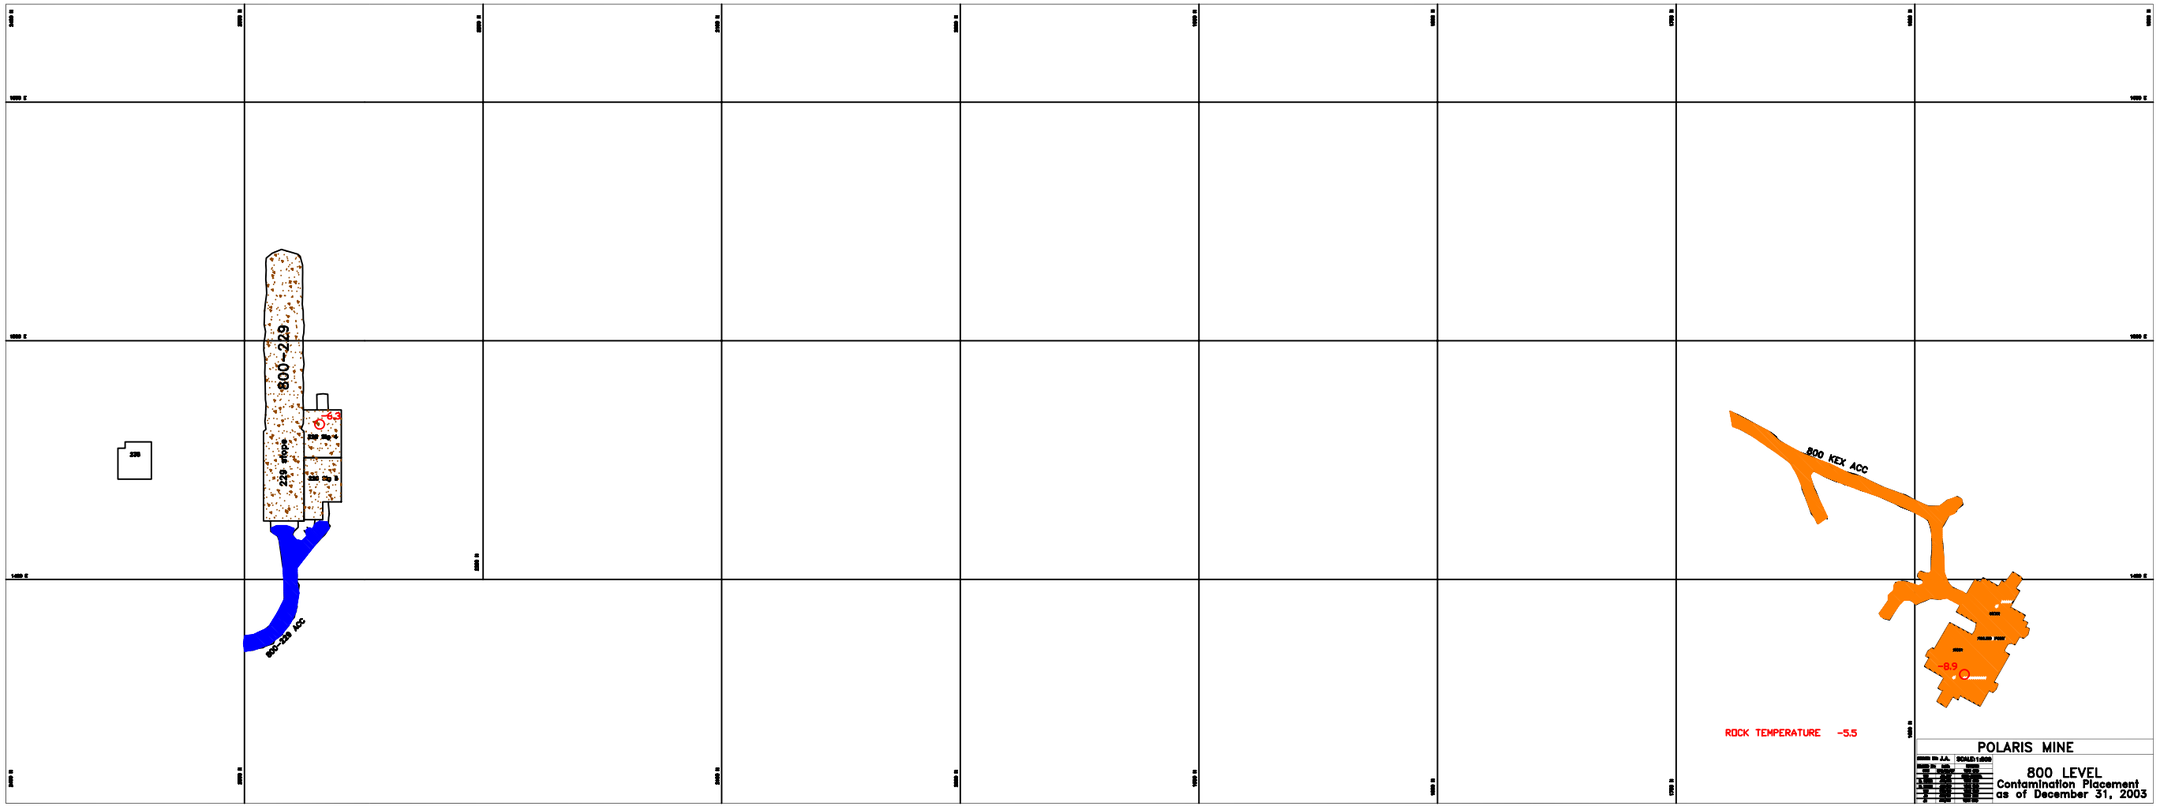
800-229
229 stope
800-229 ACC
800 KEX ACC
-8.9
ROCK TEMPERATURE -5.5
POLARIS MINE
800 LEVEL
Contamination Placement
as of December 31, 2003

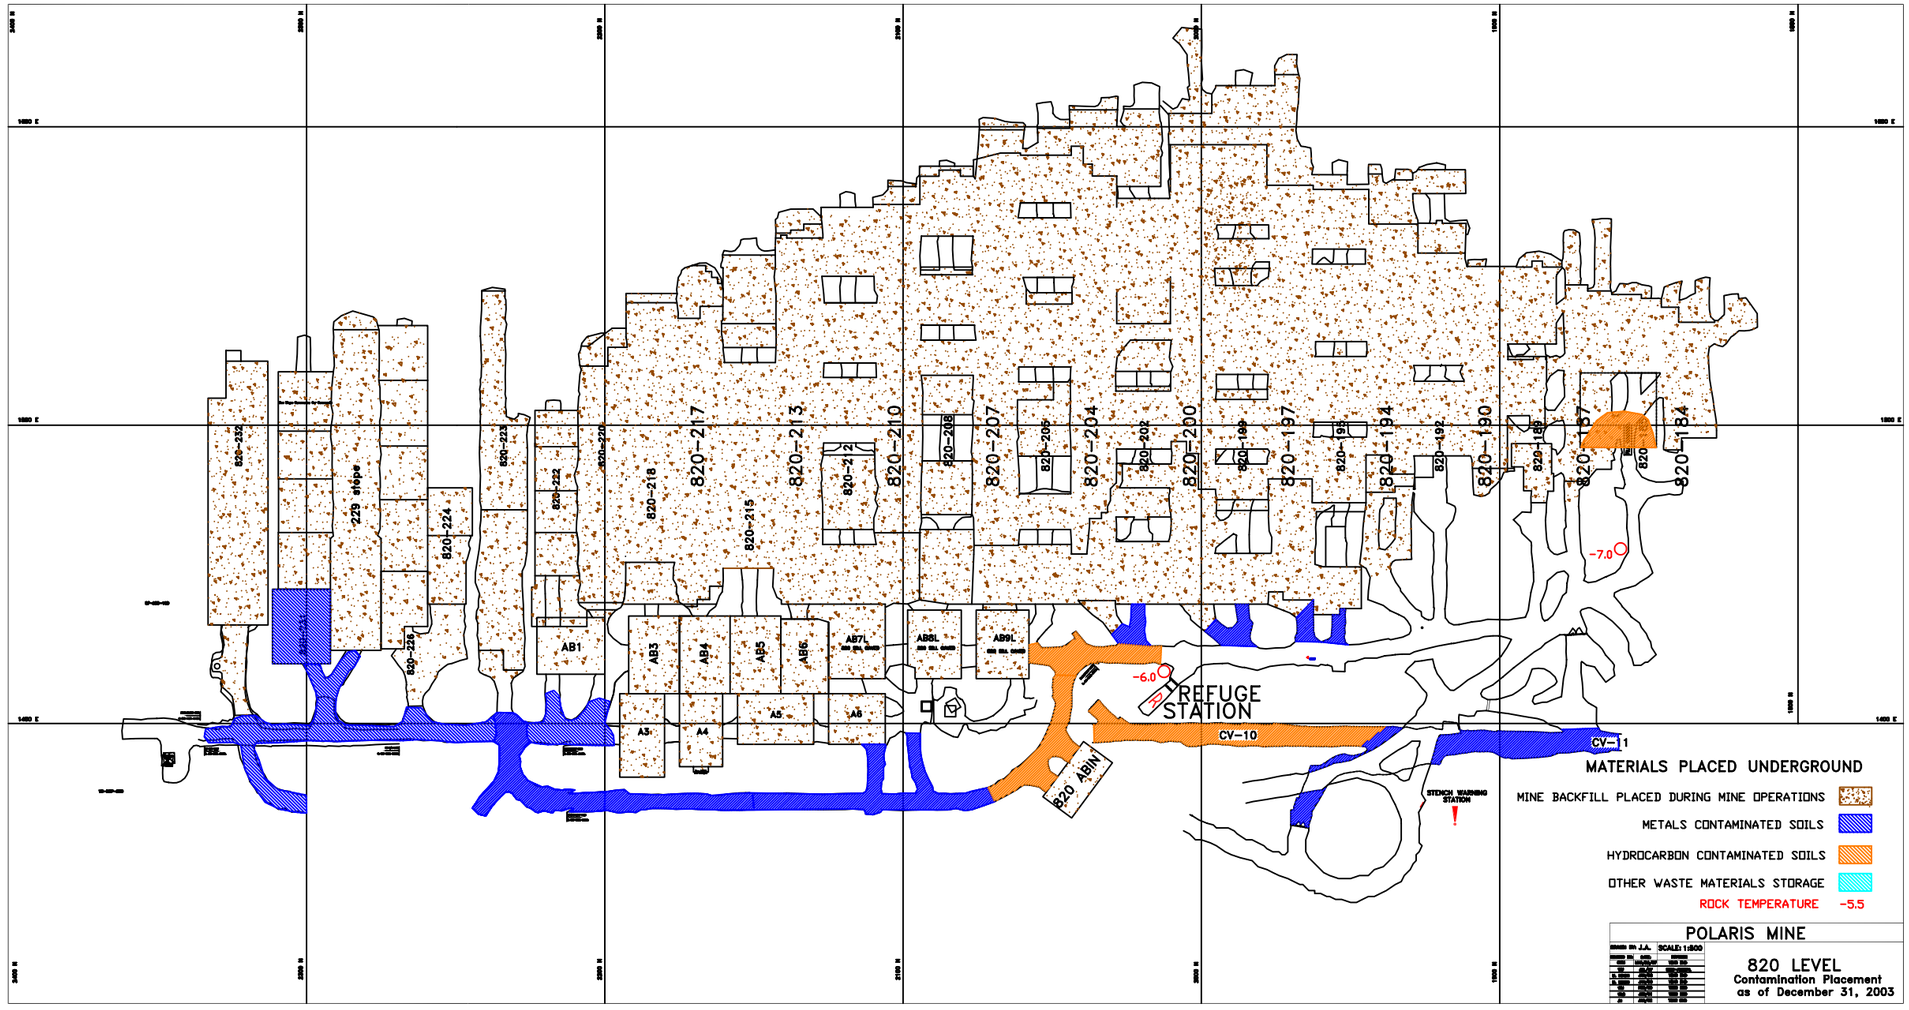
820-232
229 stope
820-224
820-225
820-223
820-222
820-220
820-218
820-217
820-215
820-213
820-212
820-210
820-208
820-207
820-205
820-204
820-202
820-200
820-199
820-197
820-195
820-194
820-192
820-190
820-188
820-187
820-185
820-184
AB1
AB3
AB4
AB5
AB6
AB7L
AB8L
AB9L
A3
A4
A5
A6
-7.0
-6.0
REFUGE STATION
CV-10
CV-11
820 ABIN
STENCH WARNING STATION
MATERIALS PLACED UNDERGROUND
MINE BACKFILL PLACED DURING MINE OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER WASTE MATERIALS STORAGE
ROCK TEMPERATURE -5.5
POLARIS MINE
820 LEVEL
Contamination Placement
as of December 31, 2003

850 NORTH LEVEL

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

ROCK TEMPERATURE -5.5

POLARIS MINE

850 LEVEL SOUTH

Contamination Placement

as of December 31, 2003

Mak Parts
Pump
Compressor
Hydraulic Pack

880-145

880-142

880-141

880-139

880-137

880-135

880 DUMP

NP-231

NP-229

NP-227

NP-142

NP-140

880-223

880-220

880-217

880-213

880-210

880-207

880-204

880-200

880-197

880-194

880-190

880-187

880-184

880-181

880-178

A STOPE

A/B UNDERCUT

B STOPE

B/C UNDERCUT

AB1 AB2 AB3 AB4 AB5 AB6 AB7 AB8 AB9 AB10 AB11 AB12 AB13 AB14 AB15 AB16 AB17 AB19 AB20

105-7

105-6

Tires, Steel
& Pallets

Tailings Lines

SLED-BAY

LADDER UP TO
REFUGE STATION

REFUGE STATION
NEXT RIGHT

125W

880-124W

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

ROCK TEMPERATURE -5.5

POLARIS MINE

880 LEVEL SOUTH
Contamination Placement
as of December 31, 2003

MATERIALS PLACED UNDERGROUND

MINE BACKFILL PLACED DURING MINE OPERATIONS

METALS CONTAMINATED SOILS

HYDROCARBON CONTAMINATED SOILS

OTHER WASTE MATERIALS STORAGE

ROCK TEMPERATURE -5.5


POLARIS MINE

DRAWN BY: J.A. SCALE:1:1000

REVISED BY:	DATE	REVISION
R.A.	1 JAN./04	
J.A.	JAN./05/05	YEAR END

885 LEVEL

Contamination Placement as of December 31, 2003

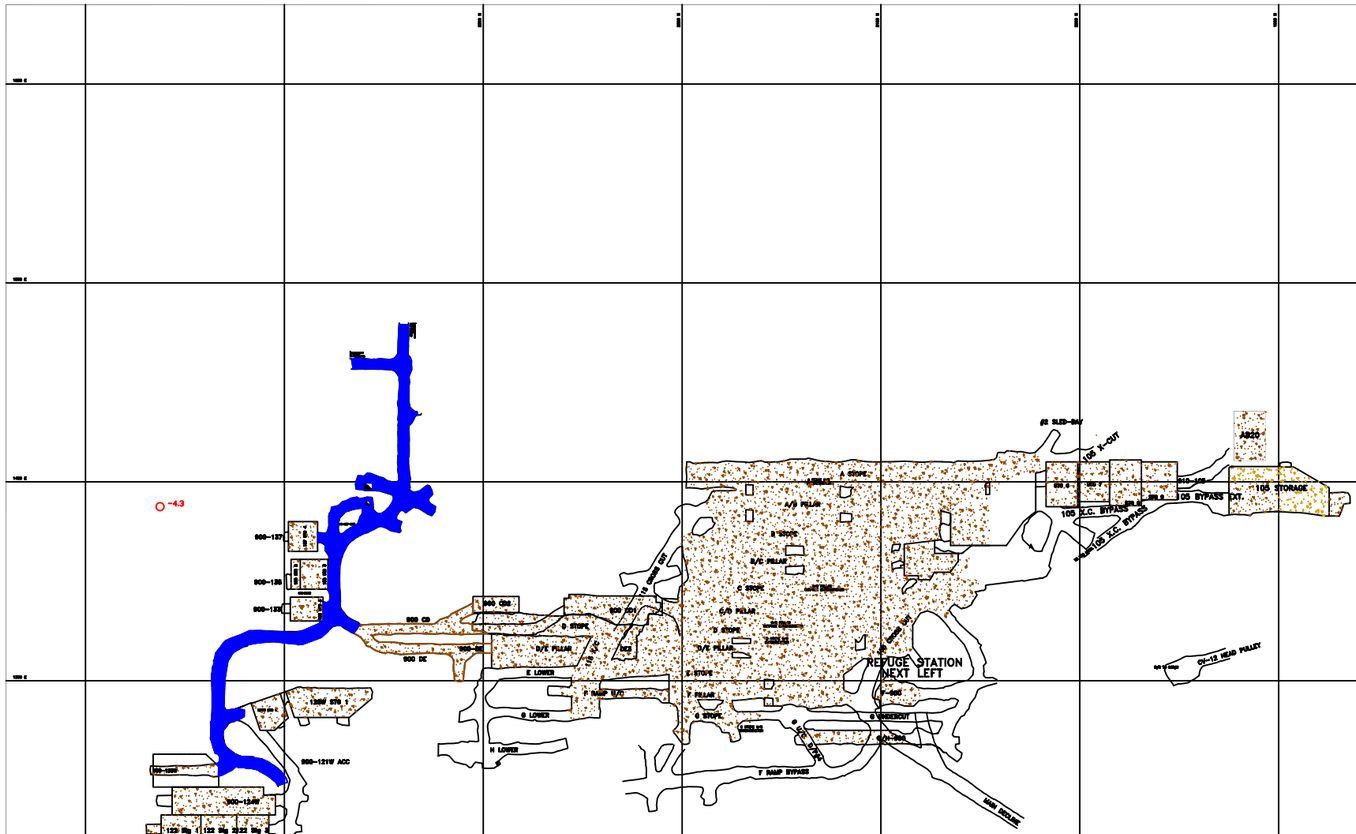

MATERIALS PLACED UNDERGROUND

- MINE BACKFILL PLACED DURING MINE OPERATIONS
- METALS CONTAMINATED SOILS
- HYDROCARBON CONTAMINATED SOILS
- OTHER WASTE MATERIALS STORAGE

ROCK TEMPERATURE -5.5


POLARIS MINE


DRAWN BY: J.A. SCALE: 1:1000


J.A.	2005/09/09	1000 ORE
JH	2005/12	1000 ORE


900 LEVEL

Contamination Placement
as of December 31, 2005

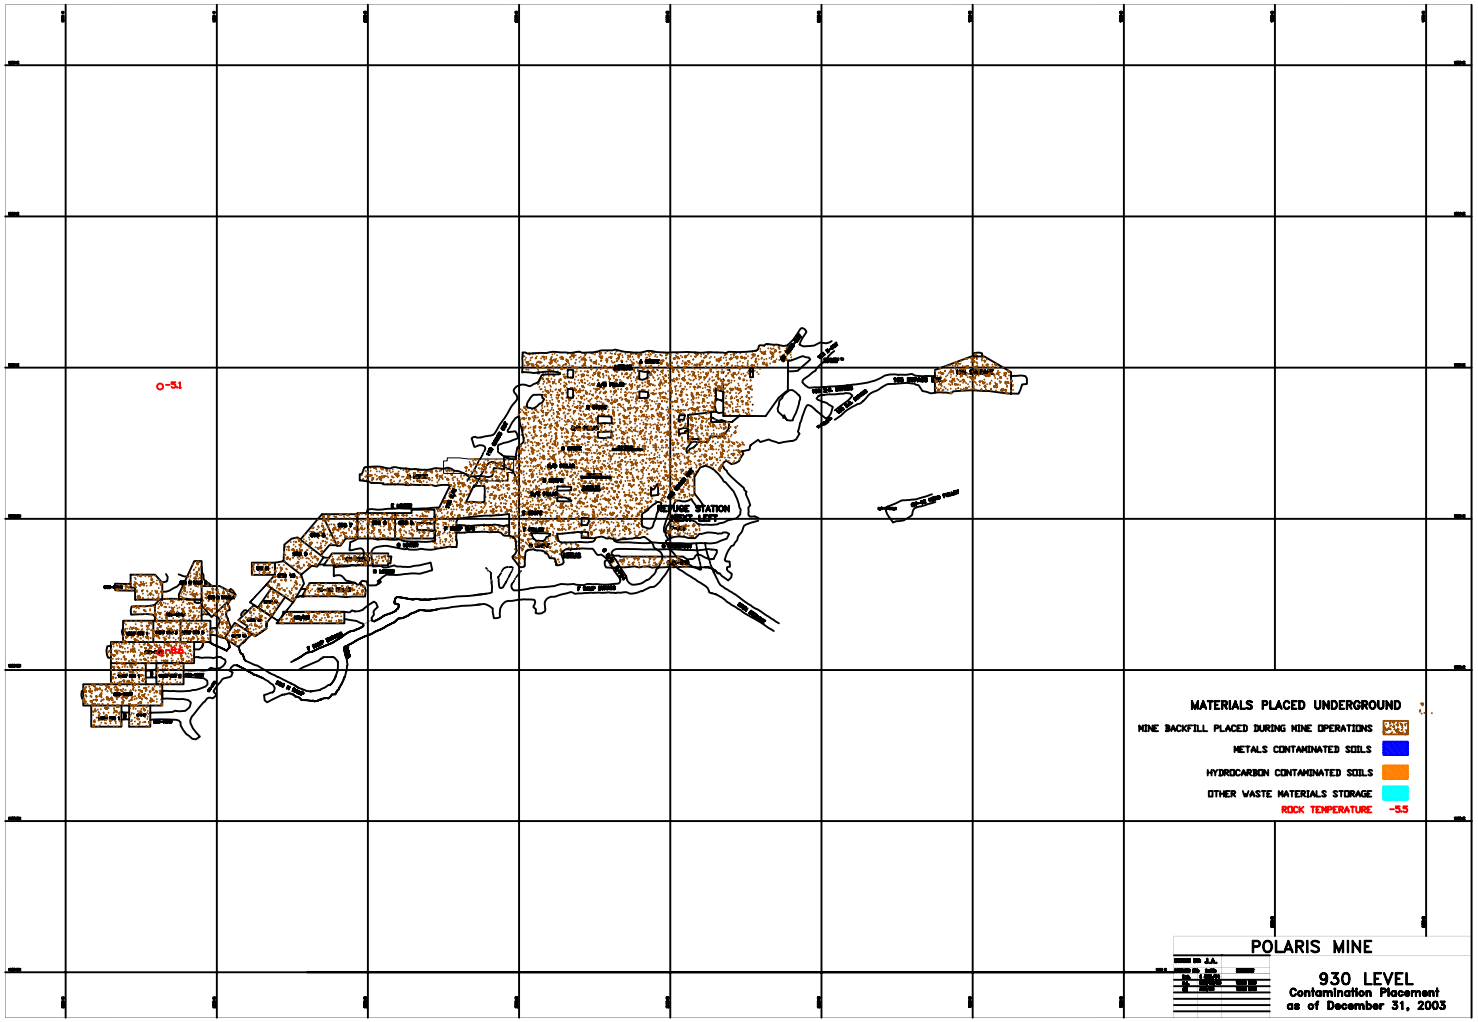
MATERIALS PLACED UNDERGROUND
MINE BACKFILL PLACED DURING MINE OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER WASTE MATERIALS STORAGE
ROCK TEMPERATURE -5.5
POLARIS MINE
930 LEVEL
Contamination Placement
as of December 31, 2003

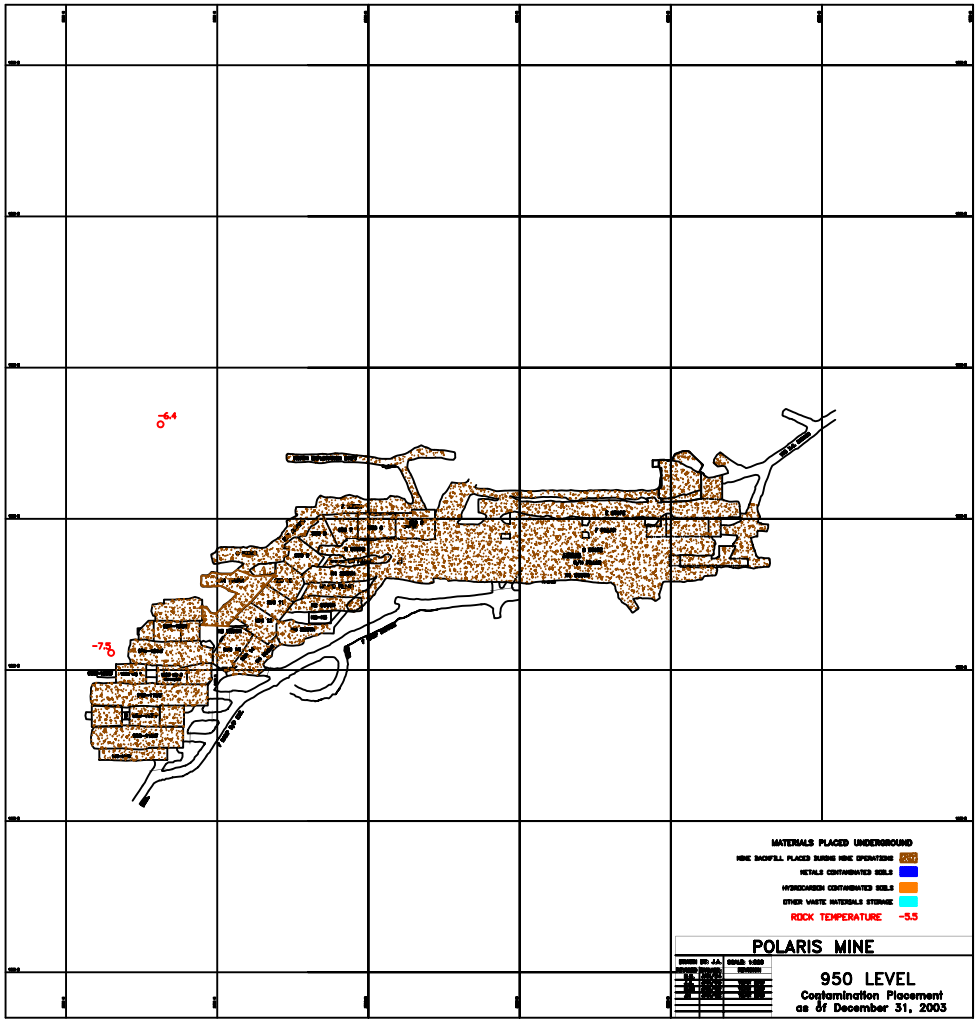
-6.4
-7.5
MATERIALS PLACED UNDERGROUND
MINE BACKFILL PLACED DURING MINE OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER WASTE MATERIALS STORAGE
ROCK TEMPERATURE -5.5
POLARIS MINE
950 LEVEL
Contamination Placement
as of December 31, 2003

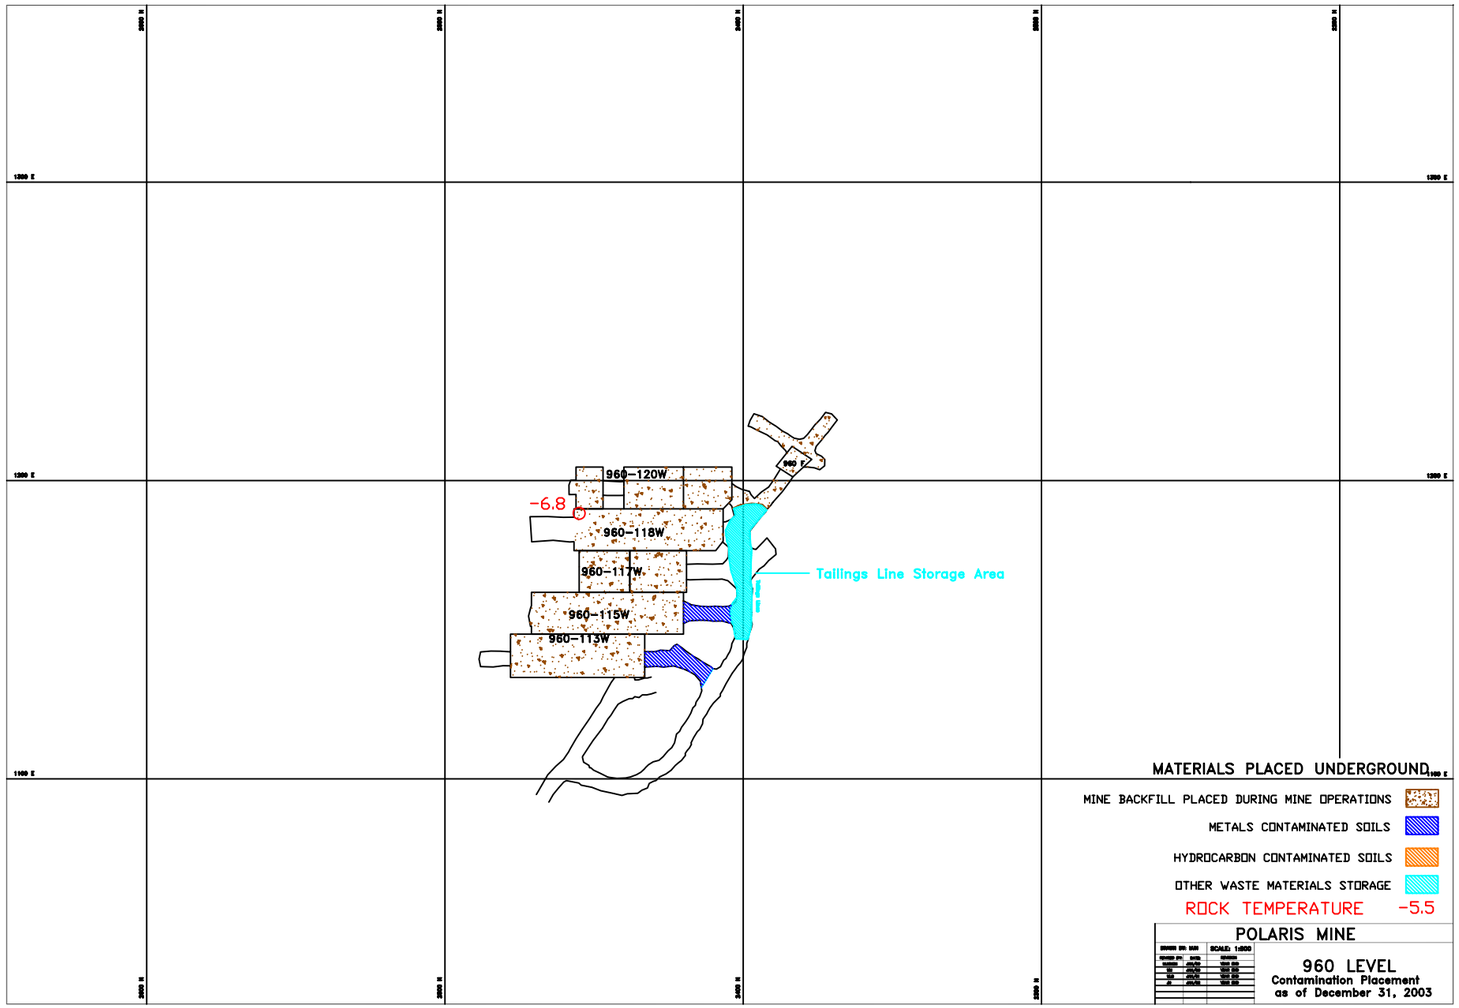
960-120W
960-118W
960-117W
960-115W
960-113W
-6.8
Tailings Line Storage Area
MATERIALS PLACED UNDERGROUND
MINE BACKFILL PLACED DURING MINE OPERATIONS
METALS CONTAMINATED SOILS
HYDROCARBON CONTAMINATED SOILS
OTHER WASTE MATERIALS STORAGE
ROCK TEMPERATURE -5.5
POLARIS MINE
960 LEVEL
Contamination Placement
as of December 31, 2003

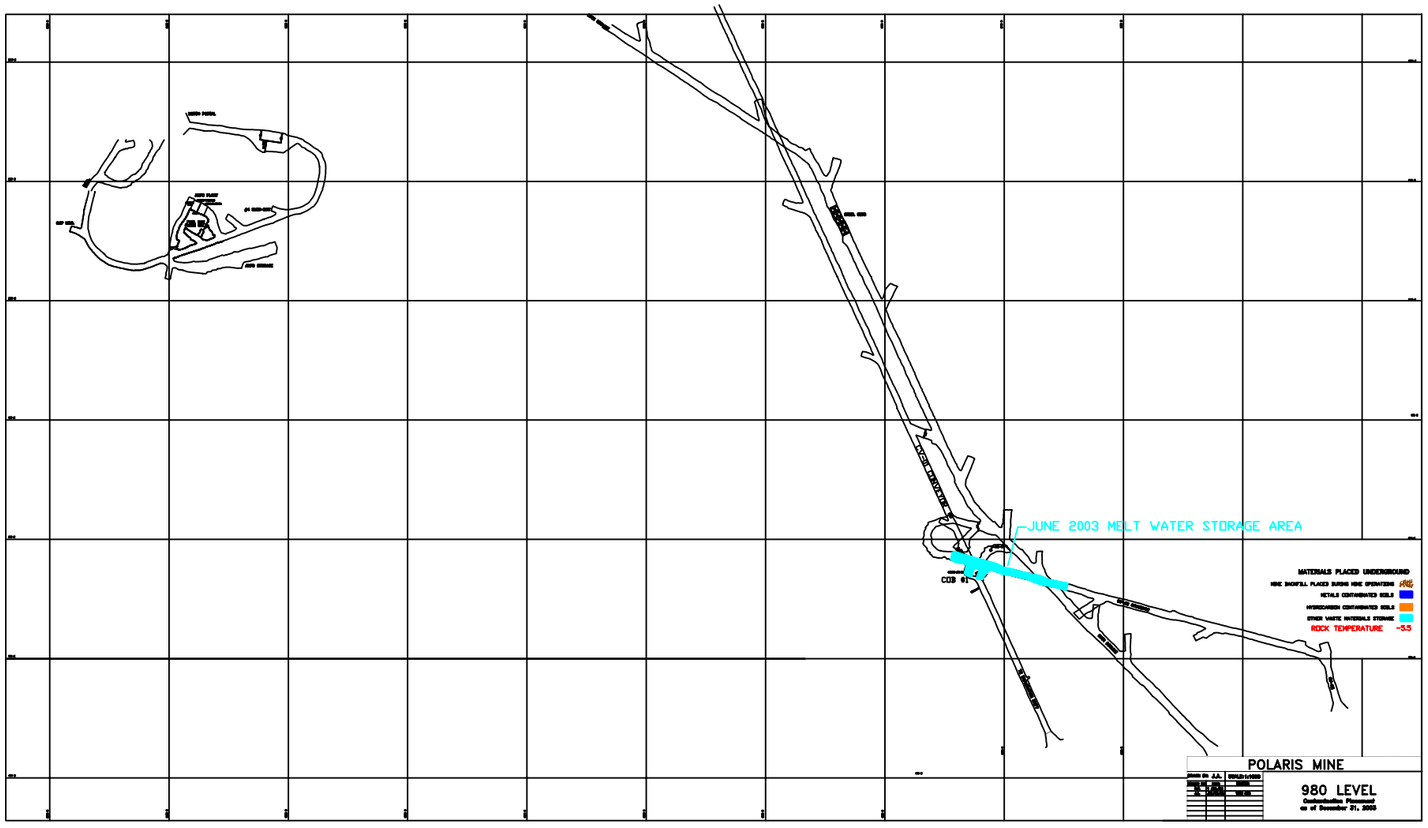
JUNE 2003 MELT WATER STORAGE AREA
CCB 91
MATERIALS PLACED UNDERGROUND
ROCK TEMPERATURE -3.5
POLARIS MINE
980 LEVEL
Condemnation Placement
as of December 31, 2003

APPENDIX 13

GARROW LAKE EROSION MONITORING

2004 GARROW LAKE EROSION MONITORING PINS

The data recorded in the attached table for the Erosion monitoring pin at Station 10 on July 17, 2004 is incorrect. Not sure whether the wrong pin was measured or if the data was just incorrectly recorded.

However, there is sufficient data to compare 2004 data to 2003 data. There is no sign of erosion at any of the locations being monitored.

There were no pictures or measurements of the erosion pins taken in either June or September due to snow conditions around the lake.

GARROW LAKE EROSION MONITORING PINS

Month	Distance (cm) - Top of Pin to Ground				Photographs Taken
	Stn. 8	Stn. 9	Stn. 10	Stn. 11	
Jul-03	56.5	45	61.5	50	Yes
Aug-03	56.5	45	61.5	50	Yes
Sep-03	56.5	44	61	50	Yes
Jun-04	n.a.	n.a.	n.a.	n.a.	No
17-Jul-04	57.0	n.a.	17.5	50.7	Yes (2 only)
18-Aug-04	56.5	45.1	61.5	50.7	Yes
Sep-04	n.a.	n.a.	n.a.	n.a.	No

Station # 8 - Garrow Lake North Quadrant
Station # 9 - Garrow Lake East Quadrant
Station # 10 - Garrow Lake South Quadrant
Station # 11 - Garrow Lake West Quadrant

Note 1 - distance measured is along the side of the pin (not vertical distance)
Note 2 - "Not Available" - Can not measure pin as either buried in snow or obstructed by ice

JULY 2004 PHOTOGRAPHS



Erosion Pin # 8 – July 17, 2004



Erosion Pin # 11 – July 17, 2004

AUGUST 2004 PHOTOGRRAPHS

-TO BE LOCATED

APPENDIX 14

GARROW CREEK EROSION MONITORING

APPENDIX 15

MARINE SHORELINE MONITORING

APPENDIX 16

GARROW LAKE STRATIGRAPHY MONITORING

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MID-WINTER SAMPLING EVENT - JANUARY 26, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m	<0.00020	<0.00020	0.00057	0.000075	0.00117	<0.010	0.00395	0.00903	<0.000010	<0.0050	0.00373	<0.010	0.236
GL Mid- 4m	0.00024	0.00024	0.000492	0.000064	0.000924	<0.010	0.00193	0.00831	-	<0.0050	0.00319	<0.010	0.197
GL Mid- 5m	<0.00020	<0.00020	0.000513	0.000069	0.00119	<0.010	0.00173	0.00833	-	<0.0050	0.00353	<0.010	0.209
GL Mid- 6m	0.00027	<0.00020	0.000591	0.000069	0.00162	0.018	0.0152	0.00858	-	<0.0050	0.00346	<0.010	0.207
GL Mid- 7m	0.00036	0.00029	0.000493	0.000061	0.000976	<0.010	0.000794	0.00819	-	<0.0050	0.00341	<0.010	0.197
GL Mid- 8m	0.00024	<0.00020	0.00048	0.00006	0.000983	<0.010	0.000447	0.00806	-	<0.0050	0.0033	<0.010	0.189
GL Mid- 9m	0.00027	<0.00020	0.00194	0.000098	0.00191	<0.010	0.000667	0.0199	-	<0.0050	0.0064	<0.010	0.702
GL Mid- 10m	0.00051	0.00039	0.00231	0.000265	0.00351	<0.010	0.00151	0.0753	<0.000010	<0.0050	0.0082	<0.010	0.932
GL Mid- 11m	0.00097	0.0004	0.00021	0.000816	0.00177	0.082	0.00246	0.0961	-	0.006	0.00821	<0.010	0.279
GL Mid- 12m	0.00094	0.00055	0.000217	0.000712	0.00315	0.108	0.0071	0.0944	-	0.0072	0.00862	<0.010	0.27
GL Mid- 13m	0.00096	0.0007	0.00021	0.000518	0.00297	0.095	0.0117	0.0827	-	0.0066	0.00826	<0.010	0.251
GL Mid- 14m	0.00105	0.00035	0.000143	0.000452	0.00273	0.104	0.00534	0.0827	-	0.0066	0.00875	<0.010	0.229
GL Mid- 15m	0.00095	0.0008	0.000094	0.00039	0.00165	0.186	0.00347	0.0825	-	0.0068	0.00847	<0.010	0.256
GL Mid- 16m	0.00081	0.00069	0.000082	0.000402	0.00143	0.211	0.00255	0.0857	-	0.0073	0.00896	<0.010	0.265
GL Mid- 17m	0.00092	0.00061	0.000086	0.000403	0.0014	0.214	0.00284	0.0848	-	0.0068	0.00893	<0.010	0.267
GL Mid- 18m	0.00078	0.00074	0.000084	0.000415	0.00151	0.225	0.003	0.086	-	0.0064	0.00922	<0.010	0.275
GL Mid- 19m	0.00084	0.00083	0.0001	0.000387	0.00144	0.217	0.00308	0.0832	-	0.0071	0.00879	<0.010	0.266
GL Mid- 20m	0.00082	0.00086	0.000081	0.000383	0.00151	0.219	0.00308	0.0844	-	0.0063	0.00866	<0.010	0.26
GL Mid- 22m	0.00087	0.00082	0.00009	0.000428	0.00167	0.236	0.0051	0.0881	-	0.0068	0.00968	<0.010	0.26
GL Mid- 30m	0.00024	0.00034	0.000076	0.00035	0.000844	0.333	0.00317	0.0861	-	0.0059	0.00862	<0.010	0.0514
GL Mid- 40m	0.00028	<0.00020	0.000552	0.00008	0.00127	0.014	0.00558	0.00966	-	<0.0050	0.00361	<0.010	0.234

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to Ice can not sample the top 2 metres

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m	<0.00020	0.00026	0.000638	0.000066	0.00112	0.012	0.00318	0.0103	<0.000010	<0.0050	0.00362	<0.010	0.234
GL Mid- 4m	<0.00020	<0.00020	0.000741	0.000073	0.00125	0.026	0.0135	0.0112	-	<0.0050	0.00382	<0.010	0.227
GL Mid- 5m	<0.00020	<0.00020	0.000608	0.000078	0.00102	0.01	0.00144	0.00975	-	<0.0050	0.00378	<0.010	0.247
GL Mid- 6m	<0.00020	<0.00020	0.000617	0.000066	0.00102	<0.010	0.00168	0.00957	-	<0.0050	0.00385	<0.010	0.229
GL Mid- 7m	<0.00020	0.00027	0.0006	0.000064	0.000985	0.039	0.0015	0.00969	-	<0.0050	0.00357	<0.010	0.227
GL Mid- 8m	<0.00020	<0.00020	0.000641	0.000071	0.000969	0.023	0.000926	0.00956	-	<0.0050	0.00363	<0.010	0.231
GL Mid- 9m	<0.00020	0.00028	0.00255	0.000153	0.00225	<0.010	0.0012	0.0209	-	<0.0050	0.00706	<0.010	0.816
GL Mid- 10m	0.00049	0.00039	0.00217	0.000386	0.00329	<0.010	0.00456	0.0898	0.000012	<0.0050	0.00735	<0.010	0.764
GL Mid- 11m	0.00087	0.0005	0.000261	0.00092	0.00163	0.136	0.00481	0.107	-	<0.0050	0.0083	<0.010	0.315
GL Mid- 12m	0.00096	0.00046	0.000207	0.000751	0.00218	0.173	0.00682	0.0971	-	<0.0050	0.00821	<0.010	0.262
GL Mid- 13m	0.00093	0.00044	0.000199	0.000614	0.00248	0.17	0.00861	0.0884	-	0.005	0.00831	<0.010	0.234
GL Mid- 14m	0.00068	0.00072	0.000151	0.00046	0.00193	0.203	0.00645	0.0878	-	0.0062	0.00854	<0.010	0.211
GL Mid- 15m	0.0006	0.00061	0.000078	0.000433	0.0012	0.27	0.00247	0.0903	-	0.0052	0.00914	<0.010	0.211
GL MId- 16m	0.00074	0.0006	0.000079	0.000431	0.0012	0.257	0.00279	0.0876	-	<0.0050	0.00875	<0.010	0.201
GL Mid- 17m	0.00064	0.00065	0.000075	0.000416	0.00127	0.25	0.00338	0.086	-	0.0053	0.00878	<0.010	0.193
GL Mid- 18m	0.0006	0.00059	0.000074	0.000428	0.00113	0.257	0.00269	0.0855	-	0.005	0.00887	<0.010	0.204
GL Mid- 19m	0.00074	0.0006	0.000074	0.000424	0.00113	0.267	0.00241	0.0852	-	<0.0050	0.00897	<0.010	0.202
GL Mid- 20m	0.00067	0.00067	0.000072	0.000415	0.0011	0.252	0.00244	0.0833	-	<0.0050	0.00873	<0.010	0.197
GL Mid- 22m	0.0007	0.00061	0.000081	0.000431	0.00113	0.258	0.00235	0.0862	-	<0.0050	0.00887	<0.010	0.199
GL Mid- 30m	<0.00020	0.00039	0.000082	0.000381	0.00103	0.382	0.00902	0.0841	-	<0.0050	0.00781	<0.010	0.117
GL Mid- 40m	<0.00020	<0.00020	0.000034	0.000129	0.00135	0.486	0.00124	0.0473	-	<0.0050	0.000892	<0.010	0.0301

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MINIMUM ICE THICKNESS SAMPLING EVENT - 2004

NOT ABLE TO DO AS ICE DID NOT LEAVE LAKE, COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m													
GL Mid- 4m													
GL Mid- 5m													
GL Mid- 6m													
GL Mid- 7m													
GL Mid- 8m													
GL Mid- 9m													
GL Mid- 10m													
GL Mid- 11m													
GL Mid- 12m													
GL Mid- 13m													
GL Mid- 14m													
GL Mid- 15m													
GL Mid- 16m													
GL Mid- 17m													
GL Mid- 18m													
GL Mid- 19m													
GL Mid- 20m													
GL Mid- 22m													
GL Mid- 30m													
GL Mid- 40m													

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

GARROW LAKE - STATION 262-3 Continued
MID WINTER SAMPLING EVENT - JANUARY 26, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m	-	7.2	<3.0	<0.0050
GL Mid- 4m	<0.020	7.4	<3.0	-
GL Mid- 5m	-	7.5	4	-
GL Mid- 6m	-	7.6	4.7	-
GL Mid- 7m	-	7.6	<3.0	-
GL Mid- 8m	<0.020	7.6	<3.0	-
GL Mid- 9m	-	24.4	7.1	-
GL Mid- 10m	-	49.6	4.7	0.0092
GL Mid- 11m	-	61.5	8.7	-
GL Mid- 12m	<0.020	61.8	5.8	-
GL Mid- 13m	-	59.2	18	-
GL Mid- 14m	-	62	20.7	-
GL Mid- 15m	-	62	21.3	-
GL Mid- 16m	<0.020	61.8	18.7	-
GL Mid- 17m	-	61.9	20.8	-
GL Mid- 18m	-	62	24.7	-
GL Mid- 19m	-	61.2	20.7	-
GL Mid- 20m	<0.020	62	26	-
GL Mid- 22m	-	62.2	36	-
GL Mid- 30m	-	62.6	24	-
GL Mid- 40m	0.021	7.3	7.3	-

Footnotes:

1. Data for TSS is believed to be incorrect. Believe that the laboratory did not rinse the salt off the filter paper. This will overstate TSS values.
2. Data for Density for GL Mid-40m is incorrect for

as this number is physically impossible.

GARROW LAKE - STATION 262-3 Continued
MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m	-	8.1	3	<0.0050
GL Mid- 4m	-	8.2	<3.0	-
GL Mid- 5m	-	8.3	<3.0	-
GL Mid- 6m	-	8.2	6.3	-
GL Mid- 7m	-	8.2	4.3	-
GL Mid- 8m	-	8.1	5.7	-
GL Mid- 9m	-	24.5	9.7	-
GL Mid- 10m	<0.020	55	23	0.0098
GL Mid- 11m	-	62.4	20.3	-
GL Mid- 12m	-	63.1	17.6	-
GL Mid- 13m	-	62.8	25.7	-
GL Mid- 14m	0.03	63.3	5.3	-
GL Mid- 15m	-	63.6	20.3	-
GL Mid- 16m	-	63.7	22.3	-
GL Mid- 17m	0.027	63.8	21.7	-
GL Mid- 18m	-	64.2	19.7	-
GL Mid- 19m	-	64.2	20.3	-
GL Mid- 20m	0.022	63.7	31	-
GL Mid- 22m	-	63.5	38.3	-
GL Mid- 30m	-	63.5	23	-
GL Mid- 40m	0.034	64.1	26.3	-

Footnotes:

Data for TSS is believed to be incorrect. Believe that the laboratory did not rinse the salt off the filter paper. This will overstate TSS values.

GARROW LAKE - STATION 262-3 Continued
MINIMUM ICE THICKNESS SAMPLING EVENT - 2004
COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m				
GL Mid- 4m				
GL Mid- 5m				
GL Mid- 6m				
GL Mid- 7m				
GL Mid- 8m				
GL Mid- 9m				
GL Mid- 10m				
GL Mid- 11m				
GL Mid- 12m				
GL Mid- 13m				
GL Mid- 14m				
GL Mid- 15m				
GL Mid- 16m				
GL Mid- 17m				
GL Mid- 18m				
GL Mid- 19m				
GL Mid- 20m				
GL Mid- 22m				
GL Mid- 30m				
GL Mid- 40m				

Footnotes:

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MID-WINTER SAMPLING EVENT - JANUARY 27, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m	0.00021	<0.00020	0.000526	0.000077	0.00108	<0.010	0.000943	0.00927	<0.000010	<0.0050	0.00366	<0.010	0.223
GL South- 4m	0.0003	<0.00020	0.000531	0.000068	0.000966	<0.010	0.00232	0.00935	-	<0.0050	0.00358	<0.010	0.211
GL South- 5m	<0.00020	<0.00020	0.000537	0.000074	0.000936	<0.010	0.000361	0.00913	-	<0.0050	0.00367	<0.010	0.223
GL South- 6m	0.00028	<0.00020	0.000518	0.000066	0.000932	<0.010	0.000483	0.00924	-	<0.0050	0.00336	<0.010	0.202
GL South- 7m	0.00025	<0.00020	0.000522	0.000067	0.000916	<0.010	0.000325	0.00906	-	<0.0050	0.00361	<0.010	0.208
GL South- 8m	0.00026	<0.00020	0.000531	0.000075	0.000884	<0.010	0.000414	0.00935	-	<0.0050	0.00375	<0.010	0.223
GL South- 9m	0.00032	<0.00020	0.00267	0.000113	0.00277	<0.010	0.000715	0.0231	-	<0.0050	0.0084	<0.010	1
GL South- 10m	0.00085	0.00054	0.000491	0.000854	0.00238	0.011	0.00145	0.13	0.000011	0.0062	0.00802	<0.010	0.423
GL South- 11m	0.00093	0.00034	0.000216	0.000865	0.00184	0.123	0.00216	0.111	-	0.0063	0.00876	<0.010	0.308
GL South- 12m	0.00098	0.00044	0.000216	0.000724	0.00283	0.13	0.00639	0.102	-	0.0079	0.00873	<0.010	0.297
GL South- 13m	0.00107	0.0003	0.000191	0.000543	0.00318	0.114	0.00737	0.0967	-	0.0076	0.00812	<0.010	0.238
GL South- 14m	0.00102	0.00056	0.000158	0.000503	0.0027	0.115	0.00602	0.0953	-	0.0074	0.00879	<0.010	0.241
GL South- 15m	0.00086	0.00068	0.000106	0.000436	0.00193	0.199	0.00347	0.0865	-	0.0061	0.00916	<0.010	0.261
GL South- 16m	0.00086	0.00079	0.000092	0.000412	0.00167	0.232	0.00265	0.0948	-	0.0059	0.00912	<0.010	0.27
GL South- 17m	0.00087	0.00088	0.000089	0.000399	0.00158	0.232	0.00261	0.0945	-	0.0078	0.00914	<0.010	0.272
GL South- 18m	0.00068	0.00053	0.000101	0.000377	0.00168	0.228	0.00267	0.0928	-	0.0067	0.0089	<0.010	0.265
GL South- 19m	0.00093	0.00071	0.000084	0.000394	0.00162	0.233	0.00287	0.0944	-	0.0071	0.00917	<0.010	0.263
GL South- 20m	0.00072	0.00059	0.000084	0.000409	0.00157	0.229	0.00283	0.0937	-	0.0074	0.00924	<0.010	0.266
GL South- 22m	0.00082	0.00078	0.000083	0.000417	0.00159	0.23	0.0027	0.0932	-	0.0071	0.00939	<0.010	0.267
GL South- 30m	0.00036	0.00025	0.000071	0.000362	0.000929	0.31	0.00258	0.0948	-	0.0076	0.00879	<0.010	0.076
GL South- 40m	0.00036	0.00044	0.000083	0.000375	0.00117	0.307	0.00261	0.0964	-	0.0059	0.00923	<0.010	0.0747

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m	<0.00020	<0.00020	0.000598	0.000066	0.00108	<0.010	0.000571	0.00965	<0.000010	<0.0050	0.00379	<0.010	0.232
GL South- 4m	<0.00020	<0.00020	0.000615	0.000112	0.000963	<0.010	0.000322	0.00994	-	<0.0050	0.00375	<0.010	0.23
GL South- 5m	<0.00020	<0.00020	0.000636	0.000076	0.00105	0.011	0.000517	0.0103	-	<0.0050	0.00404	<0.010	0.25
GL South- 6m	<0.00020	<0.00020	0.000628	0.000137	0.00104	<0.010	0.000226	0.00971	-	<0.0050	0.00398	<0.010	0.24
GL South- 7m	<0.00020	<0.00020	0.000668	0.000081	0.00127	0.025	0.00289	0.0106	-	<0.0050	0.00409	<0.010	0.252
GL South- 8m	<0.00020	0.00027	0.000628	0.000123	0.00125	0.012	0.000423	0.00983	-	<0.0050	0.00397	<0.010	0.228
GL South- 9m	<0.00020	<0.00020	0.00256	0.000151	0.00231	<0.010	0.000956	0.0238	-	<0.0050	0.00761	<0.010	0.916
GL South- 10m	0.0007	0.00034	0.000983	0.00076	0.00272	0.011	0.00288	0.114	<0.000010	<0.0050	0.00789	<0.010	0.496
GL South- 11m	0.00092	0.00046	0.000246	0.000887	0.00171	0.17	0.0034	0.103	-	<0.0050	0.00858	<0.010	0.3
GL South- 12m	0.00088	0.00035	0.000171	0.00079	0.00213	0.179	0.00384	0.0977	-	<0.0050	0.00894	<0.010	0.283
GL South- 13m	0.00095	0.00035	0.000205	0.000682	0.00255	0.153	0.00627	0.0905	-	0.0058	0.00867	<0.010	0.25
GL South- 14m	0.00081	0.00044	0.000114	0.000485	0.0019	0.198	0.0041	0.0811	-	<0.0050	0.00842	<0.010	0.203
GL South- 15m	0.00067	0.00052	0.000083	0.000402	0.00127	0.245	0.0021	0.0832	-	0.0056	0.00886	<0.010	0.211
GL South- 16m	0.0006	0.00047	0.000083	0.000369	0.00112	0.228	0.00272	0.0785	-	0.005	0.00821	<0.010	0.193
GL South- 17m	0.00074	0.00028	0.000067	0.000423	0.0011	0.214	0.00192	0.0792	-	0.0058	0.00816	<0.010	0.198
GL South- 18m	0.00072	0.00047	0.000074	0.000395	0.00105	0.207	0.00233	0.0845	-	<0.0050	0.00854	<0.010	0.198
GL South- 19m	0.00064	0.0004	0.000071	0.000395	0.00118	0.239	0.00201	0.0832	-	<0.0050	0.00903	<0.010	0.201
GL South- 20m	0.00072	0.00051	0.000074	0.000442	0.00119	0.241	0.00193	0.0834	-	<0.0050	0.00891	<0.010	0.206

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MINIMUM ICE THICKNESS SAMPLING EVENT - 2004

NOT ABLE TO DO AS ICE DID NOT LEAVE LAKE, COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m													
GL South- 4m													
GL South- 5m													
GL South- 6m													
GL South- 7m													
GL South- 8m													
GL South- 9m													
GL South- 10m													
GL South- 11m													
GL South- 12m													
GL South- 13m													
GL South- 14m													
GL South- 15m													
GL South- 16m													
GL South- 17m													
GL South- 18m													
GL South- 19m													
GL South- 20m													
GL South- 22m													
GL South- 30m													
GL South- 40m													

Footnotes: Results are expressed as milligrams per litre except where noted.
< = Less than the detection limit indicated.

GARROW LAKE - STATION 262-3A Continued
MID WINTER SAMPLING EVENT - JANUARY 27, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m	-	7.7	3.3	<0.0050
GL South- 4m	<0.020	7.7	<3.0	-
GL South- 5m	-	7.7	<3.0	-
GL South- 6m	-	7.7	3.3	-
GL South- 7m	-	7.7	<3.0	-
GL South- 8m	<0.020	7.6	<3.0	-
GL South- 9m	-	34.1	5.8	-
GL South- 10m	-	55.9	26.7	0.0098
GL South- 11m	-	62	31.3	-
GL South- 12m	<0.020	62.7	30	-
GL South- 13m	-	62.8	21.3	-
GL South- 14m	-	62.9	33.3	-
GL South- 15m	-	62.6	34	-
GL South- 16m	<0.020	62.7	41.3	-
GL South- 17m	-	61.5	33.3	-
GL South- 18m	-	61	40	-
GL South- 19m	-	62.3	15.3	-
GL South- 20m	<0.020	63	9.1	-
GL South- 22m	-	63.4	17.8	-
GL South- 30m	-	60.6	26	-
GL South- 40m	<0.020	61.7	38	-

Footnotes: Data for TSS is believed to be incorrect. Believe that the laboratory did not rinse the salt off the filter paper. This will overstate TSS values.

GARROW LAKE - STATION 262-3A Continued
MAXIMUM ICE THICNESS SAMPLING EVENT - MAY 3, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m	-	8.2	<3.0	<0.0050
GL South- 4m	-	8.2	<3.0	-
GL South- 5m	-	8.1	<3.0	-
GL South- 6m	-	8.1	<3.0	-
GL South- 7m	-	8.1	<3.0	-
GL South- 8m	-	8.2	<3.0	-
GL South- 9m	-	32.9	7	-
GL South- 10m	<0.020	58.7	23.7	0.0172
GL South- 11m	-	63	35	-
GL South- 12m	-	63.5	25	-
GL South- 13m	-	63.6	16.3	-
GL South- 14m	0.044	63.6	27	-
GL South- 15m	-	11.4	11.4	-
GL South- 16m	-	28.7	28.7	-
GL South- 17m	0.026	27.4	27.4	-
GL South- 18m	-	16.7	16.7	-
GL South- 19m	-	17.4	17.4	-
GL South- 20m	0.025	20.1	20.1	-

Footnotes:

Data for TSS is believed to be incorrect. Believe that the laboratory did not rinse the salt off the filter paper. This will overstate TSS values.

GARROW LAKE - STATION 262-3A Continued
MINIMUM ICE THICNESS SAMPLING EVENT - 2004
COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m				
GL South- 4m				
GL South- 5m				
GL South- 6m				
GL South- 7m				
GL South- 8m				
GL South- 9m				
GL South- 10m				
GL South- 11m				
GL South- 12m				
GL South- 13m				
GL South- 14m				
GL South- 15m				
GL South- 16m				
GL South- 17m				
GL South- 18m				
GL South- 19m				
GL South- 20m				
GL South- 22m				
GL South- 30m				
GL South- 40m				

Footnotes:

GARROW LAKE MONITORING - STATION 262 - 3 (MID LAKE)

	MID WINTER 26-Jan-04				MAXIMUM ICE THICKNESS 03-May-04				MINIMUM ICE THICKNESS Unable to Sample Due to Ice Conditions			
Depth (m)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)
0	-	-	-	-	-	-	-		-	-	-	-
1	-	-	-	-	-	-	-		-	-	-	-
1.5	-	-	-	-	-	-	-		-	-	-	-
2	-	-	-	-	-	-	-		-	-	-	-
3	-0.37	7.7	8.29	14.4								
4	0.38	7.7	9.95	14.09	GLL to supply data - tests were							
5	0.98	7.7	10.87	13.59	conducted as required							
6	1.3	7.7	10.89	13.55								
7	1.85	7.7	10.9	13.05								
8	2.03	7.7	10.9	12.92								
9	2.32	7.7	10.93	12.83								
10	2.49	7.5	10.9	12.74								
11	3.2	7	10.94	11.8								
12	4.03	6.8	12.91	10								
13	5.08	6.8	41.8	6.75								
14	6.59	6.8	63.3	7.18								
15	8.45	6.8	78.5	3.03								
16	8.7	6.8	80.7	2.32								
17	8.8	6.8	81.3	1.86								
18	8.89	6.8	81.4	1.66								
19	8.89	6.8	81.7	1.3								
20	9.05	6.8	82	0.97								
21	9.12	6.8	82.1	0.71								
22	9.12	6.8	82.1	0.62								
23	9.12	6.8	82.1	0.53								
24	9.12	6.8	82.2	0.45								
25	9.12	6.8	82.1	0.4								
26	9.12	6.8	82.1	0.35								
27	9.12	6.7	82.2	0.32								
28	9.12	6.7	82.2	0.28								
29	9.12	6.7	82.2	0.25								
30	9.12	6.7	82.1	0.23								
31	9.12	6.7	82.2	0.21								
32	9.12	6.7	82.2	0.19								
33	9.12	6.7	82.2	0.17								
34	9.12	6.7	82.2	0.15								
35	9.12	6.6	82.2	0.13								
36	9.12	6.6	82.2	0.12								
37	9.12	6.6	82.2	0.11								
38	9.13	6.6	82.5	0.11								
39	9.16	6.6	82.5	0.11								
40	9.25	6.6	83.9	0.1								

GARROW LAKE MONITORING - STATION 262 - 3A (NEAR OUTLET)

	MID WINTER 27-Jan-04				MAXIMUM ICE THICKNESS 03-May-04				MINIMUM ICE THICKNESS Unable to Sample Due to Ice Conditions			
Depth (m)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)	Temp (C)	pH	Conductivity (uS/cm)	Dissolved Oxygen (mg/L)
0	-	-	-	-	-	-	-		-	-	-	-
1	-	-	-	-	-	-	-		-	-	-	-
1.5	-	-	-	-	-	-	-		-	-	-	-
2	-	-	-	-	-	-	-		-	-	-	-
3	-0.3	8.36	12.4	19.2	GLL to supply data - tests were							
4	2.8	8.35	12.5	18.0	conducted as required							
5	3.3	8.34	12.4	17.5								
6	3.3	8.34	12.4	17.5								
7	3.3	8.34	12.5	17.4								
8	3.3	8.32	12.5	16.3								
9	4.1	8.26	13.0	12.4								
10	5.4	7.9	28.1	6.1								
11	6.8	7.56	76.1	0.1								
12	7.8	7.5	80.4	0.1								
13	8.0	7.5	80.6	0.1								
14	8.2	7.49	80.8	0.1								
15	8.3	7.5	80.7	0.1								
16	8.3	7.49	80.7	0.1								
17	8.3	7.49	80.8	0.1								
18	8.3	7.49	80.8	0.1								
19	8.3	7.49	80.8	0.1								
20	8.3	7.48	80.8	0.1								
21	8.3	7.48	80.8	0.1								
22	8.3	7.48	80.8	0.1								
23	8.3	7.48	80.8	0.1								
24	8.3	7.48	80.8	0.1								
25	8.3	7.48	80.9	0.1								
26	8.3	7.47	80.9	0.1								
27	8.4	7.47	80.9	0.1								
28	8.4	7.46	80.9	0.1								
29	8.4	7.46	80.8	0.1								
30	8.4	7.44	80.9	0.1								
31	8.4	7.43	80.9	0.1								
32	8.4	7.43	80.9	0.1								
33	8.4	7.43	80.9	0.1								
34	8.4	7.42	80.9	0.1								
35	8.4	7.41	80.8	0.1								

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MID-WINTER SAMPLING EVENT - JANUARY 26, 2004

	Total Metals Detection Limits (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL Mid- 4m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 5m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 6m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 7m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 8m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 9m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 10m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL Mid- 11m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 12m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 13m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 14m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 15m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 16m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 17m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 18m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 19m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 20m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 22m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 30m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 40m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to Ice can not sample the top 2 metres

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Total Metals Detection Limits (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL Mid- 4m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 5m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 6m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 7m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 8m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 9m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 10m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL Mid- 11m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 12m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 13m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 14m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 15m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL MId- 16m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 17m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 18m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 19m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 20m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 22m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 30m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL Mid- 40m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS

MINIMUM ICE THICKNESS SAMPLING EVENT - 2004

NOT ABLE TO DO AS ICE DID NOT LEAVE LAKE, COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Total Metals Detection Limits (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL Mid- 3m													
GL Mid- 4m													
GL Mid- 5m													
GL Mid- 6m													
GL Mid- 7m													
GL Mid- 8m													
GL Mid- 9m													
GL Mid- 10m													
GL Mid- 11m													
GL Mid- 12m													
GL Mid- 13m													
GL Mid- 14m													
GL Mid- 15m													
GL Mid- 16m													
GL Mid- 17m													
GL Mid- 18m													
GL Mid- 19m													
GL Mid- 20m													
GL Mid- 22m													
GL Mid- 30m													
GL Mid- 40m													

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

GARROW LAKE - STATION 262-3 Continued
MID WINTER SAMPLING EVENT - JANUARY 26, 2004

	Detection Limits			
	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m	-			
GL Mid- 4m	0.02			
GL Mid- 5m	-			
GL Mid- 6m	-			
GL Mid- 7m	-			
GL Mid- 8m	0.02			
GL Mid- 9m	-			
GL Mid- 10m	-			
GL Mid- 11m	-			
GL Mid- 12m	0.02			
GL Mid- 13m	-			
GL Mid- 14m	-			
GL Mid- 15m	-			
GL Mid- 16m	0.02			
GL Mid- 17m	-			
GL Mid- 18m	-			
GL Mid- 19m	-			
GL Mid- 20m	0.02			
GL Mid- 22m	-			
GL Mid- 30m	-			
GL Mid- 40m	0.02			

Footnotes:

GARROW LAKE - STATION 262-3 Continued
MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Detection Limits			
	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m	-	1	3	
GL Mid- 4m	0.02	1	3	
GL Mid- 5m	-	1	3	
GL Mid- 6m	-	1	3	
GL Mid- 7m	-	1	3	
GL Mid- 8m	0.02	1	3	
GL Mid- 9m	-	1	3	
GL Mid- 10m	-	1	3	
GL Mid- 11m	-	1	3	
GL Mid- 12m	0.02	1	3	
GL Mid- 13m	-	1	3	
GL Mid- 14m	-	1	3	
GL Mid- 15m	-	1	3	
GL MId- 16m	0.02	1	3	
GL Mid- 17m	-	1	3	
GL Mid- 18m	-	1	3	
GL Mid- 19m	-	1	3	
GL Mid- 20m	0.02	1	3	
GL Mid- 22m	-			
GL Mid- 30m	-			
GL Mid- 40m	0.02			

Footnotes:

GARROW LAKE - STATION 262-3 Continued
MINIMUM ICE THICKNESS SAMPLING EVENT - 2004
COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Detection Limits			
	Inorganic Parameters	**Physical Tests**		**Cyanides**
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL Mid- 3m				
GL Mid- 4m				
GL Mid- 5m				
GL Mid- 6m				
GL Mid- 7m				
GL Mid- 8m				
GL Mid- 9m				
GL Mid- 10m				
GL Mid- 11m				
GL Mid- 12m				
GL Mid- 13m				
GL Mid- 14m				
GL Mid- 15m				
GL Mid- 16m				
GL Mid- 17m				
GL Mid- 18m				
GL Mid- 19m				
GL Mid- 20m				
GL Mid- 22m				
GL Mid- 30m				
GL Mid- 40m				

Footnotes:

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MID-WINTER SAMPLING EVENT - JANUARY 27, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL South- 4m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 5m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 6m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 7m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 8m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 9m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 10m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL South- 11m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 12m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 13m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 14m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 15m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 16m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 17m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 18m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 19m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 20m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 22m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 30m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 40m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL South- 4m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 5m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 6m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 7m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 8m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 9m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 10m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	0.00001	0.005	0.00005	0.01	0.0005
GL South- 11m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 12m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 13m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 14m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 15m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 16m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 17m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 18m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 19m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005
GL South- 20m	0.0002	0.0002	0.00002	0.00005	0.00005	0.01	0.00005	0.00005	-	0.005	0.00005	0.01	0.0005

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

Due to ice can not sample the top two metres

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS

MINIMUM ICE THICKNESS SAMPLING EVENT - 2004

NOT ABLE TO DO AS ICE DID NOT LEAVE LAKE, COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Total Metals Concentrations (mg/L)												
Sample ID	Antimony	Arsenic	Cadmium	Cobalt	Copper	Iron	Lead	Manganese	Mercury	Molybdenum	Nickel	Uranium	Zinc
GL South- 3m													
GL South- 4m													
GL South- 5m													
GL South- 6m													
GL South- 7m													
GL South- 8m													
GL South- 9m													
GL South- 10m													
GL South- 11m													
GL South- 12m													
GL South- 13m													
GL South- 14m													
GL South- 15m													
GL South- 16m													
GL South- 17m													
GL South- 18m													
GL South- 19m													
GL South- 20m													
GL South- 22m													
GL South- 30m													
GL South- 40m													

Footnotes: Results are expressed as milligrams per litre except where noted.

< = Less than the detection limit indicated.

GARROW LAKE - STATION 262-3A Continued
MID WINTER SAMPLING EVENT - JANUARY 27, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m	-			
GL South- 4m	0.02			
GL South- 5m	-			
GL South- 6m	-			
GL South- 7m	-			
GL South- 8m	0.02			
GL South- 9m	-			
GL South- 10m	-			
GL South- 11m	-			
GL South- 12m	0.02			
GL South- 13m	-			
GL South- 14m	-			
GL South- 15m	-			
GL South- 16m	0.02			
GL South- 17m	-			
GL South- 18m	-			
GL South- 19m	-			
GL South- 20m	0.02			
GL South- 22m	-			
GL South- 30m	-			
GL South- 40m	0.02			

Footnotes:

GARROW LAKE - STATION 262-3A Continued
MAXIMUM ICE THICNESS SAMPLING EVENT - MAY 3, 2004

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m	-	-	-	0.005
GL South- 4m	-	-	-	-
GL South- 5m	-	-	-	-
GL South- 6m	-	-	-	-
GL South- 7m	-	-	-	-
GL South- 8m	-	-	-	-
GL South- 9m	-	-	-	-
GL South- 10m	0.02	-	-	0.005
GL South- 11m	-	-	-	-
GL South- 12m	-	-	-	-
GL South- 13m	-	-	-	-
GL South- 14m	0.02	-	-	-
GL South- 15m	-	1	3	-
GL South- 16m	-	1	3	-
GL South- 17m	0.02	1	3	-
GL South- 18m	-	1	3	-
GL South- 19m	-	1	3	-
GL South- 20m	0.02	1	3	-

Footnotes:

GARROW LAKE - STATION 262-3A Continued
MINIMUM ICE THICNESS SAMPLING EVENT - 2004
COULD NOT SAFELY ACCESS SAMPLING LOCATION

	Inorganic Parameters	Physical Tests		Cyanides
Sample ID	Sulphide S	Salinity o/oo	Total Suspended Solids	Total Cyanide CN
GL South- 3m				
GL South- 4m				
GL South- 5m				
GL South- 6m				
GL South- 7m				
GL South- 8m				
GL South- 9m				
GL South- 10m				
GL South- 11m				
GL South- 12m				
GL South- 13m				
GL South- 14m				
GL South- 15m				
GL South- 16m				
GL South- 17m				
GL South- 18m				
GL South- 19m				
GL South- 20m				
GL South- 22m				
GL South- 30m				
GL South- 40m				

Footnotes:

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS
MID WINTER SAMPLING EVENT - JANUARY 26, 2004
DUPLICATE RESULTS

Project	Polaris SNP Saline Water Analysis (Garrow Lake)
Report to	Gartner Lee Ltd.
ALS File No.	T9117
Date Received	30/01/2004
Date:	20/02/2004

Sample ID	**GL Mid- 7m**	**GL Mid- 7m**	**RPD %**	**GL Mid- 16m**	**GL Mid- 16m**	**RPD %**
Date Sampled	26/01/2004	QC# 373743		26/01/2004	QC# 373744	
Time Sampled						
ALS Sample ID	5			14		
Nature	Water			Water		
Total Metals						
Arsenic T-As	0.00029	<0.00020	36.7	0.00069	0.00089	25.3
Cadmium T-Cd	0.000493	0.000492	0.203	0.000082	0.000085	3.59
Cobalt T-Co	0.000061	0.000062	1.63	0.000402	0.000415	3.18
Copper T-Cu	0.000976	0.000944	3.33	0.00143	0.00145	1.39
Iron T-Fe	<0.010	<0.010	0	0.211	0.223	5.53
Lead T-Pb	0.000794	0.000689	14.2	0.00255	0.00254	0.393
Manganese T-Mn	0.00819	0.00807	1.48	0.0857	0.0876	2.19
Molybdenum T-Mo	<0.0050	<0.0050	0	0.0073	0.0069	5.63
Nickel T-Ni	0.00341	0.00315	7.93	0.00896	0.00919	2.53
Uranium T-U	<0.010	<0.010	0	<0.010	<0.010	0
Zinc T-Zn	0.197	0.188	4.68	0.265	0.271	2.24
Inorganic Parameters						
Sulphide S	-	-	-	<0.020	<0.020	0

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS
MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004
DUPLICATE RESULTS

Project	40137 Saline Water Analysis Garrow SNP (Polaris)
Report to	Gartner Lee Ltd.
ALS File No.	U3258
Date Received	07/05/2004
Date:	21/05/2004

Sample ID	**GL Mid- 6m**	**GL Mid- 6m**	**RPD %**	**GL Mid- 12m**	**GL Mid- 12m**	**RPD %**
Date Sampled	03/05/2004	QC# 385669		03/05/2004	QC# 385670	
Time Sampled						
ALS Sample ID	4			10		
Nature	Water			Water		
Total Metals						
Antimony T-Sb	<0.00020	<0.00020	0	0.00096	0.00105	8.96
Arsenic T-As	<0.00020	0.00023	14	0.00046	0.00046	0
Cadmium T-Cd	0.000617	0.000636	3.03	0.000207	0.00024	14.8
Cobalt T-Co	0.000066	0.00007	5.88	0.000751	0.000814	8.05
Copper T-Cu	0.00102	0.00102	0	0.00218	0.00242	10.4
Iron T-Fe	<0.010	0.01	0	0.173	0.195	12
Lead T-Pb	0.00168	0.00138	19.6	0.00682	0.00783	13.8
Manganese T-Mn	0.00957	0.00968	1.14	0.0971	0.112	14.3
Molybdenum T-Mo	<0.0050	<0.0050	0	<0.0050	0.0064	24.6
Nickel T-Ni	0.00385	0.00383	0.521	0.00821	0.009	9.18
Uranium T-U	<0.010	<0.010	0	<0.010	<0.010	0
Zinc T-Zn	0.229	0.233	1.73	0.262	0.28	6.64

GARROW LAKE - STATION 262 - 3 (MID LAKE) - TOTAL METALS ANALYSIS
MINIMUM ICE THICKNESS SAMPLING EVENT - NOT SAMPLED
DUPLICATE RESULTS

Project	
Report to	
ALS File No.	
Date Received	
Date:	

Sample ID	**RPD %**	**RPD %**
Date Sampled		
Time Sampled		
ALS Sample ID		
Nature		
Total Metals		
Antimony T-Sb		
Arsenic T-As		
Cadmium T-Cd		
Cobalt T-Co		
Copper T-Cu		
Iron T-Fe		
Lead T-Pb		
Manganese T-Mn		
Molybdenum T-Mo		
Nickel T-Ni		
Uranium T-U		
Zinc T-Zn		

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS
MID WINTER SAMPLING EVENT - JANUARY 26, 2004
DUPLICATE RESULTS

Project	Polaris SNP Saline Water Analysis (Garrow Lake)
Report to	Gartner Lee Ltd.
ALS File No.	T9118
Date Received	30/01/2004
Date:	20/02/2004

Sample ID	**GL South- 7m**	**GL South- 7m**	**RPD %**	**GL South- 16m**	**GL South- 16m**	**RPD %**
Date Sampled	27/01/2004	QC# 373745		27/01/2004	QC# 373746	
Time Sampled						
ALS Sample ID	5			14		
Nature	Water			Water		
Total Metals						
Arsenic T-As	<0.00020	<0.00020	0	0.00079	0.00073	7.89
Cadmium T-Cd	0.000522	0.000562	7.38	0.000092	0.000088	4.44
Cobalt T-Co	0.000067	0.000076	12.6	0.000412	0.000396	3.96
Copper T-Cu	0.000916	0.000896	2.21	0.00167	0.00161	3.66
Iron T-Fe	<0.010	<0.010	0	0.232	0.229	1.3
Lead T-Pb	0.000325	0.000173	61	0.00265	0.00263	0.758
Manganese T-Mn	0.00906	0.0093	2.61	0.0948	0.094	0.847
Molybdenum T-Mo	<0.0050	<0.0050	0	0.0059	0.0072	19.8
Nickel T-Ni	0.00361	0.00372	3	0.00912	0.00907	0.55
Uranium T-U	<0.010	<0.010	0	<0.010	<0.010	0
Zinc T-Zn	0.208	0.231	10.5	0.27	0.265	1.87
Inorganic Parameters						
Sulphide S	-	-	-	<0.020	<0.020	0

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS
MAXIMUM ICE THICKNESS SAMPLING EVENT - MAY 3, 2004
DUPLICATE RESULTS

Project	40137 Saline Water Analysis Garrow SNP (Polaris)
Report to	Gartner Lee Ltd.
ALS File No.	U3253
Date Received	07/05/2004
Date:	21/05/2004

Sample ID	**GL South- 4m**	**GL South- 4m**	**RPD %**	**GL South- 15m**	**GL South- 15m**	**RPD %**
Date Sampled	03/05/2004	QC# 385637		03/05/2004	QC# 385638	
Time Sampled						
ALS Sample ID	2			13		
Nature	Water			Water		
Physical Tests						
Salinity o/oo	-	-	-	64.4	64.3	0.155
Total Metals						
Antimony T-Sb	<0.00020	<0.00020	0	0.00067	0.00077	13.9
Arsenic T-As	<0.00020	<0.00020	0	0.00052	0.00065	22.2
Cadmium T-Cd	0.000615	0.00061	0.816	0.000083	0.000082	1.21
Cobalt T-Co	0.000112	0.000075	39.6	0.000402	0.000451	11.5
Copper T-Cu	0.000963	0.00106	9.59	0.00127	0.0012	5.67
Iron T-Fe	<0.010	<0.010	0	0.245	0.235	4.17
Lead T-Pb	0.000322	0.000329	2.15	0.0021	0.00214	1.89
Manganese T-Mn	0.00994	0.01	0.602	0.0832	0.0804	3.42
Molybdenum T-Mo	<0.0050	<0.0050	0	0.0056	0.0056	0
Nickel T-Ni	0.00375	0.004	6.45	0.00886	0.00847	4.5
Uranium T-U	<0.010	<0.010	0	<0.010	<0.010	0
Zinc T-Zn	0.23	0.247	7.13	0.211	0.201	4.85

GARROW LAKE - STATION 262 - 3A (NEAR OUTLET) - TOTAL METALS ANALYSIS
MINIMUM ICE THICKNESS SAMPLING EVENT - NOT SAMPLED
DUPLICATE RESULTS

Project	
Report to	
ALS File No.	
Date Received	
Date:	

Sample ID	**RPD %**	**RPD %**
Date Sampled		
Time Sampled		
ALS Sample ID		
Nature		
Total Metals		
Antimony T-Sb		
Arsenic T-As		
Cadmium T-Cd		
Cobalt T-Co		
Copper T-Cu		
Iron T-Fe		
Lead T-Pb		
Manganese T-Mn		
Molybdenum T-Mo		
Nickel T-Ni		
Uranium T-U		
Zinc T-Zn		

APPENDIX 17

CORRESPONDENCE BETWEEN

TECK COMINCO AND ENVIRONMENT CANADA

REGARDING THE APPLICATION OF THE

METAL MINING EFFLUENT REGULATIONS

Azimuth Consulting Group Inc.
218-2902 West Broadway
Vancouver, BC V6K 2G8

Phone: 604-730-1220
Fax: 604-739-8511

Our File #: TC-03-03

March 29, 2004

Sidney F. Bruinsma
Enforcement/Emergencies Officer, Nunavut
Northern Division, Environmental Protection Branch
Environment Canada
Box 1870, Iqaluit
Nunavut X0A 0H0

Dear Mr. Bruinsma:

Re: Polaris Mine EEM – Missed Sublethal Toxicity Test Sampling Event

Further to our recent discussion, we are pleased to document the issues and circumstances surrounding the missed 2003 sampling event for sublethal toxicity testing (SLTT) of effluent at Teck Cominco's Polaris Mine.

First, Azimuth Consulting Group (Azimuth) takes full responsibility for the missed sampling event, which resulted from an oversight on our part. Our staff have considerable experience conducting environmental effects monitoring (EEM) programs under the Pulp and Paper Effluent Regulations (PPER), which have been in place for some years. We understand the importance of the SLTT as an EEM investigative tool and would not knowingly miss a sampling event. The oversight comes from our interpretation of the new Metal Mining Effluent Regulations (MMER) and how they apply to the Polaris Mine, which has a unique discharge situation (i.e., limited to approximately 60 days per calendar year). Under both the PPER and MMER, two sampling events are required for the SLTT. However, if the discharge period is less than 120 days, the PPER require only one sampling event. We mistakenly assumed that these terms would also apply to the MMER, which provide less detail pertaining to the requirements of this test than the PPER. This issue was compounded by the unique discharge characteristics and receiving environment of the Polaris Mine, which make the MMER more difficult to interpret and apply compared to mines discharging under more usual conditions.

We became aware of the missed SLTT event during a December 2003 workshop intended to present results of 2003 reconnaissance studies carried out at the mine and to seek feedback from the Technical Advisory Committee (TAP) on our proposed study design for the Polaris Mine. Following our presentation, Ms. Sandra Blenkinsopp pointed out that two sampling events were indeed required under MMER. She then indicated that Environment Canada would contact us to further discuss the implications of this matter.

We agree that the missed SLTT event is unfortunate and will ensure that this test is carried out twice during the 2004 and 2005 discharge periods.

Please do not hesitate to contact us if you have any questions or require further clarification.

Sincerely,
Azimuth Consulting Group Inc.

PAllard

Patrick Allard, M.Sc., R.P.Bio.

cc: Randy Baker (Azimuth)
Bruce Donald (Teck Cominco)

Environment Canada
Environmental Protection Branch
Prairie and Northern Region
Northern Division
P.O. Box 1870 Iqaluit, Nunavut
X0A 0H0

PROTECTED

Occurrence File: 4408-2004-03-11-003

27 April 2004

WITHOUT PREJUDICE

Mr. David Thompson
Deputy Chairman and CEO
Teck Cominco Metals Ltd.
Suite 600 – 200 Burrard Street
Vancouver, British Columbia
V6C 3L9

and

Mr. John Knapp
Manager of Operations
Teck Cominco Metals Ltd.
Polaris Mine Operation
Polaris, Little Cornwallis Island, Nunavut
X0A 0Y0

RE: ***FISHERIES ACT;***
Metal Mining Effluent Regulations, Environmental Effects Monitoring
Part 1, Section 6(1)

The purpose of this correspondence is to remind Teck Cominco Metals Ltd. and John Knapp, in his capacity as Manager of Operations, Polaris Mine, in the Territory of Nunavut, of their obligations under the Environmental Effects Monitoring provisions of the Metal Mining Effluent Regulations of the *Fisheries Act*. It relates to a report of February 24, 2004 by Azimuth Consulting Group Ltd., acting as an agent for Teck Cominco Metals Ltd. and its officers. This correspondence sets out in writing the circumstances surrounding a failure to collect the appropriate samples as outlined within the regulations to wit: Part 1, Section 6, Environmental Effects Monitoring Studies of the Metal Mining Effluent Regulations.

../1

On 24 February 2004, Azimuth Consulting Group Ltd. had discussions with Environment Canada's Prairie and Northern Region, Senior Environmental Effects Monitoring Coordinator, Sandra Blenkinsopp. It was at this time that the deficiency in sampling was noted by Environment Canada. Azimuth Consulting Group acting as a contractor for Teck Cominco Metals Ltd. stated it had only collected a single sample for Sub-lethal Toxicity Testing (SLTT) contrary to the regulation requirements which required two samples to be collected.

Subsequently this matter was reported to the enforcement section of the Environmental Protection Branch of Environment Canada on the same day. Once I was notified I contacted Mr. Patrick Allard of Azimuth Consulting Group Ltd. requesting information on the circumstances surrounding this failure to meet the requirements of the Fisheries Act. Mr. Allard provided a letter to Environment Canada outlining the issues pertaining to the oversight by Azimuth Consulting Group Ltd. This letter was later also forwarded with the revised Polaris Mine - 2003 ANNUAL Metal Mining Effluent Regulations Summary Report dated March 31, 2004 and sent to Mr. Peter Blackall, Regional Director of Environmental Protection.

Environment Canada recognizes through these correspondences that Teck Cominco Metals Ltd. has taken measures to correct the aforementioned situation. Accordingly, a formal Warning Letter will not be issued in these circumstances.

This correspondence is intended to bring this matter to your attention in order for you to take necessary action to prevent a repeat of the circumstances described herein. In conclusion no further enforcement action is being considered or deemed warranted at this time. Environment Canada will be closing our file on this incident.

If you have any questions or require clarification, please contact the undersigned at (867) 975-4644.

Sidney Frank Bruinsma
Fisheries Act Inspector

cc: Craig Broome – Head of Enforcement Environmental Protection
Prairie and Northern Region, Environment Canada

../2

Bruce J. Donald
Reclamation Manager

April 27, 2004

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – Alteration of System at Final Discharge Point at Garrow Dam

As required under Section 10(2) of the Metal Mining Effluent Regulations, please be advised that the siphons at Garrow Lake dam will not be used for discharging effluent this summer. As part of our decommissioning and closure activities, the dam is being partially decommissioned with a channel constructed through the decommissioned portion of the dam. Flow through the dam will be via the original creek channel starting with this year's effluent discharge season. Sampling of the effluent will be continued from the same location as in previous years so that a change in the location of the Final Discharge Point is not being contemplated.

Yours truly,

Original signed by B. Donald

Bruce Donald

cc:
Walter Kuit (Teck Cominco Limited)
Bob Hutchinson (Teck Cominco Limited)
Trevor Feduniak (Teck Cominco Limited)
Joe Dahoy (Cascade Mgmt)
Randy Baker (Azimuth Consulting Group)

Polaris Mine EEM - Outline of Study Design for Biological Monitoring Studies

Highlights:

- Program builds on 1) results of historical studies covering pre-mining and operational periods; 2) findings of 2003 reconnaissance studies (i.e., field effluent plume delineation, underwater video survey, fish survey, and sediment survey); 3) theoretical effluent plume modeling; and 4) considerable feedback obtained during consultations with the Technical Advisory Panel (TAP) as part of two workshops (April and December 2003) and follow-up discussions.

- Approach consists of a Control/Impact design focusing on one high exposure area (i.e., aquatic receiving environment that is nearest to the mouth of Garrow Creek and that contains an appropriate habitat type with sufficient geographic area to accommodate the necessary number of replicate stations; Environment Canada, 2002) and one reference area. Both areas are located in Garrow Bay, approximately 1 km apart (see attached figure).

- Our rationale for targeting one high exposure area, rather than multiple near-field and far-field exposure areas, follows guidance from Environment Canada (2002) and reflects findings of the 2003 reconnaissance studies which clearly indicated the lack of an exposure gradient between the mouth of Garrow Creek and the reference area.

- The field program is planned from August 11th - 25th 2004, when the likelihood of safe access to Garrow Bay for sampling is optimal.

- Standard and accepted QAQC procedures will be used throughout the program.

- The proposed study design is optimistic. While every attempt will be made to achieve the goals of the program, field conditions and safety issues may require us to focus on a few priority study components. As discussed with members of the TAP, all clam, benthos, and sediment collections will be diver-assisted, so local weather and ice conditions will dictate level of effort. We propose the following priorities and would appreciate feeback from the TAP: 1) fish survey and tissue analyses; 2) supporting environmental variables (water and sediment quality surveys); 3) SIMS survey (faster to accomplish and provides semi-quantitative basis for evaluating any gross impacts to marine communities); and 4) benthic invertebrate community survey (time intensive given replication required to achieve statistically sound assessment).


Study Component	Sampling Areas	Sample Size and Replication		Mesurement Endpoints	Sampling Method
Fish Survey and Tissue Analyses - Species selected: softshell clam (*Mya truncata*)	**Garrow Bay high exposure area**: located in the area closest to the mouth of Garrow Creek where sufficient clams can be collected (approx. 6 - 8 m depth)	- Target of 40 clams[1]	- Individual clams	- Length - Width - Whole animal wet weight - Shell weight - Soft tissue fresh weight - Gonad fresh weight - Sex - Condition index - Gonadosomatic index[2]	- Diver-assisted sampling; collection of individuals by hand, only intact clams will be retained
			- 4 soft tissue composites of 10 undepurated clams	- Tissue chemistry: moisture and lipid content, suite of metals	
	Garrow Bay reference area: located approximately 1 km to the northeast, upstream of the predominant current direction (approx. 6 - 8 m depth)	- Target of 40 clams[1]	- Individual clams	Same as high exposure area	Same as high exposure area
			- 4 soft tissue composites of 10 undepurated clams	Same as high exposure area	
Benthic Invertebrate Community Survey	**Garrow Bay high exposure area**: located in the area closest to the mouth of Garrow Creek where benthic communities can be sampled (approx. 6 - 8 m depth)	- 5 replicate stations (approx. 10 m x 10 m each and separated by approx. 50 m)	- 5 x 1L subsamples per station	- Total invertebrate density - Taxon richness - Simpson's diversity index - Bray-Curtis index - Evenness - Taxon density - Taxon proportions - Taxon presence/absence	- Diver-assisted sampling; upper 10 cm of sediment will be collected for each subsample using a 1L plastic container - All 5 x 1L subsamples for a given station will be physically pooled prior to processing - Processing will be performed using a 1 mm mesh size - Identifications will be performed to the lowest practicable taxonomic level
	Garrow Bay reference area: located approximately 1 km to the northeast, upstream of the predominant current direction (approx. 6 - 8 m depth)	- 5 replicate stations (approx. 10 m x 10 m each and separated by approx. 50 m)	- 5 x 1L subsamples per station	Same as high exposure area	Same as high exposure area


Polaris Mine EEM - Outline of Study Design for Biological Monitoring Studies

Study Component	Sampling Areas	Sample Size and Replication		Mesurement Endpoints	Sampling Method
Supporting Environmental Variables					
- Water quality monitoring	**Garrow Bay high exposure area**: location matching fish and benthic survey sampling area	- 5 replicate stations for field measurements (matching benthic replicate stations)	- Measurements made at 1 m depth intervals	- Field measurements: DO, pH, temperature, salinity, transparency and water depth	- Calibrated YSI meter, pH probe, and depthmeter will be used for all field measurements - Surface water samples will be collected directly into sample containers; all 5 subsamples for a given sampling area will be composited prior to analysis - Subsurface sampling will be conducted using divers; care will be taken not to disturb sediments during sampling; all 5 subsamples for a given sampling area will be composited prior to analysis - Timing of sampling will match routine MMER effluent characterization as well as EEM effluent and water quality monitoring
		- 1 composite surface sample for laboratory analysis	- 5 subsamples matching benthic replicate stations	- Laboratory analyses: pH, temperature, DO, hardness, alkalinity, Al, As, Cd, Cu, cyanide, Fe, Hg, Pb, Mo, Ni, Zn, TSS, ammonia, nitrate, radium 226	
		- 1 composite subsurface sample for laboratory analysis (0.25 m from bottom)	- 5 subsamples matching benthic replicate stations		
	Garrow Bay reference area: location matching fish and benthic survey sampling area	- 5 replicate stations for field measurements (matching benthic replicate stations)	- Measurements made at 1 m depth intervals	Same as high exposure area	Same as high exposure area
		- 1 composite surface sample for laboratory analysis	- 5 subsamples matching benthic replicate stations		
		- 1 composite subsurface sample for laboratory analysis (0.25 m from bottom)	- 5 subsamples matching benthic replicate stations		
- Sediment quality monitoring	**Garrow Bay high exposure area**: location matching fish and benthic survey sampling area	- 5 replicate stations (matching benthic replicate stations)	- 5 subsamples (matching benthic subsamples) per station	- Sediment chemistry: TOC, grain size, suite of metals	- Diver-assisted sampling; upper 10 cm of sediment will be collected for each subsample using a 1L plastic container - All 5 subsamples for a given station will be composited prior to analysis
	Garrow Bay reference area: location matching fish and benthic survey sampling area	- 5 replicate stations (matching benthic replicate stations)	- 5 subsamples (matching benthic subsamples) per station	Same as high exposure area	Same as high exposure area
Additional Studies - Seabed Imaging and Mapping System (SIMS)	**Garrow Bay high exposure area** and **Garrow Bay reference area**	- Numerous georeferenced tracklines within each area	- Continuous imagery	- Seabed classification maps including: substrate type, vegetation type and cover, distribution and relative abundance of macrofauna	- Towed underwater camera (SIMS) providing semi-quantitative survey of physical and biological features of the seabed

[1] During the 2003 reconnaissance studies, a total of 29 clams were collected by divers; access to Garrow Bay for diving was limited to 3 out of 14 field days due to harsh weather conditions (e.g., presence of ice flows, strong winds, blizzard). Every effort will be made during the 2004 field program to meet the mininum EEM requirement of 40 individuals per sampling area; however, the total sample size may be limited by field conditions. In addition, the inherent difficulty in identifying clam sexes in the field may result in a departure from the requirement for 20 males and 20 females.

[2] The gonadosomatic index will be determined under the supervision of Sylvie St-Jean, National Water Research Institute. The sample size will be assessed once field work is completed.

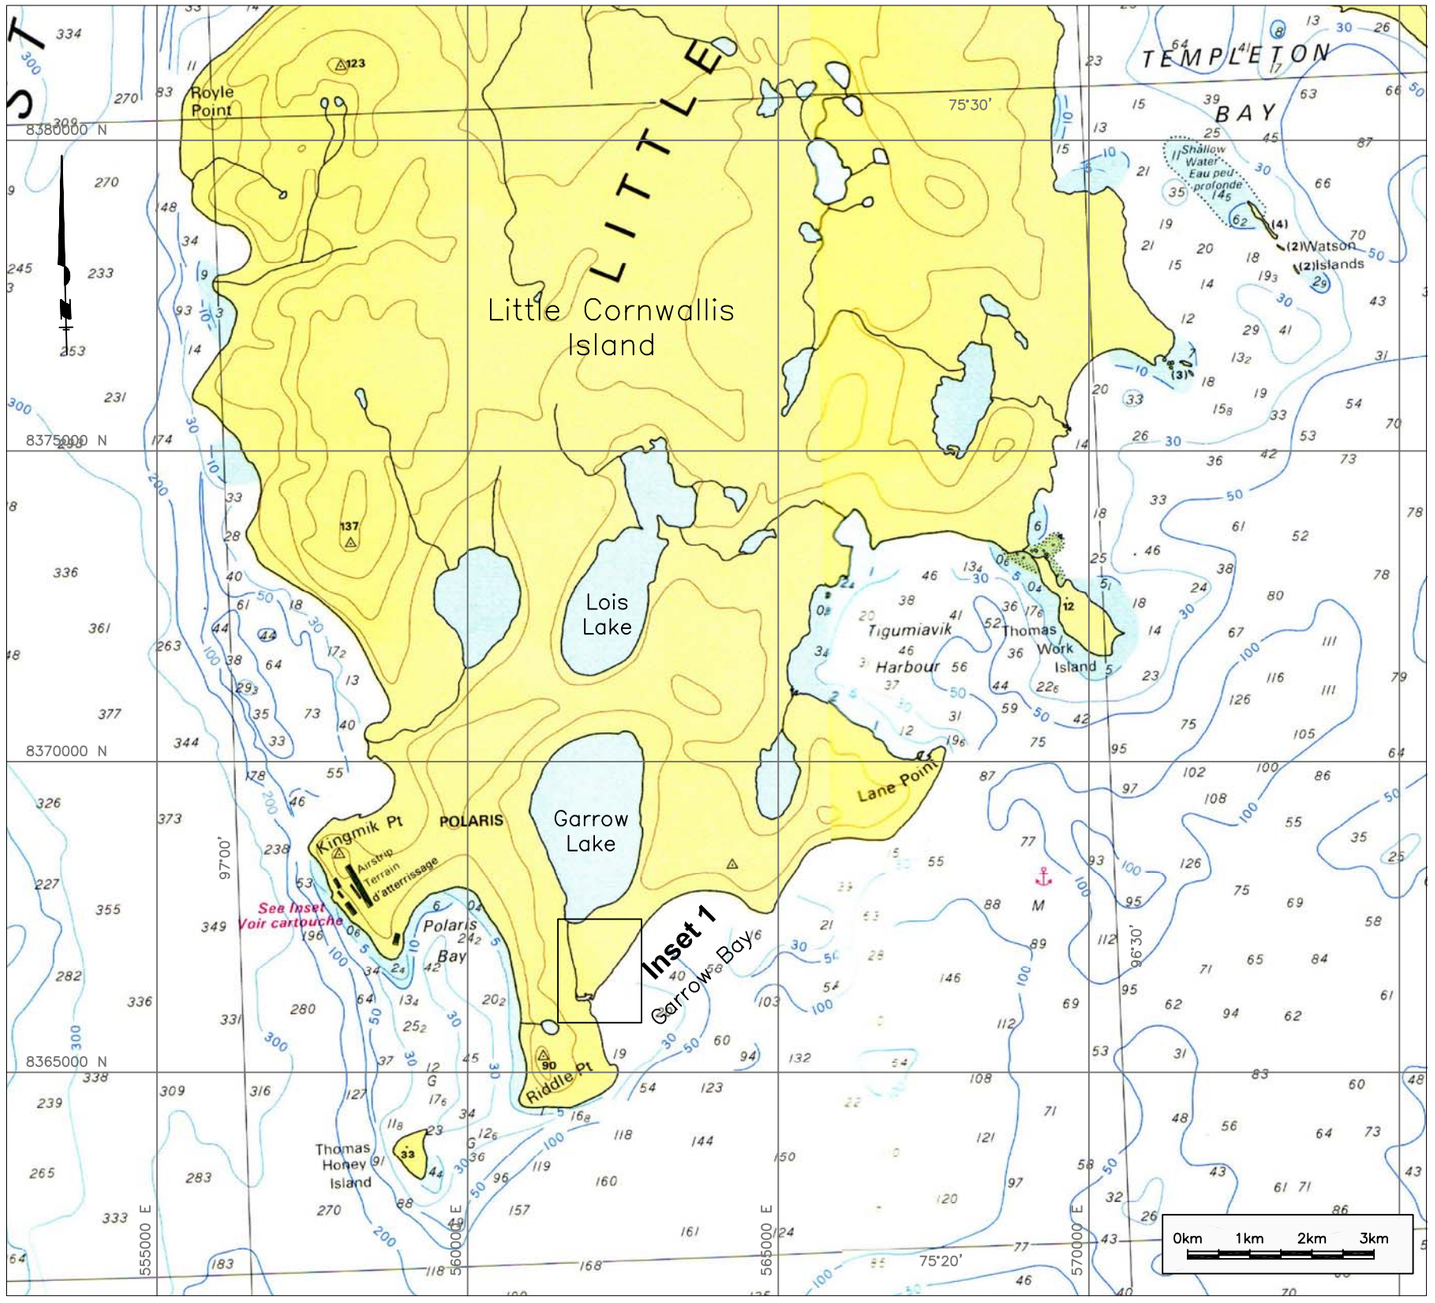

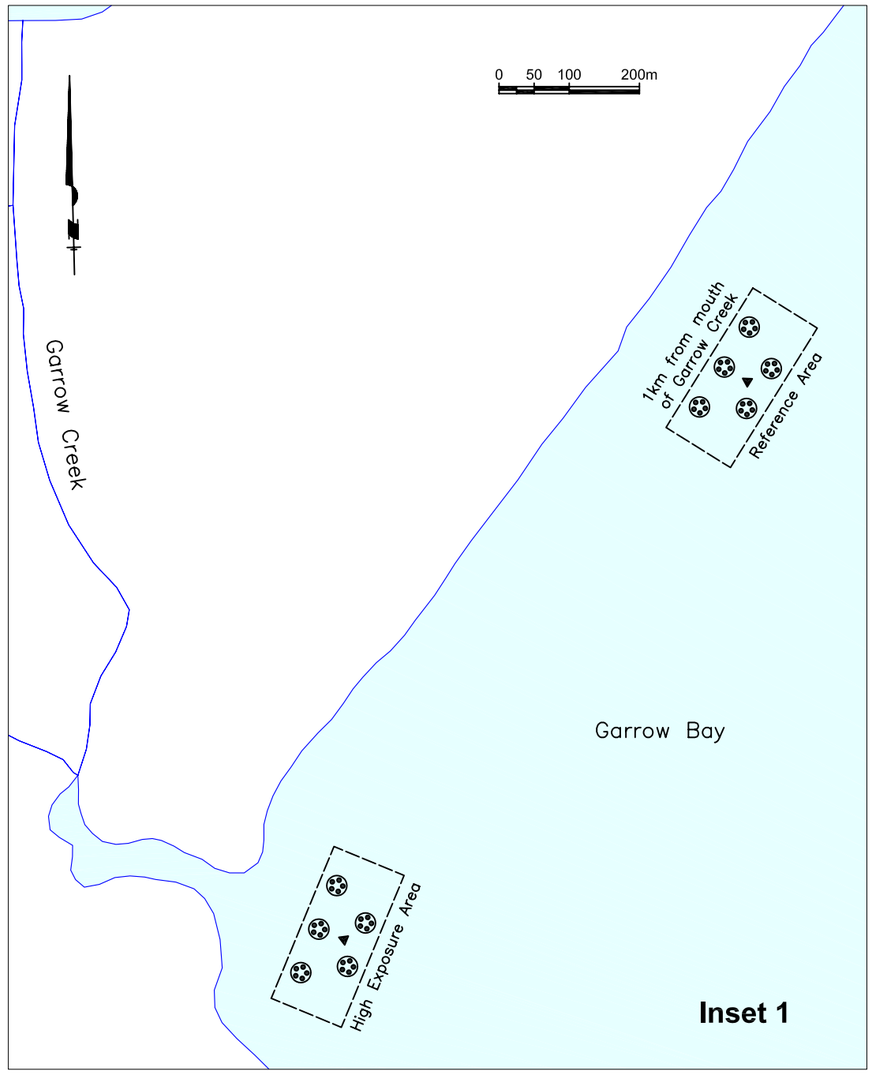

Sampling area for fish survey and benthic invertebrate community survey

Replicate station - benthos, sediment, water (field measurements)

Subsample - benthos, sediment

Surface and subsurface composite sample - water (laboratory analysis); note that subsamples will be taken from each benthic replicate station (see above)

Inset data and surrounding creeks digitized from Map 1 Sampling Sites 1980 *prepared by B.C. Research January 1978*

Other data from Crozier Strait And/Et Pullen Strait 7935 *corrected 2003-03-28 published by the Canadian Hydrographic Service*

AZIMUTH

Azimuth Consulting Group Inc.
218-2902 West Broadway
Vancouver BC, V6K 2G8

DRAWN BY:	CHK. BY:	PROJECT No:
BT	PA	TC-03-03
	DATE: 3/6/2004 1:04 PM	

PROJECT: Polaris

TITLE:

Polairs Mine EEM
Study Design for Biological Studies

CLIENT:	
Teck Cominco	Figure 1

Review of Polaris Mine EEM
Study Design Outline for Biological Monitoring Studies

Highlights Section

The benthic survey component should be given the 3rd priority rather than the 4th priority. The benthic survey is a main EEM component. If time becomes an issue, the TAP recommends that sediment and water quality sample collection be reduced as indicated in the comments below.

Fish Survey and Tissue Analysis

Gonad dry weight and animal height should be added to the list of measured endpoints.

Benthic Invertebrate Community Survey

The MMER TGD recommends that in marine systems, a stacked set of 1.0 and 0.5 mm screens be used in the field with the 0.5 mm samples being archived and processed only if appropriate.

Benthic Supporting Environmental Variables (Chapter 5 of TGD)

Please see Table 5-7 of the MM TGD for the recommended supporting explanatory variables to be measured at each station in marine/estuarine benthic invertebrate habitats. In addition to the parameters listed in your outline, this table also recommends that dissolved oxygen near the bottom, sediment Eh (redox) and sediment total sulfides, as well as substratum characteristics be measured at each benthic station.

If time is limiting, the TAP recommends that **one sediment sample be collected per station** at the same time as the benthic invertebrate sampling.

Water Quality Monitoring during biological field work (Chapter 6 of MM TGD)

If time is limiting, the TAP recommends that the water quality sample collection work be done within each fish and benthic invertebrate sampling **area at one representative station** (pg 6-5, MM TGD).

Field Measurement of Water Quality Parameters - Please note that when water depth is greater than 4m, the standard water quality parameters measurable in the field should be taken throughout the water column at one to five metre intervals depending on total depth (pg. 6-9 MM TGD). The TAP recommends that the interval at which measurements are taken be less than every meter in the upper portion of the water column, in order to pick up where the freshwater lens is, etc. It is also recommended that conductivity be added to the list of standard field measurements.

Collection of Water Samples for Laboratory Analyses - The water collected for laboratory analyses of water quality should be collected at 2 depth intervals: the subsurface and near bottom (pg. 6-10 MM TGD), as described in your outline.

FINAL MEETING MINUTES

ENVIRONMENTAL EFFECTS MONITORING
STUDY DESIGN MEETING
POLARIS MINE (TECK COMINCO) & TECHNICAL ADVISORY PANEL
Tuesday, December 16, 2003
1:00 p.m to 5:00 pm.

Bev Burns Boardroom, Environment Canada, Edmonton

Attendees:

Bruce Donald	Teck Cominco, Cranbrook
John Knapp	Teck Cominco
Randy Baker	Azimuth Consulting Group Inc., Vancouver
Patrick Allard	Azimuth Consulting Group, Inc., Vancouver
Dionne Filiatrault	Nunavut Water Board, Gjoa Haven
Chris Baron	F&O Canada, Winnipeg
Meighan Wilson	Indian and Northern Affairs, Yellowknife
Stephen Harbicht	Environment Canada, Yellowknife
Sandra Blenkinsopp	Environment Canada, Edmonton
Jenny Ferone	Environment Canada, Edmonton
Paula Siwik	Environment Canada, Edmonton

1. Attendees introduced themselves.

2. No additional items were added to the agenda.

3. Review of the objective: To discuss the findings of the August 2003 reconnaissance studies, and to incorporate these findings into a revised EEM study, scheduled for August 2004.

4. Results of the August 2003 field reconnaissance studies on water chemistry, toxicity testing, plume delineation & modeling, sediment chemistry, benthos, and fish were presented by Randy Baker and Patrick Allard. Their presentation is appended (a hard copy will be sent with the final version of the minutes). An underwater video clip was also viewed. Information from the video presentation and slide presentation is appended at the end of the minutes.

5. General Discussion on Study Design Key Components

Adult Fish Survey

- Given that fin fish were found to be very rare in Garrow Bay, clams will be used in lieu of fin fish.
- The sampling design for collecting clams was discussed, given the limitations on the divers (2 dives per day, approximately 30 -35 minutes per dive). If discrete sampling stations are used similar to a benthic invertebrate sampling design with 5 stations, the divers will only be able to collect about 5 clams per station. Further discussion is needed to confirm if 20 - 25 clams, for example, are sufficient given the variability in a natural population. Another option is to collect clams on a per area basis.
- The range of EEM endpoints found in the MMER EEM Technical Guidance for caged bivalves should be measured on the wild clams, e.g. length, width, etc. (Note: The information is found in the Alternative Monitoring Chapter - Chapter 12).
- The exposure area clams should be collected along the first depth contour where clams are exposed to the effluent from Garrow Creek. This would probably be at the 5 to 6 m depth. Note: Steve Harbicht wants to see solid baseline data from this area in the event that Garrow Lake has a release in the future.
- The reference area will be in the subtidal area to the north of the mouth of Garrow Creek. The reference area clams will be collected along the same depth contour as the exposure area clams to remove the effect of depth. Note that results from the reconnaissance work indicated that metal levels in clams and sediment in this area as well as in the exposure area were similar to background concentrations measured in Tigumiavik Harbour.
- Exposure will be assessed by conducting soft tissue analyses for a suite of metals.

Action Item: Sandra Blenkinsopp to collect information on wild clam sample size. Done - Sandra spoke with Dr. Sylvie St.-Jean en route to the EEM Science Symposium. Dr. St.-Jean suggested a minimum of 40 clams of each sex per area, which usually requires a field collection of about 120 clams.

Action Item: Sandra Blenkinsopp will send Sylvie St.-Jean's contact information to Patrick so that he can get the current information on reproductive endpoints, which are under development. Done. Patrick and Sylvie have discussed the study. Patrick indicated that it was agreed that while 40 clams of each sex per study area would be ideal, it is unlikely that such a large sample size can be achieved due to sampling limitations in Garrow Bay (e.g., diver-assisted, ice flows, weather conditions, etc). Rather, it was agreed that 40 clams total per study area will be targeted. While 20 males and 20 females are recommended for the fish survey, it was acknowledged that difficulties in sexing clams in the field may result in departures from this target ratio.

Benthic Invertebrate Community Survey

- Grabs from the surface will not work because the sediments are too hard.
- Could use diver-assisted cores or quadrats
  - Cores – subsurface too hard
  - Quadrats – difficult because of kelp beds
- Could do a combination – SIMS and diver assisted cores or through-ice cores.
- Benthic stations (5 per area) will be located along a depth contour (approx. 6 m) to remove effect of depth, using same areas as clam survey.
- Patrick suggested divers could use a 1L wide-mouth jar, and drag it at a consistent depth and in a consistent manner until full. Used this method at Burrard Inlet.
- TAP suggested increasing subsamples per station and using a smaller volume. Could possibly do 2 to 3 subsamples per 500 mL jar.
- Use of amphipods briefly discussed (& subsequently discarded).
- Unlikely to have enough time to collect samples from a far-field site. (Note to TAP: a far-field benthic site is not required for an initial MMER EEM survey.)
- SIMS will be back-up, used in same area.

Sediment Collection

- Grabs will not work because the sediments are too hard (see benthic above).
- Steve Harbicht asked about the sediment chemistry with respect to the digest, etc.

Action Item: Sandra Blenkinsopp to confirm if sediment is to be collected per station. Done - Sediment sampling is to be done at each benthic station.

Action Item: Sandra Blenkinsopp to check sediment chemistry guidance for marine environments to determine recommended digestion process for EEM. Status: In Progress.

Effluent and Water Quality Monitoring

- The effluent and water quality monitoring, which includes effluent sublethal toxicity testing, must continue for the full 3 year period until the mine receives recognized closed mine status
- Two effluent samples must be collected for sublethal toxicity testing per year. The mine indicated that it had only collected one in 2003 in 9 weeks of discharge.

Action Item: Sandra Blenkinsopp to follow up with Patrick Allard. Done. The 2004 and 2005 monitoring events will include two samples for sublethal toxicity testing.

Timing of Survey

- Survey will be conducted approximately Aug 10 – 25th, 2004.

- Based on experience during the field reconnaissance survey last year, ½ of days up there might be working days.
- Field support for divers was discussed. A lot of the infrastructure will be gone and the medical facility will be decommissioned by August. Sandra Blenkinsopp suggested that it may be better to sample in May through an ice platform when more infrastructure was present at the site. Bruce Donald indicated that effluent wouldn't be flowing in May. Sandra Blenkinsopp has discussed this site with the National EEM Office, and the National EEM Office indicated that the effluent would not have to be flowing during sampling at this site. The consultants decided to work in August. They want to concentrate on open water sampling.
- If due to inclement weather or other difficulties the survey can't be completed, Patrick asked what happens, and the following summarizes the discussion:
    - Sandra Blenkinsopp indicated that the consultants should keep in touch with her or the Authorization Officer (AO) during the field work so that the TAP can be informed if weather is causing a problem, etc., Weather problems, communications with EC, etc., should be documented by the consultants for use in writing up the interpretive report. **Human safety is of primary importance.**
    - Sandra indicated that two weeks is an acceptable level of effort to attempt to achieve the objectives of the field survey.
    - Fall-back position – Combine 2 years of data.
    - Jenny Ferone suggested prioritizing elements of study, e.g. collect clam biological endpoints first.
    - Seabed Imaging and Mapping System (SIMS – see below) will be a backup, since it will be done in the same area. There is value in having both – cores and visual.
- First weekend of September in 2004 – sea-lift. Everybody and everything goes.

Seabed Imaging and Mapping System (SIMS) – The consultants indicated that there is a F&O requirement for SIMS to be done at the dock site now that the dock structure has been removed. Ten to 15 m intervals parallel to shore will be done, followed by tows perpendicular to shore, and then oblique tows. Abundance, and presence / absence will be noted, as well as depth. Drop camera, magnify and do quadrat survey. This is a semi-quantitative method.

6. Steps Forward
    - Sandra Blenkinsopp to distribute minutes
    - Azimuth to finalize study design. Anticipate a 2 to 3 month turn-around time.
    - Randy will make a copy of the video for EC (Received by Edm Office January 7, 2004).

Video and Slide Presentation

Notes from video presentation:

- Video taken first weeks of August 2003
- Thin layer of sand/silt over cobble and gravel
- One fish; Clouds of amphipods (mysids)
- Starting at mouth of creek and moving out
- Ice scour area – rocky, no kelp
- Lot of cobble and gravel and attached kelp typical of 5 to 8 metres depth, 150 – 200 m offshore
- Stark difference in kelp/benthic community abundance between scoured intertidal and subtidal area
- Maximum depth sampled approximately 8 m. Floats were set for the collection of clams at approximately 8 m.
- Clams in softer sediments as well as between larger substrates
- Looking for clams as near to shore as possible, looking for siphons that stick out of the sand. Suspended material hung in water column
- Collected paired sediment and clam tissue samples
- Sediments collected by hand into jar prior to clam collection
- Clams (*Mya truncata*), 17 - 50 g wet body weight, approx. 4 size classes (17-19, 32, 40, & 50 g)
- Dragged a zooplankton net in shallows and collected specimens. Made a representative zooplankton collection.
- Water temperature was -0.5 to -1 ^{o}C water temp, 0 ^{o}C at surface
- 30 to 35 minutes per dive

Slide 4 - Garrow Lake Effluent Characterization

- Collected water samples weekly
- Early in the year the freshwater ice melt causes a drop in salinity
- Garrow Lake is siphoned over the dam then flows by gravity.
- Garrow Creek typical discharge was 0.1 to 0.2 m^3/s. Spring flow generally 1.5 to 2 m^3/s.
- Flow rates are higher this year because more siphons were on line.
- Approximately 20 cm remains to get lake down to level. The dam will be opened for this.
- Garrow Lake sampling performed for Fisheries & Oceans Canada in August 2003: Captured 19 sculpins, sacrificed 11; Zooplankton
- Garrow Lake top 9 or 10 m was brackish water; 2 ppt down to 7 or 8 ppt. Transition zone at 10 or 11m when salinity went from 10 to 60 ppt. Pretty well uniform at 60 ppt to bottom. Temperature inversion – about 8^{o}C at bottom.

Slide 6 – 2003 Effluent Chemistry Data

- BC Aquatic Water Quality Guidelines are marine limits based on toxicity to algae with a 2 fold safety factor

Slide 7 – Contaminants of Potential Concern

- Concentration of Zinc – low initially at ice melt and then increases
- Bruce Donald indicated that in the future Zinc concentrations should be lower, since only meltwater should be drawing down.
- High Pb, reason not known. Could have been due to new siphons.

Slide 8 – Effluent Characterization - Sublethal Toxicity Testing

- Didn't miss any holding times for getting samples to the toxicity lab in Vancouver.
- Acute Lethality Tests – included salinity controls
- SLTT – 72% v/v highest effluent concentration tested; used sea salts
- Randy Baker asked if other mines are doing the salinity adjustment. Sandra B indicated that for marine tests the standard protocol is to adjust salinity.
- Note: Only one effluent collection for SLTT was done. The mine discharged for approximately 9 weeks.

Slides 10 & 11 – Effluent Characterization - Sublethal Toxicity Testing

- Think Zinc was the cause of the toxicity. Paired samples - one for toxicity and one for chemistry.
- Arctic amphipods used by Peter Chapman were collected from discharge environment. Temperature known to affect toxicity. The higher the temperature, the higher the toxicity.

Slide 12 to 13 - Reconnaissance Studies in Garrow Bay

- 16' boat, rifle, communications – radio to mine
- Plume Delineation was done using a boat and chest-waders

Slide 14 to 20 – Plume Delineation

- Chest waders and boat survey, working from outside in
- Field measurements taken of temperature, salinity and zinc concentration
- Samples collected at surface (top 30 cm) and subsurface (10 cm off bottom)
- Effluent was 40 cm 'thick' at mouth of Garrow Creek and decreased to 10 to 20 cm 'thick' 200 m offshore
- At about 25 to 26 ppt salinity, Zinc was down to 0.05 mg/L (detection limit)
- Negative regression between zinc concentration and salinity
- Ice present in bay really accelerates mixing process as plume moves around and under ice blocks.

Slide 21 Modeling - Frick *et al.* 2003 EPA visual plumes software

- Wind and current influences mixing.
- No ice involved in model
- In the future, discharge will be approximately 1/5 to 1/10 of what it was in 2003

Slide 27 – 2003 Reconnaissance Design

- Had planned to use Tigumiavik Harbour as a reference area, but access was too difficult.
- Reference was moved to approximately 500 m north of Garrow Creek mouth, based on results of plume delineation.
- Water Quality Monitoring as well as sediment and clam tissue data indicate background conditions.

Slide 28
- Previous surveys, clams collected under ice but tried to get clams from closer to the creek mouth this time using divers. Intertidal area devoid of life except for amphipods.
- 2 reference areas, one for intertidal and one for sub-tidal, access limited.
- Plume moved both ways, went far enough away north/south to be out of the plume. Also suspected a back eddy but wind a bigger issue.
- Three exposure stations sampled & 1 reference– were limited by divers and clams.

Slide 30
- Prawn trap was baited with cat food. Worked very well in Garrow Lake when baited with cat food. Tried in marine environment – amphipods ate cat food. Was crushed by ice on second night.
- Clams – composited 3 to 4 clams per size category and analyzed composite.

Slide 31
- N=3 means 3 composite samples each comprised of 3 to 4 clams
- Metal suite on body tissue
  - Intended to depurate but not enough clams
  - Pulled them out, put them in bags, scrubbed them in lab, pulled siphon and cleaned as best as could
  - Results include everything: siphon, sediment, gut contents, etc.
- No relationship between size and metal concentration

Slide 32 – Historical Metals Concentrations in Clam Tissue
- Fallis' historical clam data was on depurated clams. Sample size is number of composites in all cases except for BC research who analyzed individual clams.

Slide 34 – Sediment Survey
- Unable to collect sediment with standard Ponar grab
- Recovered kelp on gravel most times in spaces allowed for water movement
- Rate of failure consistent between near-field, far-field and ref area

Slide 35 – Metal Concentrations in Sediment 2003
- Intertidal concentrations higher than sub-tidal concentrations.

- Did analysis on 2mm (sand) fraction and down. In both subtidal and tidal targeted fine sediments.
- Note: likely the first metals data for intertidal sediment collected at this site.

Four options raised for discussion:

- conduct an EEM compliant study design
  - consultants don't think this can be done
- conduct a limited field study using alternative tools
  - diver assisted clams and sediment
    - underwater imagery (SIMS)
    - F&O Canada requires SIMS for intertidal areas by barge
- No further biological monitoring
  - Continue effluent and water quality monitoring
- Other?

Donald Bruce KIMB

From: Donald Bruce KIMB
Sent: August 18, 2004 3:59 PM
To: 'Blenkinsopp,Sandra [Edm]'
Cc: 'Beth Power'
Subject: Polaris EEM Program Update

I just got a call from Randy Baker via the satellite phone from site. The phone system at site is not demolished (and thus no email either) along with the Accommodation Building (so the crews are now living in Sea Containers and Trailers in the temporary camp). The satellite phones do not have good connections and the signal is often distorted. The connection breaks off frequently so they need to call back two or more times to accomplish a 5 minute call.

The 3 Azimuth scientists and the two divers they contracted are on site now. They arrived August 14th as planned. They have all their gear mobilized including the sampling equipment and bottles. We have left a rental compressor on site for the divers (they have to fill their bottles on site as can't ship them full on the airlines). They have set up a tent for shelter by the bay (for the divers) and we have assigned them access to quads for transportation as well as two boats. We purchased one of the boats specifically the EEM program and flew it in during the winter so that they would have a second boat as a safety back up. The winds in Garrow Bay can get fairly strong so we need to be able reach them incase they run into trouble in the first boat. Last year we used an older boat as the backup but it is not adequate for safety and we should have had something more reliable last year. They have the SIMS gear on site with them as well, so are ready to do the video survey.

Randy asked that I pass on to you that they are currently waiting for the ice to free up in Garrow Bay. Last year the ice was off the bay at this time. Randy is concerned that the ice may not leave the bay this year. As we committed, we are having them remain on site for two weeks incase the ice is just a bit later leaving this year. We mutually agreed with Environment Canada that a two week period was as an acceptable level of effort. Hopefully we get a strong wind that frees the ice so we can complete the planned work program.

For your information, we collected our monthly water samples from Garrow Creek yesterday as well as the sub-acute samples. However, it was foggy today so the plane from Resolute was unable to come into site but it didn't really matter as it doesn't look like the commercial flights could make it into Resolute today either. There is a slim chance the weather may change and the plane will try later today but it is a slim chance. Will try to sample again if it looks like the flight can get in tomorrow. If there isn't a flight tomorrow, then we'll try again next Tuesday.

Randy will try to give you a call in a few days to update you directly.
I am in contact with the site on a regular basis incase you want to pass any messages onto them.

Regards,
Bruce Donald

Donald Bruce KIMB

From: Blenkinsopp,Sandra [Edm] [Sandra.Blenkinsopp@EC.gc.ca]
Sent: August 18, 2004 4:24 PM
To: Donald Bruce KIMB
Subject: RE: Polaris EEM Program Update

Thanks for the update Bruce!

-----Original Message-----
From: Donald Bruce KIMB [mailto:bruce.donald@teckcominco.com]
Sent: Wednesday, August 18, 2004 3:59 PM
To: Blenkinsopp,Sandra [Edm]
Cc: Beth Power
Subject: Polaris EEM Program Update

I just got a call from Randy Baker via the satellite phone from site. The phone system at site is not demolished (and thus no email either) along with the Accommodation Building (so the crews are now living in Sea Containers and Trailers in the temporary camp). The satellite phones do not have good connections and the signal is often distorted. The connection breaks off frequently so they need to call back two or more times to accomplish a 5 minute call.

The 3 Azimuth scientists and the two divers they contracted are on site now. They arrived August 14th as planned. They have all their gear mobilized including the sampling equipment and bottles. We have left a rental compressor on site for the divers (they have to fill their bottles on site as can't ship them full on the airlines). They have set up a tent for shelter by the bay (for the divers) and we have assigned them access to quads for transportation as well as two boats. We purchased one of the boats specifically the EEM program and flew it in during the winter so that they would have a second boat as a safety back up. The winds in Garrow Bay can get fairly strong so we need to be able reach them incase they run into trouble in the first boat. Last year we used an older boat as the backup but it is not adequate for safety and we should have had something more reliable last year. They have the SIMS gear on site with them as well, so are ready to do the video survey.

Randy asked that I pass on to you that they are currently waiting for the ice to free up in Garrow Bay. Last year the ice was off the bay at this time. Randy is concerned that the ice may not leave the bay this year. As we committed, we are having them remain on site for two weeks incase the ice is just a bit later leaving this year. We mutually agreed with Environment Canada that a two week period was as an acceptable level of effort. Hopefully we get a strong wind that frees the ice so we can complete the planned work program.

For your information, we collected our monthly water samples from Garrow Creek yesterday as well as the sub-acute samples. However, it was foggy today so the plane from Resolute was unable to come into site but it didn't really matter as it doesn't look like the commercial flights could make it into Resolute today either. There is a slim chance the weather may change and the plane will try later today but it is a slim chance. Will try to sample again if it looks like the flight can get in tomorrow. If there isn't a flight tomorrow, then we'll try again next Tuesday.

Randy will try to give you a call in a few days to update you directly.
I am in contact with the site on a regular basis incase you want to pass any messages onto them.

Regards,
Bruce Donald

Donald Bruce KIMB

From: Blenkinsopp,Sandra [Edm] [Sandra.Blenkinsopp@EC.gc.ca]
Sent: August 20, 2004 12:51 PM
To: Donald Bruce KIMB
Subject: RE: Garrow Bay
Attachments: 20082004_IMAGE121.jpg

Hi Bruce

Here is the info that the weather office obtained from the Canadian Ice Service. I have an interpretation of the image from the sea ice service, but it was done on the assumption that Garrow Bay was on the northern end of the island. I have gone back to them for another interpretation.

S

-----Original Message-----
From: Donald Bruce KIMB [mailto:bruce.donald@teckcominco.com]
Sent: Thursday, August 19, 2004 3:32 PM
To: Blenkinsopp,Sandra [Edm]
Subject: RE: Garrow Bay

That would be appreciated. The ice has gone out in the adjacent bay but it always goes out first as it is more exposed and is a slightly different shape.
…bruce

From: Blenkinsopp,Sandra [Edm] [mailto:Sandra.Blenkinsopp@EC.gc.ca]
Sent: August 19, 2004 3:18 PM
To: Donald Bruce KIMB
Subject: Garrow Bay

Hi Bruce

I've spoken with the weather office staff (MSC) in our building and asked them to try to get some detailed info on the ice conditions in the area of Garrow Bay. If I find out anything that looks useful I'll pass it on.

S

APPENDIX 18

GARROW LAKE EFFLUENT DISCHARGE

MONITORING DATA

Bruce J. Donald
Reclamation Manager

March 31, 2004

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2003 ANNUAL Metal Mining Effluent Regulations Summary Report

Please find attached a **revised** Polaris Mine annual MMER summary report as the original report submitted January 27, 2004 was not complete and contained errors. There were no non-compliant concentrations related to Schedule 4 limits and no non-compliant results of the acute lethality tests during the year.

The following is included in our revised 2003 Annual Submission:

1. Requirements under Schedule 6
   - Identification of Site, Owner, Location, etc.
   - Non-Compliance information
   - Table 1 – Monthly Mean Concentrations, pH Range and Volume of Effluent
   - Table 2 – Results of Acute Lethality Tests and Daphnia Magna Monitoring Tests

2. Requirements under Part 1 Section 8
   - Results of studies conducted under Part 1, Section 4 (Effluent Characterization)
   - Results of studies conducted under Part 1, Section 5 (Sublethal Toxicity Testing)
   - Part 1, Section 6 Required Frequency of Effluent Characterization
   - Results of studies conducted under Part 1, Section 7 (Water Quality Monitoring)

During 2003, Teck Cominco conducted only one series of sublethal effluent testing in error contrary to the requirements of Part 1, Section 6 of the MMER. The report contains a letter from our consultants explaining the error. Teck Cominco intends to comply with section of the regulations as part of our monitoring program planned for 2004 and 2005.

The monitoring data required to be reported in electronic format has been emailed to you along with an electronic copy of this report (emailed March 31, 2004).

Please note that the location of the final discharge point previously submitted had a typographical error which has been corrected in this report.

If you have any questions regarding the annual report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Original signed by B. Donald
Bruce Donald

Attachments: Revised 2003 MMER Annual Report
cc: Walter Kuit (Teck Cominco Limited)
Joe Dahoy (Cascade Management)
Patrick Allard (Azimuth Consulting Group)

SCHEDULE 6

(Section 22)

SCHEDULE 6

(Section 22)

Mine Name : Polaris Mine

Mine Operator: Cominco Mining Partnership and Teck Cominco Ltd.

Mine Address: Box 188, Resolute, NU X0A 0B0

Telephone: (867) 253-2201 (Site Manager, Joe Dahoy)

E-mail: joe.dahoy@teckcominco.com

Location of Final Discharge Point:
Garrow Lake Siphons at 75^0 22' 32" N, 96^0 48' 37" W.

Reporting Period: January 1, 2003 to December 31, 2003

Date of Report: **Revised** March 31, 2003

Non-Compliance Information:

There were no non-compliant effluent discharges during 2003. All effluent sample results were within Schedule 4 limits.

There were no non-compliant acute lethality tests during 2003.

SCHEDULE 6

TABLE 1

MONTHLY MEAN CONCENTRATIONS, pH RANGE AND VOLUME OF EFFLUENT (1)(2)

MONTH	As (mg/L)	Cu (mg/L)	CN (mg/L)	Pb (mg/L)	Ni (mg/L)	Zn (mg/L)	TSS (mg/L)	Ra (Bq/L)	pH	Effluent Volume ($m^{3)}$
January	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
February	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
March	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
April	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
May	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
June	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
July	0.000	0.001	0.005	0.006	0.001	0.055	3.00	0.005	7.77 - 7.84	1,555,704
August	0.001	0.001	0.005	0.001	0.002	0.137	4.25	0.005	7.85 - 8.10	2,909,048
September	0.001	0.001	0.005	0.002	0.003	0.165	8.67	0.007	7.94 - 8.06	2,824,710
October	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
November	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]
December	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]	ND[1]

Note [1] - "ND" refers to any measurement not taken because there was no deposit from the final discharge point.

Note [2] - "NMR" refers to any measurement not taken because no measurement was required in accordance with the conditions set out in Section 13 of the regulations.

SCHEDULE 6
TABLE 2

RESULTS OF ACUTE LETHALITY TESTS AND DAPHNIA MAGNA MONITORING TESTS

DATE SAMPLE COLLECTED	EFFLUENT ACUTELY LETHAL TO RAINBOW TROUT (Yes or No)	EFFLUENT ACUTELY LETHAL TO DAPHNIA MAGNA (Yes or No)
30-Jul-03	No	No
20-Aug-03	No	No
16-Sep-03	No	No

REQUIREMENTS UNDER SECTION 4 OF PART 1

EFFLUENT CHARACTERIZATION

Monthly Sampling of Effluent in Garrow Creek for EEM

(Lat 75°22'32", Long 96°48'37")

	Conventional Water Chemistry and Water Quality Parameters									
Sample Date	Lab pH	Field pH	Field Temperature	Dissolved Oxygen	Hardness	Alkalinity	Ammonia	Cyanide	Nitrate	TSS
2003-07-29	7.84	7.69	0.30	10.53	459	46	0.08	*0.005*	0.102	*3*
2003-08-19	8.10	8.70	1.22	4.94	1130	103	0.03	*0.005*	0.225	8
2003-09-16	7.96	8.75	0.19	3.95	1540	122	0.04	NA	0.217	5

	Dissolved Metal Concentrations										
Sample Date	Aluminum	Cadmium	Iron	Mercury	Molybdenum	Arsenic	Copper	Lead	Nickel	Zinc	Radium ^{226}
2003-07-29	*0.1*	0.00016	0.02	*0.00005*	*0.002*	*0.0004*	0.00057	0.00319	0.00115	0.0625	*0.005*
2003-08-19	*0.1*	0.00037	0.03	*0.00005*	*0.002*	*0.0010*	0.00097	0.00046	0.00265	0.1460	*0.005*
2003-09-16	*0.1*	0.00047	0.04	*0.00005*	*0.005*	*0.0010*	0.00099	0.00046	0.00365	0.1860	*0.005*

NA - Not Available (no sample).

Note[1] - All concentrations are in mg/L, except pH which is in pH units and temperature which is in °C

Concentrations in *red italics* were set to the detection limit.

POLARIS MINE ANNUAL MMER REPORT

REQUIREMENTS UNDER SECTION 5, PART 1

APPENDIX A

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPAW 95-EPA West Coast: 7-day Topsmelt Survival and Growth Test.

APPENDIX B

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPS 1/Rm/27-EC: 92 hr Echinoderm (sand dollar) Fertilization Test (Annual)

APPENDIX C

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPA/600/4-91-003, Method 1009.0: Algae (*Champia parvula*) 7-day Sublethal Growth Test (Annual).

APPENDIX A

7-d Topsmelt Growth and Survival Toxicity Test

Reporting Requirements for Reference Method EPA/600/R-95/136

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for yearly sublethal toxicity testing were collected:
     Wednesday August 20, 2003 - 12:30 AM

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee)

Test Organisms Imported from External Supplier

i. Species of test organism
   - Topsmelt (*Atherinops affinis*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - Aquatic Bio Systems (ABS), Fort Collins, Colorado

iv. Date test species acquired on
   - August 21, 2003

v. Indications of deviations from EC guidance on the importation of test organisms
   - No deviations from EC requirements

vi. Percent mortality of fish in 24-hour period preceding the test
   - <10% mortality

vii. Age at start of test
   - 10 days post-hatch

viii. Unusual appearance, behaviour, or treatment of larvae before their use in the test
   - Nothing unusual, no excessive crowding of larvae, larvae appear healthy, disease-free, stress free,

ix. Confirmation that larvae are actively feeding and swimbladders are not inflated
   - Larvae actively feeding and swimbladders not inflated

x. Confirmation that temperature change was <3°C and dissolved oxygen was maintained at >6mg/L during transport
   - Temperature change was <2°C and dissolved oxygen supersaturated mg/L during transport

xi. Test organism acclimation rate at the testing laboratory
   - Holding water conditions upon arrival were DO=supersaturated, pH=7.3, T=22°C
   - Organisms were acclimated slowly overnight
   - Addition of EVS lab seawater at intervals of 30 – 60min to reach acceptable conditions
   - Organisms were acclimated to DO=8mg/L, salinity=28ppt,T=20°C

Reporting Requirements for Reference Method EPA/600/R-95/136

Test Facilities and Conditions

i. Test type & method
   - 7-day Topsmelt (*Atherinops affinis*) Survival and Growth Toxicity Test
   - Static renewal
   - Sample water was renewed daily
   - Reference Method - EPA/600/R-95/136 (EPAW 95-EPA West Coast)

ii. Indications of deviations from requirements in Sections 11 of Method EPA/600/R-95/136 (EPAW 95-EPA West Coast)
   - No deviations from requirements
   - Salinity controls were run
   - Sample water salinity was 5.3ppt

iii. Date and time for start of definitive test
   - Friday August 22, 2003 - 5:00 PM

iv. Test vessel description
   - 600mL beaker

v. Person(s) performing the test and verifying the results
   - Kevin Goodearle, Julianna Kalocai, Sioe Lie Kwee, Rachel DeWynter, Edmund Canaria, and Armando Tang

vi. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - pH - 7.9, T - 20.0°C, DO - 11.0mg/L, C - 9570µmhos/cm, (salinity - 5.3 ppt)

vii. Confirmation that no adjustment of sample or solution pH occurred
   - No pH adjustment

viii. Indication of aeration of test solutions before introduction of fish
   - Pre-aeration at 6.5mL/min/L for 30mins due to supersaturation of sample with O_2 when sample was heated to 20°C
   - DO was reduced from 11.0mg/L to 7.8 mg/L

ix. Indication that EC guidance document for salinity adjustment was followed
   - No deviations from EC guidance document on preparation of hypersaline brine
   - HSB prepared from natural seawater concentrated to 90ppt (by freezing/refreezing to remove frozen layer and concentrate salts)
   - No deviations from EC guidance document for salinity adjustment of sample
   - HSB was added to samples to salinity adjust them from 5.3ppt to 30ppt

x. Type and source of control/dilution water
   - UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xi. Concentrations and volumes tested
   - Concentrations (% effluent volume / total volume) tested and total volumes used were:
   - Control (0%) - 200 mL
   - Salinity Control (0%) - 200 mL
   - 4.5% - 200mL
   - 9.0% - 200mL
   - 18.1% - 200mL
   - 36.2% - 200mL
   - 72.3% - 200mL

xii. Number of replicated per concentration
   - 5 replicates per concentration

xiii. Number of organisms added to each test vessel
   - 5 fish per vessel

xiv. Manner and rate of exchange of test solutions
   - Daily renewal

Reporting Requirements for Reference Method EPA/600/R-95/136

xv. Measurements of dissolved oxygen, pH and temperature
- DO: 6.6 - 7.8 mg/L, pH: 7.7 - 8.2, T: 19.0 - 20.0 °C, salinity: 29 - 31 ppt

Results

i. Number and % of mortalities of fish in each test solution
- Totals from all 5 replicates are presented:
- Control (0%) - 1/25 = 4%
- Salinity Control - 0/25 = 0%
- 4.5% - 0/25 = 0%
- 9.0% - 0/25 = 0%
- 18.1% - 0/25 = 0%
- 36.2% - 0/25 = 0%
- 72.3% - 1/25 = 4%

ii. Average dry weight per original fish in test vessel
- Means from all 5 replicates are presented:
- Control (0%) - 1.18 mg
- Salinity Control - 1.14 mg
- 4.5% - 1.13 mg
- 9.0% - 1.32 mg
- 18.1% - 1.09 mg
- 36.2% - 1.11 mg
- 72.3% - 1.14 mg

iii. Estimate of 7-d LC_{50} (95% CL)
- 7-d LC_{50} concentration > 72.3% effluent (highest concentration tested due to dilution for salinity adjustment)
- Quantal statistic methods not applicable

iv. Estimate of 7-d IC_{25} (95% CL) for growth
- 7-d IC_{25} concentration > 72.3% effluent (highest concentration tested due to dilution for salinity adjustment)
- Quantal statistic methods not applicable

v. Current reference toxicity tests (95% CL) for 7-d LC_{50} for survival and 7-d IC_{50} for growth
- Reference toxicity tests for Toxicant: Copper
- Test conducted on August 22, 2003, same day as effluent test
- Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
- 7-d LC_{50} survival = 122mg/L Cu, 95% CL = 111-135mg/L
- 7-d IC_{50} growth = 122mg/L Cu, 95% CL = 106-132mg/L

vi. Reference toxicity warning limits (+/- SD) for 7-d LC_{50} for survival and 7-d IC_{50} for growth
- Reference toxicity tests for Toxicant: Copper
- 7-d LC_{50} survival = 139 ± 63mg/L Cu,
- 7-d IC_{50} growth = 136 ± 52mg/L Cu

APPENDIX B

92-h Echinoderm Fertilization Test

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for yearly sublethal toxicity testing were collected:
     Wednesday August 20, 2003 - 12:30 AM

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee)

Test Organisms

i. Species of test organism
   - Sandollar Echinoid (*Dendraster excentricus*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - M-REP, Escondido, California
   - All adults providing gametes are from the same population and source
   - Gametes are spawned in-house at EVS

iv. Date test species acquired on
   - August 22, 2003

v. Holding time and conditions for adults
   - Adults received at the testing laboratory the day of the test, shipped overnight

vi. Indications of deviations from EC guidance on the importation of test organisms
   - No deviations from EC requirements

vii. Weekly percent mortality of adults being held over 7d preceding test
   - <2% per day over the 7 days preceding the test

viii. Age of test organisms
   - < 4 hours after spawning

ix. Unusual appearance, behaviour, or treatment of adults or gametes before test start
   - Organisms appear healthy

Test Facilities and Conditions

i. Test type & method
   - Echinoderm (*Dendraster excentricus*) Fertilization Toxicity Test
   - Static
   - Reference Method – EPS/1/RM/27 with 1997 amendments

ii. Test duration
   - 10:10 min (10min sperm + 10min sperm & egg)

iii. Date and time for start of definitive test

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- Friday August 22, 2003 - 5:00 PM

iv. Test vessel description
- 16 x 125mm test tubes

v. Person(s) performing the test and verifying the results
- Kevin Goodearle, Julianna Kalocai, Sioe Lie Kwee, Rachel DeWynter, Edmund Canaria, and Armando Tang

vi. Indication of rate and duration of pre-aeration of test solutions before initiation of test
- No pre-aeration

vii. Confirmation that no adjustment of sample or solution pH occurred
- No pH adjustment

viii. Procedure for sample filtration
- No sample filtration

ix. Procedure for preparation of hypersaline brine (HSB) as per EC guidance document on salinity adjustment – July 1997
- No deviations from EC guidance for salinity adjustment

x. Procedure for salinity adjustment as per EC guidance document on salinity adjustment – July 1997
- No deviations from EC guidance for salinity adjustment
- Salinity adjusted from 5ppt to 29ppt

xi. Type and source of control/dilution water
- UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xii. Concentrations and volumes tested
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- Control (0%) - 10mL
- Salinity Control (0%) - 10mL
- 4.6% - 10mL
- 9.1% - 10mL
- 18.2% - 10mL
- 36.5% - 10mL
- 73.0% - 10mL

xiii. Number of replicated per concentration
- 4 replicates per treatment concentration

xiv. Number of organisms per container
- 2000 eggs per 10mL vessel

xv. Measurements of pH and dissolved oxygen in sample water before use
- pH - 8.3, DO - 8.4mg/L

xvi. Measurements of pH, temperature, dissolved oxygen, and salinity during test
- pH - 7.9-8.4, T - 15.0-15.5°C, DO - 8.1-8.4mg/L, salinity - 29ppt

Results

i. Number and % of fertilized eggs in each test concentration
- (Number is equal to percent since totals were 100)
- Control (0%): #F = 51, 50, 52, 54 #UF = 49, 50, 49, 46
- Salinity Control: #F = 51, 52, 50, 51 #UF = 49, 48, 50, 49
- 4.6%: #F = 35, 40, 29, 45 #UF = 65, 60, 71, 55
- 9.1%: #F = 36, 28, 33, 25 #UF = 64, 72, 67, 75
- 18.2%: #F = 22, 24, 18, 20 #UF = 78, 78, 82, 80
- 36.5%: #F = 12, 8, 7, 10 #UF = 88, 92, 93, 90
- 73.0%: #F = 1, 0, 2, 0 #UF = 99, 100, 98, 100

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

ii. Estimate of IC_{25} (95% CL) for fertilization success
- IC_{25} concentration = 3.8 (1.1 - 7.2)% v/v effluent
- Quantal statistic method = log linear interpolation

iii. Current reference toxicity tests (95% CL) for IC_{50} for fertilization
- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test conducted on August 22, 2003, same day as effluent test
- Reference test conducted under same conditions
- IC_{50} for fertilization = 1.3mg/L SDS, 95% CL = 1.1-1.5mg/L

APPENDIX C

7-d Sublethal *Champia* (Algae) Toxicity Test

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for yearly sublethal toxicity testing were collected:
     Wednesday August 20, 2003 - 12:30 AM

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 1 x 4L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee)

vii. Temperature of water upon receipt at lab
   - 13°C

Test Organisms

i. Species of test organism
   - Algae (*Champia parvula*)

ii. Name and city of testing laboratory
   - Saskatchewan Research Council [SRC], Saskatoon, SK

iii. Source of test species
   - Sexually mature male and female branches
   - Obtained from USEPA, Hatfield Marine Science Center, Newport Oregon, 1995
   - Appear in good health
   - Females have trichogynes, males have sori with spermatia

Test Facilities and Conditions

i. Test type & method
   - *Champia parvula* sexual reproduction test
   - Static, non-renewal
   - 2-day exposure, followed by 5-7 day recovery period for cystocarp development
   - Reference Method - EPA/600/4-91/003, Method 1009.0

ii. Date and time for start of definitive test
   - Friday August 22, 2003 – 10:00 AM

iii. Test vessel description
   - 270mL transparent polystyrene cups with polystyrene lids

iv. Person(s) performing the test and verifying the results
   - Mary Moody

v. Indication of pre-aeration of test solutions
   - No pre-aeration

vi. Confirmation that no pH adjustment of sample or solution occurred
   - No pH adjustment

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

vii. Indication that EC guidance document for salinity adjustment was followed
- No deviations from EC guidance document on preparation of hypersaline brine
- HSB prepared from natural seawater at 90ppt
- No deviations from EC guidance document for salinity adjustment of sample
- Salinity adjustment: 642mL effluent + 258mL HSB + 9mL test nutrient solution
- Salinity of samples adjusted from 5ppt to 30ppt

viii. Type and source of control/dilution water
- Natural seawater collected at the Pacific Environmental Center, Environment Canada, North Vancouver, BC
- Filtered to 0.2µm and autoclaved prior to use
- Salinity adjusted as per EC guidance document to 30ppt with HSB from the same source

ix. Concentrations and volumes of test solutions
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- Control (Natural Seawater) (0%) - 100mL, 4.5cm depth
- Salinity Control Brine (0%) - 100mL, 4.5cm depth
- 4.5% - 100mL, 4.5cm depth
- 8.9% - 100mL, 4.5cm depth
- 17.8% - 100mL, 4.5cm depth
- 35.6% - 100mL, 4.5cm depth
- 71.3% - 100mL, 4.5cm depth

x. Number of replicated per concentration
- 3 replicates per concentration

xi. Number of organisms per test chamber
- 5 female branches + 2 male branches per chamber

xii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample before use
- pH - 7.93, T - 23.5°C, DO - 9.4mg/L, salinity - 5ppt

xiii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample during test
- DO: 7.8 - 8.0 mg/L, pH: 7.74 - 8.98, T: 23°C, salinity: 30ppt

Results

i. Number and % mortality of female plants after recovery in each test solution
- Totals from all 3 replicates are presented:
- Control (0%): 0 (0%) mortality
- Salinity Control (0%): 0 (0%) mortality
- 4.5%: 0 (0%) mortality
- 8.9%: 0 (0%) mortality
- 17.8%: 0 (0%) mortality
- 35.6%: 0 (0%) mortality
- 71.3%: 0 (0%) mortality

ii. Mean number of cystocarps per plant in each test concentration
- Control (0%): 57.4; 49.6; 44.2
- Salinity Control (0%): 66.4; 44.0; 45.2
- 4.5%: 52.2; 51.4; 57.4
- 8.9%: 61.2; 63.6; 41.2
- 17.8%: 30.4; 34.4; 18.6
- 35.6%: 6.6; 6.0; 7.6
- 71.3%: 0.0; 2.4; 1.4

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

iii. Estimate of IC_{25} (95% CL) for cystocarp development
- IC_{25} concentration = 13.6 (9.0-16.0)% effluent v/v
- Quantal statistic method was linear interpolation

iv. Current reference toxicity tests (95% CL) for IC_{50} for cystocarp development
- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test conducted on July 29, 2003, within 30 days of effluent test
- Reference toxicant test was conducted under the same experimental conditions as the effluent test
- IC_{50} cystocarp development = 1.19mg/L SDS, 95% CL = 1.14-1.23mg/L

v. Reference toxicity warning limits (+/- 2SD) for IC_{50} for cystocarp development
- Reference toxicity tests for Toxicant: SDS
- 7-d IC_{50} growth = 1.47 (1.17-1.84) mg/L SDS

REQUIREMENTS UNDER SECTION 6 OF PART 1

SUBLETHAL TOXICITY TESTING FREQUENCY

Azimuth Consulting Group Inc.
218-2902 West Broadway
Vancouver, BC V6K 2G8

Phone: 604-730-1220
Fax: 604-739-8511

Our File #: TC-03-03

March 18, 2004

Sidney F. Bruinsma
Enforcement/Emergencies Officer, Nunavut
Northern Division, Environmental Protection Branch
Environment Canada
Box 1870, Iqaluit
Nunavut X0A 0H0

Dear Mr. Bruinsma:

Re: Polaris Mine EEM – Missed Sublethal Toxicity Test Sampling Event

Further to our recent discussion, we are pleased to document the issues and circumstances surrounding the missed 2003 sampling event for sublethal toxicity testing (SLTT) of effluent at Teck Cominco's Polaris Mine.

First, Azimuth Consulting Group (Azimuth) takes full responsibility for the missed sampling event, which resulted from an oversight on our part. Our staff have considerable experience conducting environmental effects monitoring (EEM) programs under the Pulp and Paper Effluent Regulations (PPER), which have been in place for some years. We understand the importance of the SLTT as an EEM investigative tool and would not knowingly miss a sampling event. The oversight comes from our interpretation of the new Metal Mining Effluent Regulations (MMER) and how they apply to the Polaris Mine, which has a unique discharge situation (i.e., limited to approximately 60 days per calendar year). Under both the PPER and MMER, two sampling events are required for the SLTT. However, if the discharge period is less than 120 days, the PPER require only one sampling event. We mistakenly assumed that these terms would also apply to the MMER, which provide less detail pertaining to the requirements of this test than the PPER. This issue was compounded by the unique discharge characteristics and receiving environment of the Polaris Mine, which make the MMER more difficult to interpret and apply compared to mines discharging under more usual conditions.

We became aware of the missed SLTT event during a December 2003 workshop intended to present results of 2003 reconnaissance studies carried out at the mine and to seek feedback from the Technical Advisory Committee (TAP) on our proposed study design for the Polaris Mine. Following our presentation, Ms. Sandra Blenkinsopp pointed out that two sampling events were indeed required under MMER. She then indicated that Environment Canada would contact us to further discuss the implications of this matter.

We agree that the missed SLTT event is unfortunate and will ensure that this test is carried out twice during the 2004 and 2005 discharge periods.

Please do not hesitate to contact us if you have any questions or require further clarification.

Sincerely,

Azimuth Consulting Group Inc.

Patrick Allard, M.Sc., R.P.Bio.

cc: Randy Baker (Azimuth)
Bruce Donald (Teck Cominco)

REQUIREMENTS UNDER SECTION 7 OF PART 1

WATER QUALITY MONITORING

Monthly Sampling of Exposure Station in Garrow Bay at mouth of Garrow Creek

(Lat 75°22'15", Long 96°48'30")

	Conventional Water Chemistry and Water Quality Parameters									
Sample Date	Lab pH	Field pH	Field Temperature	Dissolved Oxygen	Hardness	Alkalinity	Ammonia	Cyanide	Nitrate	TSS
2003-07-29	7.86	7.75	0.47	10.29	456	46	0.04	*0.005*	0.098	4
2003-08-19	8.13	8.36	1.08	5.01	1120	104	0.03	*0.005*	0.229	8
2003-09-16	7.85	8.38	-0.76	5.45	3620	117	0.03	*0.005*	0.159	10

	Dissolved Metal Concentrations										
Sample Date	Aluminum	Cadmium	Iron	Mercury	Molybdenum	Arsenic	Copper	Lead	Nickel	Zinc	Radium ^{226}
2003-07-29	*0.1*	0.00015	0.03	*0.00005*	*0.002*	*0.0004*	0.00080	0.00435	0.00121	0.0594	*0.005*
2003-08-19	*0.1*	0.00038	0.05	*0.00005*	*0.002*	*0.001*	0.00106	0.00108	0.00304	0.1490	*0.005*
2003-09-16	*0.1*	0.00024	0.03	*0.00005*	0.006	0.001	0.00059	0.00043	0.00169	0.0881	0.005

Note[1] - All concentrations are in mg/L, except pH which is in pH units, Radium ^{226} which is in Bq/L and temperature which is in °C

Concentrations in *red italics* were set to the detection limit.

Monthly Sampling of Reference Station in Garrow Bay (1 km NE of Exposure Station)

(Lat 75°22'40", Long 96°47'12")

	Conventional Water Chemistry and Water Quality Parameters									
Sample Date	Lab pH	Field pH	Field Temperature	Dissolved Oxygen	Hardness	Alkalinity	Ammonia	Cyanide	Nitrate	TSS
2003-07-29	7.67	7.13	-0.27	9.27	989	33	0.03	*0.005*	*0.005*	*3*
2003-08-19	7.87	8.32	0.18	5.50	5830	115	*0.02*	*0.005*	*0.005*	32
2003-09-16	7.78	8.35	-1.36	3.42	5930	113	0.08	*0.005*	*0.005*	9

	Dissolved Metal Concentrations										
Sample Date	Aluminum	Cadmium	Iron	Mercury	Molybdenum	Arsenic	Copper	Lead	Nickel	Zinc	Radium ^{226}
2003-07-29	*0.1*	*0.00002*	0.01	*0.00005*	*0.002*	*0.0004*	0.00023	0.00032	0.00021	0.0010	*0.005*
2003-08-19	*0.1*	0.00003	*0.01*	*0.00005*	0.010	0.0020	0.00044	0.00021	0.00033	0.0007	*0.005*
2003-09-16	*0.1*	0.00003	0.02	*0.00005*	0.011	*0.0010*	0.00028	0.00052	0.00026	0.0011	*0.005*

Note[1] - All concentrations are in mg/L, except pH which is in pH units, Radium ^{226} which is in Bq/L and temperature which is in ^{o}C

Concentrations in *red italics* were set to the detection limit.

Bruce J. Donald
Reclamation Manager

May 13, 2004

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2004 1st Quarter Metal Mining Effluent Regulations Report

Despite having a designated discharge location for effluent identified under Section 9 of the MMER, there was no discharge from the Garrow Lake Tailings Impoundment Area during the period January 1, 2004 to March 31, 2004. While there is no data to report, I have completed the monitoring report as required by the regulations and have attached it to this letter.

If you have any questions regarding the quarterly report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Bruce Donald

Attachments: 1st Quarter 2004 Monitoring Report

cc:
Walter Kuit (Teck Cominco Limited)
Polaris Mine Site Files
Randy Baker (Azimuth Consulting Group)

POLARIS MINE – MMER MONITORING REPORT

1st QUARTER 2004

APPENDIX A

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/13

APPENDIX B

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/14

APPENDIX C

i. Concentration & monthly mean concentrations of each deleterious substance of Schedule 4
ii. pH of the effluents samples as required by subsection 12(1)
iii. Description of sample collection method
iv. Total volume of effluent deposited during each month of the quarter as per section 19
v. Mass loading of the deleterious substances set out in Schedule 4 and as per section 20

APPENDIX D

i. Results of the effluent characterization as per paragraph 15(1)(a)

APPENDIX A

Reporting Requirements for Reference Method EPS 1/RM/13

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Percent mortality of fish in stock tank(s)
   - None to report. There were no tests conducted during the period

v. Species of test organism
   - None to report as there were no tests conducted during the period

vi. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vii. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

viii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

ix. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

x. Indication of aeration of test solutions before introduction of fish
   - None to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Number of fish added to each test vessel
   - No fish added as there were no tests conducted during the period

xiv. Mean and range of fork length of control fish at end of test
   - No data to report as there were no tests conducted during the period

xv. Mean wet weight of individual control fish at end of the test
   - No data to report as there were no tests conducted during the period

xvi. Estimated loading density of fish in test solutions
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/13 - Continued

Section 8.1.3 Results

i. Number of mortalities of fish in each test solution
   - None to report. No tests conducted during the period

ii. Number of control fish showing atypical/stressed behaviour
   - None to report. No tests conducted.

iii. Mean mortality rate in solutions of effluent and control water
   - None to report. No tests conducted

iv. Estimate of 96-h LC50 in multi-concentration tests
   - No data to report. No tests conducted

v. Most recent 96-h LC50 for reference toxicity test(s)
   - No data to report. No tests conducted

APPENDIX B

Reporting Requirements for Reference Method EPS 1/RM/14

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Species of test organism
   - None to report as there were no tests conducted during the period

v. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vi. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

vii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

viii. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

ix. Indication of any adjustment of hardness of effluent sample
   - No adjustment to report as there were no tests conducted during the period

x. Indication of any aeration of sample
   - No indication to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Estimates of time to first brood, average number of neonates per brood, and percent mortality during the seven-day period prior to the test
   - No data to report as there were no tests conducted during the period

xiv. Number of neonates per test vessel and milliliters of solution per daphnid
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/14 - Continued

Section 8.1.3 Results

i. Number of dead and/or immobile daphnids in each test solution including controls
   - No data to report. No tests conducted during the period.

ii. For single-concentration test the number of daphnids dead in each of three replicate effluent solutions and in each of three replicate control solutions at end of test. Also report the mean value.
   - No data to report. No tests conducted during the period.

iii. Estimate of 48-h LC50 and 95% confidence limits in multi-concentration tests, 48-h EC50 for immobilization and 95% confidence limits, indication of statistical method on which results are based.
   - No data to report. No tests conducted during the period

iv. Most recent 48-h LC50 for reference toxicant test(s), reference chemical(s), date test initiated, historic geometric mean LC50 and warning limits.
   - No data to report. No tests conducted during the period.

APPENDIX C

2004 1st QUARTER MMER REPORT

LOCATION - FINAL DISCHARGE POINT FROM GARROW LAKE (GARROW LAKE DAM SIPHONS)

CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4 SAMPLED WEEKLY

Sample Taken During The Week of	Date Sample Taken	DELETERIOUS SUBSTANCE (mg/L)[1]								pH[1]	Collection Method
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]		
05-Jan-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
12-Jan-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
19-Jan-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
26-Jan-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
02-Feb-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
09-Feb-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
16-Feb-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
23-Feb-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
01-Mar-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
08-Mar-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
15-Mar-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
22-Mar-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
29-Mar-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L and pH which is in pH units

Note [2] - "nd" refers to no deposit of effluent discharge to sample

MONTHLY MEAN CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4

MONTH OF	MONTHLY MEAN CONCENTRATION[1] OF DELETERIOUS SUBSTANCE[3]							
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226
January/04	nd[2]	nd[2]	na[2]	na[2]	na[2]	na[2]	na[2]	nd[2]
February/04	nd[2]	n[2]	n[2]	n[2]	n[2]	n[2]	n[2]	nd[2]
March/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L

Note [2] - "nd" refers to no deposit of effluent to sample

Note[3] - Monthly Mean Concentrations - the MEAN value of the concentrations measured in all water samples collected during each month when a deleterious substance is deposited.

MASS LOADING OF DELETERIOUS SUBSTANCE FOR EACH DAY SAMPLED

Sample Taken During The Week of	Date Sample Taken	DAILY MASS LOADING OF DELETERIOUS SUBSTANCE (kg/day)[1]								Average Daily Flow Rate (m^3/day)
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	
05-Jan-04	nd[2]	0	0	0	0	0	0	0	0	0
12-Jan-04	nd[2]	0	0	0	0	0	0	0	0	0
19-Jan-04	nd[2]	0	0	0	0	0	0	0	0	0
26-Jan-04	nd[2]	0	0	0	0	0	0	0	0	0
02-Feb-04	nd[2]	0	0	0	0	0	0	0	0	0
09-Feb-04	nd[2]	0	0	0	0	0	0	0	0	0
16-Feb-04	nd[2]	0	0	0	0	0	0	0	0	0
23-Feb-04	nd[2]	0	0	0	0	0	0	0	0	0
01-Mar-04	nd[2]	0	0	0	0	0	0	0	0	0
08-Mar-04	nd[2]	0	0	0	0	0	0	0	0	0
15-Mar-04	nd[2]	0	0	0	0	0	0	0	0	0
22-Mar-04	nd[2]	0	0	0	0	0	0	0	0	0
29-Mar-04	nd[2]	0	0	0	0	0	0	0	0	0

Note[1] - Mass Loading is in kilograms per day of the deleterious substance deposited except Radium 226 which is in Bq per day

Note[2] - "nd" refers to no deposit of effluent to sample

MASS LOADING PER CALENDAR MONTH FOR EACH DELETERIOUS SUBSTANCE

CALENDAR MONTH OF	MASS LOADING[1] FOR DELETERIOUS SUBSTANCE (kg/month)[2]								Average Weekly Flow Rate[3] (m^3/week)	Total Monthly Volume[4] (m^3/month)
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[2]		
January/04	0	0	0	0	0	0	0	0	0	0
February/04	0	0	0	0	0	0	0	0	0	0
March/04	0	0	0	0	0	0	0	0	0	0

Note[1] - Total Mass Loading for Calendar month calculated by multiplying the Average Daily Mass Loading for the Month x # days in the month

Note[2] - Mass loading units are in kg per month except Radium 226, which is in Bq permonth

Note[3] - Average Weekly Flow Rate calculated by multiplying Average Daily Flow Rate x 7 days per week

Note[4] - Total Monthly Volume calculated by multiplying Average Daily Flow Rate for the month x days in month

APPENDIX D

RESULTS OF EFFLUENT CHARACTERIZATION

AS PER PARAGRAPH 15(1)(a)

No effluent samples were collected during the 1st Quarter of 2004 as there was no effluent discharge.
No Acute Lethality Testing conducted during the quarter as there was no effluent being discharged.

Bruce J. Donald
Reclamation Manager

August 11, 2004

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2004 2nd Quarter Metal Mining Effluent Regulations Report

Despite having a designated discharge location for effluent identified under Section 9 of the MMER, there was no discharge from the Garrow Lake Tailings Impoundment Area during the period April 1, 2004 to June 30, 2004. While there is no data to report, I have completed the monitoring report as required by the regulations and have attached it to this letter.

If you have any questions regarding the quarterly report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Bruce Donald

Attachments: 2nd Quarter 2004 Monitoring Report

cc:
Walter Kuit (Teck Cominco Limited)
Randy Baker (Azimuth Consulting Group)

POLARIS MINE – MMER MONITORING REPORT

2nd QUARTER 2004

APPENDIX A

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/13

APPENDIX B

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/14

APPENDIX C

i. Concentration & monthly mean concentrations of each deleterious substance of Schedule 4
ii. pH of the effluents samples as required by subsection 12(1)
iii. Description of sample collection method
iv. Total volume of effluent deposited during each month of the quarter as per section 19
v. Mass loading of the deleterious substances set out in Schedule 4 and as per section 20

APPENDIX D

i. Results of the effluent characterization as per paragraph 15(1)(a)

APPENDIX A

Reporting Requirements for Reference Method EPS 1/RM/13

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Percent mortality of fish in stock tank(s)
   - None to report. There were no tests conducted during the period

v. Species of test organism
   - None to report as there were no tests conducted during the period

vi. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vii. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

viii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

ix. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

x. Indication of aeration of test solutions before introduction of fish
   - None to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Number of fish added to each test vessel
   - No fish added as there were no tests conducted during the period

xiv. Mean and range of fork length of control fish at end of test
   - No data to report as there were no tests conducted during the period

xv. Mean wet weight of individual control fish at end of the test
   - No data to report as there were no tests conducted during the period

xvi. Estimated loading density of fish in test solutions
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/13 - Continued

Section 8.1.3 Results

i. Number of mortalities of fish in each test solution
   - None to report. No tests conducted during the period

ii. Number of control fish showing atypical/stressed behaviour
   - None to report. No tests conducted.

iii. Mean mortality rate in solutions of effluent and control water
   - None to report. No tests conducted

iv. Estimate of 96-h LC50 in multi-concentration tests
   - No data to report. No tests conducted

v. Most recent 96-h LC50 for reference toxicity test(s)
   - No data to report. No tests conducted

APPENDIX B

Reporting Requirements for Reference Method EPS 1/RM/14

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Species of test organism
   - None to report as there were no tests conducted during the period

v. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vi. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

vii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

viii. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

ix. Indication of any adjustment of hardness of effluent sample
   - No adjustment to report as there were no tests conducted during the period

x. Indication of any aeration of sample
   - No indication to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Estimates of time to first brood, average number of neonates per brood, and percent mortality during the seven-day period prior to the test
   - No data to report as there were no tests conducted during the period

xiv. Number of neonates per test vessel and milliliters of solution per daphnid
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/14 - Continued

Section 8.1.3 Results

i. Number of dead and/or immobile daphnids in each test solution including controls
   - No data to report. No tests conducted during the period.

ii. For single-concentration test the number of daphnids dead in each of three replicate effluent solutions and in each of three replicate control solutions at end of test. Also report the mean value.
   - No data to report. No tests conducted during the period.

iii. Estimate of 48-h LC50 and 95% confidence limits in multi-concentration tests, 48-h EC50 for immobilization and 95% confidence limits, indication of statistical method on which results are based.
   - No data to report. No tests conducted during the period

iv. Most recent 48-h LC50 for reference toxicant test(s), reference chemical(s), date test initiated, historic geometric mean LC50 and warning limits.
   - No data to report. No tests conducted during the period.

APPENDIX C

2004 2nd QUARTER MMER REPORT

LOCATION - FINAL DISCHARGE POINT FROM GARROW LAKE (GARROW LAKE DAM SIPHONS)

CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4 SAMPLED WEEKLY

Sample Taken During The Week of	Date Sample Taken	DELETERIOUS SUBSTANCE (mg/L)[1]								pH[1]	Collection Method
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]		
05-Apr-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
12-Apr-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
19-Apr-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
26-Apr-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
03-May-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
10-May-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
17-May-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
24-May-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
31-May-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
07-Jun-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
14-Jun-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
21-Jun-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
28-Jun-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L and pH which is in pH units

Note [2] - "nd" refers to no effluent discharge to sample

MONTHLY MEAN CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4

MONTH OF	MONTHLY MEAN CONCENTRATION[1] OF DELETERIOUS SUBSTANCE[3]							
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226
April/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
May/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
June/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L

Note [2] - "nd" refers to no effluent discharge to sample

Note[3] - Monthly Mean Concentrations - the MEAN value of the concentrations measured in all water samples collected during each month when a deleterious substance is deposited.

MASS LOADING OF DELETERIOUS SUBSTANCE FOR EACH DAY SAMPLED

Sample Taken During The Week of	Date Sample Taken	DAILY MASS LOADING OF DELETERIOUS SUBSTANCE (kg/day)[1]								Average Daily Flow Rate (m^3/day)
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	
05-Apr-04	nd[2]	0	0	0	0	0	0	0	0	0
12-Apr-04	nd[2]	0	0	0	0	0	0	0	0	0
19-Apr-04	nd[2]	0	0	0	0	0	0	0	0	0
26-Apr-04	nd[2]	0	0	0	0	0	0	0	0	0
03-May-04	nd[2]	0	0	0	0	0	0	0	0	0
10-May-04	nd[2]	0	0	0	0	0	0	0	0	0
17-May-04	nd[2]	0	0	0	0	0	0	0	0	0
24-May-04	nd[2]	0	0	0	0	0	0	0	0	0
31-May-04	nd[2]	0	0	0	0	0	0	0	0	0
07-Jun-04	nd[2]	0	0	0	0	0	0	0	0	0
14-Jun-04	nd[2]	0	0	0	0	0	0	0	0	0
21-Jun-04	nd[2]	0	0	0	0	0	0	0	0	0
28-Jun-04	nd[2]	0	0	0	0	0	0	0	0	0

Note[1] - Mass Loading is in kilograms per day of the deleterious substance deposited except Radium 226 which is in Bq per day

Note [2] - "nd" refers to no effluent discharge to sample

MASS LOADING PER CALENDAR MONTH FOR EACH DELETERIOUS SUBSTANCE

CALENDAR MONTH OF	MASS LOADING[1] FOR DELETERIOUS SUBSTANCE (kg/month)[2]								Average Weekly Flow Rate[3] (m^3/week)	Total Monthly Volume[4] (m^3/month)
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[2]		
April/04	0	0	0	0	0	0	0	0	0	0
May/04	0	0	0	0	0	0	0	0	0	0
June/04	0	0	0	0	0	0	0	0	0	0

Note[1] - Total Mass Loading for Calendar month calculated by multiplying the Average Daily Mass Loading for the Month x # days in the month

Note[2] - Mass loading units are in kg per month except Radium 226, which is in Bq permonth

Note[3] - Average Weekly Flow Rate calculated by multiplying Average Daily Flow Rate x 7 days per week

Note[4] - Total Monthly Volume calculated by multiplying Average Daily Flow Rate for the month x days in month

Bruce J. Donald
Reclamation Manager

November 17, 2004

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2004 3rd Quarter Metal Mining Effluent Regulations Report

Please find attached the Metal Mining Effluent Report for the Polaris Mine for the 3rd Quarter of 2004. Discharge from Garrow Lake is no longer controlled by siphoning as Garrow Dam was removed earlier this year. As a result the timing of flow and a wide fluctuation in the flow rates was experienced this year. Flow initiated at the beginning of July, later than expected due to an unseasonably cold winter and spring. Flow continued through July and August.

The associated water quality sampling and environmental effects monitoring were conducted as required but with some complications. To ensure we captured two sub-lethal toxicity tests this year, we initiated testing with our first water sampling event of the season. However, on our first attempt, there were problems with the laboratory specimens (the Echinoderms were stimulated to spawn and only one of 39 partially spawned so the test was not initiated) and the Champia parvula sexual reproduction tests were not conducted due to problems at the commercial laboratory. Sandra Blenkinsopp was kept informed of these issues as they arose. We subsequently conducted two additional sub-acute toxicity tests which were successfully processed. The available results from all three sub-acute sampling events are presented in this report.

The first water sample of the discharge season taken on July 7th 2004 at the final discharge point was out of compliance with respect to Total Suspended Solids (TSS). Laboratory results indicated a TSS concentration of 117 mg/L compared to the MMER Schedule 4 limit of 30 mg/L for a single grab sample. All other Schedule 4 parameters were compliant. Concurrent with the July 7th sample, a set of monthly acute lethality samples were

also taken. The results of the acute lethality were compliant with the MMER and showed no acute toxicity to either the Rainbow Trout or the Daphnia magna (i.e. LC50s in both cases were > 100% effluent). Subsequent weekly sampling results for TSS, metals concentrations and acute toxicity results have all been compliant. Sid Bruinsma and Craig Broome were both promptly notified upon our receiving the laboratory results.

Effluent from Garrow Lake ceased flowing by mid-August but surface run off from adjacent slopes maintained water flow at the designated final discharge point into August. By August 17th there was still water at the final discharge point in a pool but the flow was too low to be measured. However, we continued to collect water samples for the remainder of August, so there are water quality results presented in the attached report until August 31, 2004 but the loading calculations are zero due to the lack of flow for the last three weekly samples. The flow conditions during August as well as their implications for effluent sampling were discussed with Environmental Canada representatives in early August.

I will forward a paper copy of this report by mail. Please contact me if there are any questions related to enclosed information.

Yours truly,
Original signed by B Donald

Bruce Donald

Attachments: 3rd Quarterly Monitoring Report

cc:
Walter Kuit (Teck Cominco Limited)
Randy Baker (Azimuth Consulting Group)

POLARIS MINE – MMER MONITORING REPORT

3rd QUARTER 2004

APPENDIX A

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/13: 96 hr acute rainbow trout test

APPENDIX B

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/14: 72 hr acute *Daphnia magna* test

APPENDIX C

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPAW 95-EPA West Coast: 7-day Topsmelt Survival and Growth Tests.

APPENDIX D

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPS 1/Rm/27-EC: 92 hr Echinoderm (sand dollar) Fertilization Test

APPENDIX E

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPA/600/4-91-003, Method 1009.0: Algae (*Champia parvula*) 7-day Sublethal Growth Tests

APPENDIX F (Mass Loadings)

i. Concentration & monthly mean concentrations of each deleterious substance of Schedule 4
ii. pH of the effluents samples as required by subsection 12(1)
iii. Description of sample collection method
iv. Total volume of effluent deposited during each month of the quarter as per section 19
v. Mass loading of the deleterious substances set out in Schedule 4 and as per section 20

APPENDIX G

i. Results of the effluent characterization as per paragraph 15(1)(a)

APPENDIX A

96-h Acute Rainbow Trout Toxicity Test

Reporting Requirements for Reference Method EPS 1/RM/13

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for monthly acute toxicity testing were collected
   - Test 1: Wednesday July 7, 2004 – 2200h
   - Test 2: Tuesday July 27, 2004 – 2130h
   - Test 3: Tuesday August 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 2 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) – July 7, July 27, 2004
   - Patrick Allard (Azimuth) – August 24, 2004

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - 96-hour Rainbow Trout LC_{50}

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations from requirements
   - Salinity controls were run
   - Sample water salinity was 7ppt (Test 1); 3ppt (Test 2), and 6ppt (Test 3)

iii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iv. Percent mortality of fish in stock tank(s)
   - Test 1: 0%
   - Test 2: 0.25%
   - Test 3: 0%

v. Species of test organism
   - Rainbow Trout (*Oncorhynchus mykiss*)

vi. Date and time for start of definitive test
   - Test 1: Monday July 12, 2004 – 1445h
   - Test 2: Sunday August 1, 2004 – 1030h
   - Test 3: Friday August 27, 2004 – 1100h

vii. Person(s) performing the test and verifying the results
   - Rachel DeWynter, Robert Harrison

viii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - Test 1: pH – 8.1, T - 14.0°C, DO - 10.0mg/L, C – 11730 µS/cm
   - Test 2: pH - 7.6, T - 14.0°C, DO - 10.1mg/L, C – 4870 µS/cm
   - Test 3: pH – 7.7, T - 15.0°C, DO – 9.9mg/L, C – 7416 µS/cm

Reporting Requirements for Reference Method EPS 1/RM/13

ix. Confirmation that no adjustment of sample or solution pH occurred
- Test 1: No pH adjustment
- Test 2: No pH adjustment
- Test 3: No pH adjustment

x. Indication of aeration of test solutions before introduction of fish
- Test 1: 6.5 ± 1 mL/min/L for 30mins
- Test 2: 6.5 ± 1 mL/min/L for 30mins
- Test 3: 6.5 ± 1 mL/min/L for 30mins

xi. Concentrations and volumes tested
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- Control (0%) - 10 L (test 1&2), 12 L (test 3)
- 6.25% - 10 L (test 1&2), 12 L (test 3)
- 12.5% - 10 L (test 1&2), 12 L (test 3)
- 25% - 10 L (test 1&2), 12 L (test 3)
- 50% - 10 L (test 1&2), 12 L (test 3)
- 100% - 10 L (test 1&2), 12 L (test 3)
- Salinity Control - 10 L (test 1&2), 12 L (test 3)

xii. Measurements of dissolved oxygen, pH and temperature
- Test 1: DO: 9.3 - 10.1 mg/L, pH: 7.0 – 8.3, T: 14.0 – 16.0 °C
- Test 2: DO: 9.6 - 10.1 mg/L, pH: 6.8 - 8.3, T: 14.0 °C
- Test 3: DO: 9.1 – 10.1 mg/L, pH: 7.2 – 7.9, T: 15.0 – 16.0 °C

xiii. Number of fish added to each test vessel
- 10 fish/ vessel

xiv. Mean and range of fork length of control fish at end of test
- Test 1: 34mm (29-37)
- Test 2: 33mm (31-35)
- Test 3: 40mm (38 -44)

xv. Mean wet weight of individual control fish at end of the test
- Test 1: 0.39g (0.22-0.54)
- Test 2: 0.34g (0.29-0.42)
- Test 3: 0.45g (0.31-0.61)

xvi. Estimated loading density of fish in test solutions
- Test 1: 0.39g/L
- Test 2: 0.34g/L
- Test 3: 0.38g/L

Section 8.1.3 Results

i. Number of mortalities of fish in each test solution
- Results were the same for Test 1, Test 2, and Test 3, except where noted
- Control (0%) - 0
- 6.25% - 0
- 12.5% - 0
- 25% - 0
- 50% - 0
- 100% - 0
- Salinity Control - 0

Reporting Requirements for Reference Method EPS 1/RM/13

ii. Number of control fish showing atypical/stressed behaviour
- None in Test 1, Test 2, or Test 3

iii. Mean mortality rate in solutions of effluent and control water
- Results were the same for Test 1, Test 2, and Test 3, except where noted
- Control (0%) - 0%
- 6.25% - 0%
- 12.5% - 0%
- 25% - 0%
- 50% - 0%
- 100% - 0%
- Salinity Control - 0%

iv. Estimate of 96-h LC50 in multi-concentration tests
- Results were the same for Test 1, Test 2, and Test 3
- 96hr LC_{50} concentration > 100% effluent

v. Most recent 96-h LC50 for reference toxicity test(s)
- Reference toxicity tests for Toxicant: SDS
- Test 1: (Jun-21-04) 96-h LC_{50} = 23mg/L SDS, 95% CL = 20 - 25mg/L
- Test 2: (Jul-23-04) 96-h LC_{50} = 21mg/L SDS, 95% CL = 17 - 26mg/L
- Test 3: (Aug-27-04) 96-h LC_{50} = 38mg/L SDS, 95% CL = 33 - 44mg/L

APPENDIX B

72-h Acute *Daphnia magna* Toxicity Test

Reporting Requirements for Reference Method EPS 1/RM/14

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for monthly acute toxicity testing were collected
   - Test 1: Wednesday July 7, 2004 – 2200h
   - Test 2: Tuesday July 27, 2004 – 2130h
   - Test 3: Tuesday August 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 2 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee), Test 1 & 2
   - Patrick Allard (Azimuth), Test 3

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - 48-hour *Daphnia magna* LC_{50}

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations from requirements
   - Salinity controls were run
   - Sample water salinity was 7ppt (Test 1); 3ppt (Test 2), and 6ppt (Test 3)

iii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iv. Species of test organism
   - *Daphnia magna*

v. Date and time for start of definitive test
   - Test 1: Sunday July 11, 2004 – 1400h
   - Test 2: Friday July 30, 2004 – 1400h
   - Test 3: Friday August 27, 2004 – 1100h

vi. Person(s) performing the test and verifying the results
   - Armando Tang, Rachel DeWynter

vii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - Test 1: pH - 7.8 – 7.9, T - 20.0 – 22.0 °C, DO – 9.1 – 11.4mg/L, C - 11850µhos/cm
   - Test 2: pH - 7.8 – 8.0, T – 21.5 – 22.0 °C, DO - 8.8 – 12.1mg/L, C - 5020µhos/cm
   - Test 3: pH – 7.8 - 8.1, T – 22.0 – 23.0 °C, DO - 8.7 – 10.2mg/L, C - 9320µmhos/cm

viii. Confirmation that no adjustment of sample or solution pH occurred
   - Test 1: No pH adjustment
   - Test 2: No pH adjustment
   - Test 3: No pH adjustment

Reporting Requirements for Reference Method EPS 1/RM/14

ix. Indication of any adjustment of hardness of effluent sample
- Test 1: No hardness adjustment
- Test 2: No hardness adjustment
- Test 3: No hardness adjustment

x. Indication of any aeration of sample
- Test 1: Aeration for 9mins
- Test 2: Gentle Aeration for 10mins
- Test 3: 20mins

xi. Concentrations and volumes tested
- For all 3 Tests the concentrations (% effluent volume / total volume) tested and total volumes used were:
    - Control (0%) - 200 mL
    - 6.25% - 200 mL
    - 12.5% - 200 mL
    - 25% - 200 mL
    - 50% - 200 mL
    - 100% - 200 mL
    - Salinity Control - 200 mL

xii. Measurements of dissolved oxygen, pH and temperature
- Test 1: DO: 8.6 – 9.1 mg/L, pH: 7.7 – 8.2, T: 20.0 - 21.5 °C
- Test 2: DO: 8.6 - 9.1 mg/L, pH: 7.6 - 8.0, T: 20.0 - 21.5 °C
- Test 3: DO: 8.5 - 9.0 mg/L, pH: 7.6 - 8.1, T: 20.5 - 22.0 °C

xiii. Estimates of time to first brood, average number of neonates per brood, and percent mortality during the seven-day period prior to the test
- Test 1: 8 days to brood, 27.5 neonates/brood, 9.5% mortality in 7d prior to test
- Test 2: 7 days to brood, 24 neonates/brood, 6.0% mortality in 7d prior to test
- Test 3: 7 days to brood, 21 neonates/brood, 0% mortality in 7d prior to test

xiv. Number of neonates per test vessel and milliliters of solution per daphnid
- Methods for all tests and dilution series were the same:
- 10 neonates per vessel
- 200 mL of solution per daphnid

Section 8.1.3 Results

i. Number of dead and/or immobile daphnids in each test solution including controls
- Results were the same for Test 1, Test 2, and Test 3, except where noted
- Control (0%) - 0 dead / immobile
- 6.25% - 0 dead / immobile
- 12.5% - 0 dead / immobile
- 25% - 0 dead / immobile
- 50% - 0 dead / immobile
- 100% - 0 dead / immobile (test 1), 3 dead/immobile (test 2), 0 dead/immobile (test 3)
- Salinity Control - 0 dead / immobile

ii. For single-concentration test the number of daphnids dead in each of three replicate effluent solutions and in each of three replicate control solutions at end of test. Also report the mean value.
- Single concentration test was not conducted, dilution series tests were conducted

Reporting Requirements for Reference Method EPS 1/RM/14

iii. Estimate of 48-h LC50 and 95% confidence limits in multi-concentration tests, 48-h EC50 for immobilization and 95% confidence limits, indication of statistical method on which results are based.
- Test 1: 48-h LC_{50} = > 100% effluent
- Test 2: 48-h LC_{50} = > 100% effluent
- Test 3: 48-h LC_{50} = > 100% effluent

iv. Most recent 48-h LC50 for reference toxicant test(s), reference chemical(s), date test initiated, historic geometric mean LC50 and warning limits.
- Reference toxicity tests for Toxicant: Zinc
- Test 1: (July-6-04) 48-h LC_{50} = 483µg/L Zinc, 95% CL = 403-578µg/L
- Test 2: (July-27-04) 48-h LC_{50} = 683µg/L Zinc, 95% CL = 578-807µg/L
- Test 3: (Aug-24-04) 48-h LC_{50} = 536µg/L Zinc, 95% CL = 438-656µg/L

APPENDIX C

7-d Topsmelt Growth and Survival Toxicity Test

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

Test Organisms Imported from External Supplier

i. Species of test organism
   - Topsmelt (*Atherinops affinis*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - Aquatic Bio Systems (ABS), Fort Collins, Colorado

iv. Date test species acquired on
   - Test 1 – July 8, 2004
   - Test 2 – July 29, 2004
   - Test 3 – August 26, 2004

v. Indications of deviations from EC guidance on the importation of test organisms
   - No deviations from EC requirements

vi. Percent mortality of fish in 24-hour period preceding the test
   - Test 1 - <10% mortality
   - Test 2 - <10% mortality
   - Test 3 - <10% mortality

vii. Age at start of test
   - Test 1 - 11 days post-hatch
   - Test 2 – 10 days post-hatch
   - Test 3 – 10 days post-hatch

viii. Unusual appearance, behaviour, or treatment of larvae before their use in the test
   - None noted for any test.

ix. Confirmation that larvae are actively feeding and swimbladders are not inflated
   - All tests - Larvae actively feeding and swimbladders not inflated

x. Confirmation that temperature change was <3°C and dissolved oxygen was maintained at >6mg/L during transport

- Temperature change was <2°C and dissolved oxygen supersaturated mg/L during transport

xi. Test organism acclimation rate at the testing laboratory
- Holding water conditions upon arrival were DO=supersaturated, pH = 7.9, T = 20°C
- Organisms were acclimated slowly overnight
- Addition of EVS lab seawater at intervals of 30 – 60min to reach acceptable conditions
- Organisms were acclimated to DO = 7.4mg/L, salinity = 28ppt, T=20°C

Test Facilities and Conditions

i. Test type & method
- 7-day Topsmelt (*Atherinops affinis*) Survival and Growth Toxicity Test
- Static renewal
- Sample water was renewed daily
- Reference Method - EPA/600/R-95/136 (EPAW 95-EPA West Coast)

ii. Indications of deviations from requirements in Sections 11 of Method EPA/600/R-95/136 (EPAW 95-EPA West Coast)
- No deviations from requirements
- Salinity controls were run
- Sample water salinity for
    - Test 1 was 7ppt
    - Test 2 was 2.6 ppt
    - Test 3 was 5.2ppt

iii. Date and time for start of definitive test
- Test 1 Saturday July 10, 2004 – 1730h
- Test 2 Friday July 30, 2004 – 1500h
- Test 3 Tuesday August 27, 2004 – 1230h

iv. Test vessel description
- For all tests was a 600mL beaker

v. Person(s) performing the test and verifying the results
- Test 1: Testing by: Andy Diewald, Anja Fouche, Keven Goodearle, Ann-Marie Norris and Jenny Shao; Statistical analyses by Jenny Shao and QA/QC by Julianna Kalokai
- Test 2: Testing by: Andy Diewald, Ann-Marie Norris and Jenny Shao; Statistical analysis by Jenny Shao and Kathryn Sentance; QA/QC by Armando Tang
- Test 3: Testing by Andy Diewald, Anja Fouche and Jenny Shao; Statistics by Jenny Shao and Kathryn Sentance; QA/QC by Julianna Kalokai

vi. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
- Test 1: pH 8.1, T 19.5 °C, DO 9.3 mg/L, C 11660 µmhos/cm
- Test 2: pH 7.8, T 20.0 °C, DO 10.7 mg/L, C 4880 µmhos/cm
- Test 3: pH 7.6, T 20.0 °C, DO 10.1 mg/L, C 9230 µmhos/cm

vii. Confirmation that no adjustment of sample or solution pH occurred
- No pH adjustment

viii. Indication of aeration of test solutions before introduction of fish
- Pre-aeration at 6.5mL/min/L for 30mins due to supersaturation of sample with O_2 when sample was heated to 19°C

ix. Indication that EC guidance document for salinity adjustment was followed
- The following was done for all 3 tests:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater concentrated to 90ppt (by freezing/refreezing to remove frozen layer and concentrate salts)

- No deviations from EC guidance document for salinity adjustment of sample
- HSB was added to samples to salinity adjust them to 30ppt

x. Type and source of control/dilution water
- For all 3 tests, control/dilution water was UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xi. Concentrations and volumes tested:
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- For Test 1:
    - Control (0%) - 200 mL
    - Salinity Control (0%) - 200 mL
    - 4.5% - 200mL
    - 9.1% - 200mL
    - 18.2% - 200mL
    - 36.3% - 200mL
    - 72.6% - 200mL
- For Test 2:
    - Control (0%) - 200 mL
    - Salinity Control (0%) - 200 mL
    - 4.3% - 200mL
    - 8.6% - 200mL
    - 17.3% - 200mL
    - 34.5% - 200mL
    - 69.0% - 200mL
- For Test 3:
    - Control (0%) - 200 mL
    - Salinity Control (0%) - 200 mL
    - 4.4% - 200mL
    - 9.0% - 200mL
    - 18.0% - 200mL
    - 36.0% - 200mL
    - 71.0% - 200mL

xii. Number of replicated per concentration
- For all 3 tests: 5 replicates per concentration

xiii. Number of organisms added to each test vessel
- For all 3 tests: 5 fish per vessel

xiv. Manner and rate of exchange of test solutions
- For all 3 test: Daily renewal

xv. Measurements of dissolved oxygen, pH and temperature
- Test 1: DO: 6.1 - 7.9 mg/L, pH: 7.8 - 8.3, T: 19.0 - 21.0 °C
- Test 2: DO: 6.4 - 7.7 mg/L, pH: 7.8 - 8.1, T: 20.0 – 20.5 °C
- Test 3: DO: 6.4 - 7.6 mg/L, pH: 7.8 - 8.3, T: 20.0 - 21.0 °C

Results

i. Number and % of mortalities of fish in each test solution
- Test 1: Totals from all 5 replicates are presented:
    - Control (0%) – 1/25 = 4%

- Salinity Control 1/25 = 4%
- 4.5% - 0/25 = 0%
- 9.1% - 0/25 = 0%
- 18.2% - 0/25 = 0%
- 36.3% - 1/25 = 4%
- 72.6% - 2/25 = 8%

- Test 2: Totals from all 5 replicates are presented:
  - Control (0%) – 0/25 = 0%
  - Salinity Control 0/25 = 0%
  - 4.3% - 1/25 = 4%
  - 8.6% - 1/25 = 4%
  - 17.3% - 0/25 = 0%
  - 34.5% - 0/25 = 0%
  - 69.0% - 1/25 = 4%
- Test 3: Totals from all 5 replicates are presented:
  - Control (0%) – 0/25 = 0%
  - Salinity Control 0/25 = 0%
  - 4.4% - 0/25 = 0%
  - 9.0% - 0/25 = 0%
  - 18.0% - 0/25 = 0%
  - 36.0% - 1/25 = 4%
  - 71.0% - 0/25 = 0%

ii. Average dry weight per original fish in test vessel

- Test 1: Means from all 5 replicates are presented:
  - Control (0%) – 0.93 mg
  - Salinity Control – 1.08 mg
  - 4.5% - 1.00 mg
  - 9.1% - 1.04 mg
  - 18.2% - 0.96 mg
  - 36.3% - 1.10 mg
  - 72.6% - 0.99 mg
- Test 2: Means from all 5 replicates are presented:
  - Control (0%) – 0.98 mg
  - Salinity Control – 0.99 mg
  - 4.3% - 0.91 mg
  - 8.6% - 0.87 mg
  - 17.3% - 0.78 mg
  - 34.5% - 0.90 mg
  - 69.0% - 0.77 mg
- Test 3: Means from all 5 replicates are presented:
  - Control (0%) – 0.93 mg
  - Salinity Control – 0.96 mg
  - 4.4% - 1.06 mg
  - 9.0% - 0.87 mg
  - 18.0% - 0.97 mg
  - 36.0% - 0.92 mg
  - 71.0% - 0.87 mg

iii. Estimate of 7-d LC_{50} (95% CL)

- Test 1: 7-d LC_{50} concentration > 72.6% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 2: 7-d LC_{50} concentration > 69.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 3: : 7-d LC_{50} concentration > 71.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Quantal statistic methods not applicable

iv. Estimate of 7-d IC_{25} (95% CL) for growth

- Test 1: 7-d IC_{25} concentration > 72.6% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 2: 7-d IC_{25} concentration > 69.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 3: 7-d IC_{25} concentration > 71.0% effluent (highest concentration tested due to dilution for salinity adjustment)

v. Current reference toxicity tests (95% CL) for 7-d LC_{50} for survival and 7-d IC_{50} for growth

- Test 1 :Reference toxicity tests for Toxicant: Copper
    - Test conducted on July 10, 2004, same day as effluent test
    - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
    - 7-d LC_{50} survival = 161mg/L Cu, 95% CL = 139-188mg/L
    - 7-d IC_{50} growth = 147mg/L Cu, 95% CL = 119-169mg/L
- Test 2 :Reference toxicity tests for Toxicant: Copper
    - Test conducted on July 30, 2004, same day as effluent test
    - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
    - 7-d LC_{50} survival = 130mg/L Cu, 95% CL = 115-147mg/L
    - 7-d IC_{50} growth = 124mg/L Cu, 95% CL = 87-144mg/L
- Test 3 :Reference toxicity tests for Toxicant: Copper
    - Test conducted on August 27, 2004, same day as effluent test
    - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
    - 7-d LC_{50} survival = 121mg/L Cu, 95% CL = 107-137mg/L
    - 7-d IC_{50} growth = 128mg/L Cu, 95% CL = 85-150mg/L

vi. Reference toxicity warning limits (+/- SD) for 7-d LC_{50} for survival and 7-d IC_{50} for growth

- Test 1: Reference toxicity tests for Toxicant: Copper
    - 7-d LC_{50} survival = 137 ± 56mg/L Cu
    - 7-d IC_{50} growth = 135 ± 51mg/L Cu
- Test 2: Reference toxicity tests for Toxicant: Copper
    - 7-d LC_{50} survival = 129 ± 48mg/L Cu,
    - 7-d IC_{50} growth = 130 ± 52mg/L Cu
- Test 3: Reference toxicity tests for Toxicant: Copper
    - 7-d LC_{50} survival = 132 ± 48mg/L Cu,
    - 7-d IC_{50} growth = 131 ± 51mg/L Cu

APPENDIX D

92-h Echinoderm Fertilization Test

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75^{o} 22' 32" N, 97^{o} 48' 37" W.

ii. Date & time of sampling
   - Samples for sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

Test Organisms

i. Species of test organism
   - Sandollar Echinoid (*Dendraster excentricus*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - M-REP, Escondido, California
   - All adults providing gametes are from the same population and source
   - Gametes are spawned in-house at EVS

iv. Date test species acquired on
   - Test 1: Test was not initiated due to inability of the Sandollars to spawn.
   - Test 2: July 30, 2004
   - Test 3: August 27, 2004

v. Holding time and conditions for adults
   - Test 1: N.A.
   - Test 2: Adults received at the testing laboratory the day of the test.
   - Test 3: Adults received at the testing laboratory the day of the test.

vi. Indications of deviations from EC guidance on the importation of test organisms
   - Test 1: na
   - Test 2: No deviations from EC requirements
   - Test 3: No deviations from EC requirements

vii. Weekly percent mortality of adults being held over 7d preceding test
   - Test 1: na
   - Test 2: <2% per day over the 7 days preceding the test
   - Test 3: <2% per day over the 7 days preceding the test

viii. Age of test organisms
   - Test 1: n.a.
   - Test 2: < 4 hours after spawning

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- Test 3: < 4 hours after spawning

ix. Unusual appearance, behaviour, or treatment of adults or gametes before test start
- Test 1: Test was not initiated due to inability of the Sandollars to spawn
- Test 2 Organisms appear healthy
- Test 3: Organisms appear healthy

Test Facilities and Conditions

i. Test type & method
- Echinoderm (*Dendraster excentricus*) Fertilization Toxicity Test
- Static
- Reference Method – EPS/1/RM/27 with 1997 amendments

ii. Test duration
- Test 1: na
- Test 2: 10:10 min (10min sperm + 10min sperm & egg)
- Test 3: 10:10 min (10min sperm + 10min sperm & egg)

iii. Date and time for start of definitive test
- Test 1: na
- Test 2: Friday July 30, 2004 – 1620h
- Test 3: Friday August 27, 2004 – 1334h

iv. Test vessel description
- Test 1: na
- Test 2: 16 x 125mm test tubes
- Test 3: 16 x 125mm test tubes

v. Person(s) performing the test and verifying the results
- Test 1: na
- Test 2: Testing by Kathryn Sentance and Ann-Marie Norris. Statistical analyses by Jenny Shao and Kathryn Sentance. QA/QC reviewed by Julianna Kalokai.
- Test 3: Testing by Kathryn Sentance and Ann-Marie Norris. Statistical analyses by Jenny Shao and Kathryn Sentance. QA/QC reviewed by Julianna Kalokai.

vi. Indication of rate and duration of pre-aeration of test solutions before initiation of test
- Test 1: na
- Test 2: No pre-aeration noted.
- Test 3: No pre-aeration noted.

vii. Confirmation that no adjustment of sample or solution pH occurred
- Test 1: na
- Test 2: No pH adjustment
- Test 3: No pH adjustment

viii. Procedure for sample filtration
- Test 1: na
- Test 2: No sample filtration
- Test 2: No sample filtration

ix. Procedure for preparation of hypersaline brine (HSB) as per EC guidance document on salinity adjustment – July 1997
- Test 1: na
- Test 2: 30 ppt adjusted with hypersaline brine (HSB). Preparation of HSB and salinity adjustment as per EC guidance document on Salinity adjustment – July 1997
- Test 2: 30 ppt adjusted with hypersaline brine (HSB). Preparation of HSB and salinity adjustment as per EC guidance document on Salinity adjustment – July 1997

x. Procedure for salinity adjustment as per EC guidance document on salinity adjustment – July 1997

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- No deviations from EC guidance for salinity adjustment
- Test 1: na
- Test 2: salinity adjusted from 2.8 to 28 ppt
- Test 3: salinity adjusted from 5 to 28 ppt

xi. Type and source of control/dilution water
- Test 1: na
- Test 2: UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium
- Test 3: UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xii. Concentrations and volumes tested
- Test 1: na
- Test 2: Concentrations (% effluent volume / total volume) tested and total volumes used were:
    - Control (0%) - 10mL
    - Salinity Control (0%) - 10mL
    - 4.6% - 10mL
    - 9.1% - 10mL
    - 18.3% - 10mL
    - 36.6% - 10mL
    - 73.1% - 10mL
- Test 3: Concentrations (% effluent volume / total volume) tested and total volumes used were:
    - Control (0%) - 10mL
    - Salinity Control (0%) - 10mL
    - 4.7% - 10mL
    - 9.4% - 10mL
    - 18.8% - 10mL
    - 37.5% - 10mL
    - 75.1% - 10mL

xiii. Number of replicated per concentration
- Test 1: na
- Test 2: 4 replicates per treatment concentration
- Test 3: 4 replicates per treatment concentration

xiv. Number of organisms per container
- Test 1: na
- Test 2: 100 eggs per vessel
- Test 3: 100 eggs per vessel

xv. Measurements of pH and dissolved oxygen in sample water before use
- Test 1: na
- Test 2: pH 8.1, DO 8.5
- Test 3: pH 8.0, DO 8.5

xvi. Measurements of pH, temperature, dissolved oxygen, and salinity during test
- Test 1: na
- Test 2: pH – 8.0 – 8.1, T - 15.0-16.0°C, DO - 8.2-8.5mg/L, salinity - 28ppt
- Test 3: pH – 8.2 – 8.5, T - 15.0-16.0°C, DO - 8.2-8.5mg/L, salinity - 28ppt

Results

i. Number and % of fertilized eggs in each test concentration
- Test 1: na
- Test 2: (Number is equal to percent since totals were 100)
    - Control (0%): #F = 59, 62, 56, 65 #UF = 41, 38, 44, 35
    - Salinity Control: #F = 60, 57, 59, 62 #UF = 40, 43, 41, 38

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- 4.6%: #F = 60, 66, 56, 58 #UF = 40, 34, 44, 42
- 9.1%: #F = 46, 42, 45, 42 #UF = 54, 58, 55, 58
- 18.3%: #F = 39, 39, 37, 36 #UF = 61, 64, 63, 64
- 36.6%: #F = 31, 34, 25, 31 #UF = 69, 66, 75, 69
- 73.1%: #F = 19, 20, 21, 20 #UF = 81, 80, 79, 80

- Test 3: (Number is equal to percent since totals were 100)
  - Control (0%): #F = 77, 80, 74, 77 #UF = 23, 20, 26, 23
  - Salinity Control: #F = 76, 73, 79, 77 #UF = 24, 27, 21, 23
  - 4.7%: #F = 78, 74, 76, 72 #UF = 22, 26, 24, 28
  - 9.4%: #F = 61, 62, 62, 60 #UF = 39, 38, 38, 40
  - 18.8%: #F = 56, 58, 59, 55 #UF = 44, 42, 41, 45
  - 37.5%: #F = 49, 50, 50, 48 #UF = 51, 50, 50, 52
  - 75.1%: #F = 25, 27, 24, 27 #UF = 75, 73, 76, 73

ii. Estimate of IC_{25} (95% CL) for fertilization success

- Test 1: na
- Test 2: IC_{25} concentration = 8.7 (7.6 – 9.9)% v/v effluent
- Test 3: IC_{25} concentration = 17.5 (11.6 – 22.6)% v/v effluent

iii. Current reference toxicity tests (95% CL) for IC_{50} for fertilization

- Test 1: na
- Test 2: Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
  - Test conducted on July 30, 2004, same day as effluent test
  - Reference test conducted under same conditions
  - IC_{50} for fertilization = 2.1mg/L SDS, 95% CL = (1.9 – 2.4)mg/L
- Test 3: Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
  - Test conducted on August 27, 2004, same day as effluent test
  - Reference test conducted under same conditions
  - IC_{50} for fertilization = 2.3mg/L SDS, 95% CL = (2.1 – 2.4)mg/L

iv Reference toxicant warning limits (+/- 2SD) for IC_{50} for fertilization

- Test 1: na
- Test 2: 4.2 +/- 4.8 mg/L SDS
- Test 3: 3.9 +/- 4.6 mg/L SDS

APPENDIX E

7-d Sublethal *Champia* (Algae) Toxicity Test

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for yearly sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 1 x 4L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

vii. Temperature of water upon receipt at lab
   - Test 1: Test was not conducted as sample was delayed by weather and person qualified to conduct the work at the lab left for vacation. This was discussed with Sandra Blenkinsopp at the time to provide direction.
   - Test 2: 8°C
   - Test 3: 17°C

Test Organisms

i. Species of test organism
   - Algae (*Champia parvula*)

ii. Name and city of testing laboratory
   - Saskatchewan Research Council [SRC], Saskatoon, SK

iii. Source of test species
   - Test 1: na
   - Test 2 and Test 3
     - Sexually mature male and female branches
     - Obtained from USEPA, Hatfield Marine Science Center, Newport Oregon, 1995
     - Appear in good health
     - Females have trichogynes, males have sori with spermatia

Test Facilities and Conditions

i. Test type & method
   - *Champia parvula* sexual reproduction test
   - Static, non-renewal
   - 2-day exposure, followed by 5-7 day recovery period for cystocarp development
   - Reference Method - EPA/600/4-91/003, Method 1009.0

ii. Date and time for start of definitive test
   - Test 1: na

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

- Test 2: Friday July 30, 2004 – time not noted but lab notes state tests started within 72 hrs of collection
- Test 3: Friday August 27, 2004 – time not noted but lab notes state tests started within 72 hrs of collection

iii. Test vessel description
- Test 1: na
- Test 2: 270mL transparent polystyrene cups with polystyrene lids
- Test 2: 270mL transparent polystyrene cups with polystyrene lids

iv. Person(s) performing the test and verifying the results
- Test 1: na
- Tests 2 & 3 - Mary Moody

v. Indication of pre-aeration of test solutions
- Test 1: na
- Tests 2 & 3 - No pre-aeration

vi. Confirmation that no pH adjustment of sample or solution occurred
- Test 1: na
- Tests 2 & 3: - No pH adjustment

vii. Indication that EC guidance document for salinity adjustment was followed
- Test 1: na
- Test 2:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater at 90ppt
    - No deviations from EC guidance document for salinity adjustment of sample
    - Salinity adjustment: 600mL effluent + 250mL HSB + 8.5mL test nutrient solution
    - Salinity of samples adjusted from 4ppt to 30ppt
- Test 3:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater at 90ppt
    - No deviations from EC guidance document for salinity adjustment of sample
    - Salinity adjustment: 600mL effluent + 230mL HSB + 10 ml test nutrient solution
    - Salinity of samples adjusted from 5ppt to 30ppt

viii. Type and source of control/dilution water
- Test 1: na
- Tests 2 & 3
    - Natural seawater collected at the Pacific Environmental Center, Environment Canada, North Vancouver, BC
    - Filtered to 0.2μm and autoclaved prior to use
    - Salinity adjusted as per EC guidance document to 30ppt with HSB from the same source

ix. Concentrations and volumes of test solutions
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- Test 1: na
- Tests 2:
    - Control (Natural Seawater) (0%) - 100mL, 4.5cm depth
    - Salinity Control Brine (0%) - 100mL, 4.5cm depth
    - 4.38% - 100mL, 4.5cm depth
    - 8.75% - 100mL, 4.5cm depth
    - 17.5% - 100mL, 4.5cm depth

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

- 35.0% - 100mL, 4.5cm depth
- 70.0% - 100mL, 4.5cm depth

- Tests 3:
  - Control (Natural Seawater) (0%) - 100mL, 4.5cm depth
  - Salinity Control Brine (0%) - 100mL, 4.5cm depth
  - 4.5% - 100mL, 4.5cm depth
  - 9.0% - 100mL, 4.5cm depth
  - 18.0% - 100mL, 4.5cm depth
  - 36.0% - 100mL, 4.5cm depth
  - 72.0% - 100mL, 4.5cm depth

x. Number of replicated per concentration
- Test 1: na
- Tests 2 & 3: 3 replicates per concentration

xi. Number of organisms per test chamber
- Test 1: na
- Tests 2 & 3: 5 female branches + 2 male branches per chamber

xii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample before use
- Test 1: na
- Test 2: pH - 7.78, T – 22.0 °C, DO – 7.9mg/L, salinity - 4ppt
- Test 3: pH - 7.58, T – 23.0 °C, DO – 8.0mg/L, salinity - 5ppt

xiii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample during test
- Test 1: na
- Test 2: pH – 8.20, T – 23 °C, DO – 7.9, salinity: 30ppt
- Test 3: pH – 8.33, T – 22 °C, DO – 7.9, salinity: 29ppt

Results

i. Number and % mortality of female plants after recovery in each test solution
- Totals from all 3 replicates are presented:
- Test 1: na
- Test 2:
  - Control (0%): 0 (0%) mortality
  - Salinity Control (0%): 0 (0%) mortality
  - 4.38%: 0 (0%) mortality
  - 8.75%: 0 (0%) mortality
  - 17.5%: 0 (0%) mortality
  - 35.0%: 0 (0%) mortality
  - 70.0%: 0 (0%) mortality
- Test 3:
  - Control (0%): 0 (0%) mortality
  - Salinity Control (0%): 0 (0%) mortality
  - 4.5%: 0 (0%) mortality
  - 9.0%: 0 (0%) mortality
  - 18.0%: 0 (0%) mortality
  - 36.0%: 0 (0%) mortality
  - 72.0%: 0 (0%) mortality

Reporting Requirements for Reference Method EPA/600/4-91/003 Method 1009.0

ii. Mean number of cystocarps per plant in each test concentration

- Test 1: na
- Test 2:
    - Control (0%): 92.1
    - Salinity Control (0%): 92.5
    - 4.38%: 105.1
    - 8.75%: 105.1
    - 17.5%: 90.7
    - 35.0%: 61.9
    - 70.0%: 13.3
- Test 3:
    - Control (0%): 58.3
    - Salinity Control (0%): 58.6
    - 4.5%: 59.7
    - 9.0%: 59.4
    - 18.0%: 60.9
    - 36.0%: 51.3
    - 72.0%: 26.3

iii. Estimate of IC_{25} (95% CL) for cystocarp development

- Test 1: na
- Test 2: IC_{25} concentration = 26.6 (20.8 – 31.5)% effluent v/v
- Test 3: IC_{25} concentration = 45.3 (36.3 – 58.1)% effluent v/v
- Quantal statistic method was linear interpolation

iv. Current reference toxicity tests (95% CL) for IC_{50} for cystocarp development

- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test 1: na
- Test 2: Test conducted on July 27, 2004, within 30 days of effluent test
    - Reference toxicant test was conducted under the same experimental conditions as the effluent test
    - IC_{50} cystocarp development = 1.48mg/L SDS, 95% CL = (1.38 - 1.62) mg/L
    - Reference toxicity warning limits 1.40 (+/- 2SD) for IC_{50} for cystocarp development
- Test 3: Test conducted on July 27, 2004, within 30 days of effluent test
    - Reference toxicant test was conducted under the same experimental conditions as the effluent test
    - IC_{50} cystocarp development = 1.48mg/L SDS, 95% CL = (1.38 - 1.62) mg/L
    - Reference toxicity warning limits 1.40 (+/- 2SD) for IC_{50} for cystocarp development

v. Reference toxicant warning limits (+/- 2SD) for IC_{50} for cystocarp development

- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test 1: na
- Test 2: 1.40 (1.6-1.70) mg/L SDS
- Test 3: 1.40 (1.6-1.70) mg/L SDS

APPENDIX F

Effluent Metals Concentrations and Loadings

2004 3rd QUARTER MMER REPORT

LOCATION - FINAL DISCHARGE POINT FROM GARROW LAKE (GARROW LAKE DAM SIPHONS)

CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4 SAMPLED WEEKLY

Sample Taken During The Week of	Date Sample Taken	DELETERIOUS SUBSTANCE (mg/L)[1] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	pH[1]	Collection Method
05-Jul-04	7-Jul-04	0.001	0.003	0.005	0.003	0.004	0.198	117	0.020	8.1	Water pump
12-Jul-04	13-Jul-04	0.002	0.001	0.005	0.000	0.002	0.106	6	0.007	7.9	Water pump
19-Jul-04	20-Jul-04	0.002	0.000	0.005	0.001	0.001	0.044	3	0.005	7.9	Water pump
26-Jul-04	27-Jul-04	0.001	0.001	0.005	0.002	0.002	0.043	3	0.005	7.9	Water pump
02-Aug-04	3-Aug-04	0.000	0.001	0.005	0.003	0.003	0.035	3	0.006	8.0	Grab
09-Aug-04	10-Aug-04	0.001	0.001	0.006	0.001	0.007	0.048	3	0.005	8.0	Grab
16-Aug-04	17-Aug-08	0.000	0.001	0.005	0.002	0.006	0.042	5	0.010	8.0	Water pump
23-Aug-04	24-Aug-04	0.000	0.001	0.005	0.001	0.010	0.050	4	0.008	7.8	Water pump
30-Aug-04	31-Aug-04	0.000	0.001	0.005	0.003	0.013	0.078	15	0.008	7.9	Grab
06-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
13-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
20-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
27-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L and pH which is in pH units

Note [2] - "nd" refers to no effluent discharge to sample

MONTHLY MEAN CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4

MONTH OF	MONTHLY MEAN CONCENTRATION[1] OF DELETERIOUS SUBSTANCE[3] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226
July/04	0.002	0.001	0.005	0.002	0.002	0.098	32	0.009
August/04	0.001	0.001	0.005	0.002	0.005	0.072	18	0.008
September/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L

Note [2] - "nd" refers to no effluent discharge to sample

Note[3] - Monthly Mean Concentrations - the MEAN value of the concentrations measured in all water samples collected during each month when a deleterious substance is deposited.

MASS LOADING OF DELETERIOUS SUBSTANCE FOR EACH DAY SAMPLED

Sample Taken During The Week of	Date Sample Taken	DAILY MASS LOADING OF DELETERIOUS SUBSTANCE (kg/day)[1]								Average Daily Flow Rate (m^3/day)
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	
05-Jul-04	7-Jul-04	0.018	0.054	0.091	0.054	0.072	3.588	2120	362,440	18,122
12-Jul-04	13-Jul-04	0.752	0.376	1.880	0.000	0.752	39.850	2256	2,631,608	375,944
19-Jul-04	20-Jul-04	0.205	0.000	0.512	0.102	0.102	4.509	307	512,395	102,479
26-Jul-04	27-Jul-04	0.028	0.028	0.141	0.056	0.056	1.213	85	141,090	28,218
02-Aug-04	3-Aug-04	0.000	0.026	0.132	0.079	0.079	0.926	79	158,700	26,450
09-Aug-04	10-Aug-04	0.026	0.026	0.155	0.026	0.181	1.243	78	129,470	25,894
16-Aug-04	17-Aug-08	0	0	0	0	0	0	0	0	0
23-Aug-04	24-Aug-04	0	0	0	0	0	0	0	0	0
30-Aug-04	31-Aug-04	0	0	0	0	0	0	0	0	0
06-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
13-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
20-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
27-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0

Note[1] - Mass Loading is in kilograms per day of the deleterious substance deposited except Radium 226 which is in Bq per day

Note [2] - "nd" refers to no effluent discharge to sample

MASS LOADING PER CALENDAR MONTH FOR EACH DELETERIOUS SUBSTANCE

CALENDAR MONTH OF	MASS LOADING[1] FOR DELETERIOUS SUBSTANCE (kg/month)[2]								Average Weekly Flow Rate[3] (m^3/week)	Total Monthly Volume[4] (m^3/month)
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[2]		
July/04	7.77	3.55	20.33	1.65	7.62	381.00	36,952.22	28,268,381	131,191	4,066,913
August/04	0.16	0.32	1.78	0.65	1.62	13.45	973.60	1,786,654	10,469	324,533
September/04	0	0	0	0	0	0	0	0	0	0

Note[1] - Total Mass Loading for Calendar month calculated by multiplying the Average Daily Mass Loading for the Month x # days in the month

Note[2] - Mass loading units are in kg per month except Radium 226, which is in Bq permonth

Note[3] - Average Weekly Flow Rate calculated by multiplying Average Daily Flow Rate x 7 days per week

Note[4] - Total Monthly Volume calculated by multiplying Average Daily Flow Rate for the month x days in month

APPENDIX G

Results of Effluent Characterization

RESULTS OF EFFLUENT CHARACTERIZATION

AS PER PARAGRAPH 15(1)(a)

Nine effluent samples were collected on a weekly basis during the 3rd Quarter of 2004 beginning on July 7, 2004 and ceasing on August 31, 2004. Four of the nine samples were "monthly" samples and analysed for a wider suite of elements, as per the guidance document. Monthly loadings of metals to Garrow Bay were calculated based on average weekly discharge volumes from Garrow Lake to Garrow Bay via the creek outflow.

Monthly characterization samples were attempted during early July however ice conditions at Garrow Bay made it unsafe to collect Garrow Bay water samples until July 27, 2004. During the July 27th sampling event it was still not safe to collect reference samples due to ice conditions. On August 17th and again on August 24th monthly characterization samples were obtained including Garrow Bay and the reference location.

No holding times were missed for any of the water chemistry of toxicity testing samples.

Water samples for acute and sublethal toxicity testing were collected using a pump system from about 20 m downstream of the dam on Garrow Lake, within the main flow of the creek. Acute Lethality Testing was conducted 3 times during two months (2 in July and 1 in August) during the quarter. There were no adverse effects observed for either the 96-hr Rainbow Trout toxicity tests, or the 48-hr *Daphnia magna* toxicity tests. LC_{50} values were >100% effluent for both species in all testing events.

Sublethal Toxicity Testing was attempted three times during the quarter with the first test being partially successfully completed (7-D Topsmelt successfully completed, the echinoderm fertilization toxicity test was not initiated due to the inability of the sand dollars to spawn, and the Champia parvula Sexual Reporduction test was not conducted due to laboratory problems which were out of our control), and the other two sets of sublethal toxicity tests were completed successfully. As this is considered a marine discharge, marine species were used for sublethal testing following brine adjustment of the brackish effluent (as per test protocols). Testing for fish (7-d Topsmelt growth and survival) and invertebrates (Sand dollar) was conducted at EVS Environment Consultants, Vancouver, while algae (48-h *Champia*) testing was undertaken by the Saskatchewan Research Council, Saskatoon.

There were no effects observed in the Topsmelt Survival and Growth Test at maximum concentration tested which were below 100% v/v effluent due to the salinity adjustments.

Sublethal effects were observed for the echinoid and algal tests and concentrations less than 100% effluent v/v. In the echinoid *(Dendraster excentricus)* fertilization tests (EVS Consultants) for:

- The July 27, 2004 tests, the LOAEL was 4.6% v/v effluent, the IC_{25} was 8.7% v/v, and the IC_{50} was 37.3% v/v.
- The August 24, 2004 tests, the LOAEL was 4.7 %v/v effluent, the IC_{25} was 17.5%v/v, and the IC_{50} was 50.7%v/v.

In the *Champia parvula* sexual reproduction test (Saskatchewan Research Council) for:

- The July 27, 2004 tests, the LOAEL was 35%v/v effluent, the IC_{25} (95% CL) was 26.6% v/v and the IC_{50} (95% CL) was 43.3% v/v.
- The August 24, 2004 tests, the LOAEL was 72%v/v effluent, the IC_{25} (95% CL) was 45.3% v/v and the IC_{50} (95% CL) was 66.8% v/v.

Zinc was the primary contaminant of potential concern (COPC) identified in mine effluent and is the only metal to consistently exceed BC Ambient Water Quality Guidelines (BC AWQG) in effluent. During the 9 week discharge period, effluent zinc concentration averaged 72 µg/L (range 35 – 198µg/L), which is well below the MMER effluent limit of 500µg/L. The BC AWQG is 10µg/L. On July 27, 2004 and August 24, 2004 when the sublethal samples were collected, the respective concentrations of Zn in the effluent was 43µg/L and 50 µg/L. Converting the echinoid test endpoints for the July 27, 2004 tests into Zn concentrations results in a Lowest Observed Adverse Effect Level (LOAEL) of 1.9µg/L Zinc, an IC_{25} of 3.7µg/L, and an IC_{50} of 16.0µg/L. Converting the echinoid test endpoints for the August 24, 2004 tests into Zn concentrations results in a Lowest Observed Adverse Effect Level (LOAEL) of 2.3µg/L Zinc, an IC_{25} of 8.8µg/L, and an IC_{50} of 25.4µg/L. Reference toxicity tests of zinc on *Dendraster* fertilization give mean EC_{50} concentrations of 8.5-60µg/L (Dinnel et al. 1983). The concentrations of zinc in the effluent that corresponds to the IC_{50} (i.e., 16.0 to 25.4 µg/L) are within the effects range reported in reference *Dendraster* fertilization tests. Thus the echinoid test is quite sensitive to zinc, with the LOAELs being less than the BC AWQG concentration.

Endpoints for the July 27, 2004 *Champia* test in terms of zinc concentrations were 15.1µg/L Zn (LOAEL), 11.4µg/L (IC_{25}), and 18.6µg/L (IC_{50}). Endpoints for the August 24, 2004 *Champia* test in terms of zinc concentrations were 36µg/L Zn (LOAEL), 22.6µg/L (IC_{25}), and 33.4µg/L (IC_{50}). The reference IC_{25} endpoint for zinc in the *Champia* test performed in-house at SRC was 27µg/L (95% confidence limits 16-42µg/L). This reference concentration is very similar to zinc concentrations in the mine effluent at the toxicity endpoints observed in the *Champia* test.

Given the similarity between zinc concentrations in the effluent samples and the effects concentrations of zinc in reference tests, it is likely that zinc is responsible for the sublethal effects observed in both the *Dendraster* and *Champia* tests.

Reference: Dinnel, P.A., Q.J. Stober, J.M. Link, M.W. Letourneau, W.E. Roberts, S.P. Felton, and R.E. Nakatan. 1983. Methodology and Validation of a Sperm Cell Toxicity Test for Testing Toxic Substances in Marine Waters. Final Report, FRI-UW-8306, Fisheries Research Inst., School of Fisheries, University of Washington, Seattle, WA :208. Source: EPA EcoTox database.

March 22, 2005

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2004 ANNUAL Metal Mining Effluent Regulations Summary Report

Please find attached the Polaris Mine annual MMER summary report. There was one non-compliant concentration related to Schedule 4 limits (TSS) as previously reported. There were no non-compliant results of the acute lethality tests during the year.

The following is included in our 2004 Annual Submission:

1. Requirements under Schedule 6
   - Identification of Site, Owner, Location, etc.
   - Non-Compliance information
   - Table 1 – Monthly Mean Concentrations, pH Range and Volume of Effluent
   - Table 2 – Results of Acute Lethality Tests and Daphnia Magna Monitoring Tests

2. Requirements under Part 1 Section 8
   - Results of studies conducted under Part 1, Section 4 (Effluent Characterization)
   - Results of studies conducted under Part 1, Section 5 (Sublethal Toxicity Testing)
   - Results of studies conducted under Part 1, Section 7 (Water Quality Monitoring)

In addition, attached is a revised 3rd Quarter Regulatory data set. Regulatory data in the 3rd Quarter had originally been submitted with average daily flows of 0 m^3 per day for the weeks of Aug. 17, Aug. 24, and Aug. 31, 2004, as flow was too low to be measured. However, EEM data and acute lethality samples were still collected during this time period. Upon submitting the regulatory data into the online RISS system for the annual report, these August data were not accepted with a flow of zero. To adjust for this, a nominal flow of 1 m^3 per day was entered. As a result the revised data set is slightly different from the data submitted in our original 3rd Quarter report.

Please note that the MMER and EEM data required to be reported in electronic format have been submitted electronically through the RISS online system. In addition, an electronic copy of this report is being emailed to you (e-mailed March 22, 2005).

If you have any questions regarding the annual report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Original signed by B. Donald
Bruce Donald

Attachments: 2004 MMER Annual Report; Revised 2004 3rd Quarter Regulatory Data Tables
cc: Walter Kuit (Teck Cominco Limited)
Randy Baker (Azimuth Consulting Group)

INFORMATION TO BE INCLUDED IN ANNUAL REPORT SUMMARY

The following information is to be submitted for each final discharge point.

Mine Name :	Polaris Mine
Mine Operator :	Cominco Mining Partnership and Teck Cominco Metals Lt
Address :	Bag 2000
	Kimberley, BC
	V1A 3E1
Telephone :	(250) 427-8405 Bruce Donald
E-mail :	bruce.donald@teckcominco.com
Location of Final Discharge point :	Garrow Lake Former Dam at 75o22'32"N, 96o48'37"W.
Reporting Period :	January 1, 2004 to December 31, 2004.
Date of Report :	March 21, 2005.

Non-Compliance Information

There was one non-compliant effluent discharge during 2004 (I.e., TSS of 117 mg/L, July 7, 2004), with respect to Schedule 4 limits. Upon receiving the results from the lab, this exceedance was reported to Environment Canada regulatory authorites in a letter dated August 12, 2004. The exceedance was due to the initial ice melt unplugging Garrow Lake, resulting in a flushing of sediment. There were no other non-compliant concentrations of substances during this initial flow, and TSS dropped to values of approximately 3-15 mg/L in all subsequent sampling events. Upon review of the information, Environment Canada recommended no further action in a letter date January 11, 2005 from Sidney Bruinsma. There were no non-compliant acute lethality tests during 2004, including tests performed on the July 7, 2004 sample.

TABLE 1

MONTHLY MEAN CONCENTRATIONS, pH RANGE AND VOLUME OF EFFLUENT (1)(2)

Month	As (mg/L)	Cu (mg/L)	CN (mg/L)	Pb (mg/L)	Ni (mg/L)	Zn (mg/L)	TSS (mg/L)	Ra (Bq/L)	pH range	Effluent Volume (m3)
Jan.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Feb.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Mar.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Apr.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
May	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
June	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
July	0.0015	0.0011	0.0050	0.0014	0.0024	0.0980	32.0000	0.0090	7.90 - 8.05	4066913.00
Aug.	0.0004	0.0012	0.0051	0.0019	0.0081	0.0508	6.1000	0.0074	7.84 - 8.04	324551.00
Sept.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Oct.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Nov.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)
Dec.	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)	ND(1)

(1) Any measurement not taken because there was no deposit from the final discharge point shall be identified by the letters "ND" - (No Deposit)

(2) Any measurement not taken because no measurement was required in accordance with the conditions set out in section 13 of the Regulations shall be identified by the letters "NMR" - (No Measurement Required).

TABLE 2

RESULTS OF ACUTE LETHALITY TESTS AND
DAPHNIA MAGNA MONITORING TESTS

Date Sample Collected	Effluent Acutely Lethal to Rainbow Trout (yes or no)	Effluent Acutely Lethal to *Daphnia magna* (yes or no)
7/7/2004	No	No
7/27/2004	No	No
8/24/2004	No	No

Effluent Characterization Results (Part 1, Section 4)

Facility Name	FDP Name	Effluent Characterization Date	Sample Method	Hardness	Alkalinity	Aluminum	Cadmium	Iron	Mercury	Molybdenum	Ammonia	Nitrate
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/7/2004	Grab	1400	138	0.34	0.000588	0.487	< 0.00001	< 0.005	0.071	0.277
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	Grab	483	62.4	0.021	0.00014	0.084	< 0.00001	0.0013	< 0.02	0.0644
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/17/2004	Grab	973	111	< 0.1	0.00023	0.042	< 0.00001	< 0.005	0.146	0.525
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	Grab	1380	128	< 0.1	0.000335	0.014	< 0.00001	< 0.005	0.133	0.531

[1] Concentrations of Radium226 are in Bq/L

Effluent Characterization Results (Part 1, Section 4)

Facility Name	FDP Name	Effluent Characterization Date	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226	PH Value	Notes
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/7/2004	< 0.001	0.00265	< 0.005	0.00269	0.00442	0.198	117	0.02	8.05	
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	< 0.001	0.000518	< 0.005	0.00157	0.00207	0.0429	< 3	< 0.005	7.87	
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/17/2004	< 0.0002	0.00121	< 0.005	0.00177	0.00644	0.0418	5.3	0.01	7.95	
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	< 0.0002	0.00134	< 0.005	0.00119	0.00967	0.0498	4.4	0.008	7.84	

[1] Concentrations of Radium226 are in Bq/L

Sublethal Toxicity Testing Results EC50 (Part 1, Section 5)

Facility Name	FDP Name	EC25 Test Date	Species Test	Sublethal Test Type	Sample Method	Consultant Laboratory
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/7/2004	Atherinops affinis	Growth	Grab	EVS Consultants, North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	Atherinops affinis	Growth	Grab	EVS Consultants, North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	Dendraster excentricus	Reproduction	Grab	EVS Consultants North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	Champia parvula	Reproduction	Grab	Saskatchewan Research Council (SRC)
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	Champia parvula	Reproduction	Grab	Saskatchewan Research Council (SRC)
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	Dendraster excentricus	Reproduction	Grab	EVS Consultants North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	Atherinops affinis	Growth	Grab	EVS Consultants North Vancouver, BC

Sublethal Toxicity Testing Results EC50 (Part 1, Section 5)

EC25 Test Date	Species Test	EC25 or IC25	EC25 or IC25 Lower Confidence Limit	EC25 or IC25 Upper Confidence Limit	Notes
7/7/2004	Atherinops affinis	> 72.6	72.6	72.6	IC25 (95%CL) was > 72.6%, the highest exposure concentration due to salinity adjustment.
7/27/2004	Atherinops affinis	> 69	69	69	IC25 (95% CL) was > 69%, the highest concentration tested due to salinity adjustment.
7/27/2004	Dendraster excentricus	8.7	7.6	9.9	July 7 sandollar test not initiated because sandollars did not spawn.
7/27/2004	Champia parvula	26.6	20.8	31.5	
8/24/2004	Champia parvula	45.3	36.3	58.1	
8/24/2004	Dendraster excentricus	17.5	11.6	22.6	
8/24/2004	Atherinops affinis	> 71	71	71	IC25 (95% CL) was > 71%, the highest concentration tested due to salinity adjustment.

Sublethal Toxicity Testing Results LC50 (Part 1, Section 5)

Facility Name	FDP Name	LC50 Test Date	Species Tested	Sublethal Test Type	Sample Method	Consultant Laboratory
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/7/2004	Atherinops affinis	Survival	Grab	EVS Consultants, North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	7/27/2004	Atherinops affinis	Survival	Grab	EVS Consultants, North Vancouver, BC
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	8/24/2004	Atherinops affinis	Survival	Grab	EVS Consultants, North Vancouver, BC

Sublethal Toxicity Testing Results LC50 (Part 1, Section 5)

LC50 Test Date	Species Tested	LC50	LC50 Lower Limit	LC50 Upper limit	Notes
7/7/2004	Atherinops affinis	> 72.6	72.6	72.6	LC50 (95% CL) was > 72.6%, the highest exposure concentration tested, due to salinity adjustment.
7/27/2004	Atherinops affinis	> 69	69	69	LC50 (95% CL) was > 69%, the highest concentration tested due to salinity adjustment.
8/24/2004	Atherinops affinis	> 71	71	71	LC50 (95% CL) was > 71%, the highest concentration tested due to salinity adjustment.

POLARIS MINE – MMER ANNUAL SUMMARY REPORT 2004

APPENDIX A

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPAW 95-EPA West Coast: 7-day Topsmelt Survival and Growth Tests.

APPENDIX B

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPS 1/Rm/27-EC: 92 hr Echinoderm (sand dollar) Fertilization Test

APPENDIX C

i. Information specified in Schedule 5 of the MMER (June 2002) for Reference Method EPA/600/4-91-003, Method 1009.0: Algae (*Champia parvula*) 7-day Sublethal Growth Tests

APPENDIX A

7-d Topsmelt Growth and Survival Toxicity Test

Reporting Requirements for Reference Method EPAW 95-EPA West Coast (Topsmelt)

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

Test Organisms Imported from External Supplier

i. Species of test organism
   - Topsmelt (*Atherinops affinis*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - Aquatic Bio Systems (ABS), Fort Collins, Colorado

iv. Date test species acquired on
   - Test 1 – July 8, 2004
   - Test 2 – July 29, 2004
   - Test 3 – August 26, 2004

v. Indications of deviations from EC guidance on the importation of test organisms
   - No deviations from EC requirements

vi. Percent mortality of fish in 24-hour period preceding the test
   - Test 1 - <10% mortality
   - Test 2 - <10% mortality
   - Test 3 - <10% mortality

vii. Age at start of test
   - Test 1 - 11 days post-hatch
   - Test 2 – 10 days post-hatch
   - Test 3 – 10 days post-hatch

viii. Unusual appearance, behaviour, or treatment of larvae before their use in the test
   - None noted for any test.

ix. Confirmation that larvae are actively feeding and swimbladders are not inflated
   - All tests - Larvae actively feeding and swimbladders not inflated

x. Confirmation that temperature change was <3°C and dissolved oxygen was maintained at >6mg/L during transport

Reporting Requirements for Reference Method EPAW 95-EPA West Coast (Topsmelt)

- Temperature change was <2°C and dissolved oxygen supersaturated mg/L during transport

xi. Test organism acclimation rate at the testing laboratory
- Holding water conditions upon arrival were DO=supersaturated, pH = 7.9, T = 20°C
- Organisms were acclimated slowly overnight
- Addition of EVS lab seawater at intervals of 30 – 60min to reach acceptable conditions
- Organisms were acclimated to DO = 7.4mg/L, salinity = 28ppt, T=20°C

Test Facilities and Conditions

i. Test type & method
- 7-day Topsmelt (*Atherinops affinis*) Survival and Growth Toxicity Test
- Static renewal
- Sample water was renewed daily
- Reference Method - EPA/600/R-95/136 (EPAW 95-EPA West Coast)

ii. Indications of deviations from requirements in Sections 11 of Method EPA/600/R-95/136 (EPAW 95-EPA West Coast)
- No deviations from requirements
- Salinity controls were run
- Sample water salinity for
    - Test 1 was 7ppt
    - Test 2 was 2.6 ppt
    - Test 3 was 5.2ppt

iii. Date and time for start of definitive test
- Test 1 Saturday July 10, 2004 – 1730h
- Test 2 Friday July 30, 2004 – 1500h
- Test 3 Tuesday August 27, 2004 – 1230h

iv. Test vessel description
- For all tests was a 600mL beaker

v. Person(s) performing the test and verifying the results
- Test 1: Testing by: Andy Diewald, Anja Fouche, Keven Goodearle, Ann-Marie Norris and Jenny Shao; Statistical analyses by Jenny Shao and QA/QC by Julianna Kalokai
- Test 2: Testing by: Andy Diewald, Ann-Marie Norris and Jenny Shao; Statistical analysis by Jenny Shao and Kathryn Sentance; QA/QC by Armando Tang
- Test 3: Testing by Andy Diewald, Anja Fouche and Jenny Shao; Statistics by Jenny Shao and Kathryn Sentance; QA/QC by Julianna Kalokai

vi. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
- Test 1: pH 8.1, T 19.5 °C, DO 9.3 mg/L, C 11660 µmhos/cm
- Test 2: pH 7.8, T 20.0 °C, DO 10.7 mg/L, C 4880 µmhos/cm
- Test 3: pH 7.6, T 20.0 °C, DO 10.1 mg/L, C 9230 µmhos/cm

vii. Confirmation that no adjustment of sample or solution pH occurred
- No pH adjustment

viii. Indication of aeration of test solutions before introduction of fish
- Pre-aeration at 6.5mL/min/L for 30mins due to supersaturation of sample with O_2 when sample was heated to 19°C

ix. Indication that EC guidance document for salinity adjustment was followed
- The following was done for all 3 tests:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater concentrated to 90ppt (by freezing/refreezing to remove frozen layer and concentrate salts)

Reporting Requirements for Reference Method EPAW 95-EPA West Coast (Topsmelt)

- No deviations from EC guidance document for salinity adjustment of sample
- HSB was added to samples to salinity adjust them to 30ppt

x. Type and source of control/dilution water
- For all 3 tests, control/dilution water was UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xi. Concentrations and volumes tested:
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- For Test 1:
  - Control (0%) - 200 mL
  - Salinity Control (0%) - 200 mL
  - 4.5% - 200mL
  - 9.1% - 200mL
  - 18.2% - 200mL
  - 36.3% - 200mL
  - 72.6% - 200mL
- For Test 2:
  - Control (0%) - 200 mL
  - Salinity Control (0%) - 200 mL
  - 4.3% - 200mL
  - 8.6% - 200mL
  - 17.3% - 200mL
  - 34.5% - 200mL
  - 69.0% - 200mL
- For Test 3:
  - Control (0%) - 200 mL
  - Salinity Control (0%) - 200 mL
  - 4.4% - 200mL
  - 9.0% - 200mL
  - 18.0% - 200mL
  - 36.0% - 200mL
  - 71.0% - 200mL

xii. Number of replicated per concentration
- For all 3 tests: 5 replicates per concentration

xiii. Number of organisms added to each test vessel
- For all 3 tests: 5 fish per vessel

xiv. Manner and rate of exchange of test solutions
- For all 3 test: Daily renewal

xv. Measurements of dissolved oxygen, pH and temperature
- Test 1: DO: 6.1 - 7.9 mg/L, pH: 7.8 - 8.3, T: 19.0 - 21.0 °C
- Test 2: DO: 6.4 - 7.7 mg/L, pH: 7.8 - 8.1, T: 20.0 – 20.5 °C
- Test 3: DO: 6.4 - 7.6 mg/L, pH: 7.8 - 8.3, T: 20.0 - 21.0 °C

Results

i. Number and % of mortalities of fish in each test solution
- Test 1: Totals from all 5 replicates are presented:
  - Control (0%) – 1/25 = 4%

- Salinity Control 1/25 = 4%
- 4.5% - 0/25 = 0%
- 9.1% - 0/25 = 0%
- 18.2% - 0/25 = 0%
- 36.3% - 1/25 = 4%
- 72.6% - 2/25 = 8%

- Test 2: Totals from all 5 replicates are presented:
  - Control (0%) – 0/25 = 0%
  - Salinity Control 0/25 = 0%
  - 4.3% - 1/25 = 4%
  - 8.6% - 1/25 = 4%
  - 17.3% - 0/25 = 0%
  - 34.5% - 0/25 = 0%
  - 69.0% - 1/25 = 4%
- Test 3: Totals from all 5 replicates are presented:
  - Control (0%) – 0/25 = 0%
  - Salinity Control 0/25 = 0%
  - 4.4% - 0/25 = 0%
  - 9.0% - 0/25 = 0%
  - 18.0% - 0/25 = 0%
  - 36.0% - 1/25 = 4%
  - 71.0% - 0/25 = 0%

ii. Average dry weight per original fish in test vessel

- Test 1: Means from all 5 replicates are presented:
  - Control (0%) – 0.93 mg
  - Salinity Control – 1.08 mg
  - 4.5% - 1.00 mg
  - 9.1% - 1.04 mg
  - 18.2% - 0.96 mg
  - 36.3% - 1.10 mg
  - 72.6% - 0.99 mg
- Test 2: Means from all 5 replicates are presented:
  - Control (0%) – 0.98 mg
  - Salinity Control – 0.99 mg
  - 4.3% - 0.91 mg
  - 8.6% - 0.87 mg
  - 17.3% - 0.78 mg
  - 34.5% - 0.90 mg
  - 69.0% - 0.77 mg
- Test 3: Means from all 5 replicates are presented:
  - Control (0%) – 0.93 mg
  - Salinity Control – 0.96 mg
  - 4.4% - 1.06 mg
  - 9.0% - 0.87 mg
  - 18.0% - 0.97 mg
  - 36.0% - 0.92 mg
  - 71.0% - 0.87 mg

Reporting Requirements for Reference Method EPAW 95-EPA West Coast (Topsmelt)

iii. Estimate of 7-d LC_{50} (95% CL)

- Test 1: 7-d LC_{50} concentration > 72.6% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 2: 7-d LC_{50} concentration > 69.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 3: : 7-d LC_{50} concentration > 71.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Quantal statistic methods not applicable

iv. Estimate of 7-d IC_{25} (95% CL) for growth

- Test 1: 7-d IC_{25} concentration > 72.6% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 2: 7-d IC_{25} concentration > 69.0% effluent (highest concentration tested due to dilution for salinity adjustment)
- Test 3: 7-d IC_{25} concentration > 71.0% effluent (highest concentration tested due to dilution for salinity adjustment)

v. Current reference toxicity tests (95% CL) for 7-d LC_{50} for survival and 7-d IC_{50} for growth

- Test 1 :Reference toxicity tests for Toxicant: Copper
  - Test conducted on July 10, 2004, same day as effluent test
  - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
  - 7-d LC_{50} survival = 161mg/L Cu, 95% CL = 139-188mg/L
  - 7-d IC_{50} growth = 147mg/L Cu, 95% CL = 119-169mg/L
- Test 2 :Reference toxicity tests for Toxicant: Copper
  - Test conducted on July 30, 2004, same day as effluent test
  - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
  - 7-d LC_{50} survival = 130mg/L Cu, 95% CL = 115-147mg/L
  - 7-d IC_{50} growth = 124mg/L Cu, 95% CL = 87-144mg/L
- Test 3 :Reference toxicity tests for Toxicant: Copper
  - Test conducted on August 27, 2004, same day as effluent test
  - Reference toxicant test was conducted on the same batch of externally supplied topsmelt used in the effluent test and under the same experimental conditions as the effluent test
  - 7-d LC_{50} survival = 121mg/L Cu, 95% CL = 107-137mg/L
  - 7-d IC_{50} growth = 128mg/L Cu, 95% CL = 85-150mg/L

vi. Reference toxicity warning limits (+/- SD) for 7-d LC_{50} for survival and 7-d IC_{50} for growth

- Test 1: Reference toxicity tests for Toxicant: Copper
  - 7-d LC_{50} survival = 137 ± 56mg/L Cu
  - 7-d IC_{50} growth = 135 ± 51mg/L Cu
- Test 2: Reference toxicity tests for Toxicant: Copper
  - 7-d LC_{50} survival = 129 ± 48mg/L Cu,
  - 7-d IC_{50} growth = 130 ± 52mg/L Cu
- Test 3: Reference toxicity tests for Toxicant: Copper
  - 7-d LC_{50} survival = 132 ± 48mg/L Cu,
  - 7-d IC_{50} growth = 131 ± 51mg/L Cu

APPENDIX B

92-h Echinoderm Fertilization Test

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75^{o} 22' 32" N, 97^{o} 48' 37" W.

ii. Date & time of sampling
   - Samples for sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 4 x 20L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

Test Organisms

i. Species of test organism
   - Sandollar Echinoid (*Dendraster excentricus*)

ii. Name and city of testing laboratory
   - EVS Environment Consultants, North Vancouver, BC

iii. Source of test species
   - M-REP, Escondido, California
   - All adults providing gametes are from the same population and source
   - Gametes are spawned in-house at EVS

iv. Date test species acquired on
   - Test 1: Test was not initiated due to inability of the Sandollars to spawn.
   - Test 2: July 30, 2004
   - Test 3: August 27, 2004

v. Holding time and conditions for adults
   - Test 1: N.A.
   - Test 2: Adults received at the testing laboratory the day of the test.
   - Test 3: Adults received at the testing laboratory the day of the test.

vi. Indications of deviations from EC guidance on the importation of test organisms
   - Test 1: na
   - Test 2: No deviations from EC requirements
   - Test 3: No deviations from EC requirements

vii. Weekly percent mortality of adults being held over 7d preceding test
   - Test 1: na
   - Test 2: <2% per day over the 7 days preceding the test
   - Test 3: <2% per day over the 7 days preceding the test

viii. Age of test organisms
   - Test 1: n.a.
   - Test 2: < 4 hours after spawning

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- Test 3: < 4 hours after spawning

ix. Unusual appearance, behaviour, or treatment of adults or gametes before test start
- Test 1: Test was not initiated due to inability of the Sandollars to spawn
- Test 2 Organisms appear healthy
- Test 3: Organisms appear healthy

Test Facilities and Conditions

i. Test type & method
- Echinoderm (*Dendraster excentricus*) Fertilization Toxicity Test
- Static
- Reference Method – EPS/1/RM/27 with 1997 amendments

ii. Test duration
- Test 1: na
- Test 2: 10:10 min (10min sperm + 10min sperm & egg)
- Test 3: 10:10 min (10min sperm + 10min sperm & egg)

iii. Date and time for start of definitive test
- Test 1: na
- Test 2: Friday July 30, 2004 – 1620h
- Test 3: Friday August 27, 2004 – 1334h

iv. Test vessel description
- Test 1: na
- Test 2: 16 x 125mm test tubes
- Test 3: 16 x 125mm test tubes

v. Person(s) performing the test and verifying the results
- Test 1: na
- Test 2: Testing by Kathryn Sentance and Ann-Marie Norris. Statistical analyses by Jenny Shao and Kathryn Sentance. QA/QC reviewed by Julianna Kalokai.
- Test 3: Testing by Kathryn Sentance and Ann-Marie Norris. Statistical analyses by Jenny Shao and Kathryn Sentance. QA/QC reviewed by Julianna Kalokai.

vi. Indication of rate and duration of pre-aeration of test solutions before initiation of test
- Test 1: na
- Test 2: No pre-aeration noted.
- Test 3: No pre-aeration noted.

vii. Confirmation that no adjustment of sample or solution pH occurred
- Test 1: na
- Test 2: No pH adjustment
- Test 3: No pH adjustment

viii. Procedure for sample filtration
- Test 1: na
- Test 2: No sample filtration
- Test 2: No sample filtration

ix. Procedure for preparation of hypersaline brine (HSB) as per EC guidance document on salinity adjustment – July 1997
- Test 1: na
- Test 2: 30 ppt adjusted with hypersaline brine (HSB). Preparation of HSB and salinity adjustment as per EC guidance document on Salinity adjustment – July 1997
- Test 2: 30 ppt adjusted with hypersaline brine (HSB). Preparation of HSB and salinity adjustment as per EC guidance document on Salinity adjustment – July 1997

x. Procedure for salinity adjustment as per EC guidance document on salinity adjustment – July 1997

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- No deviations from EC guidance for salinity adjustment
- Test 1: na
- Test 2: salinity adjusted from 2.8 to 28 ppt
- Test 3: salinity adjusted from 5 to 28 ppt

xi. Type and source of control/dilution water
- Test 1: na
- Test 2: UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium
- Test 3: UV-sterilized, 0.45µm-filtered natural seawater from the Vancouver Aquarium

xii. Concentrations and volumes tested
- Test 1: na
- Test 2: Concentrations (% effluent volume / total volume) tested and total volumes used were:
    - Control (0%) - 10mL
    - Salinity Control (0%) - 10mL
    - 4.6% - 10mL
    - 9.1% - 10mL
    - 18.3% - 10mL
    - 36.6% - 10mL
    - 73.1% - 10mL
- Test 3: Concentrations (% effluent volume / total volume) tested and total volumes used were:
    - Control (0%) - 10mL
    - Salinity Control (0%) - 10mL
    - 4.7% - 10mL
    - 9.4% - 10mL
    - 18.8% - 10mL
    - 37.5% - 10mL
    - 75.1% - 10mL

xiii. Number of replicated per concentration
- Test 1: na
- Test 2: 4 replicates per treatment concentration
- Test 3: 4 replicates per treatment concentration

xiv. Number of organisms per container
- Test 1: na
- Test 2: 100 eggs per vessel
- Test 3: 100 eggs per vessel

xv. Measurements of pH and dissolved oxygen in sample water before use
- Test 1: na
- Test 2: pH 8.1, DO 8.5
- Test 3: pH 8.0, DO 8.5

xvi. Measurements of pH, temperature, dissolved oxygen, and salinity during test
- Test 1: na
- Test 2: pH – 8.0 – 8.1, T - 15.0-16.0°C, DO - 8.2-8.5mg/L, salinity - 28ppt
- Test 3: pH – 8.2 – 8.5, T - 15.0-16.0°C, DO - 8.2-8.5mg/L, salinity - 28ppt

Results

i. Number and % of fertilized eggs in each test concentration
- Test 1: na
- Test 2: (Number is equal to percent since totals were 100)
    - Control (0%): #F = 59, 62, 56, 65 #UF = 41, 38, 44, 35
    - Salinity Control: #F = 60, 57, 59, 62 #UF = 40, 43, 41, 38

Reporting Requirements for Reference Method EPS1/RM/27-EC 92 (Sperm Cell)

- 4.6%: #F = 60, 66, 56, 58 #UF = 40, 34, 44, 42
- 9.1%: #F = 46, 42, 45, 42 #UF = 54, 58, 55, 58
- 18.3%: #F = 39, 39, 37, 36 #UF = 61, 64, 63, 64
- 36.6%: #F = 31, 34, 25, 31 #UF = 69, 66, 75, 69
- 73.1%: #F = 19, 20, 21, 20 #UF = 81, 80, 79, 80

- Test 3: (Number is equal to percent since totals were 100)
  - Control (0%): #F = 77, 80, 74, 77 #UF = 23, 20, 26, 23
  - Salinity Control: #F = 76, 73, 79, 77 #UF = 24, 27, 21, 23
  - 4.7%: #F = 78, 74, 76, 72 #UF = 22, 26, 24, 28
  - 9.4%: #F = 61, 62, 62, 60 #UF = 39, 38, 38, 40
  - 18.8%: #F = 56, 58, 59, 55 #UF = 44, 42, 41, 45
  - 37.5%: #F = 49, 50, 50, 48 #UF = 51, 50, 50, 52
  - 75.1%: #F = 25, 27, 24, 27 #UF = 75, 73, 76, 73

ii. Estimate of IC_{25} (95% CL) for fertilization success

- Test 1: na
- Test 2: IC_{25} concentration = 8.7 (7.6 – 9.9)% v/v effluent
- Test 3: IC_{25} concentration = 17.5 (11.6 – 22.6)% v/v effluent

iii. Current reference toxicity tests (95% CL) for IC_{50} for fertilization

- Test 1: na
- Test 2: Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
  - Test conducted on July 30, 2004, same day as effluent test
  - Reference test conducted under same conditions
  - IC_{50} for fertilization = 2.1mg/L SDS, 95% CL = (1.9 – 2.4)mg/L
- Test 3: Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
  - Test conducted on August 27, 2004, same day as effluent test
  - Reference test conducted under same conditions
  - IC_{50} for fertilization = 2.3mg/L SDS, 95% CL = (2.1 – 2.4)mg/L

iv Reference toxicant warning limits (+/- 2SD) for IC_{50} for fertilization

- Test 1: na
- Test 2: 4.2 +/- 4.8 mg/L SDS
- Test 3: 3.9 +/- 4.6 mg/L SDS

APPENDIX C

7-d Sublethal *Champia* (Algae) Toxicity Test

Reporting Requirements for Reference Method EPA/600/4-91-003, Method 1009.0 (*Champia*)

Effluent Sample

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 97° 48' 37" W.

ii. Date & time of sampling
   - Samples for yearly sublethal toxicity testing were collected:
     Test 1 - Wednesday July 7, 2004 – 1100h
     Test 2 - Tuesday July 27, 2004 – 0930h
     Test 3 – Tuesday Aug 24, 2004 – 1500h

iii. Type of sample
   - Final effluent water

iv. Brief description of sampling point
   - 20m downstream of the siphon discharge point at Garrow Lake dam

v. Sampling method
   - Water was collected from at least 15cm below the surface using a water pump with silicon tubing
   - Water was collected from the upstream direction
   - The pump was flushed with site water for at least one minute prior to sample collection
   - 1 x 4L sample bottles were filled

vi. Name of person submitting samples
   - Dennis Lu (Gartner Lee) Tests 1 & 2
   - Patrick Allard (Azimuth) Test 3

vii. Temperature of water upon receipt at lab
   - Test 1: Test was not conducted as sample was delayed by weather and person qualified to conduct the work at the lab left for vacation. This was discussed with Sandra Blenkinsopp at the time to provide direction.
   - Test 2: 8°C
   - Test 3: 17°C

Test Organisms

i. Species of test organism
   - Algae (*Champia parvula*)

ii. Name and city of testing laboratory
   - Saskatchewan Research Council [SRC], Saskatoon, SK

iii. Source of test species
   - Test 1: na
   - Test 2 and Test 3
     - Sexually mature male and female branches
     - Obtained from USEPA, Hatfield Marine Science Center, Newport Oregon, 1995
     - Appear in good health
     - Females have trichogynes, males have sori with spermatia

Test Facilities and Conditions

i. Test type & method
   - *Champia parvula* sexual reproduction test
   - Static, non-renewal
   - 2-day exposure, followed by 5-7 day recovery period for cystocarp development
   - Reference Method - EPA/600/4-91/003, Method 1009.0

ii. Date and time for start of definitive test
   - Test 1: na

- Test 2: Friday July 30, 2004 – time not noted but lab notes state tests started within 72 hrs of collection
- Test 3: Friday August 27, 2004 – time not noted but lab notes state tests started within 72 hrs of collection

iii. Test vessel description
- Test 1: na
- Test 2: 270mL transparent polystyrene cups with polystyrene lids
- Test 2: 270mL transparent polystyrene cups with polystyrene lids

iv. Person(s) performing the test and verifying the results
- Test 1: na
- Tests 2 & 3 - Mary Moody

v. Indication of pre-aeration of test solutions
- Test 1: na
- Tests 2 & 3 - No pre-aeration

vi. Confirmation that no pH adjustment of sample or solution occurred
- Test 1: na
- Tests 2 & 3: - No pH adjustment

vii. Indication that EC guidance document for salinity adjustment was followed
- Test 1: na
- Test 2:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater at 90ppt
    - No deviations from EC guidance document for salinity adjustment of sample
    - Salinity adjustment: 600mL effluent + 250mL HSB + 8.5mL test nutrient solution
    - Salinity of samples adjusted from 4ppt to 30ppt
- Test 3:
    - No deviations from EC guidance document on preparation of hypersaline brine
    - HSB prepared from natural seawater at 90ppt
    - No deviations from EC guidance document for salinity adjustment of sample
    - Salinity adjustment: 600mL effluent + 230mL HSB + 10 ml test nutrient solution
    - Salinity of samples adjusted from 5ppt to 30ppt

viii. Type and source of control/dilution water
- Test 1: na
- Tests 2 & 3
    - Natural seawater collected at the Pacific Environmental Center, Environment Canada, North Vancouver, BC
    - Filtered to 0.2μm and autoclaved prior to use
    - Salinity adjusted as per EC guidance document to 30ppt with HSB from the same source

ix. Concentrations and volumes of test solutions
- Concentrations (% effluent volume / total volume) tested and total volumes used were:
- Test 1: na
- Tests 2:
    - Control (Natural Seawater) (0%) - 100mL, 4.5cm depth
    - Salinity Control Brine (0%) - 100mL, 4.5cm depth
    - 4.38% - 100mL, 4.5cm depth
    - 8.75% - 100mL, 4.5cm depth
    - 17.5% - 100mL, 4.5cm depth

Reporting Requirements for Reference Method EPA/600/4-91-003, Method 1009.0 (*Champia*)

- 35.0% - 100mL, 4.5cm depth
- 70.0% - 100mL, 4.5cm depth

- Tests 3:
  - Control (Natural Seawater) (0%) - 100mL, 4.5cm depth
  - Salinity Control Brine (0%) - 100mL, 4.5cm depth
  - 4.5% - 100mL, 4.5cm depth
  - 9.0% - 100mL, 4.5cm depth
  - 18.0% - 100mL, 4.5cm depth
  - 36.0% - 100mL, 4.5cm depth
  - 72.0% - 100mL, 4.5cm depth

x. Number of replicated per concentration
- Test 1: na
- Tests 2 & 3: 3 replicates per concentration

xi. Number of organisms per test chamber
- Test 1: na
- Tests 2 & 3: 5 female branches + 2 male branches per chamber

xii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample before use
- Test 1: na
- Test 2: pH - 7.78, T – 22.0 °C, DO – 7.9mg/L, salinity - 4ppt
- Test 3: pH - 7.58, T – 23.0 °C, DO – 8.0mg/L, salinity - 5ppt

xiii. Measurements of pH, temperature, dissolved oxygen, and salinity of sample during test
- Test 1: na
- Test 2: pH – 8.20, T – 23 °C, DO – 7.9, salinity: 30ppt
- Test 3: pH – 8.33, T – 22 °C, DO – 7.9, salinity: 29ppt

Results

i. Number and % mortality of female plants after recovery in each test solution
- Totals from all 3 replicates are presented:
- Test 1: na
- Test 2:
  - Control (0%): 0 (0%) mortality
  - Salinity Control (0%): 0 (0%) mortality
  - 4.38%: 0 (0%) mortality
  - 8.75%: 0 (0%) mortality
  - 17.5%: 0 (0%) mortality
  - 35.0%: 0 (0%) mortality
  - 70.0%: 0 (0%) mortality
- Test 3:
  - Control (0%): 0 (0%) mortality
  - Salinity Control (0%): 0 (0%) mortality
  - 4.5%: 0 (0%) mortality
  - 9.0%: 0 (0%) mortality
  - 18.0%: 0 (0%) mortality
  - 36.0%: 0 (0%) mortality
  - 72.0%: 0 (0%) mortality

Reporting Requirements for Reference Method EPA/600/4-91-003, Method 1009.0 (*Champia*)

ii. Mean number of cystocarps per plant in each test concentration

- Test 1: na
- Test 2:
    - Control (0%): 92.1
    - Salinity Control (0%): 92.5
    - 4.38%: 105.1
    - 8.75%: 105.1
    - 17.5%: 90.7
    - 35.0%: 61.9
    - 70.0%: 13.3
- Test 3:
    - Control (0%): 58.3
    - Salinity Control (0%): 58.6
    - 4.5%: 59.7
    - 9.0%: 59.4
    - 18.0%: 60.9
    - 36.0%: 51.3
    - 72.0%: 26.3

iii. Estimate of IC_{25} (95% CL) for cystocarp development

- Test 1: na
- Test 2: IC_{25} concentration = 26.6 (20.8 – 31.5)% effluent v/v
- Test 3: IC_{25} concentration = 45.3 (36.3 – 58.1)% effluent v/v
- Quantal statistic method was linear interpolation

iv. Current reference toxicity tests (95% CL) for IC_{50} for cystocarp development

- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test 1: na
- Test 2: Test conducted on July 27, 2004, within 30 days of effluent test
    - Reference toxicant test was conducted under the same experimental conditions as the effluent test
    - IC_{50} cystocarp development = 1.48mg/L SDS, 95% CL = (1.38 - 1.62) mg/L
    - Reference toxicity warning limits 1.40 (+/- 2SD) for IC_{50} for cystocarp development
- Test 3: Test conducted on July 27, 2004, within 30 days of effluent test
    - Reference toxicant test was conducted under the same experimental conditions as the effluent test
    - IC_{50} cystocarp development = 1.48mg/L SDS, 95% CL = (1.38 - 1.62) mg/L
    - Reference toxicity warning limits 1.40 (+/- 2SD) for IC_{50} for cystocarp development

v. Reference toxicant warning limits (+/- 2SD) for IC_{50} for cystocarp development

- Reference toxicity tests for Toxicant: Sodium Dodecyl Sulfate
- Test 1: na
- Test 2: 1.40 (1.6-1.70) mg/L SDS
- Test 3: 1.40 (1.6-1.70) mg/L SDS

Water Quality Monitoring Results (Part 1, Section 7)

Facility Name	FDP Name	Area Name	EEM Water Quality Monitoring Date	Hardness	Alkalinity	Aluminum	Cadmium	Iron	Mercury	Molybdenum	Ammonia
Exposure Area											
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	7/27/2004	482	37.5	0.033	0.00007	0.046	< 0.00005	0.00156	< 0.02
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	2270	45	< 0.1	< 0.00002	< 0.01	< 0.00001	< 0.005	< 0.02
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	1750	38.8	< 0.1	0.000028	< 0.01	< 0.00001	< 0.005	0.02
Reference Area											
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	2960	46	< 0.1	< 0.00002	< 0.01	< 0.00001	0.0062	< 0.02
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	1560	36.1	< 0.1	< 0.00002	< 0.01	< 0.00001	< 0.005	< 0.02

[1] Concentrations of Radium226 are in Bq/L

Water Quality Monitoring Results (Part 1, Section 7)

Facility Name	FDP Name	Area Name	EEM Water Quality Monitoring Date	Nitrate	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS
Exposure Area											
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	7/27/2004	0.0372	< 0.001	0.000405	< 0.005	0.00026	0.000979	0.0242	3.7
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	< 0.02	< 0.0002	0.000216	< 0.005	< 0.00005	0.000252	0.00118	3.3
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	< 0.02	0.00027	0.000209	< 0.005	0.000267	0.000267	0.00092	8.4
Reference Area											
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	< 0.02	0.00044	0.000231	< 0.005	0.000052	0.000217	0.0005	9.3
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	< 0.02	< 0.0002	0.000205	< 0.005	< 0.00005	0.000186	< 0.0005	7

[1] Concentrations of Radium226 are in Bq/L

Water Quality Monitoring Results (Part 1, Section 7)

Facility Name	FDP Name	Area Name	EEM Water Quality Monitoring Date	Radium226	PH	Water Temperature	Dissolved Oxygen	Notes
Exposure Area								
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	7/27/2004	< 0.005	7.91	0.2	13.23	Note that this is the first exposure area sample of 2004, because the Garrow Bay exposure area (mouth of the creek) was frozen during the prior sampling event (i.e., July 7, 2004).
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	< 0.005	7.79	0.2	13.78	
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	0.006	7.64	0.9	15.2	
Reference Area								
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/17/2004	< 0.005	7.92	0.1	14.04	Note that the reference area was ice free only during August 17 and August 24, 2004 sampling events.
Teck Cominco Metals Limited - Polaris Mine (Little Cornwallis Island)	Garrow Lake Syphons	Garrow Bay	8/24/2004	< 0.005	7.62	1.2	15.13	Note that the reference area was ice free only during August 17 and August 24, 2004 sampling events.

[1] Concentrations of Radium226 are in Bq/L

March 22, 2005

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – Revised 2004 3rd Quarter Metal Mining Effluent Regulations Report

Please find attached a **revised** Polaris Mine 3rd Quarter MMER regulatory data tables. The reason for the revision is to ensure consistency between the data entered electronically online through the RISS system, and the hard copy Annual and 3rd Quarter reports provided. As explained in the original 3rd Quarter report cover letter, effluent from Garrow Lake ceased flowing by mid-August but surface run off from adjacent slopes maintained minimal water flow at the designated final discharge point into August. By August 17, there was water at the final discharge point in a pool, but flow was too low to be measured. As a result, regulatory concentration data in the 3rd Quarter had originally been submitted with average daily flows of 0 m^3 per day for the weeks of Aug. 17, Aug. 24, and Aug. 31, 2004. However, we continued to collect effluent, water quality and acute and sublethal toxicity samples on these latter three dates. Upon submitting the regulatory data into the online RISS system for the annual report, these August concentration data were not accepted with a flow rate of zero. Thus a nominal flow rate of 1 m^3 per day was entered. As a result the loadings data set is slightly different from the data submitted in the original 3rd Quarter report. Note that these low flow conditions during August, as well as their implications for effluent sampling, were discussed with Environment Canada representatives early in August.

If you have any questions regarding the annual report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Original signed by B. Donald
Bruce Donald

Attachments: Revised 2003 3rd Quarter Regulatory Data
cc: Walter Kuit (Teck Cominco Limited)
Randy Baker (Azimuth Consulting Group)

2004 3rd QUARTER MMER REPORT - REVISED

LOCATION - FINAL DISCHARGE POINT FROM GARROW LAKE (GARROW LAKE DAM SIPHONS)

CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4 SAMPLED WEEKLY

Sample Taken During The Week of	Date Sample Taken	DELETERIOUS SUBSTANCE (mg/L)[1] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	pH[1]	Collection Method
5-Jul-04	7-Jul-04	0.00100	0.00265	0.0050	0.00269	0.00442	0.1980	117	0.0200	8.05	Grab
12-Jul-04	13-Jul-04	0.00200	0.00070	0.0050	0.00032	0.00204	0.1060	5.7	0.0070	7.90	Grab
19-Jul-04	20-Jul-04	0.00200	0.00043	0.0050	0.00084	0.00088	0.0435	3.0	0.0050	7.86	Grab
26-Jul-04	27-Jul-04	0.00100	0.00052	0.0050	0.00157	0.00207	0.0429	3.0	0.0050	7.87	Grab
2-Aug-04	3-Aug-04	0.00020	0.00082	0.0050	0.00280	0.00338	0.0349	3.3	0.0060	8.00	Grab
9-Aug-04	10-Aug-04	0.00100	0.00100	0.0055	0.00120	0.00748	0.0482	3.0	0.0050	8.04	Grab
16-Aug-04	17-Aug-08	0.00020	0.00121	0.0050	0.00177	0.00644	0.0418	5.3	0.0100	7.95	Grab
23-Aug-04	24-Aug-04	0.00020	0.00134	0.0050	0.00119	0.00967	0.0498	4.4	0.0080	7.84	Grab
30-Aug-04	31-Aug-04	0.00020	0.00137	0.0050	0.00261	0.01340	0.0794	14.5	0.0080	7.90	Grab
6-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
13-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
20-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
27-Sep-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L and pH which is in pH units

Note [2] - "nd" refers to no effluent discharge to sample

MONTHLY MEAN CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4

MONTH OF	MONTHLY MEAN CONCENTRATION[1] OF DELETERIOUS SUBSTANCE[3] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226
July/04	0.0015	0.00107	0.0050	0.00135	0.00235	0.0976	32	0.0093
August/04	0.0004	0.00115	0.00510	0.00191	0.00807	0.0508	6.1	0.0074
September/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L

Note [2] - "nd" refers to no effluent discharge to sample

Note[3] - Monthly Mean Concentrations - the MEAN value of the concentrations measured in all water samples collected during each month when a deleterious substance is deposited.

MASS LOADING OF DELETERIOUS SUBSTANCE FOR EACH DAY SAMPLED

Sample Taken During The Week of	Date Sample Taken	DAILY MASS LOADING OF DELETERIOUS SUBSTANCE (kg/day)[1]								Average Daily Flow Rate (m^3/day)
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	
5-Jul-04	7-Jul-04	0.018	0.048	0.091	0.049	0.080	3.588	2120	362,440	18,122
12-Jul-04	13-Jul-04	0.752	0.264	1.880	0.120	0.767	39.850	2143	2,631,608	375,944
19-Jul-04	20-Jul-04	0.205	0.044	0.512	0.086	0.090	4.458	307	512,395	102,479
26-Jul-04	27-Jul-04	0.028	0.015	0.141	0.044	0.058	1.211	85	141,090	28,218
2-Aug-04	3-Aug-04	0.005	0.022	0.132	0.074	0.089	0.923	87	158,700	26,450
9-Aug-04	10-Aug-04	0.026	0.026	0.142	0.031	0.194	1.248	78	129,470	25,894
16-Aug-04	17-Aug-08	0.000	0.000	0.000	0.000	0.000	0.000	0	0	1
23-Aug-04	24-Aug-04	0.000	0.000	0.000	0.000	0.000	0.000	0	0	1
30-Aug-04	31-Aug-04	0.000	0.000	0.000	0.000	0.000	0.000	0	0	1
6-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
13-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
20-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0
27-Sep-04	nd[2]	0	0	0	0	0	0	0	0	0

Note[1] - Mass Loading is in kilograms per day of the deleterious substance deposited except Radium 226 which is in Bq per day

Note[2] - "nd" refers to no effluent discharge to sample

MASS LOADING PER CALENDAR MONTH FOR EACH DELETERIOUS SUBSTANCE

CALENDAR MONTH OF	MASS LOADING[1] FOR DELETERIOUS SUBSTANCE (kg/month)[2]								Average Weekly Flow Rate[3] (m^3/week)	Total Monthly Volume[4] (m^3/month)
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[2]		
July/04	7.77	2.87	20.33	2.31	7.71	380.58	36,078.15	28,268,381	131,191	4,066,913
August/04	0.19	0.29	1.70	0.65	1.76	13.46	1,022.95	1,786,654	10,469	324,551
September/04	0	0	0	0	0	0	0	0	0	0

Note[1] - Total Mass Loading for Calendar month calculated by multiplying the Average Daily Mass Loading for the Month x # days in the month

Note[2] - Mass loading units are in kg per month except Radium 226, which is in Bq permonth

Note[3] - Average Weekly Flow Rate calculated by multiplying Average Daily Flow Rate x 7 days per week

Note[4] - Total Monthly Volume calculated by multiplying Average Daily Flow Rate for the month x days in month

APPENDIX D

RESULTS OF EFFLUENT CHARACTERIZATION

AS PER PARAGRAPH 15(1)(a)

No effluent samples were collected during the 2nd Quarter of 2004 as there was no effluent discharge.
No Acute Lethality Testing conducted during the quarter as there was no effluent being discharged.

Bruce J. Donald
Reclamation Manager

March 15, 2005

Prairie & Northern Region
Environment Canada
Room 200, 4999 98th Ave.
Edmonton, AB T6B 2X3

Attention: Peter Blackall, Regional Director of Environmental Protection

Dear Sir;

Re: Polaris Mine – 2004 4th Quarter Metal Mining Effluent Regulations Report

Despite having a designated discharge location for effluent identified under Section 9 of the MMER, there was no discharge from the Garrow Lake Tailings Impoundment Area during the period October 1, 2004 to December 31, 2004. While there is no data to report, I have completed the monitoring report as required by the regulations and have attached it to this letter.

If you have any questions regarding the quarterly report or aspects of the application of the MMER to the Polaris Mine, please feel free to contact me at any time.

Yours truly,

Bruce Donald

Attachments: 4th Quarter 2004 Monitoring Report

cc:
Walter Kuit (Teck Cominco Limited)
Randy Baker (Azimuth Consulting Group)

POLARIS MINE – MMER MONITORING REPORT

4th QUARTER 2004

APPENDIX A

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/13

APPENDIX B

i. Information specified by Section 8.1 of Reference Method EPS 1/Rm/14

APPENDIX C

i. Concentration & monthly mean concentrations of each deleterious substance of Schedule 4
ii. pH of the effluents samples as required by subsection 12(1)
iii. Description of sample collection method
iv. Total volume of effluent deposited during each month of the quarter as per section 19
v. Mass loading of the deleterious substances set out in Schedule 4 and as per section 20

APPENDIX D

i. Results of the effluent characterization as per paragraph 15(1)(a)

APPENDIX A

Reporting Requirements for Reference Method EPS 1/RM/13

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Percent mortality of fish in stock tank(s)
   - None to report. There were no tests conducted during the period

v. Species of test organism
   - None to report as there were no tests conducted during the period

vi. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vii. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

viii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

ix. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

x. Indication of aeration of test solutions before introduction of fish
   - None to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Number of fish added to each test vessel
   - No fish added as there were no tests conducted during the period

xiv. Mean and range of fork length of control fish at end of test
   - No data to report as there were no tests conducted during the period

xv. Mean wet weight of individual control fish at end of the test
   - No data to report as there were no tests conducted during the period

xvi. Estimated loading density of fish in test solutions
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/13 - Continued

Section 8.1.3 Results

i. Number of mortalities of fish in each test solution
   - None to report. No tests conducted during the period

ii. Number of control fish showing atypical/stressed behaviour
   - None to report. No tests conducted.

iii. Mean mortality rate in solutions of effluent and control water
   - None to report. No tests conducted

iv. Estimate of 96-h LC50 in multi-concentration tests
   - No data to report. No tests conducted

v. Most recent 96-h LC50 for reference toxicity test(s)
   - No data to report. No tests conducted

APPENDIX B

Reporting Requirements for Reference Method EPS 1/RM/14

Section 8.1.1 Effluent

i. Name & location of operation generating the effluent
   - Polaris Mine, Little Cornwallis Island, Nunavut
   - Final Discharge Point for Garrow Lake is geo referenced as 75° 22' 32" N, 96° 48' 37" W.

ii. Date & time of sampling
   - No sampling conducted as there was no effluent discharge during the quarter.

iii. Type of sample
   - No sampling conducted as there was no effluent discharge during the quarter

iv. Brief description of sampling point
   - Discharge point of siphon at Garrow Lake dam

v. Sampling method
   - No sampling conducted as there was no effluent discharge during the quarter

vi. Name of person submitting samples
   - No sampling conducted as there was no effluent discharge during the quarter

Section 8.1.2 Test Facilities and Conditions

i. Test type & method
   - No testing conducted as there was no effluent discharge during the quarter

ii. Indications of deviations from requirements in Sections 2 to 7 of Method EPS 1/RM/13
   - No deviations to report as there was no testing conducted during the quarter

iii. Name and city of testing laboratory
   - No laboratory used during the quarter

iv. Species of test organism
   - None to report as there were no tests conducted during the period

v. Date and time for start of definitive test
   - None to report as there were no tests conducted during the period

vi. Person(s) performing the test and verifying the results
   - No tests performed during the quarter

vii. pH, temperature, dissolved oxygen, and conductivity of unadjusted, undiluted effluent
   - No data to report as there were no tests conducted during the period

viii. Confirmation that no adjustment of sample or solution pH occurred
   - No adjustment to report as there were no tests conducted during the period

ix. Indication of any adjustment of hardness of effluent sample
   - No adjustment to report as there were no tests conducted during the period

x. Indication of any aeration of sample
   - No indication to report as there were no tests conducted during the period

xi. Concentrations and volumes tested
   - No data to report as there were no tests conducted during the period

xii. Measurements of dissolved oxygen, pH and temperature
   - No data to report as there were no tests conducted during the period

xiii. Estimates of time to first brood, average number of neonates per brood, and percent mortality during the seven-day period prior to the test
   - No data to report as there were no tests conducted during the period

xiv. Number of neonates per test vessel and milliliters of solution per daphnid
   - No data to report as there were no tests conducted during the period

Reporting Requirements for Reference Method EPS 1/RM/14 - Continued

Section 8.1.3 Results

i. Number of dead and/or immobile daphnids in each test solution including controls
   - No data to report. No tests conducted during the period.

ii. For single-concentration test the number of daphnids dead in each of three replicate effluent solutions and in each of three replicate control solutions at end of test. Also report the mean value.
   - No data to report. No tests conducted during the period.

iii. Estimate of 48-h LC50 and 95% confidence limits in multi-concentration tests, 48-h EC50 for immobilization and 95% confidence limits, indication of statistical method on which results are based.
   - No data to report. No tests conducted during the period

iv. Most recent 48-h LC50 for reference toxicant test(s), reference chemical(s), date test initiated, historic geometric mean LC50 and warning limits.
   - No data to report. No tests conducted during the period.

APPENDIX C

2004 4th QUARTER MMER REPORT

LOCATION - FINAL DISCHARGE POINT FROM GARROW LAKE

CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4 SAMPLED WEEKLY

Sample Taken During The Week of	Date Sample Taken	DELETERIOUS SUBSTANCE (mg/L)[1] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	pH[1]	Collection Method
04-Oct-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
11-Oct-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
18-Oct-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
25-Oct-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
01-Nov-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
08-Nov-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
15-Nov-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
22-Nov-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
29-Nov-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
06-Dec-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
13-Dec-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
20-Dec-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
27-Dec-04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L and pH which is in pH units

Note [2] - "nd" refers to no effluent discharge to sample

MONTHLY MEAN CONCENTRATIONS OF EFFLUENT FOR MMER SCHEDULE 4

MONTH OF	MONTHLY MEAN CONCENTRATION[1] OF DELETERIOUS SUBSTANCE[3] Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226
October/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
November/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]
December/04	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]	nd[2]

Note[1] - All concentrations are in mg/L except Radium 226 which is Bq/L

Note [2] - "nd" refers to no effluent discharge to sample

Note[3] - Monthly Mean Concentrations - the MEAN value of the concentrations measured in all water samples collected during each month when a deleterious substance is deposited.

MASS LOADING OF DELETERIOUS SUBSTANCE FOR EACH DAY SAMPLED

Sample Taken During The Week of	Date Sample Taken	DAILY MASS LOADING OF DELETERIOUS SUBSTANCE (kg/day)[1]								Average Daily Flow Rate (m^3/day)
		Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[1]	
04-Oct-04	nd[2]	0	0	0	0	0	0	0	0	0
11-Oct-04	nd[2]	0	0	0	0	0	0	0	0	0
18-Oct-04	nd[2]	0	0	0	0	0	0	0	0	0
25-Oct-04	nd[2]	0	0	0	0	0	0	0	0	0
01-Nov-04	nd[2]	0	0	0	0	0	0	0	0	0
08-Nov-04	nd[2]	0	0	0	0	0	0	0	0	0
15-Nov-04	nd[2]	0	0	0	0	0	0	0	0	0
22-Nov-04	nd[2]	0	0	0	0	0	0	0	0	0
29-Nov-04	nd[2]	0	0	0	0	0	0	0	0	0
06-Dec-04	nd[2]	0	0	0	0	0	0	0	0	0
13-Dec-04	nd[2]	0	0	0	0	0	0	0	0	0
20-Dec-04	nd[2]	0	0	0	0	0	0	0	0	0
27-Dec-04	nd[2]	0	0	0	0	0	0	0	0	0

Note[1] - Mass Loading is in kilograms per day of the deleterious substance deposited except Radium 226 which is in Bq per day

Note [2] - "nd" refers to no effluent discharge to sample

MASS LOADING PER CALENDAR MONTH FOR EACH DELETERIOUS SUBSTANCE

CALENDAR MONTH OF	MASS LOADING[1] FOR DELETERIOUS SUBSTANCE (kg/month)[2]								Average Weekly Flow Rate[3] (m^3/week)	Total Monthly Volume[4] (m^3/month)
	Arsenic	Copper	Cyanide	Lead	Nickel	Zinc	TSS	Radium 226[2]		
October/04	0	0	0	0	0	0	0	0	0	0
November/04	0	0	0	0	0	0	0	0	0	0
December/04	0	0	0	0	0	0	0	0	0	0

Note[1] - Total Mass Loading for Calendar month calculated by multiplying the Average Daily Mass Loading for the Month x # days in the month

Note[2] - Mass loading units are in kg per month except Radium 226, which is in Bq permonth

Note[3] - Average Weekly Flow Rate calculated by multiplying Average Daily Flow Rate x 7 days per week

Note[4] - Total Monthly Volume calculated by multiplying Average Daily Flow Rate for the month x days in month

APPENDIX D

RESULTS OF EFFLUENT CHARACTERIZATION

AS PER PARAGRAPH 15(1)(a)

No effluent samples were collected during the 4th Quarter of 2004 as there was no effluent discharge.
No Acute Lethality Testing conducted during the quarter as there was no effluent being discharged.

APPENDIX 19

Limnology and Ecology of Garrow Lake

FINAL
May 2005
Project No.TC-03-03

Limnology and Ecology of Garrow Lake, Little Cornwallis Island, Nunavut - August 2003







Prepared for:

Teck Cominco Metals Ltd.

Bag 2000
Kimberley, BC
V1A 3E1

Prepared by:

AZIMUTH

Azimuth Consulting Group Inc.
218-2902 West Broadway Vancouver,BC V6K 2G8
Tel: 604-730-1220 * Fax: 604-739-8511

Limnology and Ecology of Garrow Lake, Little Cornwallis Island, Nunavut – August 2003

Prepared for

Teck Cominco Metals Ltd.
Bag 2000
Kimberley BC
V1A 3E1

May 2005



Azimuth Consulting Group Inc.
218-2902 West Broadway
Vancouver, BC
V6K 2G8

Project No.

TC–03–03

TABLE OF CONTENTS

TABLE OF CONTENTS i

LIST OF TABLES ii

LIST OF FIGURES ii

APPENDICES iii

ACKNOWLEDGEMENTS iv

GLOSSARY v

EXECUTIVE SUMMARY ES1

1. INTRODUCTION 1

1.1. Background 1
1.2. Limnology 1
1.3. Mining Operations 2
1.4. Objective 3

2. MATERIALS AND METHODS 5

2.1. Limnology and Water Chemistry 5
2.2. Sediment Chemistry 5
2.3. Biota 6
2.3.1. Zooplankton 6
2.3.2. Benthic Invertebrates 7
2.3.3. Fish 7

3. RESULTS AND DISCUSSION 8

3.1. Limnology 8
3.1.1. Physical Attributes and History 8
3.1.2. pH, Temperature, Salinity and Oxygen 9
3.1.2.1. Pre-Mining Profiles 9
3.1.2.2. Post-Mining Profiles 11
3.1.3. Metals 13
3.2. Sediment Chemistry 16
3.3. Ecology 17

3.3.1. Zooplankton 17
3.3.2. Benthic Invertebrates 18
3.3.3. Fish 19
3.3.3.1. Size 19
3.3.3.2. Age 20
3.3.3.3. Diet 21
3.3.3.4. Sex and Maturity 21
3.3.3.5. Tissue Metals 22
3.3.4. Summary 22
4. REFERENCES 24

LIST OF FIGURES

Figure 1. Location of Garrow Lake, Little Cornwallis Island, Nunavut 27

Figure 2. Location of littoral zone sediment and biota stations and water quality profile station, Garrow Lake, August 2003. 28

Figure 3. Temperature (^{o}C; 3a), oxygen (mg/L; 3b) and salinity (ppt; 3c) vs depth (m) profiles, Garrow Lake, 1976 (Fallis et al. 1987) and 2003. 29

Figure 4. Comparison of length – frequency distribution of fourhorn sculpin from 1976 (Fallis et al. 1987) and 2003. 30

LIST OF TABLES

Table 1. Details of sediment, water and biota collections from Garrow Lake, August 8 – 10, 2003. 32

Table 2. Summary of Garrow Lake water column metals concentration (mean, range, µ/L), 1976 to present. 33

Table 3. Conventional parameters and total metal concentrations (µg/L) in water samples from Garrow Lake, August 2003. 34

Table 4. Total metals (mg/kg dw) in Garrow Lake sediment prior to mining. .. 35

Table 5. Conventional sediment parameters and total metals concentration (mg/kg dw) in Garrow Lake littoral zone sediment, August 2003. 36

Table 6. Species diversity and density (#/m^2) of benthic invertebrates, August 2003… 37

Table 7. Biological data for fourhorn sculpin from Garrow Lake, August 2003…. 38

Table 8. Mean (range), total length (mm), weight (g) and condition (K) of Garrow Lake sculpin (1976, 1977 and 2003). 39

Table 9. Length – weight relationship for Garrow Lake sculpin, 1976, 1977 and 2003… 40

Table 10. Mean (range) of fourhorn sculpin whole body metal concentration (mg/kg ww) from Garrow Lake, 1976 (Fallis et al. 1987), 1977 (BC Research, 1978) and 2003. 41

LIST OF PHOTOS

Photo 1. Garrow Lake showing ice cover, August 4 2003 44

Photo 2. Launching the boat in Garrow Lake, August 8, 2003. 44

Photo 3. Garrow Lake showing gravel shorline and mostly ice-free, August 8, 2003… 45

Photo 4. Fourhorn sculpin Myoxocephalus quadricornis from Garrow Lake. ..45

Photo 5. Garrow Lake fourhorn sculpin (140 mm total length) prior to dissection August 2003....46

LIST OF APPENDICES

APPENDIX A Department of Fisheries and Oceans Habitat Authorization

APPENDIX B Garrow Lake Water Chemistry Data, 1976 and 2003

APPENDIX C Fish Metals Data (mg/kg ww) from Garrow Lake, 2003

ACKNOWLEDGEMENTS

We would like to acknowledge the support of Teck Cominco Polaris staff for their assistance and logistical support while on site. Bruce Donald, Teck Cominco is especially thanked for his support of the study and providing latitude to conduct an independent investigation of Garrow Lake. Bruce Donald and Walter Kuit (Teck Cominco) are also thanked for providing historical insight about Garrow Lake and for their review of this report.

Applied Technical Services, Victoria BC is thanked for their careful taxonomic identification of benthic invertebrates. ALS Vancouver is acknowledged for their care in chemical analysis of water, sediment and fish samples.

Randy Baker (Azimuth Consulting Group) authored this report. Patrick Allard and Gary Mann (Azimuth) provided field assistance and Beth Power (Azimuth) is thanked for her technical review. I would also like to thank Bruce Fallis (Department of Fisheries and Oceans, Winnipeg) for sharing his historical experience at Garrow Lake with me.

GLOSSARY

Aquatic – Pertaining to plants or animals that live in freshwater or marine environments.

Arctic – The Arctic is a geographic region that is circumpolar in extent and generally characterized as being north of the treeline, in an area of continuous permafrost.

Benthic – Pertaining to the bottom region of a water body, such as a lake.

Benthic invertebrates / Benthos – Assemblage of organisms living in or on the bottom sediment of a water body and dependent upon the decomposition cycle for most, if not all, of their food supply.

Biomass – The total mass of living organisms usually expressed as a weight per unit area or volume (e.g., mg/m^3 of water).

Bivalves – Mollusks with shells consisting of two halves (i.e., valves) such as clams.

Chironomids – Midges (two-winged insects) in the order Diptera. The aquatic larval form of this insect is typically the most abundant and diverse group of insects found in lakes.

Density of organisms – A term that describes abundance. The total number of living organisms expressed per unit area (e.g., $no./m^2$) or volume ($\#/m^3$).

Dissolved concentrations (water) – The concentration of chemical parameters in water filtered through a 0.45µm glass fiber filter. This is operationally defined as the dissolved fraction in water.

Dipteran insects – Insects of the Order Diptera, consisting of flies having two-wings that includes chironomids, flies, and mosquitoes.

Diversity – A measure (e.g., Shannon-Weaver index) of the variety of living organisms in an area (e.g., number or richness of species).

Drainage basin – The term given to a geographic area that contributes surface and groundwater to a particular lake, river, or stream (also see watershed).

Ecosystem – A community of interacting organisms considered together with the chemical and physical factors that make up their environment.

Environment – Components of the earth including land, water, air, and all layers of the atmosphere. Also included are organic and inorganic matter, living organisms, and all interacting natural systems.

Food chain – Organisms that are linked together in a series that, by consuming lower level organisms, transfer nutrients and energy from one group to another.

Food web – The concept used to describe the relationships of organisms within an ecosystem that are interconnected through various feeding linkages, resulting in the transfer of nutrients and energy.

Freshet – The increased flow of water over a relatively short period of time, usually during spring, caused by snowmelt.

Global Positioning System (GPS) – A sophisticated system used to define a precise geographic location with the aid of a satellite system. Units are typically expressed as UTM (Universal Transverse Mercator) or in latitude and longitude.

Habitat – Any area that provides food, water and/or shelter for an organism.

Invertebrates – A collective term for all animals without a backbone or spinal column and includes all aquatic animal organisms except fish.

Larva – The immature stage, between egg and pupa, of an insect with complete metamorphosis. Many insect larvae are aquatic, including chironomids, mayflies, stoneflies and caddisflies.

Limnology – The study of freshwater lakes including biological, geological, physical, and chemical aspects.

Littoral – The region of a lake, including water and sediment, from the surface to a depth at which photosynthesis ceases, usually within the upper 10m of the water column.

Meromictic – A permanently stratified lake, usually without oxygen (or fish) in its deeper portions due to a density gradient and lack of turnover.

Micro (μ) – A unit of measurement denoting a factor of one-millionth, such as μg/g.

Milligram (mg) – A unit of measurement denoting a factor of one-thousandth, such as mg/g.

Mixolimnion – The low-density surface layer above the pycnocline in a meromictic layer.

Monimolimnion – The high-density bottom layer below the pycnocline in a meromictic lake.

Nutrient – Any substance that provides essential nourishment for the maintenance of life (e.g., carbon, nitrogen, and phosphorous).

Oligochaete – True worms from the Phylum Annelida (segmented worms) that are common in sediment of freshwater habitats.

Oligotrophic – Nutrient deficient waters with low productivity. The vast majority of Arctic lakes are oligotrophic.

Organic Carbon (sediments) – The non-mineral fraction of the sediments that consists of organic carbon, expressed as a percent (%) of the total weight of sediment. This includes all forms of carbon except carbonates.

Phytoplankton – Microscopic or small floating plants suspended in the water column of aquatic ecosystems.

Planktonic – Referring to organisms with limited mobility that are free-floating and living in the water column.

Predator – Any organism that consumes another organism.

Prey – Any organism that is consumed by another organism.

Primary consumers – Organisms such as zooplankton that feed on primary producers (e.g., phytoplankton) for their source of nutrients and energy.

Primary production – Production by photosynthetic organisms, such as algae, phytoplankton and periphyton. Photosynthetic organisms comprise the bottom of the food chain.

Primary productivity – A term given to the rate at which new biomass (i.e., plant tissue) is generated by photosynthetic organisms (i.e., plants) using energy captured from the sun.

Pycnocline – The term given to the density layer of rapid change in temperature and salinity that separates the surface water (epilimnion) from the bottom water (hypolimnion).

Quality Assurance / Quality Control [QA/QC] – Sampling and analytical procedures (such as lab replicate sample analysis) that are integrated in field collection and analytical procedures to ensure acceptable data quality.

Richness – The number of unique taxa (e.g., species) found at a particular location.

Secondary productivity – The rate of increase in biomass of organisms that consume plants or other primary producers.

Secondary consumer – Organisms such as forage fish that consume primary consumers (e.g., zooplankton) for their source of nutrients and energy.

Sediment grain size – Refers to the size and relative size distribution of the particles that make up the sediment. Typically they are divided into four groups including clay, silt, sand and gravel.

Stratification – Vertical differences in water temperature, causing a density difference between warm, less dense surface water and cold, more dense bottom water, retarding or preventing mixing of surface and bottom water.

Terrestrial – Pertaining to plants or animals that live on land.

Total metals concentrations (water) – The total concentration of a metal in the water, which includes both freely dissolved and particle-bound forms of the metal.

Total Suspended Solids [TSS] – The weight of solids that are suspended in a given volume of water, expressed as weight per unit volume (e.g., mg/L).

Trophic Levels – A functional classification of organisms in an ecosystem according to feeding relationships, from primary producers through primary consumers, through secondary consumers.

Tundra – Habitat typically found in the Arctic north of the treeline that is adapted to cold temperatures, a short growing season, and low precipitation. Typical tundra vegetation includes moss, lichen, Labrador tea, and small shrubs.

Turbidity – A condition of reduced transparency in water caused by suspended colloidal or particulate material; measured by a turbidimeter and recorded as nephelometric turbidity units (NTU).

Ultra-oligotrophic – Lakes with extremely low nutrient levels, high water clarity, low primary productivity, and a dominance of small unicellular phytoplankton species. Total phosphorous concentrations are typically <0.005ug/L in these lakes (Vollenweider 1968).

Watershed – An entire geographic area that contributes surface and groundwater to a particular lake, river, or stream.

Water Quality Guidelines – Reference concentrations of contaminants in water that, if exceeded, indicates that organism-level effects may occur.

Zooplankton – Small, floating or weakly swimming animals found in fresh and marine waters, such as copepods and cladocerans.

EXECUTIVE SUMMARY

The objective of this study was to determine the limnology and ecology of Garrow Lake and assess changes to the lake after more than 20 years of tailings disposal. Prior to mining, the lake supported a depauperate biological community including a small, dwarf population of landlocked fourhorn sculpin (*Myoxocephalus quadricornis*). Teck Cominco has regularly monitored lake water quality and stratification since pre-mine investigations. However, no study of sediment quality or biological studies have been conducted since disposal of tailings to the lake began in 1980. As part of a 2002 DFO habitat authorization (02-HCAA-000-000063), Teck Cominco was specifically required to determine TSS and turbidity in different strata of Garrow Lake, metals concentration in littoral zone sediment and whole-body metal concentration in fourhorn sculpin.

Teck Cominco Ltd.'s Polaris Mine (75^{o}23'N 96^{o}50'W) on southern Little Cornwallis Island, Nunavut used Garrow Lake for tailings disposal pursuant to its designation as a Tailings Impoundment Area (*Fisheries Act* Schedule 2). as a Tailings Impoundment Area (*Fisheries Act* Schedule 2). Underground zinc-lead mining permanently ceased in September 2002. Since then the mine has undergone reclamation and decommissioning that concluded in fall 2004. Polaris Mine is undergoing a full cycle of Environmental Effects Monitoring (EEM) under the federal Metal Mining Effluent Regulations that will conclude in 2005.

Garrow Lake is small, ultra-oligotrophic, permanently chemically and thermally stratified (i.e., meromictic) lake with a surface area of 4.18 km^2, maximum depth of 42 m and a depauperate biological community. Prior to tailings deposition, the biologically active mixolimnion ranged between zero and 12 m – 14 m in depth and was well oxygenated, cold and brackish (3 – 7 ppt salinity). The deep monimolimnion extended from about 18 m to the bottom and was unusually warm (8^{o}C), completely anoxic, sulphide rich and hypersaline, with a salinity of up to 90 ppt. These layers were separated by a 6 m thick pycnocline where temperature increased, oxygen concentrations fell and salinity increased rapidly with increasing depth.

Between 1981 and 2002, approximately 15 million tonnes of tailings solids were deposited into the monimnolimnion. Gradual displacement of water upwards has reduced total depth of the lake from 46 m to 42 m, and reduced depth of the mixolimnion and thickness of the pycnocline. Discharge of tailings into the monimolimnion has also reduced mean salinity, from 90 ppt to 70 ppt, and caused complete mixing within the monimolimnion, such that temperature and salinity profiles are uniform from just beneath the pycnocline to the bottom.

Tailings deposition has not changed limnological conditions of the mixolimnion. Winter and summer water temperatures remain cold, ranging from –0.5 ^{o}C to 4 ^{o}C with little difference between seasons. Salinity ranged from 3.8 ppt at the surface to 7.1 ppt at the

pycnocline (9 m) with slight inverse stratification. Oxygen concentration was stratified and high in winter (13 – 20 mg/L) and supersaturated, a condition also noted during pre-mine conditions, presumably from algae and photosynthetic bacteria. In August oxygen was uniform at 11.5 mg/L, but was not supersaturated because absence of ice cover and mixing by wind, allowing oxygen to escape to the atmosphere.

Depth of the mixolimnion extends to 9 m at the top of the pycnocline. Maximum salinity is reached at the top of the monimolimnion at 12 m, a depth of only 3 m. Formerly, mixolimnion depth extended to 12 m and the bottom of the pycnocline ended at about 20 m. Oxygen concentration in the monimolimnion was nil and there was a strong hydrogen sulphide odor to the water.

Tailings deposition has displaced the mixolimnion depth by 4 – 5 m. Lake elevation in 2003 was 2 m higher than pre-mine elevation because of the dam that was still in place at the lake outlet. Removal of the dam in spring 2004 has allowed water level in the lake to return to near pre-dam elevations and will have reduced lake level and total depth of the mixolimnion to about 8 m, a further reduction of 2 m.

Prior to tailings deposition, sediment metals concentrations did not differ with depth and were relatively low, but reflected natural mineralization of the area, with elevated lead and zinc. A pipeline break in 1984/1985 caused tailings to spill into the littoral zone along the western shore of the lake, resulting in widespread contamination of lead and zinc in littoral zone sediment. This caused an increase in dissolved zinc concentration in surface waters of Garrow Lake and the outflow creek. Currently, zinc concentration in the Garrow Lake mixolimnion averages about 0.22 ppm, below the permit limit of 0.5 ppm established in 1992.

The only species of zooplankton known to be present in Garrow Lake is *Limnocalanus macrurus*, which was captured during pre-mine surveys. Amphipods (*Gammarus* sp.) and a mysid species (*Mysis oculata*) were also present in Garrow Lake prior to mining. No zooplankton species were captured during the 2003 survey. It is not known why zooplankton appeared to be absent. It is possible zooplankters were deeper in the water column than was sampled, or that changes to mixolimnion water chemistry may have caused a decline or extirpation of *L. macrurus* or its primary food source, phytoplankton. Phytoplankton were not collected in 2003.

Oligochaetes (F. Enchytraidae), nematodes and Foraminifera were the only benthic invertebrates identified in sediment collected at four stations within the mixolimnion zone in 2003. Although chironomid larvae were not collected from sediment, they were observed in stomachs of fourhorn sculpin. Pre-mining surveys also indicated a depauperate benthic fauna dominated by Foraminifera and a few harpacticoid copepods and chironomids. Garrow Creek sediment contained nematodes, oligochaetes a single mayfly (Ephemeroptera) species *Baetis bicaudatus* and several chironomid species.

All 19 sculpins captured in 2003 appeared to be healthy with no external or internal tumors, scars or other abnormalities. Mean length (149 mm), weight (25 g) and condition (0.70) of sculpins from 2003 were similar to sculpins collected in 1976 (155 mm, 26 g, 0.72) using the same gear. Length – frequency distributions of sculpins from 1976, 1977 and 2003 also demonstrated that the basic size distribution of adult sculpins has not changed over time.

Mean age of sculpins captured in 2003 was 5.7 years, with a range of 3 – 9 years. The small size, low lipid content (10%) and small size at age confirm that Garrow Lake sculpins are slow growing relative to other Arctic sculpin populations because of limitations in food and habitat.

Four of 11 sculpins stomachs examined contained food, with only a few chironomid larvae distinguishable. Pre-mine examination of stomachs indicated that half were empty while copepods, unidentified eggs, plant material, and a few amphipods were present in the other half. Copepods were not identified in stomachs in 2003, providing circumstantial evidence that zooplankton may not be abundant and comprise a very small component of the aquatic community in Garrow Lake post-mining.

Gonads of most sculpins examined appeared ripe or nearly ripe and these individuals would certainly spawn within the next few months during mid-winter, a trend that is consistent for this species.

Whole body concentration of manganese, lead (0.81 mg/kg ww) and zinc (72 mg/kg) in sculpins was higher in 2003 than prior to mining. Other metals including arsenic, cadmium, copper, mercury, and nickel were lower or did not differ among years. Elevated lead and zinc concentrations in sediment and the water column as a result of the spill may be responsible for elevated tissue concentration, however, the magnitude of increase in tissue was small, only 2 – 3 times higher than pre-mining concentration, despite a two-order of magnitude increase in lead and zinc concentration in sediment.

Overall, it appears as if the size, distribution, growth rate and reproductive status of the sculpin community has not changed markedly since pre-mining studies. Although catch-per-unit-effort was not recorded, sculpins were more difficult to capture and did not appear to be as abundant or as easy to capture as pre-mine surveys indicate. This may be related to the absence of zooplankton and reduced benthic habitat available to sculpins and their food sources because of gradual upward displacement of the mixolimnion. Nevertheless, sculpins have survived in Garrow Lake throughout the history of mining and tailings deposition to the lake, which is still designated as a tailings disposal facility.

Tailings introduction and upward displacement the pycnocline and mixolimnion will have reduced depth of the mixolimnion above the pycnocline to about 8 m in 2004, after removal of the dam. It has been determined that the magnitude of the thermal and salinity

difference between the mixolimnion and the monimolimnion in the lake will be sufficient to maintain separation of the two layers and prevent turnover and mixing.

1. INTRODUCTION

1.1. Background

Teck Cominco Metals Ltd.'s Polaris Mine (75°23'N 96°50'W) is situated on southern Little Cornwallis Island, Nunavut, in the high Arctic, approximately 90 km northwest of Resolute Bay (Figure 1). This region is characterized by short, cold summers and extremely cold, long and dark winters. Mean average air temperature is –17°C with an average of only 8 frost-free days annually. Precipitation is very low and is typical of desert conditions with only 25 cm of annual precipitation, most of this as snowfall. Winds are strong and predominantly from the northeast with an average wind speed of 20 kph (Gartner Lee, 2001).

Underground zinc-lead mining operations, which initially began in 1981, permanently ceased on September 3, 2002 with the final shipment of concentrate, taking place later that same month. The Polaris Mine has undergone a two-year reclamation and decommissioning phase (Garner Lee, 2001) that concluded in September 2004. In addition to remediation of upland soils, Polaris Mine is undergoing a full cycle of Environmental Effects Monitoring (EEM) under the federal Metal Mining Effluent Regulations (MMER; DFO, 2002). The MMER document (Azimuth Consulting Group, 2004) describes how the three main components of MMER are to be applied; routine effluent monitoring (chemistry, toxicity, mass loading) in Garrow Creek, emergency response, and Environmental Effects Monitoring (EEM) of receiving environment biota (benthic community and fish survey) in Garrow Bay.

As part of mine closure activities, Teck Cominco was required to undertake a basic ecological study of Garrow Lake as part of a Department of Fisheries and Oceans Habitat Authorization (see Section 1.4 and Appendix A). This document satisfies that directive.

1.2. Limnology

Garrow Lake is a small, permanently chemically and thermally stratified (i.e., meromictic) lake with a surface area of 4.18 km^2, a maximum depth of 46 m and unique limnological characteristics (BC Research, 1975; Ouellet and Dickman, 1984; Fallis et al., 1987). The lake is ultra-oligotrophic with very low nutrient concentration and a depauperate biological community (Fallis et al., 1987; BC Research, 1978). Because of its unique physical/chemical features, Garrow Lake has been the subject of much study, notwithstanding its designation as a Tailings Impoundment Area for Polaris Mine. Garrow is still considered a Tailings Impoundment under the current MMER (DFO, 2002).

The meromictic nature of Garrow Lake means that there are three distinct depth zones within the lake that never inter-mix, because of their particular thermal and chemical properties. These are the mixolimnion, pycnocline layer and monimolimnion, from top to bottom.

Prior to mining, the mixolimnion of Garrow Lake ranged from the surface to about 12 m – 14 m depth. It was well oxygenated, cold (0^{o}C to 4^{o}C) and brackish, ranging from 3 ppt at the surface to 7 ppt above the pycnocline. The monimolimnion ranged in depth from about 18 – 20 m to the bottom of the lake, at a maximum depth of 46 m. This deep layer was unusually warm (8^{o}C), completely anoxic, sulphide rich and hypersaline, with a salinity of up to 90 ppt, nearly triple the salinity of seawater. These two very different layers were separated by a pycnocline. The pycnocline represents the transition zone between the mixolimnion and monimolimnion where temperature increases, oxygen concentration falls and salinity increases rapidly with increasing depth. The large increase in density transitioning from the mixolimnion to the monimolimnion through the pycnocline is great enough to maintain complete separation of the layers and prevent mixing, even over thousands of years.

Garrow Lake is situated in an area of continuous permafrost and is ice-covered for much of the year (Photo 1). In some years, the ice does not completely melt, leaving an ice cover. The lake slopes steeply from the narrow littoral zone into the anoxic, hyper-saline profundal zone within tens of meters from shore. The drainage area of Garrow Lake is very small and is only double the surface area of the lake. The small drainage area and low precipitation means that total annual discharge from the lake via Garrow Creek is correspondingly small.

Discharge to Garrow Bay, 1.4 km south of the lake outlet occurs during the brief open water period from mid to late July through late-August or early September. In the nearly 3,000 years since its separation from adjacent marine waters, the annual freeze-thaw cycle at the lake's surface has transferred and concentrated salt in the deeper parts of the lake. Interestingly, bottom temperature is nearly 8^{o}C, much warmer than surface waters that are always near zero.

1.3. Mining Operations

Polaris was a zinc-lead mine that operated between 1981 and 2002 inclusive. Mined ore was crushed underground and moved by conveyor to a mill. Ore concentrate was stockpiled above ground in a covered building and shipped by ocean going bulk carrier to Europe during the brief open water period. Garrow Lake is a designated Tailings Disposal Facility. Over the life of the mine approximately 15 million tonnes of tailings solids were deposited to the bottom of Garrow Lake at a rate of up to 100 tonnes per hour (Gartner-Lee, 2001). Mill tailings were pumped via a 4 km long tailings line to a

thickener before being discharged to Garrow Lake via a submerged pipe. The pipe extended between 600 m and 1.2 km offshore and to a depth of 30 m (BC Research, 1988), at least 10 m below the pycnocline and 15 m above the bottom. The tailings line was moved every year to distribute tailings over the bottom. Small piles of tailings are apparent from lake bathymetry (Figure 2).

This disposal system was very effective, except for an incident in 1984/85 where a failure of the pipe resulted in tailings discharge into near-surface waters of Garrow Lake. This spill caused tailings to be deposited along the western shore of the lake near the tailings line and caused dissolved zinc concentration in surface waters to increase to more than 0.4 mg/L. Since the spill, zinc concentration in the mixolimnion has been slowly declining. Currently, zinc concentration in Garrow Lake averages about 0.23 ppm, below the permit limit (0.5 ppm) that was established in 1992.

To dilute zinc concentration in the mixolimnion and hence reduce zinc concentration in water discharged to Garrow Bay via Garrow Creek, Teck Cominco constructed a dam in 1989/1990 across the creek, about half way between the outlet and the mouth (Figure 2). Water was retained within the lake for three years, causing in increase in lake elevation and mixolimnion depth by about 2 m. Between 1994 and 2003 stream discharge and lake level was controlled by active siphoning of water over the dam into Garrow Creek between mid-July and early-September. Therefore, discharge was relatively constant throughout the discharge period, ranging between 0.19 m^3/s and 0.55 m^3/s, depending on the number of siphons in operation. The dike and siphons were removed in spring 2004 to allow the lake to return to its former level and in future, fluctuate naturally.

Prior to installation of the dam, flow in Garrow Creek was ephemeral with discharge typically occurring over a six to eight week period beginning in mid-July, once the stream mouth and channel had thawed. Stream flow began with melting and freshet, which lasts about two weeks (0.5 – 1.5 m^3/sec) before rapidly diminishing to relatively low discharge volume (0.1 m^3/sec) for the remainder of the summer/fall until freeze-up in early September. It is expected that since the dam and siphons have been removed, discharge will return to normal patterns, except with smaller discharge volume as no water is displaced by the addition of mine tailings.

1.4. Objective

Our objective was to describe the current limnology and ecology of Garrow Lake and assess changes after more than 20 years of use of Garrow as a tailings disposal facility. Prior to mining, the surface waters and littoral sediment of Garrow Lake supported a small community of zooplankton and benthos that sustained a small, dwarf population of landlocked fourhorn sculpin (*Myoxocephalus quadricornis*). It was not known if surface water conditions had deteriorated sufficiently as to cause unfavorable conditions for

aquatic life. Since pre-mine investigations in 1977 (BC Research, 1977), 1979 (Fallis et al. 1987) and 1980 (BC Research, 1981), very few studies on water quality have been conducted, outside of routine monitoring by Teck Cominco two or three times per year. No study of surface sediment quality (e.g., BC Research, 1988) or ecology of the lake has been conducted since deposition of mine tailings began. Therefore, as part of a 2002 DFO habitat authorization (02-HCAA-000-000063; Appendix A) during the decommissioning and dam removal process, Teck Cominco was specifically required to determine the following (see Section 4.0 of authorization; Appendix A):

- "TSS and turbidity in different strata of Garrow Lake to confirm the absence of contaminants in surface waters;
- metals concentration in sediment in the littoral zone of Garrow Lake; and
- whole-body metal concentration in fourhorn sculpin".

This report describes limnological and ecological features of Garrow Lake several months after cessation of more than 20 years of tailings disposal and satisfies requirements of the DFO Habitat Authorization. The data reported here extends beyond the requirements of the Habitat Authorization to review historical trends and provide a broader base of information.

2. MATERIALS AND METHODS

2.1. Limnology and Water Chemistry

Water sampling was conducted from a 3 m aluminum boat with 12 hp motor on August 8, 2003 (Photo's 2 and 3). Shifting ice pans covered at least 50% of the lake. One week earlier, ice cover on the lake was at least 80% (Photo 1). Based on historic bathymetric data and using a hand-held depth meter, the deepest depth on Garrow Lake that could be accessed because of ice, was located in 42.5 m of water (Figure 2). At this point, a vertical pH, temperature (^{o}C), oxygen (ppm), conductivity (mS) and salinity (ppt) profile of the lake was acquired using a Hydrolab^{TM} meter. Measurements were recorded at 1 m intervals between the surface and bottom. Vertical temperature and salinity profiles were compared with pre-mine profiles (BC Research, 1975; Fallis et al. 1987; BC Research, 1978) and during-mining profiles (BC Research, 1988) to determine the effects of mine tailings disposal on lake stratification, limnological parameters and water chemistry (Appendix B).

To acquire water samples for chemical analysis from this location (WQ-1), water was pumped from discrete depths using a direct pumping system. Depths were selected based on temperature and salinity data acquired with the Hydrolab. Weighted, ultra-clean metered Teflon tubing was deployed from the boat and lowered to the desired depth. A diaphragm pump was attached and water was pumped from depth for at least 1 minute before being discharged directly into sample collection bottles that were triple rinsed and held on ice. Water samples requiring filtering were filtered in the field by placing a 45 μm inline Gelman filter onto the end of the hose and discharging water directly into sample bottles.

Water was collected from the surface, mid-epilimnion (6 m), pycnocline (11 m) and hypolimnion layers (15 m and 30 m) to characterize each discrete layer. A 1-L plastic bottle with no preservative was used to hold water for determination of pH, conductivity, salinity, total suspended solids (TSS), alkalinity, sulphate and fluoride. A 250 ml glass amber bottle with no preservative was used to hold water for determination of DOC. Total metals and dissolved metals were collected in 250 mL plastic bottles preserved with nitric acid. Standard field collection and quality assurance/quality control (QA/QC) procedures were followed (BCMELP, 2003). Water samples were held on ice and during shipping to ALS Environmental Laboratory, Vancouver for analysis.

2.2. Sediment Chemistry

Sediment was collected from six littoral zone stations around the lake as ice conditions permitted using a 0.024 m^2 petite Ponar grab (Figure 2). Four stations were synoptically

sampled for sediment metals (GL-X-SED), benthos and zooplankton. Two stations (GL-N, GL-S) in the vicinity of the historic spill were only sampled for sediment metals. Stations were selected based on depth (<9 m) using a hand-held depth meter to ensure that sampling occurred within the mixolimnion layer of the lake to ensure consistency in grain size and avoid shallow depths with coarse substrate (Table 1).

Sediment was collected using proven sample collection and handling techniques (Environment Canada, 1994; BCMELP, 2003). Each deployed grab sample was examined to ensure acceptable sample quality (i.e., no large foreign objects; adequate penetration; not overfilled; no leaking water; no disturbance or winnowing). Once the grab sample quality was determined to be acceptable, overlying water was siphoned off and the top few cm of sediment was removed from the center of each grab using a pre-cleaned stainless steel spoon and placed in a pre-cleaned stainless steel mixing bowl. Two samples were acquired from each station and composited in the same bowl. Sediment was mixed using the spoon until it was homogenous in texture and colour. Aliquots of sediment were placed into 250-mL glass jars for analysis of total metals including mercury, total organic carbon (TOC) and grain size by ALS, Vancouver BC. Samples were stored in coolers with frozen gel packs on ice until analysis by the laboratory.

Total metals were analyzed using procedures from the BC Contaminated Sites Regulations (CSR) Analytical Method 8 *Strong Acid Leachable Metals (SALM) in Soil* and procedures adapted from *Test Methods for Evaluating Solid Waste SW-846* (US EPA Method 3050B or Method 3051). Sediment samples were manually homogenized, dried at 60 ^{o}C, sieved through a 2 mm (10 mesh) sieve, and a representative subsample of the dry material was weighed. The sample was then digested at 90 ^{o}C for two hours by either hotplate or block digester using a 1:1 ratio of concentrated nitric and hydrochloric acids. Instrumental analysis was by atomic absorption/fluorescence spectrometry (CVAAS/CVAFS)(US EPA Method 7000 series) and/or inductively coupled plasma – optical emission spectrometry (US EPA Method 6010B).

2.3. Biota

2.3.1. Zooplankton

Vertical zooplankton tows were conducted from the four synoptic stations (Figure 2) using a 2 m long, 0.5 m diameter conical net, with 250 µm mesh size. The mouth of the net was lowered to a depth of 8 m and after waiting 30 sec, was towed vertically towards the lake surface. Two vertical tows were conducted and composited to determine zooplankton density (# organisms/m^3). Contents of the cod end were washed into a 500 mL HDPE jar and preserved with a 10% formalin solution. In addition, a horizontal tow was conducted at station 3. The net was weighted and towed behind the boat at a depth of

1 m for 3 minutes, to attempt to collect zooplankton for taxonomic analysis. Preserved samples were shipped to Applied Technical Services, Victoria BC for taxonomic identification.

2.3.2. Benthic Invertebrates

Sediment was acquired using a petite Ponar grab (0.024 m^2) at each of the four synoptic stations (Table 1). The top 5 cm of acceptable grabs was removed and sieved through a 500 μm sieve. Three grab samples were acquired at each station and composited (i.e., 0.072 m^2) to determine density of organisms (#/m^2).

Garrow Creek, just downstream from its outlet from Garrow Lake (i.e., below the dam) was sampled for benthic invertebrates using a kick-style sampler. Substrate upstream of a 250 μm net was disturbed, causing attached or burrowed organisms to drift into the net. This sampling was non-quantitative and was intended to determine species composition and relative abundance of benthic organisms in this ephemeral stream. Material retained by the sieve was transferred to a 500 mL HDPE container and preserved in a 10% buffered formalin solution. Preserved benthos samples were shipped to Applied Technical Services, Victoria BC for taxonomic identification and enumeration.

2.3.3. Fish

Pre-mining ecological surveys of Garrow Lake in 1976 (Fallis et al., 1987), 1977 (BC Research, 1987) and 1980 (BC Research, 1981) confirmed that Garrow Lake contained a glacial relict population of fourhorn sculpin (*Myoxocephalus quadricornis*). Since tailings deposition in Garrow Lake began in 1980, no sculpins have been collected from the lake, although divers have purportedly observed sculpins on an annual basis during maintenance and movement of the tailings line (W. Gzowski, Arctic Divers Ltd., August 2003). We collected sculpins in August 2003 using small-mesh (20 mm – 50 mm) Swedish gill nets and a baited prawn trap at various locations around the lake, as ice conditions permitted. Fallis et al. (1987) used similar size nets (19 – 64 mm stretch mesh) to catch sculpins in 1976.

All sculpins captured were measured for total length (mm), weight (g) and examined externally for any abnormalities. A subsample of sculpins were sacrificed and examined internally for gender, state of sexual maturity, stomach contents, parasites and internal condition and abnormalities. These sculpins were retained and frozen for subsequent whole-body analysis of metals concentration by ALS, Vancouver.

Length-frequency distribution, condition factor (K = length^3/weight x 10^5), sex ratio, maturity and diet from 2003 fish were compared with data collected from the pre-mining (1978 – 1979) period to determine changes in biology and life history characteristics.

3. RESULTS AND DISCUSSION

3.1. Limnology

3.1.1. Physical Attributes and History

Garrow Lake is one of the few meromictic (i.e., permanently stratified) lakes found in the Arctic and has the highest salinity content of all polar lakes (Ouellet et al., 1989). Strong vertical stratification due to large differences in salinity and temperature between the cold (~0^{o}C), slightly brackish (2 – 7 ppt salinity) mixolimnion and the warm (8^{o}C), anoxic, hypersaline, hydrogen sulphide rich monimolimnion maintains complete separation of these two discrete layers.

Garrow Lake was formed by isostatic rebound during the most recent Wisconsin glaciation period that ended 10,000 years ago. A marine depression was progressively uplifted, eventually isolating the marine water-filled depression from the surrounding ocean. Several independent estimates place the age of Garrow Lake (i.e., when it was physically separated from the marine environment) at between 2,500 and 3,500 years ago. ^{14}Carbon dating of marine bivalve shells collected near the shoreline elevation of Garrow Lake indicated a date of 3,350 years before present (BP). Isotopic examination of bottom water from Garrow Lake by Page et al. (1984) revealed that exposure of this water to air last took place at least 2,580 years ago. Using post-glacial rebound rates Thornsteinsson and Kerr (1968), Stewart and Platford (1986) and Fallis et al. (1987) independently estimated the age of Garrow Lake as 3,000, 2,600 and 2,500 – 3,000 years BP, respectively.

How the deep monimolimnion of Garrow Lake became to be nearly three times the salinity of sea water is a matter of some debate and several theories have been advanced to explain how this situation arose. Stuart and Platford (1986) favor the idea that brine currents were formed during the freeze-out of salts from surface waters that sank and, over time, accumulated to form the hypersaline monimolimnion. They contended that the ionic proportion and ratio between surface and deep waters was very similar and did not demonstrate the major differences that would necessarily occur if there was differential mineral precipitation in the monimolimnion or intrusion of hypersaline ground water from freeze-out. Furthermore, if freeze-out of salts beneath lakes was prevalent, this should be observed in many Arctic lakes, but it is not.

Alternatively, Ouellet and Dickman (1983) and Dickman and Ouellet (1987) hypothesized that after separation of Garrow Lake 3,000 years ago, gradually advancing permafrost froze out the freshwater, concentrating salts in deeper water of the lake over time. Ouellet et al. (1989) theorized that pore water trapped between sediment particles

would have been progressively frozen during isostatic rebound as Garrow Lake rose and "advanced" inland. The formation and presence of an unfrozen column of water or talik beneath Garrow Lake would favor the movement or displacement and gradual accumulation of frozen-out salts in the bottom of the lake. Based on their results and citing other similar studies on Antarctic lakes, Ouellet et al. (1989) concluded that cryogenic concentration of salts from surface waters or freeze-out of salts from surface soils over time were only of minor importance and refute the Stewart and Platford (1986) theory of major contribution by surface sources. This matter is still unresolved. A more thorough discussion of this can be found in the above papers and Fallis et al. (1987).

Fallis et al. (1987) and Ouellet et al. (1989) also offered an explanation as to why the monimolimnion is so warm relative to the mixolimnion. Lack of snow cover and clear ice allows light to penetrate through the mixolimnion and be absorbed by a bacterial layer within and just below the pycnocline boundary atop the monimnolimnion. The strong density difference between the surface and bottom layers does not allow mixing and allowed more heat to be absorbed within the deep layer than escapes. Over time, heat has been accumulated within the monimolimnion, eventually reaching an equilibrium temperature.

The chemical and thermal structure of the monimolimnion has been disturbed by the physical disturbance of tailings disposal into the mid-water column. Vertical mixing action within the monimolimnion caused by buoyant tailings water and tailings solids falling through the water column has gradually caused temperature and salinity profiles to become more uniform or homogeneous. This has also resulted in a less saline, slightly cooler and more uniformly mixed monimnolimnion than existed prior to mining (Figure 3; Appendix B).

3.1.2. pH, Temperature, Salinity and Oxygen

3.1.2.1. Pre-Mining Profiles

Pre-mining studies in 1976 and 1981 (Fallis et al., 1987), 1977 and 1980 (BC Research, 1978; 1981), and 1980 and 1981 (Dickman and Ouellet, 1987) recorded very similar vertical pH, temperature, oxygen and salinity profiles and stratification parameters in Garrow Lake. Studies conducted in 1982 (Stewart and Platford, 1986), and 1983 and 1984 (Ouellet and Dickman, 1987; Ouellet et al., 1989), shortly after commencement of mining, also reported similar results to pre-mining. In all studies, mixolimnion depth extended to about 12 m at which point temperature and salinity began to increase rapidly with increasing depth (the pycnocline) to reach a maximum at about 20 m, the top of the monimolimnion (Figure 3). This zone extended to the bottom of Garrow Lake at its deepest depth (46 m).

Water column pH typically ranged between 6.9 and 8.0 and tended to be slightly lower within the monimolimnion than in the mixolimnion (BC Research, 1977; Fallis et al., 1987).

Water temperature in the mixolimnion ranged between just above zero to four or five degrees Celsius, depending on the month (cold in June, warmer in August), and tended to gradually increase with depth towards the pycnocline (BC Research, 1978; Stewart and Platford, 1987; Ouellet et al., 1989). Wind mixing during open water conditions in late fall resulted in more uniform temperature between surface and deeper water of the mixolimnion (BC Research, 1978).

Oxygen concentration was always high, reflecting surface mixing in summer and biological activity by plankton in the mixolimnion. Fallis et al. (1987), Ouellet and Dickman (1987) and Stewart and Platford (1986) observed supersaturation (>100%) of normal oxygen solubility at deeper depths in the mixolimnion especially in spring. Supersaturation is believed to result from freezing-out of oxygen during ice formation and from biological productivity. A dense plate of photosynthetic bacteria exists just above the pycnocline (Fallis et al. 1987). During late winter and spring, these bacteria and phytoplankton produce an excess of oxygen that accumulates and is trapped in the water column beneath the ice cover.

Total suspended solids (TSS) concentration (mg/L) was measured in effluent from Garrow Lake, which represents concentrations found in the upper few meters of the mixolimnion. In all cases, TSS was less than detection limits (i.e., either 1 mg/L or 3 mg/L, depending on the laboratory). Visual observations of the lake from water sampling throughout the water column confirmed that there was no visible turbidity to the water, regardless of depth.

Salinity of the mixolimnion varied between slightly brackish at the surface to about 7 or 8 ppt in all studies showing slight vertical stratification (Table 2; Figure 2). Salinity in the upper water column is lower in summer and fall than in winter because of dilution by ice melt. Anion and cation concentrations and conductivity mirrored salinity and increased proportionately with depth (Ouellet et al., 1989). In January 1983, two years after commencement of tailings disposal, salinity of the mixolimnion was 4.8 ppt and did not differ from pre-mine conditions. Sampling of the water column beneath the ice in June 1984, three years after discharge of tailings, revealed dilute surface water salinity (0.5 ppt at 1 m) with uniform salinity to 12 m (5.7 ppt)(Ouellet et al. 1989).

Within the top of the pycnocline (12 – 14 m) oxygen concentration diminished while temperature and salinity increased with increasing depth. All researchers observed this trend. At the bottom of the pycnocline (18 m – 20 m), oxygen had diminished to zero while temperature had increased to 9^{o}C in the upper monimolimnion. The bacterial plate near the bottom of the pycnocline observed by BC Research (1980) and Ouellet and

Dickman (1983) is likely responsible for increased turbidity at this depth as well as increased hydrogen sulphide concentration, which continued to increase with increasing depth. Salinity increased very strongly between 12 m (9 ppt) and 20 m (66 ppt)(Stewart and Platford, 1986; Fallis et al, 1987). Ouellet et al. (1989) also observed that salinity increased rapidly with increasing depth through the pycnocline from 5.7 ppt at 12 m to 35.2 ppt at 17 m and 76.7 ppt at 21 m. Stewart and Platform (1986) and Fallis et al. (1987) observed similar salinities at the same depths.

Within the monimolimnion extending from 20 m to the lake bottom, oxygen concentration was nil and water temperature decreased very gradually from 9^{o}C to 5^{o}C and did not differ among seasons or years (BC Research, 1977; 1981; Stewart and Platford, 1986; Fallis et al., 1987; Ouellet et al., 1989). Salinity also gradually increased with depth, reaching maximum salinity (between 80 and 90 ppt depending on the study) at the lake bottom (46 m). Because of the isolated, undisturbed nature of the monimolimnion prior to mining, temperature and salinity profiles were virtually identical among studies, regardless of season or year.

3.1.2.2. Post-Mining Profiles

BC Research (1988) analysed surveillance water quality data from Garrow Lake between 1982 and 1987 to evaluate changes in metals concentrations within the different layers during the period of discharge of mine tailings to the monimolimnion. Vertical temperature and conductivity profiles were essentially unchanged except for the fact that the salinity gradient within the monimolimnion was steeper, suggesting that stratification within this layer was disturbed. As expected, continuous discharge of tailings to 30 m depth, 12 m above the bottom, was causing vertical mixing within the monimolimnion beneath the pycnocline, resulting in more uniform salinity and temperature profile and raising metals concentrations. Teck Cominco continued to collect vertical temperature and salinity profiles of Garrow Lake during winter and summer periods to monitor the limnology of the lake in order to ensure that the integrity of the pycnocline was maintained and that mixing of the monimolimnion into surface water was not occurring.

In 2003, Garrow Lake was completely ice-covered until late-July. During mid- to late-August, the lake became mostly ice-free, although ice pans persisted over about 20% of the lake and shifted around according to wind direction. In 2004, the lake remained completely ice-covered and sampling was not possible. Effective mixing of surface waters is only possible during ice-free conditions when sufficient surface area of the lake is exposed to wind to cause turn-over and vertical mixing.

Teck Cominco staff sampled water during February and March 2003 from a single location near the middle of the lake. In August, we collected a single vertical profile from the lake from the deepest accessible location (42.5 m), GL-1-WQ (Figure 2). Winter and

summer vertical profiles of temperature, oxygen and salinity were very similar to pre-mining data (Figure 3) with two notable differences. Salinity of the monimolimnion and depth of the mixolimnion have both diminished, reflecting the physical effects of tailings deposition to the lake bottom.

Mixolimnion salinity ranged from 3.8 ppt (6.7 mS) at the surface to 7.1 ppt (12.5 mS) at the top of the pycnocline (9 m). Melting ice caused lower salinity and conductivity at the surface than at deeper depths, with a slight inverse stratification. In winter 2003, salinity and conductivity within the epilimnion was uniform (Appendix B). Oxygen concentration was stratified and high in winter (13 – 20 mg/L) and supersaturated, a condition also noted during pre-mine conditions, presumably from photosynthetic bacteria. In August oxygen was also high and uniform (11.5 mg/L), but was not supersaturated because absence of ice cover and mixing by wind allowed oxygen to escape to the atmosphere (Figure 3).

Winter and summer water temperatures were cold, ranging from –0.5 ^{o}C to 4 ^{o}C with very little difference between seasons. Surface water temperature (<2 m) was slightly warmer in summer than in winter. Below 2 m depth, water temperature ranged between 3^{o} and 4^{o}C. Field pH was 8.2 in the mixolimnion and declined through the pycnocline and monimolimnion to 7.35 that was unchanged with depth to the bottom (Appendix B). Limnological conditions within the mixolimnion were very similar in 2003 as pre-mining conditions and do not appear to have changed substantially.

Pycnocline depth below the surface is shallower and has become thinner compared to pre-mining profiles (BC Research, 1981; Fallis et al., 1987; Ouellet et al., 1989). The depth of the surface of the pycnocline, where large, rapid salinity increases occurred in 2003 was at 10 m, reaching near maximum salinity of the monimolimnion by 12 m, a thickness of only 2 m. Formerly, mixolimnion depth extended to 12 m and the bottom of the pycnocline ended at about 20 m. Salinity of the monimolimnion (field based Hydrolab data) was 58 ppt (Appendix B; Figure 3), which is about 32 ppt less than maximum salinity observed in pre-mining studies. Laboratory analysis of mixolimnion water showed a maximum salinity of 64 ppt. Nevertheless, salinity has diminished gradually over time as expected (AXYS, 2001) owing to the large amount of tailings deposited to the lake over more than 20 years, diluting bottom waters. Oxygen concentration was nil and there was a strong hydrogen sulphide odor to the water.

Tailings deposition between 1981 and 2002 has displaced the mixolimnion upwards and is 3 – 4 m shallower than pre-mining, beginning at 9 m, up from the pre-mine depth of about 12.5 m. However, lake elevation in 2003 was also about 2 m higher than pre-mine elevation because of the dam structure that was still in place at the lake outlet (Figure 2). The dam was installed in 1990 to increase water level of the lake to reduce zinc concentration in water discharged to Garrow Bay (see Section 1.3). Removal of the dam in spring 2004 will allow water level in the lake to return to near pre-dam elevations and

will reduce lake level and depth of the mixolimnion by a further 2 m, beginning at a depth of approximately 7 or 8 m.

In 2000, Teck Cominco commissioned AXYS (2001) to determine if diminishing mixolimnion depth would risk turnover and mixing of the mixolimnion and monimolimnion. If this occurred, water chemistry of the entire lake and Garrow Creek would be considerably altered. AXYS (2001) concluded that the density barrier of the pycnocline is strong enough that it cannot be broken down or compromised by wind and wave action after decommissioning of the dam and lake drawdown. Thus, no mixing of the mixolimnion and monimolimnion is possible. Furthermore, AXYS (2001) stated that zinc concentration in the mixolimnion will remain below 300 µg/L and that levels should decline over time, however, no time frame was given.

3.1.3. Metals

Between 1980 and 2002 approximately 15 million tonnes of tailings solids were deposited to the monimolimnion of Garrow Lake (Gartner-Lee, 2001). Tailings were discharged via a pipe suspended in the water column, well below the pycnocline at a depth of about 26 – 31 m. The location of the pipe was moved horizontally and laterally on an annual basis, to distribute tailings more evenly over the bottom. Small, discrete piles of tailings are evident from the bathymetric map of Garrow Lake (Figure 2). These piles are spread out over the deep basin opposite the tailings disposal line. Maximum depth of Garrow Lake has diminished to about 42 m, which is approximately equivalent to the depth that the mixolimnion has been displaced upwards.

Prior to mining, it was believed that discharging tailings to the monimolimnion of Garrow Lake would prevent dissolved metals from diffusing upwards through the pycnocline and into the mixolimnion. The high density of the pycnocline presents a physical barrier, while the abundance of sulphides would bind and scavenge metals from the water column and act as a chemical barrier. The tailings disposal system has been effective at preventing upward migration of metals. However, as discussed below, three spills of tailings into surface waters has been responsible for elevated metal concentrations in the mixolimnion.

In winter 1981 the tailings pipe became clogged and resulted in a small tailings spill on the ice surface near the northwest corner of the lake (Dickman and Ouellet, 1987). This material was deposited into nearshore water and may have contributed to elevated metal concentrations in surface waters. A more substantive spill occurred in the winter of 1984 – 1985. At that time, the down-leg section of the pipe broke at about 0.6 m depth and discharged a considerable amount of thickened tailings under the ice. The break was not detected for about three months until results of water sampling indicated elevated zinc (150 µg/L) at 10 m depth. Repairs were made in February 1985.

The total amount of zinc spilled into the mixolimnion was estimated by BC Research (1988) to be in the order of 800 tonnes, based on a zinc content of 0.5%, assuming a discharge rate of tailings at 1,600 tonnes/day. They further estimated that 42.7 tonnes of zinc was dissolved in the upper 20 m of Garrow Lake. Another spill occurred in the winter of 1989 (Gartner Lee, 2001), however we could not determine how much tailings were spilled or at what location. In 1992, a submerged, double-walled pipe was installed to eliminate the possibility of future spills.

The tailings spill caused a minor increase in lead concentration and a large increase in zinc concentration within the mixolimnion from 10 µg/L (1977) to 230 µg/L (1987) (BC Research, 1988). The extent of surface contamination was not realized because zinc concentration in Garrow Creek continued to be relatively low (61 µg/L) in summer 1986. However, vertical mixing of water during summer and under-ice caused zinc trapped above the pycnocline to become mixed into the mixolimnion, causing zinc to increase from 170 µg/L to 280 µg/L throughout the upper water column. Sampling of the lake beneath the ice in January 1988 revealed a sharp increase in zinc concentration in the upper pycnocline at 11 and 12 m depth (BC Research, 1988) and an increase in the mixolimnion to 310 µg/L. At the time, it was not known if the pycnocline would continue to be a "reservoir" of dissolved zinc or if zinc would be precipitated by sulphides within the pycnocline, and removed from the active mixolimnion by settling. Dissolved lead concentration continued to be low and was likely precipitated by sulphides. BC Research (1988) speculated that upward displacement of the pycnocline would increase average and peak zinc concentrations discharged from Garrow Lake over time, threatening to exceed Teck Cominco's permitted discharge concentration of 100 µg/L. Ice melt usually sufficiently diluted discharge of surface water to Garrow Creek such that limits were not exceeded except perhaps during first or last weeks of discharge from the lake.

In 1990 AXYS (1991) measured dissolved zinc concentrations of 410 µg/L and 1,800 µg/L within the mixolimnion and pycnocline respectively. Concentrations of total and dissolved zinc were very similar, suggesting that precipitation and loss to the monimolimnion was not occurring. These concentrations exceeded the discharge permit concentration. Therefore, Teck Cominco constructed a small dam across the creek in 1990 and 1991 about half way between the lake outlet and the creek mouth at Garrow Bay. The purpose of the dam was to prevent zinc contaminated surface water from reaching Garrow Bay by allowing lake level to increase by about 2.5 m and 10 Mm^3 in volume over a period of three years, diluting the mixolimnion and allowing tailings contaminated particulates in the lake to settle.

Water was not discharged from Garrow Lake until spring of 1994. During the intervening period several studies were undertaken to examine the effects of lead and zinc on receiving environment biota in Garrow Bay (AXYS, 1991; EVS, 1992). Results of these studies suggested that harmful effects of elevated zinc concentration were unlikely.

Consequently, the discharge limit for zinc was increased to 500 µg/L in 1992 (AXYS, 2001). This concentration was not exceeded during the remainder of mine life.

Subsequent to 1994, until removal of the dam, siphons were used to discharge water over the dam that allowed control over timing and volume of release. Gartner Lee (2001) reported that zinc concentration in the mixolimnion of Garrow Lake had gradually diminished from 400 µg/L in 1990 to 280 µg/L in 1999 and 2000. In 2003, mixolimnion dissolved zinc concentration was 240 µg/L, similar to 2000 data (Table 3).

Sampling of the water column at discrete depths in 2003 (GL-WQ-1) revealed that total metals concentrations within the mixolimnion (2 m and 6 m), pycnocline (11 m) upper monimolimnion (15 m) and deep monimolimnion (31 m) did not differ in concentration with the exception of lead and zinc (Table 3). Lead was more than an order of magnitude higher in concentration in the monimolimnion (12.1 µg/L) than the mixolimnion (0.8 µg/L). Zinc was higher in the monimolimnion (338 µg/L) than in the mixolimnion (240 µg/L) and highest within the pycnocline (1,140 µg/L), a pattern that was also observed in 1988 (1,800 µg/L at 16 m; BC Research, 1988) and 1990 (1,820 µg/L at 13 m; AXYS, 1991)(Table 2). Cadmium, lead and copper concentrations were also highest in the pycnocline. These data suggest that the pycnocline is a barrier, preventing transfer of metals from the monimolimnion upwards, but it also may prevent sinking of metals. Bacteria near the bottom of the pycnocline may be partly responsible for maintaining elevated metals in water owing to accumulation of zinc within the bacterial tissue.

Pre-mining, mining and post-mining water column metals data within the mixolimnion, pycnocline and monimolimnion are compared in Table 3. Concentrations of most metals, including arsenic, cadmium and copper, did not appear to change with any discernable pattern over mine life. Arsenic concentrations were low in the mixolimnion and pycnocline and were one to two orders of magnitude higher in the monimolimnion. Cadmium concentration was uniformly low and near detection limits in most water samples. Copper data were variable and did not demonstrate any trend or pattern over time or within discrete layers. Lead concentration in the mixolimnion increased after the metals spill in 1985 and has remained somewhat elevated since then, but has diminished over time.

Only zinc has demonstrated consistent trends in concentration over time and within discrete layers in Garrow Lake. During tailings discharge, prior to the spill, zinc concentration in the mixolimnion was low, less than 24 µg/L (0.024 mg/L) (Fallis et al., 1987; BC Research, 1978). BC Research (1981) measured higher concentrations in 1980, although Dickman and Ouellet (1987) measured low concentrations (16 µg/L) in 1981, the same year that tailings discharge was initiated. Zinc concentration increased in the monimolimnion shortly after tailings disposal was initiated, reflecting the addition of zinc rich material dispersed into the mid-water column. Zinc concentration in the monimolimnion has consistently been measured between 200 and 300 µg/L since tailings

disposal began. Note that this concentration is still below the discharge limit in Garrow Creek of 500 µg/L and is only slightly higher than zinc concentration in the mixolimnion.

As discussed above, the tailings spill into surface waters of Garrow Lake has caused dissolved zinc concentration to become and remain elevated (~250 µg/L) in the mixolimnion and especially the pycnocline layer (1,140 µg/L). This concentration has remained consistent since the mid-1990s. Elevated concentrations of dissolved zinc will likely be maintained for some time due to high concentration in the pycnocline, but also by elevated zinc concentration in the sediment due to the spill in 1985. The widespread zinc contamination throughout nearshore, littoral zone sediment of the lake (see following section) may present an on-going source of dissolved zinc to the mixolimnion.

3.2. Sediment Chemistry

No study has examined sediment chemistry of Garrow Lake since deposition of mine tailings was initiated. This is because tailings were especially deposited into the monimolimnion, which has proven to be an effective barrier at preventing movement of metals upwards through the pycnocline into surface waters (see Section 3.1). Despite the tailing spill to shallow sediment in 1984/85, no survey of sediment chemistry was undertaken.

In 1976, prior to mining, Fallis et al. (1987) collected sediment from 9 stations around Garrow Lake from depths ranging between 3 m and 48 m (Table 4). Six stations were situated within littoral zone sediments in depths of 12 m or less, within the mixolimnion. Three stations were in depths of greater than 12 m within the pycnocline or monimolimnion, in the anoxic, lifeless (except bacteria) zone of the lake. BC Research (1978) collected sediment from only two stations (12 m and 19 m) in 1977 and from 19 stations in May (5) and August (14) in 1980 (BC Research, 1981) at depths ranging from 5 – 48 m.

Concentrations of most metals including lead (<0.25 – 11 mg/kg), zinc (30 – 103 mg/kg), cadmium (0.25 – 3.1 mg/kg), arsenic (4.2 – 11.4 mg/kg), copper (15 – 31 mg/kg) and manganese (59 – 209 mg/kg) did not differ markedly with depth, even between littoral zone (<12 m) and monimolimnion zone sediment. Metal concentrations were only slightly higher in the deepest part of the lake, otherwise there were no meaningful differences among depths or between different areas of the lake in both the BC Research (1978 and 1981) and Fallis et al. (1987) studies. Interestingly, Fallis et al. (1987) found that metal concentration tended to be positively correlated with grain size.

Unfortunately, several spills of tailings (1981, 1985/85, 1989) introduced metals contaminated material to littoral zone sediment. The substantive spill under the ice during the winter of 1984 – 1985 discharged approximately 800 tonnes of zinc in thickened

tailings (BC Research, 1988). No study was conducted to determine the spatial extent and magnitude of contamination until the present study. However, given the designation of Garrow Lake as a tailings disposal facility, this was not necessary.

We sampled surface sediments from between 6 and 8 m within the mixolimnion at four locations around the lake, as well as two locations within the area of the 1984/85 tailings spill along the western shore of the lake (Figure 2). Grain size was predominantly silty-clay at all stations with a very fine, flocculent, oxidized surface layer with some organics, over grey colored sediment of uniform color, consistency and appearance (Table 1). With the exception of lead and zinc, sediment metal concentration throughout the littoral zone was no more than double pre-mining metal concentration (Table 5). Mean lead (137 µg/g dw) and zinc (742 µg/g dw) concentrations in littoral sediments from around the lake however, were considerably higher than pre-mine concentrations (0.25 µg/g and 61 µg/g dw respectively; Fallis et al., 1987) and are a reflection of the spill.

Given that sampling of sediment was conducted at similar depths over most of the lake that was accessible by boat (ice conditions permitting), these data indicate that the spill of metal contaminated tailings resulted in lake-wide contamination of surface sediment. Lead and zinc concentrations were only slightly higher at GL-2, nearest the historic spill area, than at the other three littoral stations. Suspended sediment introduced into the water column during the spill settled throughout most of the lake, causing contamination of surface (at least upper 1 – 2 cm) sediment in the littoral zone.

Two sediment samples collected from the immediate vicinity of the historic spill area had similar or lower concentrations for several metals (aluminum, barium, chromium, mercury, molybdenum, nickel, strontium) than littoral sediment and higher concentrations of lead (1,000 µg/g dw) and zinc (7360 µg/g dw)(Table 5). Most other metals for which pre-mine data were available are not substantially elevated or are lower than pre-mining concentrations.

3.3. Ecology

3.3.1. Zooplankton

No true zooplankton species were captured during the 2003 survey from the vertical tows at each of the four sediment stations (Figure 2), nor from a horizontal tow, conducted <1 m below the water surface. However, a single oligochaete worm and at least one cyclopoid copepod of benthic origin were sampled from each station.

Limnocalanus macrurus is the only species of zooplankton known to be present in Garrow Lake. This species was identified in 1976 by Fallis et al. (1987) and in 1977 and 1980 by BC Research (1978 and 1981 respectively). *L. macrurus* is a relatively common

species in the Arctic and is also present in many large, deep freshwater lakes. *L. macrurus* is known as a glacial relict species (Pennack, 1978). BC Research (1978) also captured or observed amphipods (*Gammarus* sp.) and a mysid species (*Mysis oculata*). Apparently, mysids were relatively abundant and of a large size, based on observations made during SCUBA surveys of Garrow Lake by BC Research (1978). Each of these species was also observed in nearby Frustration Lake in 1977 beach seines (BC Research, 1978).

In 1980, BC Research (1981) determined the density of plankton in vertical hauls from different depths (10 m, 15 m and 19 m, just above the pycnocline) and found that abundance of *L. macrurus* was much greater at the deepest depth, corresponding with the depth where the greatest abundance of phytoplankton was found.

It is not known why zooplankton were apparently absent from the lake during the present survey. Abundance of zooplankters is normally low in oligotrophic Arctic lakes, however, if plankton were present, at least a few individuals should have been captured. Perhaps plankton were situated at a deeper depth than was sampled in 2003 (8 m), or the mesh size used in the current study (250 µm) was too large; Fallis et al. (1987) used a 73 µm net. However, adult zooplankters of this species reach 2 mm in length (Pennack, 1978) so this may not explain their absence.

It is also possible that changes in water quality of the mixolimnion since pre-mine surveys have diminished abundance of the primary food source of *L. macrurus*, phytoplankton, or has directly affected zooplankton abundance. Phytoplankton were not collected during the 2003 survey.

3.3.2. Benthic Invertebrates

Oligochaete worms of the Family Enchytraidae, nematodes and Foraminifera were the only benthic invertebrates retained on a 250 µm sieve from petite ponar sampling in Garrow Lake in 2003 (Table 6). Abundance and density of oligochaetes was reasonably good, however, diversity of species was low. Chironomid larvae were present in the lake because several larvae were collected from the stomachs of fourhorn sculpin (see Section 3.3.3). However, density of chironomids in the lake appears to be quite low because none were collected from sieving of sediment. Given the high northern latitude and brief open water period, abundance of flying insects is naturally very low in this region. In fact, few flying insects were observed, with no mosquitoes or blackflies, which was a blessing.

Nematodes and Foraminifera were not included in the density estimate because these organisms are smaller than the mesh size used (250 µm) although they can be retained in small numbers. Nematodes and Foraminifera are very abundant and widespread in all lakes and their density is very infrequently estimated.

Fallis et al. (1987) also found a depauperate benthic fauna in Garrow Lake, dominated by Foraminifera. They identified 19 species with *Protelphidium orbiculare* being most abundant, followed by *Elphidium translucens*, *Ammotium cassis* and *Trochamina rotaliformis*. A single mollusk species, *Astarte warhami*, and an unidentified harpacticoid copepod were the only other species identified. Fossils of polychaetes, echinoderms and ostracods were identified in sediments, probably species that had been weathered out of historic, marine sediments as the lake has risen since the most recent glaciation.

BC Research (1978) identified nematodes, oligochaetes and harpacticoid copepods from Garrow Lake, although their abundance was not determined.

Garrow Creek sediment contained nematodes, oligochaetes a single mayfly (Ephemeroptera) species *Baetis bicaudatus* and several chironomid species (Table 6). These data indicate that, despite the ephemeral flow of the creek, it is capable of supporting aquatic life, dominated by oligochaetes. Chironomids were present in low abundance and their presence confirms that these organisms are capable of surviving in the creek and therefore, presumably Garrow Lake.

3.3.3. Fish

Nineteen fourhorn sculpins (*M. quadricornis*) were captured in gill nets and a prawn trap from Garrow Lake in 2003 (Table 7). Eleven sculpins were sacrificed to determine gender, sexual maturity, gut contents, age (using otoliths), internal condition and tissue metals concentration (whole fish). All 19 fish were measured for total length and weight to determine condition factor (Table 8) and length-weight relationship (Table 9).

Fallis et al. (1987) and BC Research (1978, 1980) were the first investigators to document sculpin biology (length, weight, growth, age, metals) prior to mining. No biological study of the sculpin population of Garrow Lake had been conducted until the present investigation. So, comparisons made here represent data collected prior to mining and after mining had ceased.

3.3.3.1. Size

All sculpins captured in 2003 appeared to be healthy with no external or internal tumors (Photo's 4 and 5), scars or other abnormalities (Table 7). Sculpins ranged from 85 mm to 184 mm (mean 149 mm) in length and 4.2 g to 40.3 g (mean 24.9 g) in weight. Mean condition factor (K) was 0.70 (Table 8). Fallis et al. (1987) captured 51 sculpins in 1976 using small-mesh, Swedish style gill nets, similar in size to the nets used in the current survey. All fish were acquired from above the pycnocline and none were found below 15 m. BC Research (1978) captured 137 sculpins using beach seines and observed that sculpins were found throughout the lake and appeared to be abundant and easily captured. Sculpins continued to be observed in the lake throughout the period of mining during

SCUBA maintenance of the tailings line (Gartner Lee, 2001; W. Gzowski, Arctic Divers Ltd., Yellowknife NWT personal communication, May 5, 2003), although no biological study was conducted.

Meristic data from 2003 were very similar to mean length (155 mm), weight (26.6 g) and condition factor (0.72) of sculpins captured by Fallis et al. (1987) using the same fishing gear (Table 8) prior to mining. Fish captured by BC Research (1978) in beach seines and nets had a wider size distribution (20 – 170 mm) and had a lower mean weight and condition factor.

Length – frequency distributions of sculpins from 1976 (Fallis et al. 1987), 1977 (BC Research, 1978) and 2003 demonstrate that the basic size distribution of adult sculpins has not changed markedly (Figure 4) since prior to mining. The maximum size of fish captured in 1976 was greater than in 2003, however, this is likely due to the small number of fish captured in 2003. Small, juvenile fish were collected, indicating that successful reproduction of fish had occurred and that recruitment of small fish into the population was occurring. Unfortunately, seining was not conducted, so many of the small fish captured in 1977 by BC Research (1978) were not represented here.

Length-weight relationships derived for each year (Table 9) were also quite similar suggesting that growth of sculpins, based on weight at length, has not changed since mining began. The 1976 data are most relevant to 2003 because similar fishing gear was used. Sculpins captured in 2003 (modal length of 155 mm) may have been slightly smaller than in 1976 (modal length of 175 mm). However, given the similarity in mean size and condition of fish caught in 1976 as in 2003 (Figure 4), suggests that the current size, size distribution and health of sculpins is similar to pre-mining conditions (Fallis et al. 1987).

3.3.3.2. Age

Mean age of sculpins captured in 2003 was 5.7 years, with a range of 3 – 9 years (Table 7). Fallis et al. (1987) and BC Research (1977) did not age sculpins. However, the small size, low lipid content (10%) and small size at age confirm that the sculpin population of Garrow Lake is very slow growing. Fallis et al. (1987) also stated that Garrow Lake sculpin have very slow growth rates relative to other Arctic sculpin populations (Bohn and Fallis, 1978), because of limited food as well as habitat. The deep, circular shape of the lake basin and the anoxic monimolimnion prevents sculpins from existing beneath the pycnocline, thus limiting benthic habitat for sculpins to littoral zone sediments. Given that 2 m of this shoreline habitat is eliminated during winter by ice, available habitat for food production is very limited indeed. The lack of food and cold water temperature explain their small size and slow growth rate relative to fish age.

3.3.3.3. Diet

Stomachs of 7 of 11 sculpins were empty. Of the four stomachs containing food, only a few chironomid larvae were distinguishable, as well as some unidentifiable plant matter and algae (Table 7). The presence of chironomids confirms that they do exist in Garrow Lake, despite the fact that chironomids were not identified from benthic grabs. This suggests that benthic productivity is very limited and even during the "height of summer" there is little food to be had.

Fallis et al. (1987) examined 27 sculpin stomachs of which half (14) were empty. Stomach contents included unidentified eggs, plant material, copepods and a few amphipods. BC Research (1977) found that the copepod *L. macrurus* dominated the diet. We did not identify copepods in the water column or in stomachs, suggesting that this species no longer comprises a significant portion of the sculpin diet. If the zooplankton community has diminished in Garrow Lake, and sculpins have been forced to become strictly dependent on benthic food sources, their population abundance would be expected to have declined. Although catch-per-unit-effort statistics were not recorded, Fallis et al. (1987) captured 51 sculpins in three net sets of 24 h each. The 2003 survey captured only 8 sculpins using gillnets over three days, with a baited prawn trap responsible for the remaining catch. Sculpins seemed to be more difficult to catch in 2003 and therefore may be less abundant than prior to mining (Fallis et al. 1987; BC Research, 1978). Given the lesser amount of habitat available to the population because of the reduced size of the mixolimnion, this result is not surprising.

3.3.3.4. Sex and Maturity

Sex ratio of sculpins captured in 2003 was split evenly between males and females and all fish autopsied appeared sexually mature, with nearly ripe gonads. Fallis et al. (1987) found that most sculpins were female (22 of 27) with 12 having developing eggs. Spawning by sculpins takes place in late fall or winter (Scott and Scott, 1988). Eggs are laid in a small clump within a shallow depression and are guarded by the male during incubation. Given the very slow growth rate and maturation of gonads, it is possible that all of the apparently mature sculpins may not have spawned in winter of 2003/2004 and some individuals may have waited an additional year. Nevertheless, the gonads of most individuals did appear to be quite ripe and these individuals would certainly spawn within the next few months. Fallis et al. (1987) observed eggs in sculpin stomachs in 1976. Presuming these were from sculpins, it is possible that some individuals may spawn during late summer.

3.3.3.5. Tissue Metals

Whole body concentrations of manganese, lead and zinc in sculpins were higher in 2003 than was measured in sculpin tissue prior to mining (Fallis et al., 1987; BC Research, 1978) (Appendix C; Table 10). Other metals including arsenic, cadmium, copper, mercury, and nickel were lower or did not differ among years. Elevated lead and zinc concentrations in sediment and the water column as a result of the spill have resulted in increased tissue metals concentrations, however the magnitude of increase is relatively small. Prior to mining, mean zinc concentration was about 30 mg/kg and increased to only 72 mg/kg in 2003. The magnitude increase in lead concentration between pre-mining (0.58 mg/kg) and post mining (0.81 mg/kg) was also similar (Fallis et al., 1987). Fallis et al. (1987) stated that only copper and iron were significantly positively correlated with fish size while all other metals showed no relationship or a declining trend.

Relative to metals in sculpins elsewhere, Bohn and Fallis (1978) found that Garrow Lake sculpins were higher in lead and zinc but lower in cadmium and arsenic than Strathcona Sound sculpins. Elevated lead and zinc concentration prior to mining is presumably due to naturally higher mineralization. The tailings spill has caused a further increase in lead and zinc concentration.

3.3.4. Summary

The sculpin community of Garrow Lake is unique and has survived in this small, brackish water meromictic lake since glacial uplift isolated it from the marine environment nearly 3,000 years ago. The sculpin population has survived twenty years of mining tailings disposal to the monimolimnion and at least one significant tailings spill into the mixolimnion.

Overall, it appears as if the size, distribution, growth rate and reproductive status of the sculpin community has not changed markedly since pre-mining studies by Fallis et al. (1987) and BC Research (1978; 1980) although population size appears to have diminished. Only concentrations of lead and zinc in tissue have increased over the course of mining, likely as a result of the tailings spill in 1984/85. However, based on a survey of the zooplankton and benthic communities and diet of sculpins, it appears that the planktonic invertebrate community of Garrow Lake may have declined since tailings deposition began and that sculpins may be relying solely on benthos as a food source.

Introduction of tailings into the monimolimnion of the lake has caused the bottom layer to become less saline, more homogeneous and has caused a gradual displacement of the pycnocline and mixolimnion upwards in the water column. In 2004, once the lake has been drawn down to its original level, the depth of the mixolimnion above the pycnocline should diminish to about 7.5 or 8 m. Although the magnitude of the thermal and salinity

difference between the mixolimnion and the monimolimnion in the lake will be sufficient to maintain separation of the two layers and prevent turnover and mixing (AXYS, 2001) the largest change in the limnology of the lake is the reduced depth of the mixolimnion and surface area of the littoral zone.

Garrow Lake is very unproductive with low water column nutrient concentrations, a depauperate planktonic community and a benthic community dominated by oligochaetes, with very few insect larvae. A reduction in the planktonic community and diminishment in mixolimnion depth and littoral zone area will necessarily reduce habitat area and benthic invertebrate abundance. This loss of habitat and diminishment of food resources will ultimately, reduce population abundance. Sculpins seemed to be more difficult to capture in 2003 than in fishing efforts by Fallis et al. (1987) and BC Research (1978; 1980), which supports the hypothesis of a smaller population size in 2003 than pre-mining.

Nevertheless, sculpins have survived in Garrow Lake throughout the history of mining and tailings deposition to the lake, which is still designated as a tailings disposal facility (DFO, 2002). Provided that sufficient habitat and food resources exist within the spatially small littoral zone, the sculpin population will be sustained through the future.

4. REFERENCES

AXYS Environmental Consulting Ltd. (AXYS). 1991. Concentrations of zinc, lead, cadmium and copper in Garrow Bay, 1990. Prepared by AXYS Environmental Consulting Ltd., Sidney BC for Cominco Ltd. 40 p + App.

AXYS Environmental Consulting Ltd. (AXYS). 2001. Garrow Lake dam. Effect of removal on lake stability and outflow water quality. Prepared for Cominco Ltd. Polaris Operations by P. Erickson, AXYS Environmental Consulting and E. Bennett, Applied Ocean Sciences. March 2001.

Azimuth Consulting Group. 2004. Environmental Effects Monitoring (EEM) study design – Teck Cominco Polaris Mine, Nunavut. Prepared for Teck Cominco, Kimberley BC and Environment Canada, Edmonton AB, by Azimuth Consulting Group Inc. June 2004.

BC Ministry of Environment Lands and Parks. 2003. British Columbia field sampling manual. Prepared by Water, Air and Climate Change Branch, BC WLAP. January 2003. 401 p.

BC Research. 1975. Environmental study of Polaris Mine, Little Cornwallis Island. Project No. 1642. February, 1975. Prepared for Cominco Ltd., Trail BC.

BC Research. 1978. Polaris Mine aquatic environmental studies, 1977. Prepared for Cominco Ltd. Trail BC. 63 p.

BC Research. 1981. Polaris Mine aquatic studies. 1980. Garrow Lake, Pullen Strait. Prepared for Cominco Ltd., Yellowknife NWT. 59 p.

BC Research. 1988. Garrow Lake: Independent sampling (May 1988) and analyses of long term surveillance data. Prepared by BC Research, Vancouver BC for Cominco Ltd. Polaris Operations, NWT, July 1988.

Bohn, A. and B.W. Fallis. 1978. Metal concentrations (As, Cd, Cu, Pb and Zn) in shorthorn sculpin *Myoxocephalus scorpius* and Arctic char *Salvelinus alpinus* from the vicinity of Strathcona Sound, NWT. Water Research 12: 659 – 663.

Department of Fisheries and Oceans. 2002. Metal Mining Effluent Regulations. Ottawa, Ontario.

Dickman, M. and M. Ouellet. 1987. Limnology of Garrow Lake, NWT, Canada. Polar Record 23(146): 531 – 549.

Environment Canada. 1994. Guidance document on collection and preparation of sediments for physicochemical characterization and biological testing. Environmental Protection Series. Report EPS 1/RM/29. Ottawa, Ontario.

EVS Environment Consultants. 1992. Studies into the biological significance of Garrow Lake discharge to Arctic marine waters. Prepared for Cominco Ltd. Vancouver BC by EVS Consultants, North Vancouver BC. March 1992. 53 p. + App.

Fallis, B.W., S. M. Harbicht and B.J. Mackenzie. 1987. A preliminary study of the limnology and biology of Garrow Lake, Northwest Territories; an Arctic meromictic lake. Department of Fisheries and Oceans, Winnipeg, MB. Unpublished data. ii + 55 p.

Gartner Lee. 2001. Polaris Mine decommissioning and reclaimation plan. Prepared for Cominco Ltd., Polaris Mine by Gartner Lee Ltd. Vancouver BC. GLL 20-935

Ouellet, M. and M. Dickman. 1983. The meromictic Garrow Lake, Canadian Arctic Archipelago. INRS-Eau, Rep. 77. 85 p.

Page, P., M. Ouellet and M. Dickman. 1984. Isotopic analysis (^{18}O, ^{13}C, ^{14}C) of two meromictic lakes in the Canadian Arctic Archipelago. Limnol. Oceanogr. 29(3): 564 – 573.


Pennack, R.W. 1978. Fresh-water invertebrates of the United States. Second Edition. John Wiley and Sons, Toronto. 803 p.

Scott, W.B. and M.G. Scott. 1988. Atlantic fishes of Canada. Can. Bull. Fish. Aquat. Sci. No. 219. 731 p.

Stewart, K.M. and R.F. Platford. 1986. Hypersaline gradients in two Canadian high Arctic lakes. Can. J. Fish. Aquat. Sci. 43: 1795 – 1803.

Thornsteinsson, R. and J.W. Kerr. 1968. Cornwallis Island and adjacent smaller islands, Canadian Arctic archipelago. Geol. Surv. Can. Pap. 67-64: 1 – 16.

FIGURES

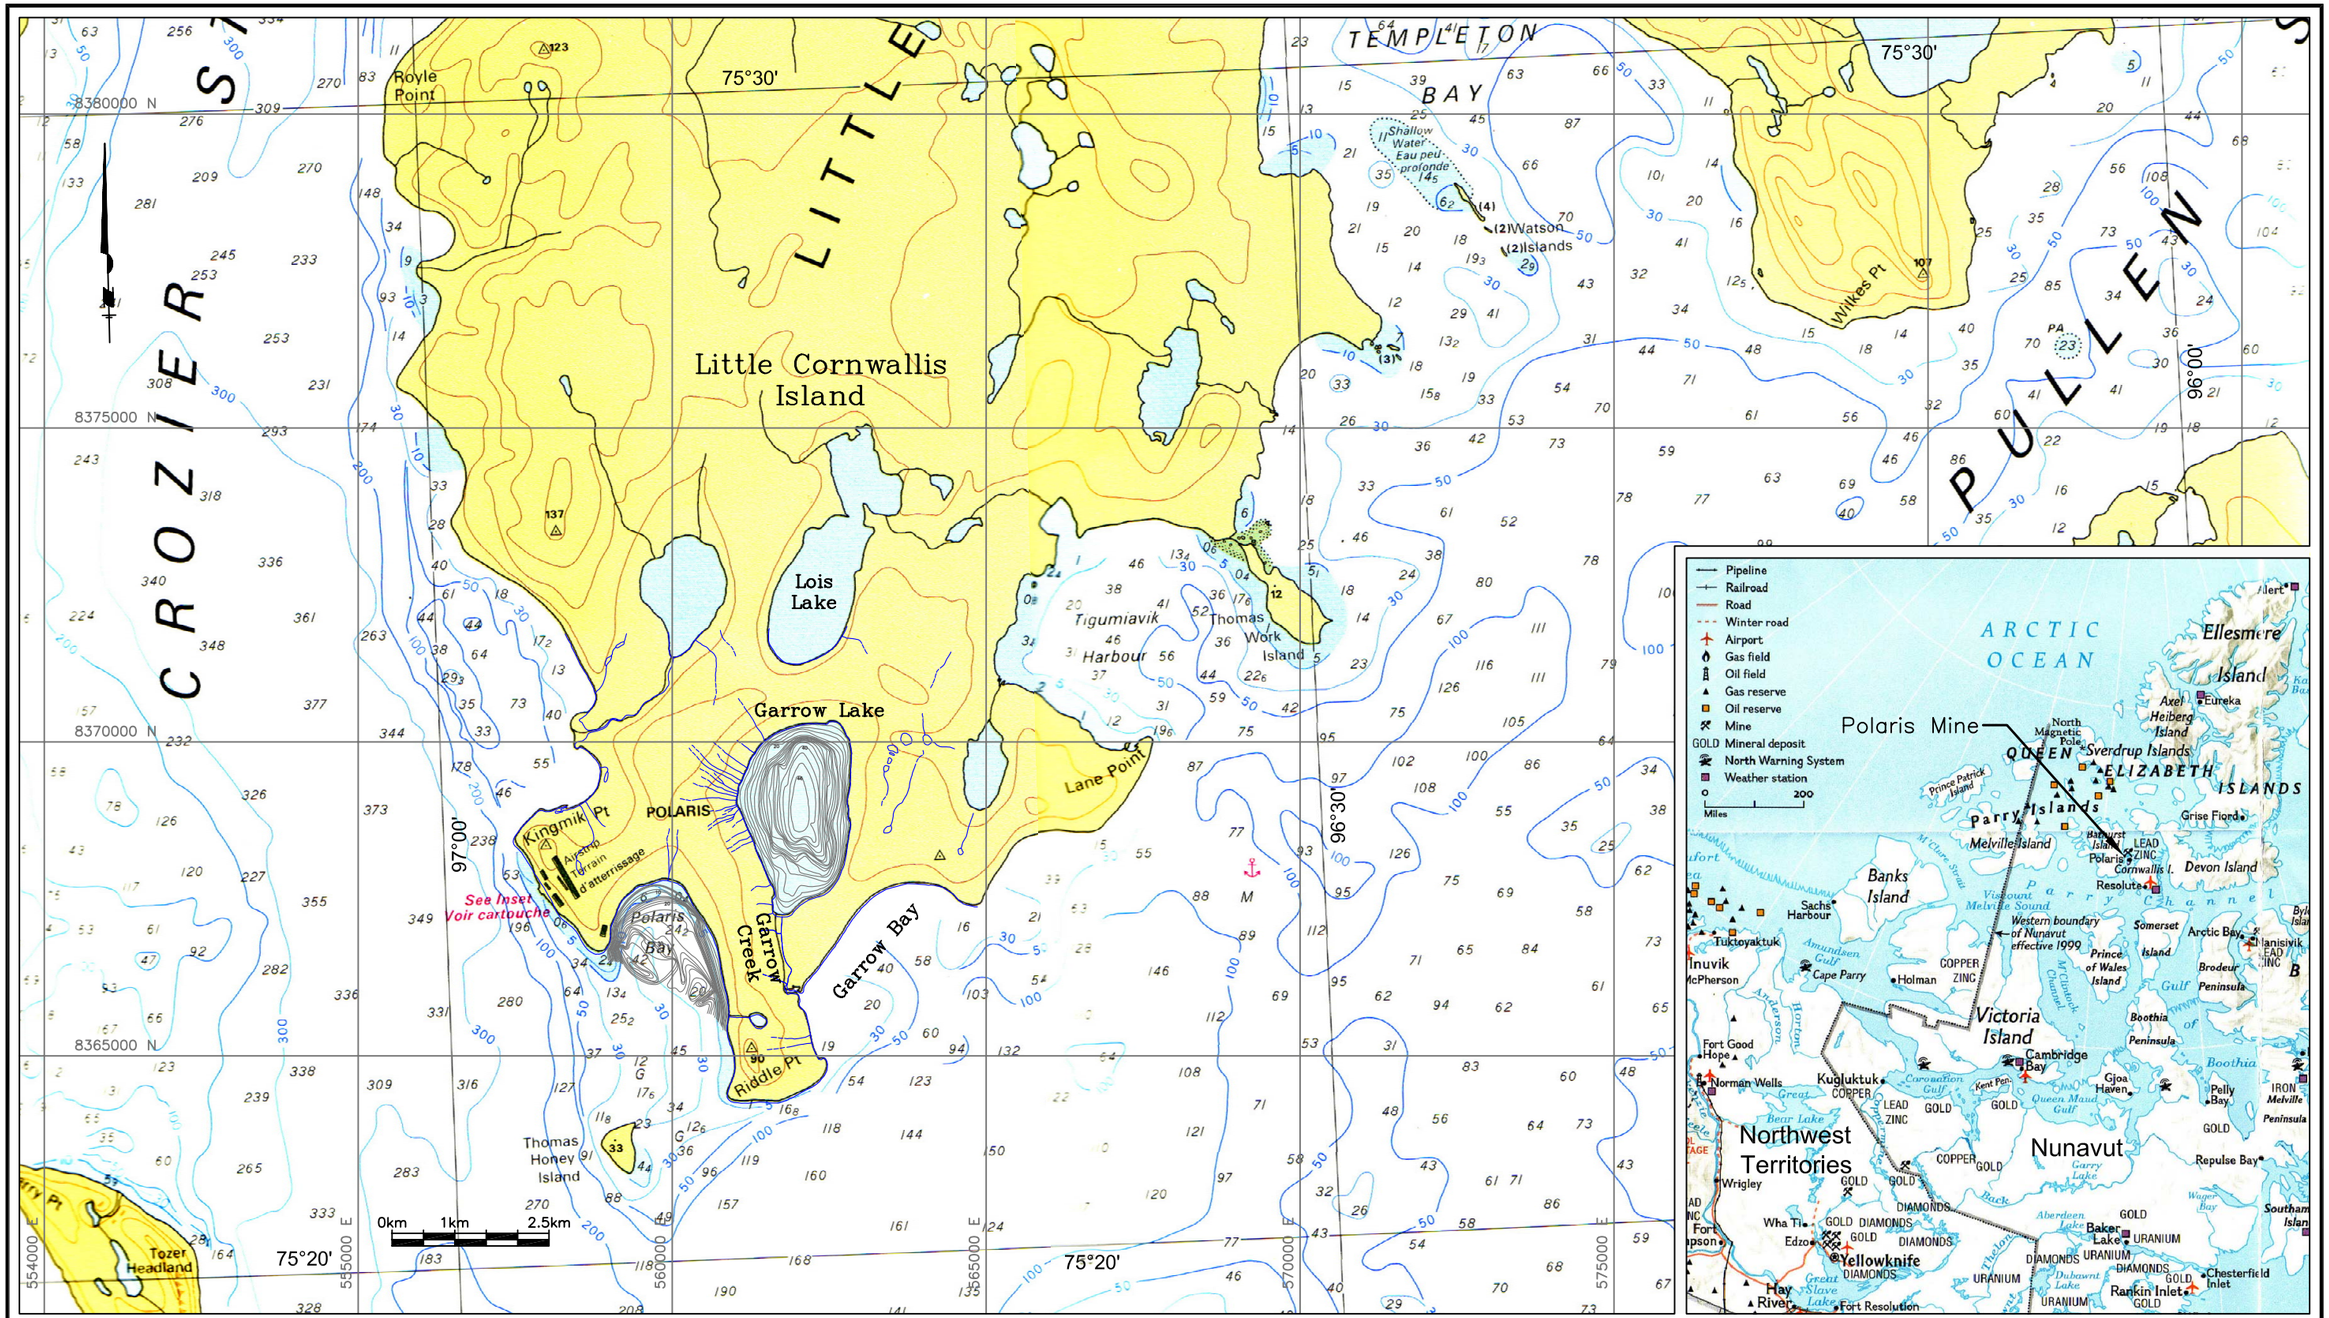

Carrow Lake, Polaris Bay contour data and surrounding creeks digitized from Map 1 Sampling Sites 1980 *prepared by B.C. Research January 1978*

Other data from Crozier Strait And/Et Pullen Strait 7935 *corrected 2003-03-28 published by the Canadian Hydrographic Service*

Insert Location Map from The Modern North: Roads, Radar Stations, and the End of Isolation, *Produced by National Geographic Maps for National Geographic Magazine, Sept. 1997*

AZIMUTH

Azimuth Consulting Group Inc.
218-2902 West Broadway
Vancouver BC, V6K 2G8


DRAWN BY:	CHK. BY:	PROJECT No:
BT	RB	TC-03-03
SCALE:	DATE: 6/10/2003 2:52 PM	

PROJECT: Polaris

TITLE: **Polaris Mine Study Area**

CLIENT: Teck Cominco

Figure 1-1

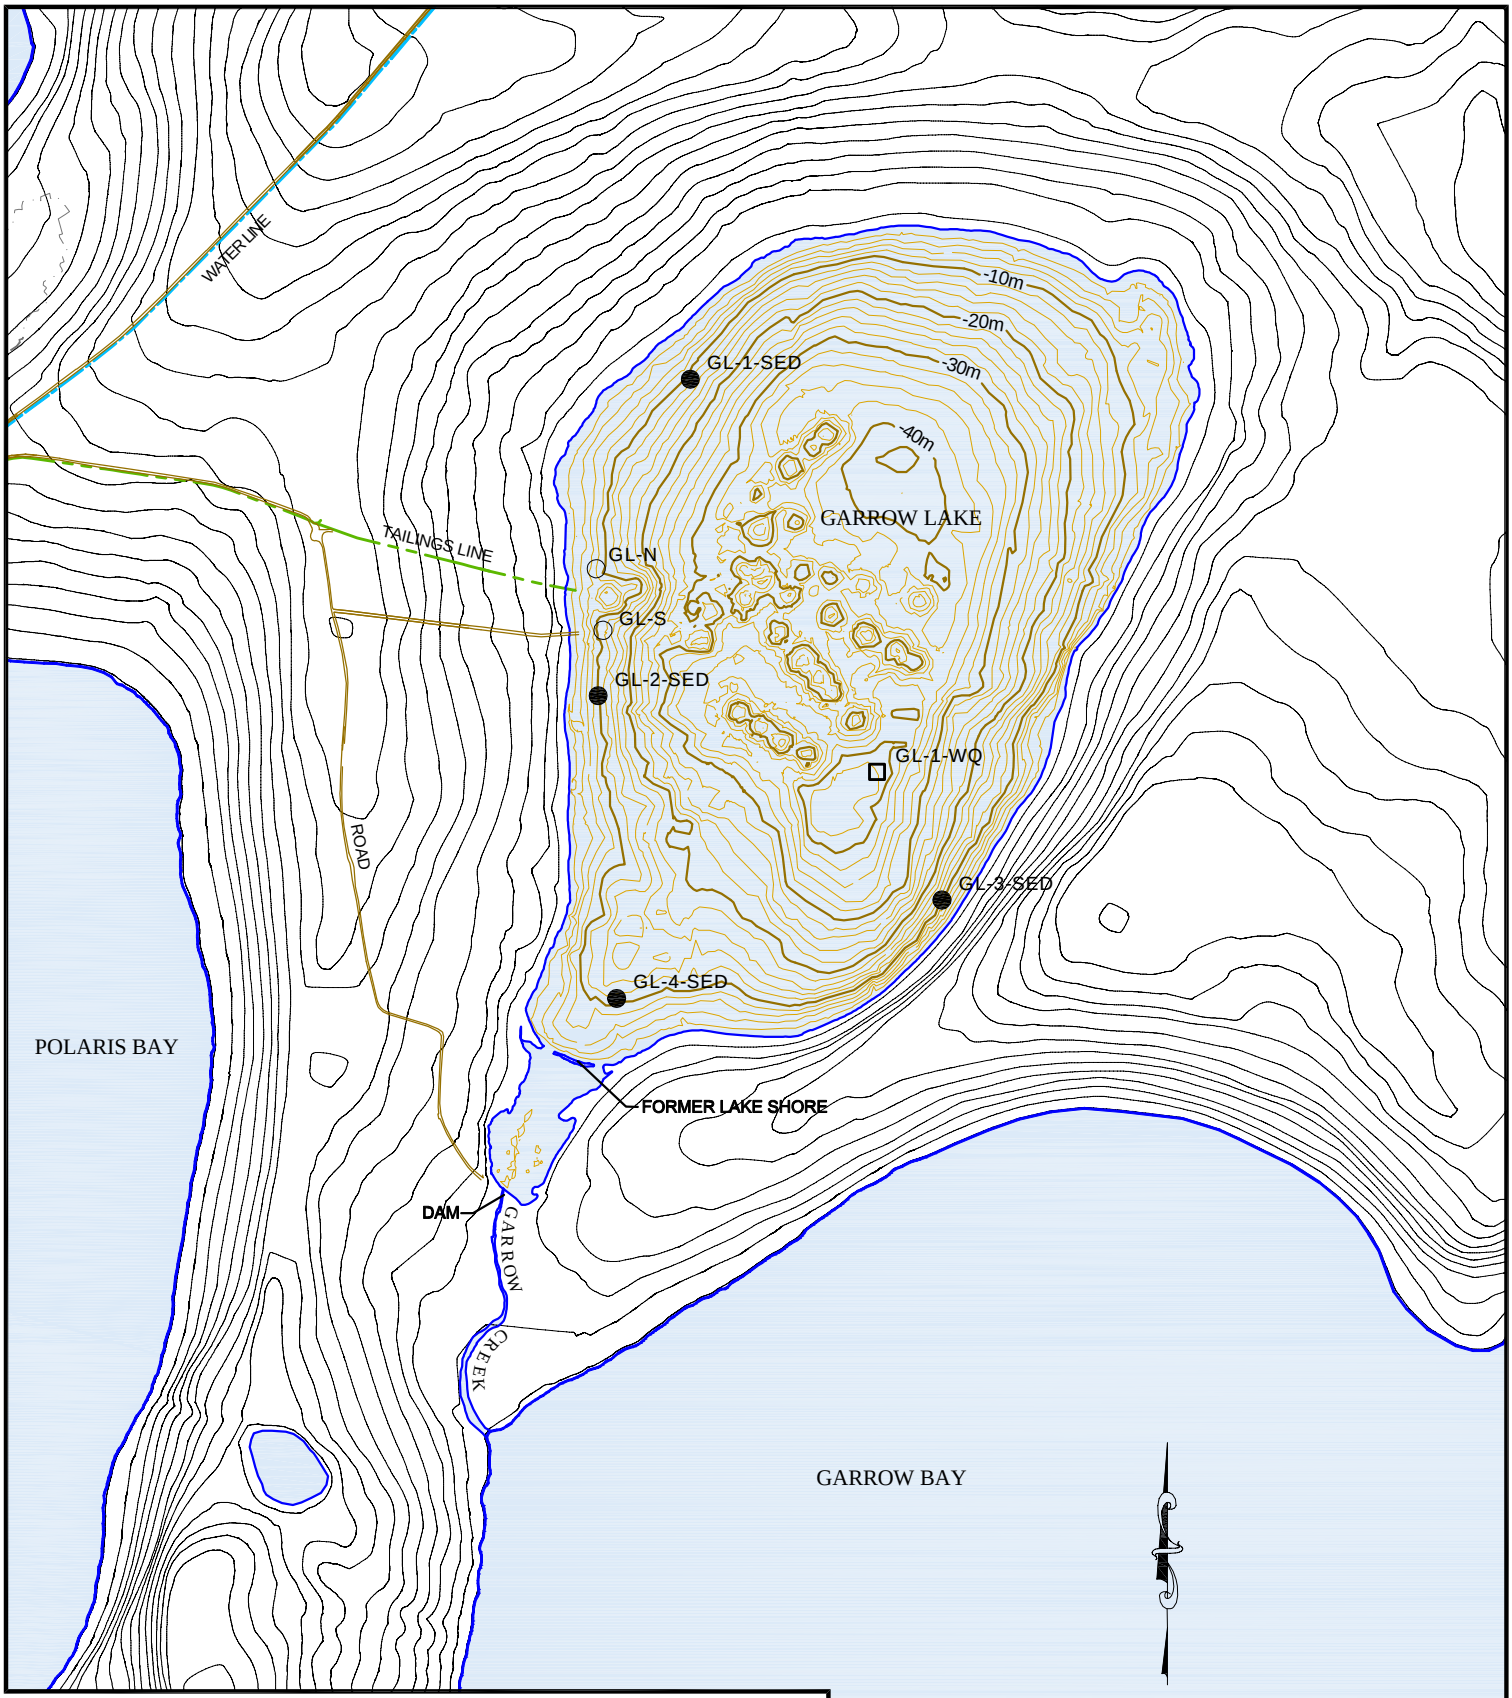

LEGEND

- BENTHOS, ZOOPLANKTON, SEDIMENT
- LAKE WATER (VERTICAL PROFILE)
- SEDIMENT

NOTE:

SURROUNDING CREEKS DIGITIZED FROM MAP 1 SAMPLING SITES 1980, PREPARED BY B.C. RESEARCH JANUARY 1978.

AZIMUTH
218 - 2902 WEST BROADWAY
VANCOUVER BC, V6K 2G8

CLIENT: TECK COMINCO

SHEET TITLE: LOCATION OF LITTORAL ZONE SEDIMENT / BIOTA STATIONS AND WATER QUALITY PROFILE STATION - GARROW LAKE, AUGUST 2003

PROJECT: POLARIS

REVISIONS

CHECKED BY: RB
SCALE: 1:25,000
Charone
www.charone.ca

JOB NO.: TC-03-03
DATE: 11-22-2004
DRAWN BY: CCL

FIGURE: 002

Figure 3a. Temperature (C) depth profile in Garrow Lake, 2003.

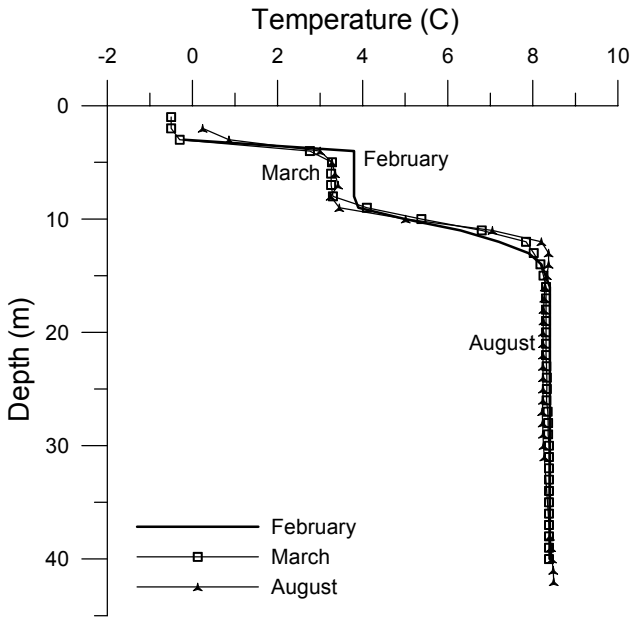


Figure 3b. Dissolved oxygen (mg/L) depth profile in Garrow Lake, 2003.

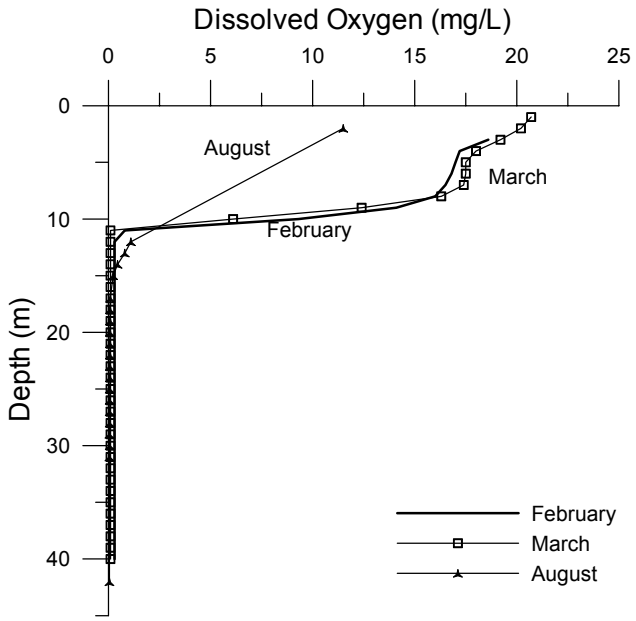


Figure 3a. Temperature (C) depth profile in Garrow Lake, 1976.

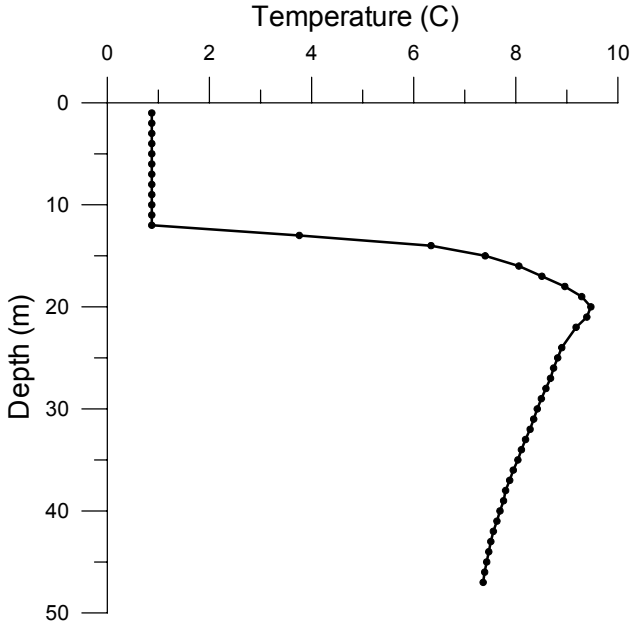


Figure 3b. Dissolved oxygen (mg/L) depth profile in Garrow Lake, 1976.

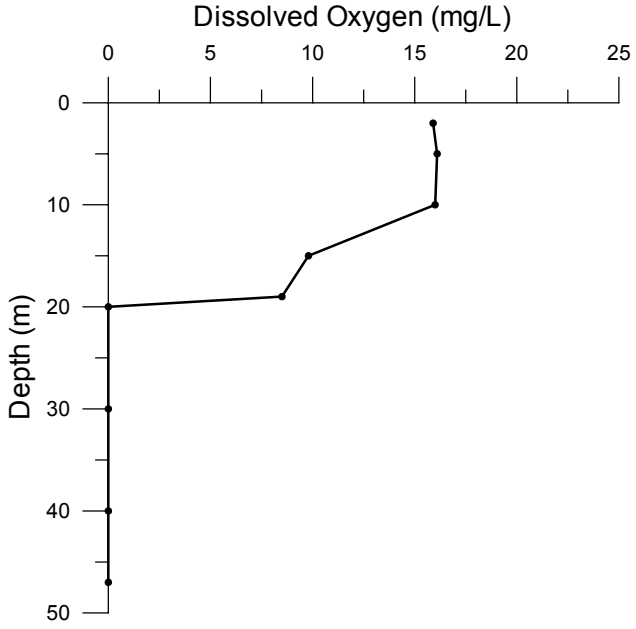


Figure 3c. Salinity (ppt) depth profile in Garrow Lake, 2003.

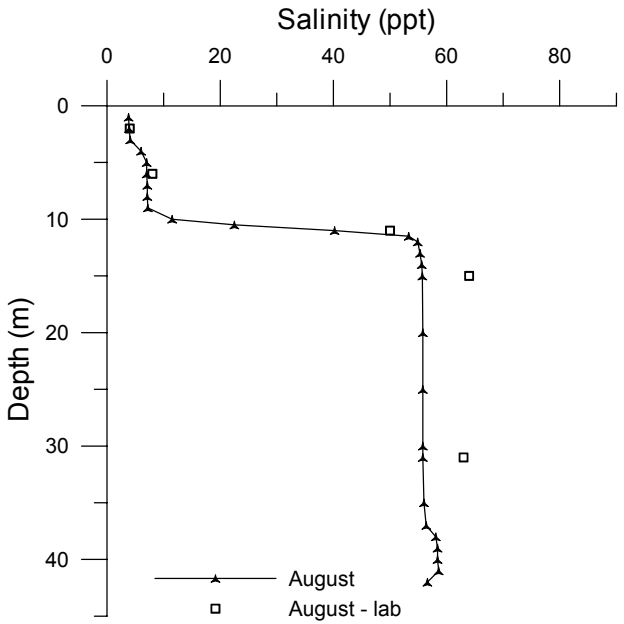


Figure 3c. Salinity (ppt) depth profile in Garrow Lake, 1976.




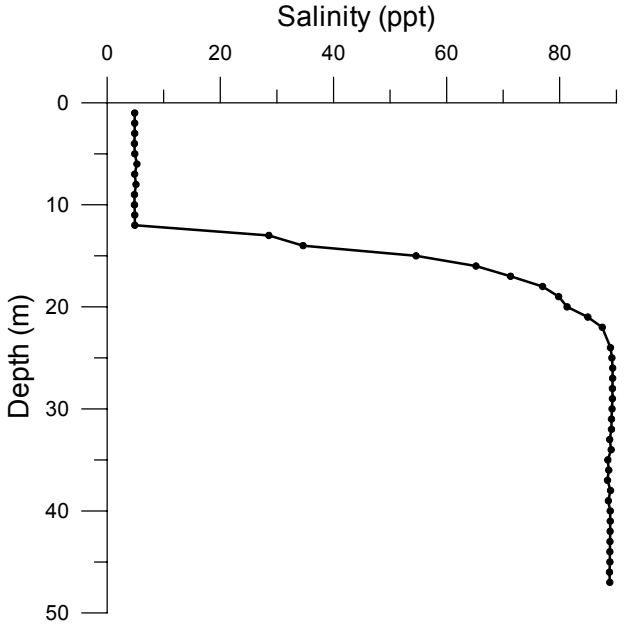


Figure 4. Comparison of length - frequency distribution of fourhorn sculpin from 1976 (Fallis et al., 1987) 1977 (BC Research (1978) and 2003.

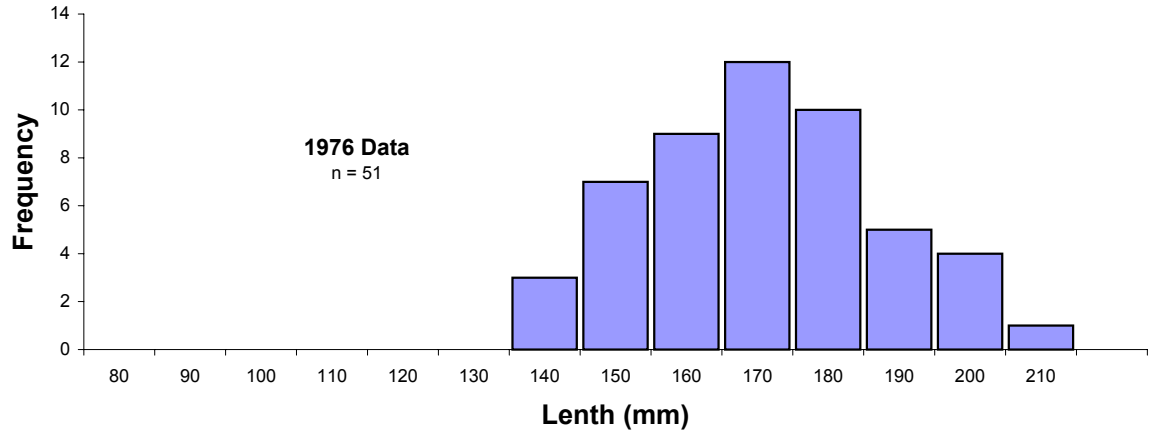

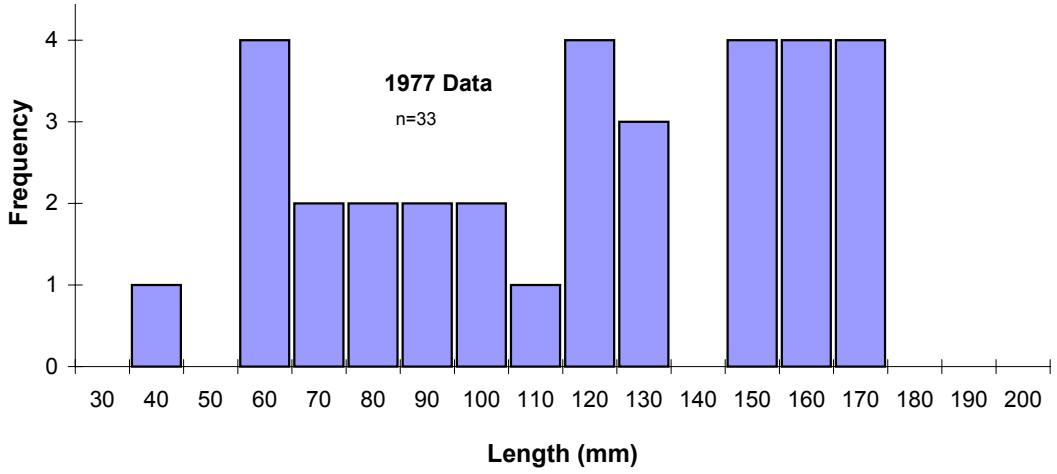

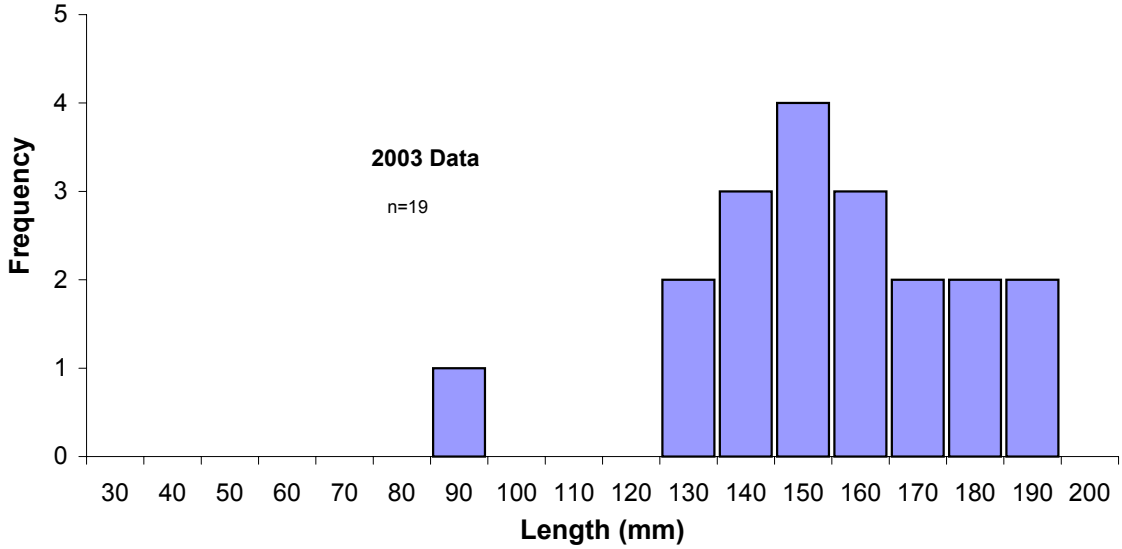

TABLES

Table 1. Details of sediment, water and biota collections from Garrow Lake, August 8 – 10, 2003.

Station	UTM		Depth (m)	Parameter				Observations
	N	E		Water	Benthos	Zooplankton	Sediment	
GL-1-SED	8369695	0561130	7.5		X	X	X	Thin light brown soft flocculent surface layer. Some algal growth on surface. Beneath, sediment is uniform grey clay, uniform consistency and appearance.
GL-2-SED	8368612	0561266	6.5 – 8.5		X	X	X	Similar in appearance to SED-1; rusty oxidized, brown surface layer over battleship grey layer of uniform consistency with fine organic matter.
GL-3-SED	8368424	0562669	6 – 8		X	X	X	Fine brown organic 2 – 3 mm layer over grey-brown clay. Grab 3 different from 1 and 2 with darker sediment and more organically rich layer.
GL-4-SED	8367556	0561764	7		X	X	X	Fine orangey-brown layer (2 – 3 mm) over grey-brown silty clay. Benthos not apparent.
GL-N-SED			8				X	Sediment appeared to be consistent with tailings; chalky white, fine grain flocculent sediment throughout grab with black sticky varves.
GL-S-SED			8				X	
GL-1-WQ	8369695	0561130	0 – 42	X				

Table 2. Summary of Garrow Lake water column metals concentration (mean, range; ug/L), 1976 - present.

			Arsenic		Cadmium		Copper		Lead		Nickel		Zinc	
		n	mean	range	mean	range	mean	range	mean	range	mean	range	mean	range
June 1976[AB]	Mixolimnion	19	0.3	0.1 - 1.1	0.3	0.1 - 1.3	1	0.2 - 2.7	0.3	0.1 - 0.5			3	1.3 - 6.7
(Fallis et al., 1987)	Pycnocline	4	1.9	0.3 - 3.5	0.2		2.8	1.5 - 4.1	0.4				2.9	1.9 - 3.8
	Monimolimnion	7	13.4	4.7 - 20.4	0.2	0.1 - 0.2	4	0.9 - 14.5	0.3	0.1 - 0.5			1	0.1 - 2.2
August 1977	Mixolimnion	12	<1		0.2	<0.1 - 0.6	10	1 - 60	5	<1 - 16			24	6 - 100
(BC Research 1978)	Pycnocline	17	<1		0.3	<0.1 - 0.6	12	2 - 22	3	<1 - 7			21	4 - 50
	Monimolimnion	13	4.6	<1 - 6.4	<0.5	<0.5	18	5 - 22	8	<5 - 27			18	8 - 28
May & August 1980	Mixolimnion	14	<1		>0.5		19	6 - 32	<1				49	20 - 95
(BC Research 1981)	Pycnocline	24	<1		>0.5		23	13 - 36	<5				46	28 - 85
	Monimolimnion	18	8	3.4 - 13	>0.5		16	3 - 50	<10				48	15 - 113
August 1981	Mixolimnion	2			>0.5		1.0		<10		7		10	9 - 12
(Ouellet & Dickman 87)	Pycnocline	1			1.0		>1		<10		10		9	
	Monimolimnion	7			<1.2		<2.4		<24		11		16	7 - 34
October 1981	Mixolimnion	2	0.06	0.06 - 0.06	0.06	0.06 - 0.06	0.35	0.3 - 0.4	0.35	0.3 - 0.4			3.3	2 - 4.6
(Fallis et al. 1987)	Pycnocline	3	0.29	0.17 - 0.34	0.3	0.2 - 0.4	5.5	1.5 - 8.9	1.0	0.8 - 1.2			5.7	4.2 - 6.8
	Monimolimnion	27	13.3	1.6 - 20	0.1	<0.05 - 0.2	1.3	<0.1 - 6.4	0.3	<0.1 - 1.8			4.1	1.2 - 6.3
September 1984	Mixolimnion	1							5				20	
(BC Research, 1988)	Pycnocline	1							5				40	
	Monimolimnion	1							14				30	
September 1987	Mixolimnion	1							7				230	
(BC Research, 1988)	Pycnocline	1							5				220	
	Monimolimnion	2							25				45	
May 1990	Mixolimnion	1							10				410	
(BC Research, 1988)	Pycnocline	1							21				1,820	
August 1998	Mixolimnion	4	<1		1.0	<1 - 1	1.0	<1 - 1	2	<1 - 5	<2		198	150 - 320
(Teck Cominco)														
August 1999	Mixolimnion	4	<1		1.0		2.3	<1 - 4	15.3	13 - 22	5	4 - 5	233	220 - 270
(Teck Cominco)														
August 2001	Mixolimnion	4	<1		<2		1.5	<1 - 2	1.8	<1 - 3	4	3 - 5	223	180 - 330
(Teck Cominco)														
August 2003	Mixolimnion	2	<1	<1 - 1	0.5	0.3 - 0.6	1	0.9 - 1.4	0.8		3	2.1 - 3.7	184	127 - 240
	Pycnocline	1	<1		2.5		7		4		9		1,140	
	Monimolimnion	2	1	<1 - 1	0.4	0.3 - 0.5	5	3.8 - 5.2	12	11.8 - 12.1	9	8.8 - 9.0	278	217 - 338

[A] Values below detection limit were treated as absolute values.

[B] Dissolved metals, otherwise, total metals

Table 3. Conventional parameters and total metal concentration (ug/L) in water samples collected from Garrow Lake, August 2003.

Sample ID	GL-1-WQ-2m	GL-1-WQ-6m	GL-1-WQ-11m	GL-1-WQ-15m	GL-1-WQ-31m
CONVENTIONAL PARAMETERS					
pH	8.2	8.0	7.2	7.3	7.4
Salinity o/oo	4.0	8.0	50.0	64.0	63.0
Temperature (C)	0.2	3.4	7.1	8.3	8.3
TOTAL METALS (µg/L)					
Aluminum	<100	<100	<100	<100	<100
Arsenic	<1	<1	<1	1.0	<1
Cadmium	0.3	0.6	2.5	0.3	0.5
Copper	0.9	1.4	7.1	5.2	3.8
Lead	0.8	0.8	4.3	11.8	12.1
Molybdenum	<2	3	2	4	<2
Nickel	2	4	9	9	9
Zinc	127	240	1140	338	217

Table 4. Total metals (mg/kg dw) in Garrow Lake sediment, prior to mining.

	Fallis et al. (1987) June 1976 (n=9)		BC Research (1978) August 1977 (n=2)		BC Research (1981) May and August 1980 (n~19)	
Total Metals	**Mean**	**Range**	**Mean**	**Range**	**Mean**	**Range**
Arsenic	6	2 - 11	5	4 - 6	4.7	3.2 - 57.6
Cadmium	1.00	<0.25 - 3.1	0.7	0.4 - 1.0	1.3	0.3 - 3.0
Copper	23	15 - 31	18.5	18 - 19	22	12 - 27
Lead	0.25	<0.25 - 0.75	8	8	8.4	5.9 - 11
Manganese	150	59 - 209				
Mercury	0.15	0.005 - 0.025			<0.05	<0.5 - 0.6
Nickel	19	12 - 39				
Zinc	61	30 - 103	65	59 - 70	84	52 - 96
Depth Range (m)		3 - 48		12 and 19		5 - 48

Table 5. Conventional sediment parameters and total metals concentration (mg/kg) in Garrow Lake littoral zone sediment.

	Garrow Lake Stations (Aug 2003)					Tailings Spill Area		1976 (Pre-Mine)
Sample ID	**GL-1**	**GL-2**	**GL-3**	**GL-4**		**GL-N North**	**GL-S South**	**Fallis et al. 1987**
Depth (m)	**7.5**	**6.5 - 8.5**	**6 - 8**	**2 - 7**	**Mean**	**7 - 8**	**7 - 8**	**3 - 48**
CONVENTIONAL PARAMETERS								
Organic Parameters								
Total Organic Carbon (% dw)	<0.8	1.2	<0.9	2.4	1.3	-	-	-
Particle Size (%)								
Gravel (>2.00mm)	<0.1	<0.1	0.9	<0.1	0.3	-	-	-
Sand (2.00mm - 0.063mm)	5.4	7.5	12.3	6.8	8.0	-	-	-
Silt (0.063mm - 4um)	64.2	68.3	70.3	76.1	69.7	-	-	-
Clay (<4um)	30.4	24.2	16.5	17.1	22.1	-	-	-
Total Metals								
Aluminum	8560	7380	6030	6680	7162	781	547	
Antimony	<10	<10	<10	<10	<10	<20	<20	
Arsenic	11	9	<5	9	8.5	<10	<10	6
Barium	1420	1070	1040	1150	1170	122	124	
Beryllium	0.6	<0.5	<0.5	<0.5	0.5	<1	<1	
Cadmium	1.9	3	1.1	1.4	1.9	17	15	1.0
Chromium	19	18	15	16	17	22	9	
Cobalt	6	6	4	5	5.3	<4	<4	
Copper	31	32	17	24	26	68	24	23
Lead	114	308	47	78	137	1000	680	0.25
Manganese	183	222	175	172	188	487	493	150
Mercury	0.1	0.09	0.05	0.17	0.1	0.08	0.06	0.15
Molybdenum	4	<4	<4	<4	4	<8	<8	
Nickel	36	30	19	26	28	<10	<10	19
Strontium	268	209	217	289	246	64	52	
Zinc	700	1210	498	560	742	7360	5980	61

Table 6. Abundance and density of benthic invertebrates in Garrow Lake and Garrow Creek, Little Cornwallis Island, August, 2003.

Location		Creek-mid	Creek-up	GL-1	GL-2	GL-3	GL-4
Date		4-Aug-03	4-Aug-03	7-Aug-03	7-Aug-03	8-Aug-03	8-Aug-03
Species/Group	Stage**						
FORAMINIFERA							
Unidentified							350
NEMATODA							
Unidentified		5		1		20	
OLIGOCHAETA							
Unidentified	juv*	5		17	65	200	100
Enchytraidae		471	10	418	390	1470	550
COPEPODA							
Cyclopoida	juv*						1
EPHEMEROPTERA							
Baetidae							
Baetis bicaudatus	N	2					
DIPTERA							
Chironomidae	P	1					
Tanypodinae							
Procladius	L	1					
Orthocladiinae							
Eukiefferiella	L	1					
Orthocladius	L	1					
Diamesinae							
Diamesa	L	4	1				
Total		491	11	436	455	1690	1001
Oligochaete Abundance				435	455	1670	650
Oligochaete Density (#/m^2)				18125	18958	69583	27083

**Key:

L = Larva

N = Nymph

P - Pupa

juv = Juvenile

* = Too small to be idetified further, damaged

Table 7. Biological data for fourhorn sculpin from Garrow Lake, August 2003.

Code	Total Length (mm)	Body Weight (g)	Lipid (%)	Age (yrs)	K[1]	Gender	Maturity	Stomach Content	Condition	
									Liver	External
SC-1-03	149	24.8	14.3	6	0.75	F	Ripe	1 chironomid and plant material	large, healthy	good
SC-2-03	129	16.0	8.8	5	0.75	F	Ripe	3 chironomids, small stomach	healthy, pink	good
SC-3-03	138	20.5	12.8	6	0.78	M	Ripe	Empty	large, healthy	good
SC-4-03	163	34.5	15.7	4	0.80	F	Ripe	Empty	healthy	healthy
SC-5-03	184	37.9	7.2	9	0.61	M	Ripe	Unidentified material in stomach	healthy	healthy
SC-6-03	160	25.7	8.9	6	0.63	M	Ripe	Empty	healthy	healthy
SC-7-03	121	12.2	10.6	4	0.69	M	Ripe	Empty	healthy	healthy
SC-8-03	182	40.3	7.8	6	0.67	F	Ripe,well-developed, large	Empty	healthy	healthy
SC-9-03	146	21.4	10.6	7	0.69	M	Ripe	Empty	healthy	healthy
SC-10-03	142	20.0	8.7	7	0.70	F	Ripe	Empty, algae lower in intestine	healthy	healthy
SC-11-03	85	4.2	9.9	3	0.68	F	Ripe, large GSI, may spawn.	Empty	healthy	healthy
SC-12-03	176	34.8	-	-	0.64	-	-	-	-	-
SC-13-03	157	31.3	-	-	0.81	-	-	-	-	-
SC-14-03	159	31.2	-	-	0.78	-	-	-	-	-
SC-15-03	141	21.2	-	-	0.76	-	-	-	-	-
SC-16-03	139	17.7	-	-	0.66	-	-	-	-	-
SC-17-03	174	41.2	-	-	0.78	-	-	-	-	-
SC-18-03	132	14.9	-	-	0.65	-	-	-	-	-
SC-19-03	161	24.0	-	-	0.58	-	-	-	-	-
Mean	149	24.9	10.5	5.7	0.70	-	-	-	-	-
SD	23.8	10.1	2.7	1.7	0.07	-	-	-	-	-

[1]K = Condition Factor = (body weight x 10^5) / total length^3

Note: SC-1-03 to SC-11-03 used for tissue chemistry analyses, the other 8 were measured live and released.

Table 8. Mean (range) total length (mm), weight (g) and condition (K) of Garrow Lake sculpin from pre-mine (1976, Fallis et al. 1987; 1977, BC Research 1978) and 2003.

Year	n	Total Length (mm)			Body Weight (g)			Condition Factor (K)		
		Mean	Range	SD	Mean	Range	SD	Mean	Range	SD
1976	51	155	120 - 194	2	26.6	10 - 45		- (0.72^)	-	-
1977	33	112	38 - 168	40	10.8	0.9 - 26.6	8.2	0.56[#] (0.77^)	(0.43 - 0.70)[#]	0.07[#]
2003	19	149	85 - 184	24	24.9	4.2 - 41.2	10.1	0.70 (0.75^)	(0.58 - 0.81)	0.07

[1]K = Condition Factor = (body weight x 10^5) / total length^3

^ calculated from mean length and weight

[#] using fish with minimum length of 90mm

Table 9. Length - weight relationship for Garrow Lake sculpin, 1976, 1977 and 2003.

Year	n	Regression	R^2
1976[A]	51	$Log_{10}(weight) = 2.82 * Log_{10}(length) - 4.78$	0.99[A]
1977	33	$Log_{10}(weight) = 2.40 * Log_{10}(length) - 3.98$	0.97
2003	19	$Log_{10}(weight) = 2.96 * Log_{10}(length) - 5.06$	0.97

[A] Regression equation for 1976 data derived using curvilinear plot.
1976 (Fallis et al. 1987); 1977 (BC Research, 1978)

Table 10. Mean (range) of fourhorn sculpin whole body metal concentration (mg/kg ww) from Garrow Lake during pre-mine (1976, Fallis et al. 1987; 1977, BC Research 1978; 1980, BC Research 1981) and 2003 (post-mine).

	Pre - Mine						Post-Mine	
	1976 (n=10)		1977 (n=34)		1980 (n = 35)		2003 (n=11)	
	Mean	Range	Mean	Range	Mean	Range	Mean	Range
Body Length (mm)			112	38 - 168	132	78 - 164	145	85 - 184
Body Weight (g)			11	1 - 27	10	2 - 19.2	23	4 - 40
Total Metals (mg/kg ww)								
Aluminum							16	3 - 40
Antimony							<0.01	
Arsenic	0.74	0.47 - 1.18	1.15	0.53 - 2.58	0.55	0.22 - 1.1	0.88	0.53 - 1.48
Barium							3.33	1.59 - 5.36
Beryllium							<0.1	
Cadmium	0.07	0.04 - 0.12	0.11	0.01 - 0.24	0.1	0.02 - 0.33	0.057	0.026 - 0.103
Chromium							<0.1	
Cobalt							0.12	0.07 - 0.19
Copper	1.17	0.53 - 1.67	2.16	1.09 - 12.69	2.4	1.0 - 10.7	0.95	0.46 - 1.55
Lead	0.58	0.25 - 0.96	0.38	0.09 - 0.84	0.24	0.10 - 0.67	0.81	0.43 - 1.71
Manganese	0.77	0.56 - 1.03					3.15	1.24 - 6.46
Mercury	0.01	<0.01 - 0.02					0.006	<0.005 - 0.012
Molybdenum							<0.01	<0.01 - 0.01
Nickel	0.35	0.06 - 1.06					0.1	<0.1 - 0.2
Strontium							32	21 - 46.1
Zinc	28.9	15.6 - 41.8	34.4	16.0 - 66.7	34.5	16.3 - 55	72.3	50.4 - 120

PHOTOS

Photo 1 Garrow Lake showing ice cover August 4, 2003.



Photo 2 Launching the boat in Garrow Lake, August 8, 2003.



Photo 3 Garrow Lake showing gravel shoreline and mostly ice-free, August 8, 2003.



Photo 4 Garrow Lake Fourhorn sculpin *Myoxocephalus quadricornis*.



Photo 5 Garrow Lake fourhorn sculpin (140 mm total length) prior to dissection.



APPENDICES

Appendix A Department of Fisheries and Oceans Habitat Authorization

Fisheries and Oceans | Pêches et Océans

AUTHORIZATION FOR WORKS OR UNDERTAKINGS AFFECTING FISH HABITAT

AUTHORISATION POUR DES OUVRAGES OU ENTREPRISES MODIFIANT L'HABITAT DU POISSON

DFO File No. 02-HCAA-000-000063
Authorization No./N° de l'autorisation

Authorization Issued To/Autorisation délivrée à

Name: Bruce Donald

Address: Teck Cominco Ltd.
Polaris Operations
Box 188
Resolute Bay, Nunavut
Canada X0A 0E0

Telephone: (867) 253-2201

Facsimile: (867) 253- 6862

Location of Project/Emplacement du projet

Polaris Mine is located on Little Cornwallis Island (centred at 391500 E, 8 369 000 degrees N UTM zone 15) in the Qikiqtalluk Region of Nunavut (approximately 100 km northwest of Resolute Bay). The project site encompasses fish habitat at Garrow Lake, Garrow Creek, and Crozier Strait.

Valid Authorization Period/Période de validité

From/De: June 2, 2003 **To/À:** October 30th , 2004

Description of HADD Works or Undertakings/Description des ouvrages ou entreprises

In order to decommission Teck Cominco's (TCL) Polaris Mine, draining of water from the surface layer of Garrow Lake (the mine's tailings facility) and partial removal of Garrow Lake Dam will be required. This will result in the harmful alteration, disruption and/or destruction of fish habitat (HADD) due to lowering of the level of the lake and excavation of benthic fish habitat adjacent to the dam. Partial removal of a sheet-pile dock on Crozier Strait, and excavation to contour the adjacent marine foreshore area will also temporarily alter fish habitat during construction. The above works will hereafter be referred to as the "Project Activities".

Summary of Habitat Loss

- Lowering the lake level of Garrow Lake and removal of the Garrow Lake Dam will dewater approximately 30 ha. of fish habitat. Garrow Lake has been documented to be habitat for fourhorn

sculpin *(Myoxocephalus quadricornus)* and has the potential to provide habitat for other fish species. Garrow Lake drains into Garrow Bay via Garrow Creek and provides supporting habitat for other fish species in Crozier Strait.

- Partial removal of the dock and excavation of the marine foreshore area at Polaris will alter 2512 m^2 of fish habitat. The marine foreshore area at Polaris is habitat for arctic charr, arctic cod, and marine mammals (e.g., narwhal, ringed seals, walrus).

Conditions of Authorization/Conditions de l'autorisation

1.0 All works and undertakings shall be undertaken in accordance with the documents approved by DFO entitled:

1.1 Application for Authorization for Works or Undertakings Affecting Fish Habitat submitted to DFO, dated October 5th, 2001 and signed by Bruce Donald, TCL.

1.2 The approved documents include the works or undertakings, proposed mitigative measures and compensation requirements (the *Project Plan*).

2.0 To compensate for the harmful alteration, disruption or destruction of fish habitat as a result of the Project Activities, the following shall be implemented, maintained and monitored by TCL, as indicated in the *Project Plan* or otherwise specified by DFO:

2.1 To rehabilitate and enhance fish habitat in Garrow Lake, upon completion of water withdrawal and dam removal, TCL shall conduct the following as indicated in the *Project Plan*:

Restore a natural stream channel to Garrow Bay by removing at least 19,000 cubic metres of dam fill material. The constructed 500 m long by 15 metre wide stream channel through the decommissioned dam will emulate natural stream conditions with a gravel/cobble streambed. Enhancement efforts will result in the banks of the remaining dam having a slope of at least 4:1.
The enhanced stream channel draining Garrow Lake will be on average 11 m wide and restore natural drainage patterns in the Garrow Lake area. Clean rock rip-rap will be placed to prevent erosion in the vicinity of the decommissioned dam;

2.1.3 A Fish Habitat Monitoring Report shall be submitted to DFO, including detailed photographs of Garrow Lake, stream channel development, prior to completion of the work. The intent of this Monitoring Report shall be to assess the success of fish habitat compensation upon implementation.

AUTHORIZATION FOR WORKS OR UNDERTAKINGS AFFECTING FISH HABITAT

AUTHORISATION POUR DES OUVRAGES OU ENTREPRISES MODIFIANT L'HABITAT DU POISSON

DFO File No. 02-HCAA-000-000063
Authorization No./N° de l'autorisation

2.2 To rehabilitate and enhance fish habitat in the area of the dock and marine foreshore area, TCL shall conduct the following as indicated in the *Project Plan*:

2.2.1 Partial removal of the dock pilings to a depth of 3m below the low tide water level will develop natural inter-tidal conditions with slope and substrate adequate to control erosion into Crozier Strait.

2.2.2 Excavation of the inter-tidal shoreline adjacent to the dock to develop 12,800 m^2 of marine nearshore habitat with a slope of less than 17.5:1 to prevent erosion.

2.2.3 A Fish Habitat Monitoring Report shall be submitted to DFO, including detailed photographs of the marine foreshore area adjacent to the dock. Underwater photographs or video footage of the dock will be provided to DFO. The intent of this Monitoring Report shall be to assess the success of fish habitat compensation upon implementation.

3.1 The following mitigation measures are intended to minimize or prevent further harmful alteration, disruption or destruction of fish habitat adjacent to Garrow Lake and Garrow Creek:

3.1.1 Excavation of the dam will be conducted prior to spring break-up in 2004 and all silt and loose fines shall be removed from the construction area prior to spring break-up.

3.1.2 Rock rip-rap will be placed on the banks of the stream channel adjacent to the dam to prevent erosion and sedimentation.

3.1.3 Appropriate mitigation measures will be implemented to control TSS, including the construction of a dam at the discharge of Garrow Lake, if water quality deteriorates due to release of sediment. Other contingencies may be required as mitigation measures to protect fish habitat such as silt fences.

3.2 Appropriate mitigation measures will be implemented in the marine foreshore area, at and adjacent to the dock, as follows:

3.2.1 To minimize erosion in the marine foreshore area mitigation measures will be implemented to prevent deposition of sediment into the marine waters by use of silt fences and a floating silt curtain along the perimeter of the marine foreshore area if this is deemed necessary.
Water quality sampling for turbidity will be conducted daily during work and mitigation measures will be implemented to address potential sediment release.

AUTHORIZATION FOR WORKS OR UNDERTAKINGS AFFECTING FISH HABITAT

AUTHORISATION POUR DES OUVRAGES OU ENTREPRISES MODIFIANT L'HABITAT DU POISSON

DFO File No. 02-HCAA-000-000063
Authorization No./N° de l'autorisation

4.0 Monitoring will be conducted to ensure that compensation measures are successfully implemented and identify potential long-term project effects:

4.1 Sampling of TSS and turbidity will be undertaken by TCL in different strata of Garrow Lake to monitor stability of the halocline and to confirm the absence of contaminants in the upper strata of the lake.

4.2 A study of the metal concentrations in sediments adjacent to the shore of Garrow Lake, Garrow Creek, and the centre of Garrow Bay will be commissioned by TCL. TCL will provide a study design prior to July 2003 for approval by DFO.

4.3 TCL will conduct a study on fish in Garrow Lake and Garrow Bay to examine metal levels in fish muscle tissue. A study design will be proposed by TCL to collect fish tissue samples for analysis by DFO. TCL will propose a sampling protocol for this study prior to July 2003.

4.4 Erosion will be monitored on the shore of Garrow Lake and Garrow Creek Stream channel. The study objective will be to quantify erosion rates adjacent to the lake and stream channel. This study will be proposed by TCL for DFO approval prior to July 2003.

4.5 TCL will conduct water quality sampling for TSS and turbidity at the Garrow Lake outflow in Garrow Creek. TCL will provide a Water Quality Sampling Report of TSS levels to the DFO Eastern Arctic Office on an annual basis for the duration of this authorization. Water quality sampling for TSS will not cease at the Garrow Lake outflow prior to 2004.

4.6 TCL will conduct water quality sampling for TSS and turbidity along the marine foreshore area prior to, during, and immediately following work in the inter-tidal zone. At least seven water quality samples will be routinely collected on a daily basis in the marine foreshore area during work in the inter-tidal zone. Two water quality samples per day will be collected adjacent to the dock.

5.0 A DFO Fishery Officer shall be notified at the Iqaluit Office ((867) 979-8000) of the proposed start time prior to commencement of the work.

6.0 Any deviation from the *Project Plan*, the construction schedule or the mitigation and compensation measures stated above that may potentially affect fish or fish habitat, must be discussed and approved in writing by DFO prior to implementation.

7.0 A copy of this Authorization shall be at the Polaris work site during all work periods. Work crews shall be made familiar with the conditions of this Authorization prior to implementation of the works or undertakings.

AUTHORIZATION FOR WORKS OR UNDERTAKINGS AFFECTING FISH HABITAT

AUTHORISATION POUR DES OUVRAGES OU ENTREPRISES MODIFIANT L'HABITAT DU POISSON

DFO File No. 02-HCAA-000-000063
Authorization No./N° de l'autorisation

The holder of this Authorization is hereby authorized under the authority of subsection 35(2) of the *Fisheries Act*, R.S.C., 1985, c. F. 14, to carry out the work or undertaking described herein. This Authorization is valid only with respect to fish habitat and for no other purposes. It does not purport to release the applicant from any obligation to obtain permission from or to comply with the requirements of any other regulatory agencies.

Failure to comply with any condition of this Authorization may result in charges being laid under the *Fisheries Act*.

This Authorization form should be held on site and work crews should be made familiar with the terms and conditions of this authorization.

Le détenteur de la présente est autorisé en vertu du paragraphe 35(2) de la *Loi sur les pêches*, L.R.C. 1985, ch. F. 14, à exploiter les ouvrages ou entreprises décrits aux présentes.
L'autorisation n'est valide qu'en ce qui concerne l'habitat du poisson et pour aucune autre fin. Elle ne dispense pas le requérant de l'obligation d'obtenir la permission d'autres organismes réglementaires concernés ou de se conformer à leurs exigences.

En vertu de la *Loi sur les pêches*, des accusations pourront être porteés contre ceux qui ne respectent pas les conditions prévues dans la présente autorisation.

Cette autorisation doit être conservée sur les lieux des travaux, et les équipes de travail devraient en connaître les conditions.

Date of Issuance: Following NIRB Environmental Assessment

Signed by:

Burt Hunt
Area Director
Eastern Arctic Area
Fisheries and Oceans Canada
Central and Arctic Region

Prepared by:

Jordan DeGroot
Area Habitat Biologist
Fish Habitat Management
Eastern Arctic Area
Fisheries and Oceans Canada

Bruce Donald- Reclamation Manager, Environment and Corporate Affairs

Canada

AUTHORIZATION FOR WORKS OR UNDERTAKINGS AFFECTING FISH HABITAT

AUTHORISATION POUR DES OUVRAGES OU ENTREPRISES MODIFIANT L'HABITAT DU POISSON

DFO File No. 02-HCAA-000-000063
Authorization No./N° de l'autorisation

Witness:

Teck Cominco Ltd.

Signature: Brian McKenzie

Teck Cominco Ltd.

Signature:

Copy signed by TCL received by DFO

Signature: Stephanie Critch

Date: July 23, 2003

Appendix B Garrow Lake Water Chemistry Data

Appendix B. Vertical profile of water chemistry parameters pre-mining (Fallis et al. 1987) and in 2003, after mining.

	Pre-Mine Profile			Post-Mine Profile							
	June 1976 (Fallis et al. 1987)			Winter 2003 (Teck Cominco)			August 2003				
Depth (m)	Temperature (oC)	Salinity ppt	D.O. mg/L	Temperature (oC)	Conductivity (mS)	D.O. mg/L	Temperature (oC)	Conductivity (mS)	pH	Salinity ppt	D.O. mg/L
1	0.85	4.9		-0.5	14.5	20.7	0	6.74	8.18	3.8	11.5
2	0.85	4.9	15.9	-0.5	14.8	20.2	0.24	6.93	8.18	3.9	11.5
3	0.85	4.9		-0.3	13.8	18.9	0.86	7.38	8.14	4.1	11.5
4	0.85	4.8	16.1	3.3	14.6	17.6	3	11.45	7.98	6	11.5
5	0.85	4.9		3.5	14.5	17.2	3.28	12.18	8	7	11.5
6	0.85	5.3		3.5	14.5	17.1	3.35	12.28	8	7	11.5
7	0.85	4.9		3.5	14.6	16.9	3.42	12.37	8.07	7.1	11.5
8	0.85	5.1		3.6	14.6	16.1	3.25	12.43	8.08	7.1	11.5
9	0.85	4.8		4.0	15.3	13.2	3.45	12.51	8.07	7.2	11.5
10	0.85	4.8	16	5.2	27.1	7.7	5.01	18	7.83	11.5	11.5
10.5							6.0		7.26	22.5	6.7
11	0.85	4.9		6.6	77.4	0.4	7.05	65.6	7.16	40.2	4.3
12	0.85	4.9		7.5	94.0	0.2	8.2	78.9	7.2	54.9	1.1
13	3.76	28.6		8.0	94.2	0.2	8.37	79.8	7.24	55.3	0.8
14	6.34	34.6		8.2	94.4	0.2	8.37	80.1	7.26	55.6	0.45
15	7.4	54.6	9.8	8.3	94.4	0.2	8.33	80.3	7.27	55.7	0.23
16	8.06	65.2		8.4	94.5	0.2	8.28	80.4	7.3	55.7	0.0
17	8.51	71.3		8.4	94.5	0.2	8.27	80.4	7.3	55.7	0.0
18	8.96	77.0		8.4	94.5	0.2	8.25	80.5	7.31	55.7	0.0
19	9.29	79.8	8.5	8.4	94.5	0.2	8.25	80.5	7.31	55.7	0.0
20	9.47	81.3	0.0	8.4	94.5	0.2	8.24	80.5	7.32	55.8	0.0
21	9.39	85.0		8.4	94.5	0.2	8.24	80.4	7.33	55.8	0.0
22	9.18	87.5		8.4	94.5	0.2	8.24	80.5	7.33	55.8	0.0
23	9.0	88.8		8.4	94.5	0.2	8.24	80.5	7.33	55.8	0.0
24	8.9	89.0		8.4	94.5	0.2	8.24	80.5	7.34	55.8	0.0
25	8.82	89.2		8.4	94.6	0.2	8.24	80.5	7.34	55.8	0.0
26	8.74	89.4		8.4	94.6	0.2	8.24	80.5	7.34	55.8	0.0
27	8.68	89.3		8.4	94.6	0.2	8.22	80.5	7.35	55.8	0.0
28	8.59	89.3		8.4	94.6	0.2	8.23	80.5	7.35	55.8	0.0
29	8.5	89.3		8.4	94.5	0.2	8.24	80.5	7.35	55.8	0.0
30	8.42	89.2	0.0	8.4	94.7	0.2	8.25	80.5	7.35	55.8	0.0
31	8.35	89.1		8.4	94.6	0.2	8.25	80.5	7.35	55.8	0.0
32	8.28	89.1		8.4	94.6	0.2	8.25	80.5	7.35	55.8	0.0
33	8.19	88.8		8.4	94.7	0.2	8.25	80.5	7.35	55.8	0.0
34	8.11	89.1		8.4	94.7	0.2	8.25	80.5	7.35	55.8	0.0
35	8.04	88.5		8.4	94.6	0.2	8.27	80.5	7.35	55.8	0.0
36	7.95	88.7		8.4	94.6	0.2	8.27	80.5	7.35	56	0.0
37	7.88	88.4		8.4	94.7	0.2	8.27	80.5	7.35	56.4	0.0
38	7.8	89.0		8.4	94.7	0.2	8.4	83.4	7.35	58.1	0.0
39	7.76	88.6		8.4	94.7	0.2	8.43	83.9	7.35	58.4	0.0

Appendix C Fish Metals Concentrations, Garrow Lake 2003.

Appendix C. Total metal concentration (mg/kg ww) for individual fourhorn sculpin, Garrow Lake, August 2003.

Sample ID Total Metals (mg/kg ww)	SC-1	SC-2	SC-3	SC-4	SC-5	SC-6	SC-7	SC-8	SC-9	SC-10	SC-11	Mean	SD	Range
Aluminum	20	13	21	19	5	9	23	3	21	40	7	16	10.61	3 - 40
Antimony	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	0.00	
Arsenic	0.59	0.93	0.59	1.10	1.42	1.48	0.66	0.82	0.77	0.81	0.53	0.88	0.33	0.53 - 1.48
Barium	3.63	2.93	3.70	3.00	2.55	2.32	2.83	1.59	5.36	5.15	3.61	3.33	1.14	1.59 - 5.36
Beryllium	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	0.0	
Cadmium	0.087	0.051	0.044	0.038	0.062	0.042	0.103	0.026	0.051	0.075	0.043	0.057	0.023	0.026 - 0.103
Chromium	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	0.0	
Cobalt	0.14	0.15	0.09	0.09	0.09	0.10	0.13	0.07	0.14	0.19	0.10	0.12	0.04	0.07 - 0.19
Copper	0.74	0.65	0.59	1.06	0.75	0.94	0.74	0.46	1.55	1.43	1.52	0.95	0.39	0.46 - 1.55
Lead	0.80	0.57	0.83	0.73	0.87	0.92	0.78	0.43	0.63	1.71	0.62	0.81	0.33	0.43 - 1.71
Manganese	3.37	6.46	2.29	3.15	1.24	2.78	3.34	1.60	3.36	4.31	2.77	3.15	1.40	1.24 - 6.46
Mercury	<0.005	<0.005	<0.005	0.005	0.012	0.006	<0.005	<0.005	<0.005	0.005	0.006	0.006	0.002	<0.005 - 0.012
Molybdenum	0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	0.01	0.01	<0.01	<0.01	0.00	<0.01 - 0.01
Nickel	0.1	0.1	0.1	0.1	0.1	0.1	0.2	<0.1	0.2	0.2	0.2	0.1	0.1	<0.1 - 0.2
Strontium	21	30.4	27.9	36	46.1	41.5	25.1	35.7	30.8	29.8	25.6	31.8	7.4	21 - 46.1
Zinc	53.1	71.5	60.9	78.6	120	86.5	54.3	50.4	85.1	78	57.3	72.3	20.6	50.4 - 120

APPENDIX 20

REPORT AND STUDY

CD'S AND DVD'S
