Remediation of FOX-C Former Military Station
Ekalugad, Fjord, NU

ID	Task Name	OPI	Duration	Start	Finish
1	Review previous reports	PWGSC	42 days	Thu 4/1/04	Fri 5/28/04
2	Program Options Review & Selection	PWGSC	15 days	Mon 5/10/04	Fri 5/28/04
3	**Project Coordination**		**956 days**	**Fri 4/2/04**	**Thu 11/29/07**
13	**Community Consultations**		**962 days**	**Thu 4/1/04**	**Thu 12/6/07**
14	Establish Working Groups	DIAND	10 days	Thu 4/1/04	Wed 4/14/04
15	Meeting #1 - Project Introduction to Communities (Clyde River & Broughton Island)	DIAND	4 days	Mon 5/17/04	Thu 5/20/04
16	Meeting #2 - Presentation of Project Assessment Details & Preliminary Site Visit	DIAND	5 days	Mon 7/12/04	Fri 7/16/04
17	Meeting #3 - Final Work Plan Delivery	DIAND	3 days	Mon 11/29/04	Wed 12/1/04
18	Meeting #4 - Bidder's Conference	PW/DIAND	2 days	Thu 3/10/05	Fri 3/11/05
19	Meeting #5 - Site Remediation planning meeting	DIAND	2 days	Wed 12/14/05	Thu 12/15/05
20	Meeting #6 - Discussions with communities prior to beginning site activities in July 2006	PW/DIAND	2 days	Thu 6/8/06	Fri 6/9/06
21	Meeting #7 - 2006 Project review and planning meeting	PW/DIAND	2 days	Mon 12/5/05	Tue 12/6/05
22	Meeting #8 - Discussions with communities prior to beginning site activities in July 2007	PW/DIAND	2 days	Tue 6/5/07	Wed 6/6/07
23	Meeting #9 - 2007 Project review and closeout meeting	PW/DIAND	2 days	Wed 12/5/07	Thu 12/6/07
24	**Regulatory Approvals - Assessment Activities**		**83 days**	**Thu 4/1/04**	**Fri 7/23/04**
29	**Support Services Contract(s)**		**51 days**	**Mon 5/31/04**	**Fri 8/6/04**
30	Prepare Equipment & Camp Supply Spec #1 for Site Assessment Activities	PWGSC	14 days	Mon 5/31/04	Wed 6/16/04
31	French Translation for Spec #1	PWGSC	1 day	Thu 6/17/04	Thu 6/17/04
32	Tender Period Spec #1	PWGSC	20 days	Fri 6/18/04	Thu 7/15/04
33	Award Contract #1	PWGSC	5 days	Fri 7/16/04	Thu 7/22/04
34	Mobilize Equipment and Camp to Ekalugad Fjord	PWGSC	5 days	Mon 8/2/04	Fri 8/6/04
35	**Obtain assessment contracts**		**158 days**	**Mon 6/21/04**	**Wed 1/26/05**
36		PWGSC	15 days	Mon 6/21/04	Fri 7/9/04
37	Establish Criteria for Site Restoration	DIAND	1 day	Fri 7/2/04	Fri 7/2/04
38	Additional site assessment activities	PWGSC	15 days	Mon 8/9/04	Fri 8/27/04
39	Laboratory Analyses	PWGSC	21 days	Fri 8/20/04	Fri 9/17/04
40	Obtain All Draft Reporting	PWGSC	6 days	Mon 10/11/04	Mon 10/18/04
41	Prepare and submit draft work plan for entire site clean up to DIAND	PWGSC	25 days	Fri 11/5/04	Thu 12/9/04
42	Review and Approval of work plan by DIAND and Community Consultation Group	DIAND	25 days	Fri 12/10/04	Thu 1/13/05
43	Finalize work plan and project description	PWGSC	8 days	Mon 1/17/05	Wed 1/26/05
44	**Regulatory Approvals - Site Construction**		**96 days**	**Wed 1/26/05**	**Wed 6/8/05**
45	Complete an Environmental Impact Assessment	PWGSC	23 days	Wed 1/26/05	Fri 2/25/05
46	Prepare & submit land/water use applications and CEAA to Agency	PWGSC	8 days	Wed 1/26/05	Fri 2/4/05
47	DIAND Review of Regulatory Packages	DIAND	9 days	Mon 2/7/05	Thu 2/17/05
48	Present project plan to NIRB and other agencies	PW/DIAND	1 day	Mon 2/28/05	Mon 2/28/05
49	Project review by Nunavut WB/LB/NIRB/Federal Res. Authorities	PWGSC	80 days	Thu 2/17/05	Wed 6/8/05
50	**Site Remediation Contract**		**757 days**	**Thu 12/23/04**	**Fri 11/16/07**
51	Prepare Site Remediation Specification	PW	30 days	Thu 12/23/04	Wed 2/2/05
52	DIAND Review of Specification	PWGSC	5 days	Wed 2/2/05	Tue 2/8/05
53	Specification edits	PW	2 days	Wed 2/9/05	Thu 2/10/05
54	Prepare and submit Requisition, RMP, PAAA	PW	4 days	Mon 1/24/05	Thu 1/27/05
55	Procurement Plan Review and Approval	PW	5 days	Thu 1/27/05	Wed 2/2/05
56	Provide advance notice of remediation project to Land Claim offices	PW/DIAND	1 day	Mon 2/7/05	Mon 2/7/05
57	Post RFP (with 90% remediation specification) on MERX	PW	1 day	Mon 2/14/05	Mon 2/14/05
58	Tender Period	PW	30 days	Tue 2/15/05	Mon 3/28/05
59	Bidders conference in Iqaluit	PW/DIAND	2 days	Wed 3/9/05	Thu 3/10/05
60	Tender close	PW	1 day	Thu 3/31/05	Thu 3/31/05
61	Bid evaluation	PW/DIAND	5 days	Fri 4/1/05	Thu 4/7/05
62	Clarification and negotiation with proposed contractor	PW	21 days	Thu 4/7/05	Thu 5/5/05
63	Prepare contract request and regional QA	PW	10 days	Fri 5/6/05	Thu 5/19/05
64	Minister Approval to Award	PW	20 days	Fri 5/20/05	Thu 6/16/05
65	Obtain Documents from Contractor	PW	5 days	Fri 6/17/05	Thu 6/23/05
66	Contract Award	PW	1 day	Fri 6/24/05	Fri 6/24/05
67	Prepare equipment	PW	28 days	Mon 6/27/05	Wed 8/3/05
68	Transport equipment to Ekalugad Fjord	PW	10 days	Thu 8/4/05	Wed 8/17/05
69	2005 Remediation activities	PW	25 days	Mon 8/8/05	Fri 9/9/05
70	2006 Remediation activities	PW	44 days	Mon 7/3/06	Thu 8/31/06
71	2007 Remediation activities	PW	31 days	Mon 7/2/07	Mon 8/13/07
72	Demobilization of equipment from site	PW	10 days	Mon 8/13/07	Fri 8/24/07
73	Ship hazardous waste south for disposal	PW	10 days	Mon 8/13/07	Fri 8/24/07
74	Obtain reporting on remediation activities	PW	60 days	Mon 8/27/07	Fri 11/16/07

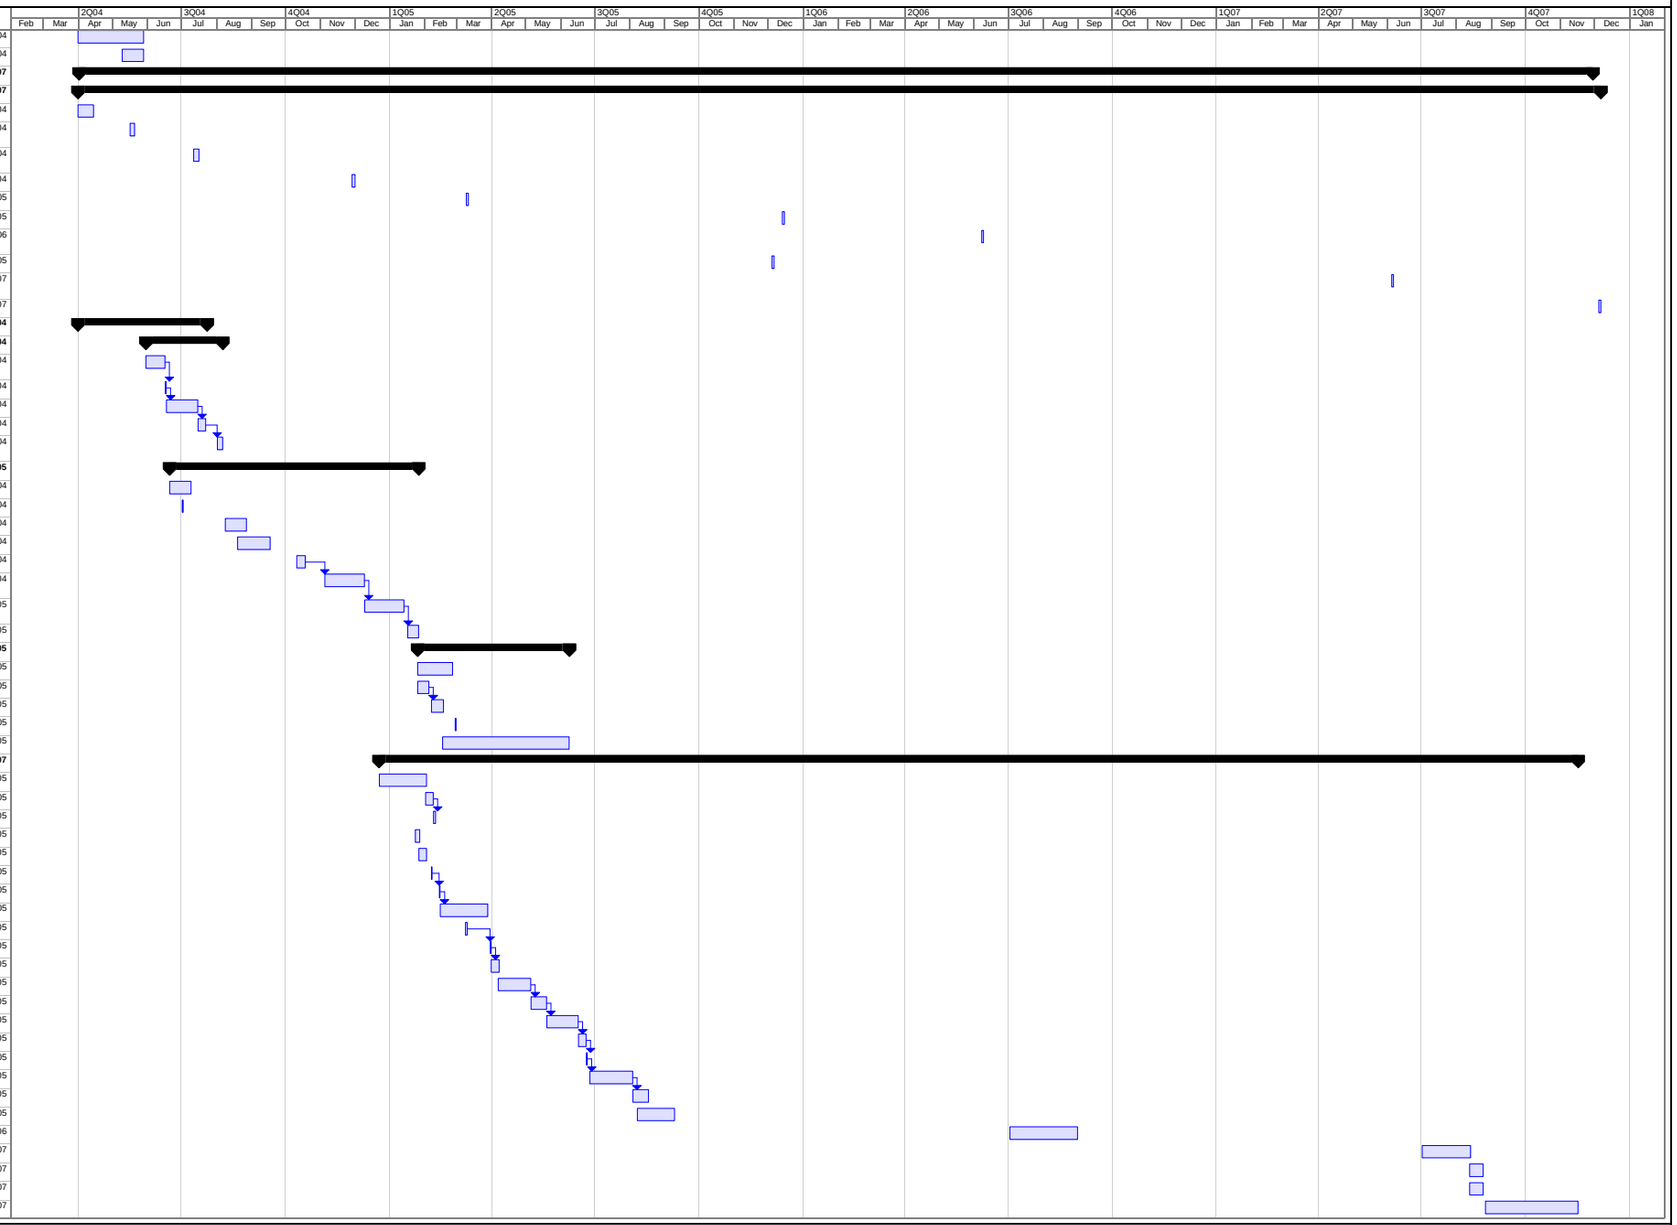

Figure 1: Proposed Project Schedule

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
