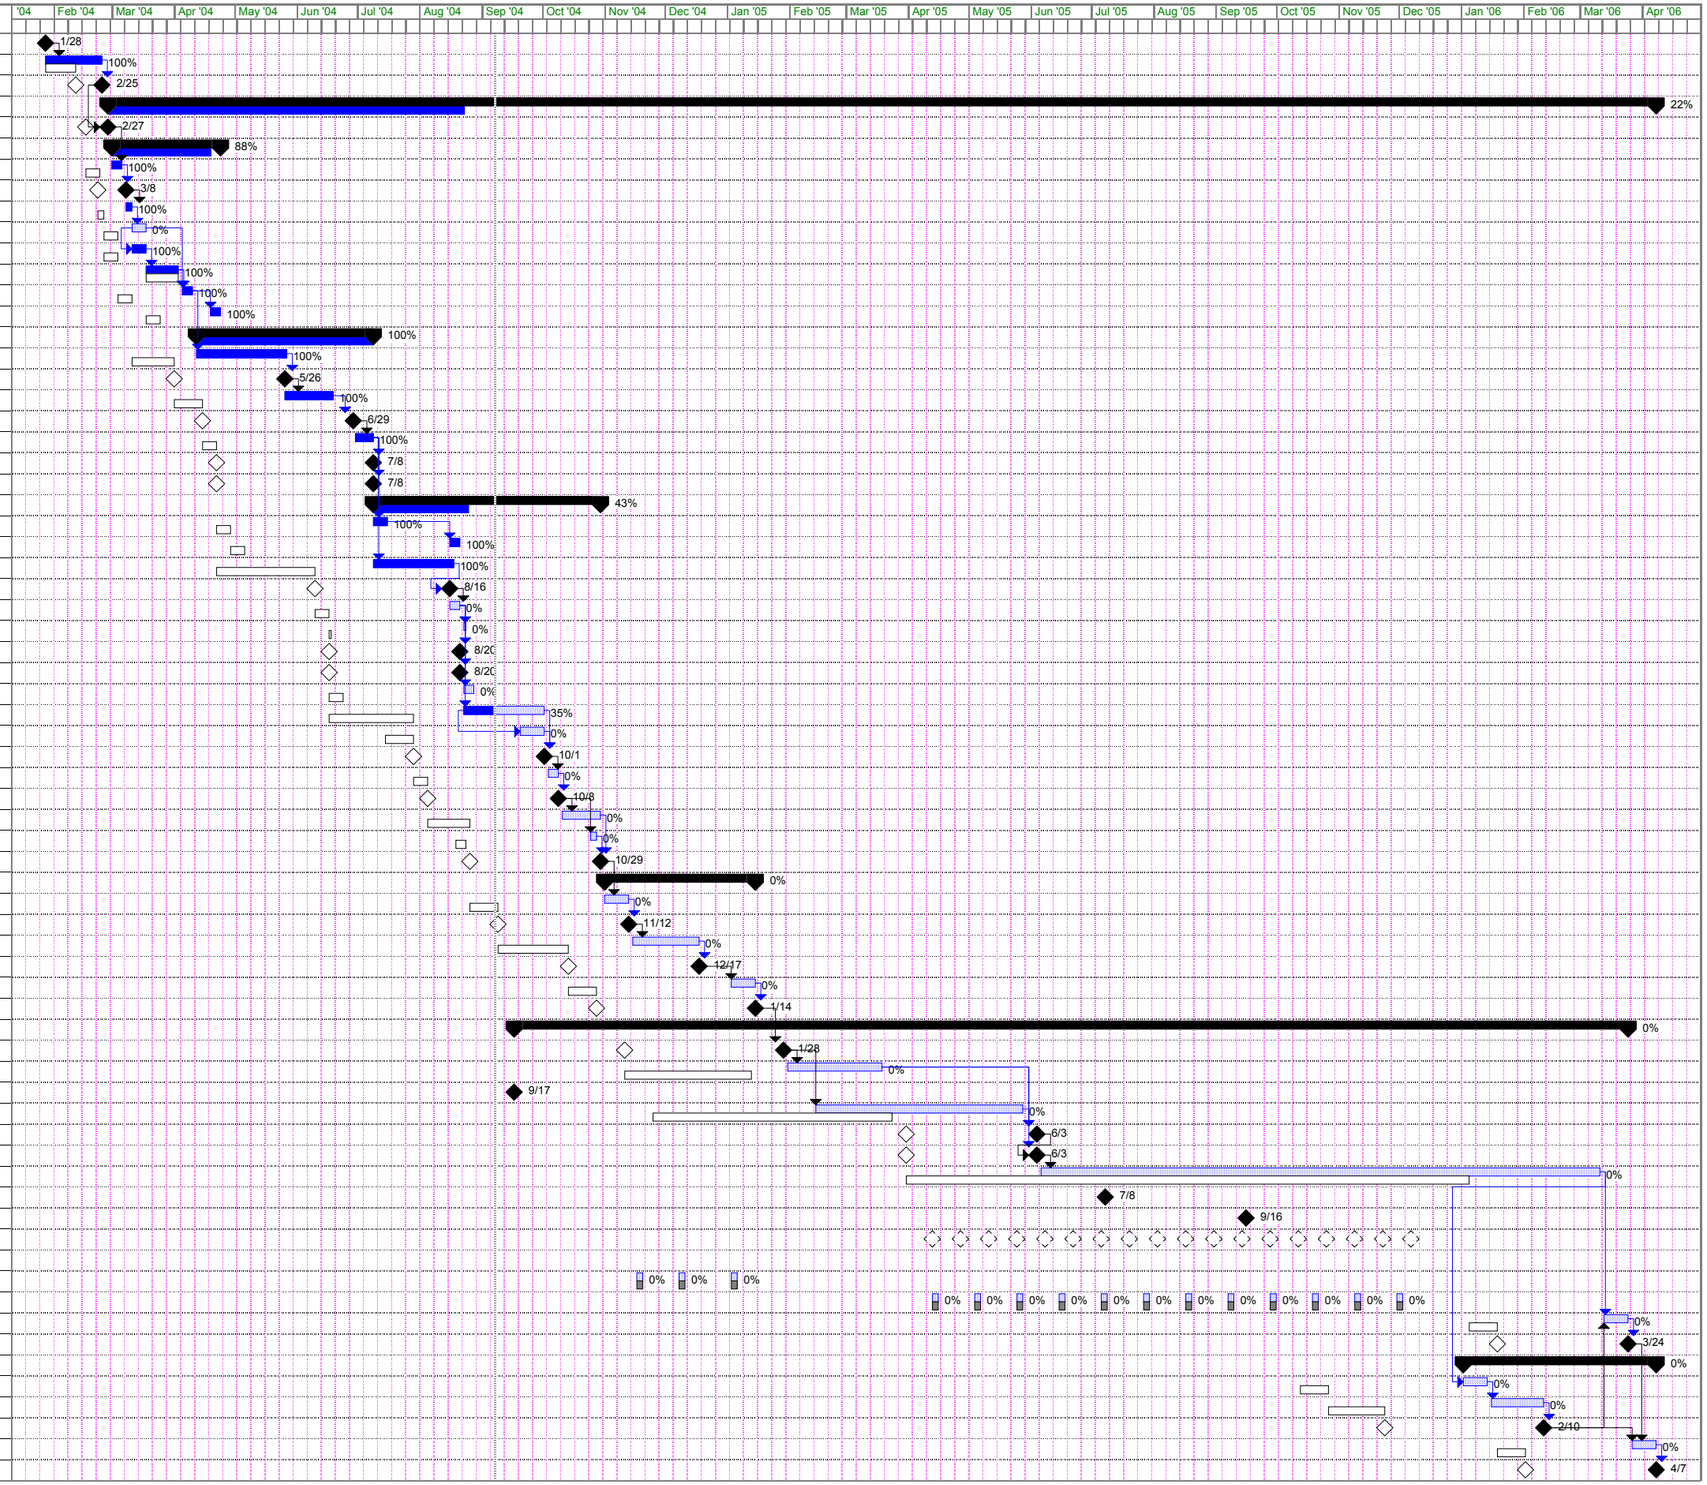ID	Task Name	Duration	Base Start	Actual Start	Base Fin	Actual Fin
1	Submit Proposal	0 days	Jan 28	NA	Jan 28	NA
2	Proposal Review	20 days	Jan 28	Jan 28	Feb 11	Feb 24
3	Award	0 days	Feb 11	Feb 25	Feb 11	Feb 25
4	**Project Management**	**530 days**	**Feb 16**	**Feb 27**	**Feb 1**	**NA**
5	Project Start	0 days	Feb 16	Feb 27	Feb 16	Feb 27
6	**Project Initiation**	**40 days**	**Feb 17**	**Mar 1**	**Mar 24**	**NA**
7	Project Set-up	1 wk	Feb 17	Mar 1	Feb 23	Mar 5
8	Kick-off Meeting - Telephone	0 days	Feb 23	Mar 8	Feb 23	Mar 8
9	Data Collection	3 days	Feb 23	Mar 8	Feb 25	Mar 10
10	Site Inspection/review	1 wk	Feb 26	NA	Mar 3	NA
11	Review Data/reports	1 wk	Feb 26	Mar 11	Mar 3	Mar 17
12	ESTABLISH TREATMENT GOALS (DELAY)	12 days	Mar 18	Mar 18	Apr 2	Apr 2
13	Confirm Potential Treatment Systems	1 wk	Mar 4	Apr 5	Mar 10	Apr 9
14	Initial Equipment/Components Salvage Review	1 wk	Mar 18	Apr 19	Mar 24	Apr 23
15	**Preliminary Design**	**64 days**	**Mar 11**	**Apr 12**	**Apr 21**	**Jul 8**
16	Prepare Preliminary Design Report	6.6 wks	Mar 11	Apr 12	Mar 31	May 26
17	Submit Draft Preliminary Design Report	0 days	Mar 31	May 26	Mar 31	May 26
18	City of Iqaluit Review	3.6 wks	Apr 1	May 26	Apr 14	Jun 18
19	Preliminary Design Workshop - Telephone	0 days	Apr 14	Jun 29	Apr 14	Jun 29
20	Complete Report	1.4 wks	Apr 15	Jun 30	Apr 21	Jul 8
21	Submit Final Pre-design Report to Regulatory	0 days	Apr 21	Jul 8	Apr 21	Jul 8
22	Submit Final Pre-design Report to City	0 days	Apr 21	Jul 8	Apr 21	Jul 8
23	**Detail Design**	**81 days**	**Apr 22**	**Jul 9**	**Aug 25**	**NA**
24	Geotechnical Investigation	1 wk	Apr 22	Jul 9	Apr 28	Jul 15
25	Site Survey	1 wk	Apr 29	Aug 16	May 5	Aug 20
26	Commence Final Design	5.6 wks	Apr 22	Jul 9	Jun 9	Aug 17
27	Submit 50% Design Submission	0 days	Jun 9	Aug 16	Jun 9	NA
28	City of Iqaluit Review	1 wk	Jun 10	NA	Jun 16	NA
29	Public Open House (if required)	1 day	Jun 17	NA	Jun 17	NA
30	Review Meeting - Telephone	0 days	Jun 16	NA	Jun 16	NA
31	Submit Design to Regulatory	0 days	Jun 16	NA	Jun 16	NA
32	Equipment Salvage Optimization	1 wk	Jun 17	NA	Jun 23	NA
33	Continue Final Design	6 wks	Jun 17	Aug 23	Jul 28	NA
34	Specifications	2 wks	Jul 15	NA	Jul 28	NA
35	Submit 95% Tender Set	0 days	Jul 28	NA	Jul 28	NA
36	City of Iqaluit Review	1 wk	Jul 29	NA	Aug 4	NA
37	Final Review Meeting - Telephone	0 days	Aug 4	NA	Aug 4	NA
38	Finalize Tender Package	3 wks	Aug 5	NA	Aug 25	NA
39	Class "A" Estimate	3 days	Aug 19	NA	Aug 23	NA
40	Tender Document Submission	0 days	Aug 25	NA	Aug 25	NA
41	**Tendering Services**	**45 days**	**Aug 26**	**NA**	**Oct 27**	**NA**
42	Tender Document Printing/Preparation	2 wks	Aug 26	NA	Sep 8	NA
43	Tender Date	0 days	Sep 8	NA	Sep 8	NA
44	Tender Inquiries / Addendum	5 wks	Sep 9	NA	Oct 13	NA
45	Tender Close	0 days	Oct 13	NA	Oct 13	NA
46	Review Tenders	2 wks	Oct 14	NA	Oct 27	NA
47	Recommend Award	0 days	Oct 27	NA	Oct 27	NA
48	**Construction Services**	**376 days**	**Sep 17**	**NA**	**Jan 18**	**NA**
49	Preconstruction Meeting - Teleconference	0 days	Nov 10	NA	Nov 10	NA
50	Initial Building Preparation/Demolition/Salvage	7 wks	Nov 11	NA	Jan 12	NA
51	Approximate Last 2004 Sealift	0 days	Sep 17	NA	Sep 17	NA
52	Shop Drawing Review/Equipment Ordering	15 wks	Nov 25	NA	Mar 23	NA
53	Contractor Remobilizes	0 days	Mar 30	NA	Mar 30	NA
54	Main Construction Commences	0 days	Mar 30	NA	Mar 30	NA
55	Construction	38 wks	Mar 31	NA	Jan 4	NA
56	Approximate First 2005 Sealift	0 days	Jul 8	NA	Jul 8	NA
57	Approximate Last 2005 Sealift	0 days	Sep 16	NA	Sep 16	NA
58	**Progress Meetings - Telephone (bi-weekly)**	**170 days**	**Apr 13**	**NA**	**Dec 7**	**NA**
77	**Site Inspection Trips**	**263 days**	**Nov 17**	**NA**	**Dec 2**	**NA**
78	**Initial Site inspection Trips (3)**	**26 days**	**Nov 17**	**NA**	**Jan 5**	**NA**
82	**Discipline Trips (12)**	**168 days**	**Apr 13**	**NA**	**Dec 2**	**NA**
95	Substantial Completion / Commissioning / Training	2 wks	Jan 5	NA	Jan 18	NA
96	Construction Complete	0 days	Jan 18	NA	Jan 18	NA
97	**Post Construction Services**	**70 days**	**Oct 13**	**NA**	**Feb 1**	**NA**
98	Review O&M Data	2 wks	Oct 13	NA	Oct 26	NA
99	Prepare O&M Manual	4 wks	Oct 27	NA	Nov 23	NA
100	Submit Draft O&M Manual	0 days	Nov 23	NA	Nov 23	NA
101	Finalize O&M Manual	2 wks	Jan 19	NA	Feb 1	NA
102	Project Complete	0 days	Feb 1	NA	Feb 1	NA
