ID		Task Name	Duration	Start	Finish	Predece
0		**Fuel pipe replacement**	**121 days**	**Fri 3/14/14**	**Mon 9/1/14**	
1		Design and Tender Documents 100% Complete	0 days	Fri 3/14/14	Fri 3/14/14	
2		Last Day for Heavy Loads to Fly-in to Eureka	0 days	Mon 6/30/14	Mon 6/30/14	
3		Fuel Resupply	0 days	Mon 9/1/14	Mon 9/1/14	
4		**Project Tender**	**40 days**	**Fri 3/14/14**	**Thu 5/8/14**	
5		Gov Canada Prepares and Advertises Tender	1 wk	Fri 3/14/14	Thu 3/20/14	1
6		Tender	28 days	Fri 3/21/14	Tue 4/29/14	5
7		Tender award	7 days	Wed 4/30/14	Thu 5/8/14	6
8		**Construction**	**77 days**	**Fri 5/9/14**	**Mon 8/25/14**	
9		**Mobilization**	**49 days**	**Fri 5/9/14**	**Wed 7/16/14**	**7**
10		Project Start-up Meeting	1 day	Fri 5/9/14	Fri 5/9/14	
11		Prepare shop drawings	1 wk	Mon 5/12/14	Fri 5/16/14	10
12		Shop drawing approval	1 wk	Mon 5/19/14	Fri 5/23/14	11
13		Pipe fabrication	5 wks	Mon 5/26/14	Fri 6/27/14	12
14		Shipping pipes to Yelllowknife	8 days	Mon 6/30/14	Wed 7/9/14	13
15		Airlift pipes to Eureka	1 wk	Thu 7/10/14	Wed 7/16/14	14
16		**Construction**	**19 days**	**Wed 7/30/14**	**Mon 8/25/14**	
17		Contractors Staff to Eureka	3 days	Wed 7/30/14	Fri 8/1/14	15
18		Preparing work site drain pipelines	2 days	Mon 8/4/14	Tue 8/5/14	17
19		**Pipeline area C**	**2 days**	**Wed 8/6/14**	**Thu 8/7/14**	
20		Cut &remove fuel pipe from culvert	1 day	Wed 8/6/14	Wed 8/6/14	18
21		Replace a new double walled pipe thru existing calve	1 day	Thu 8/7/14	Thu 8/7/14	20
22		**Pipeline area B**	**2 days**	**Fri 8/8/14**	**Mon 8/11/14**	**19**
23		Excavate trench adjacent existing pipeline	0.5 days	Fri 8/8/14	Fri 8/8/14	21
24		Put new double walled pipe in the trench	0.5 days	Fri 8/8/14	Fri 8/8/14	23
25		Cut & remove existing pipeline from culvert	0.5 days	Mon 8/11/14	Mon 8/11/14	24
26		Change over and connect new pipe into the fuel pipel	0.5 days	Mon 8/11/14	Mon 8/11/14	25
27		**Pipeline area A**	**2 days**	**Tue 8/12/14**	**Wed 8/13/14**	**22**
28		Excavate trench thru the dike adjacent existing pipelir	0.5 days	Tue 8/12/14	Tue 8/12/14	26
29		Cut and remove existing pipeline from PVC conduit b	0.5 days	Tue 8/12/14	Tue 8/12/14	28
30		Install new double walled piping thru the dike	1 day	Wed 8/13/14	Wed 8/13/14	29
31		X ray testing the welded pipes	1 day	Thu 8/14/14	Thu 8/14/14	30,27
32		Hydrostatic Test	2 days	Fri 8/15/14	Mon 8/18/14	31
33		Backfill trenches	2 days	Tue 8/19/14	Wed 8/20/14	32
34		Replace topsoil and clean-up	1 day	Thu 8/21/14	Thu 8/21/14	33
35		Final Inspection	2 days	Fri 8/22/14	Mon 8/25/14	34
36		Project Complete	0 days	Mon 8/25/14	Mon 8/25/14	35

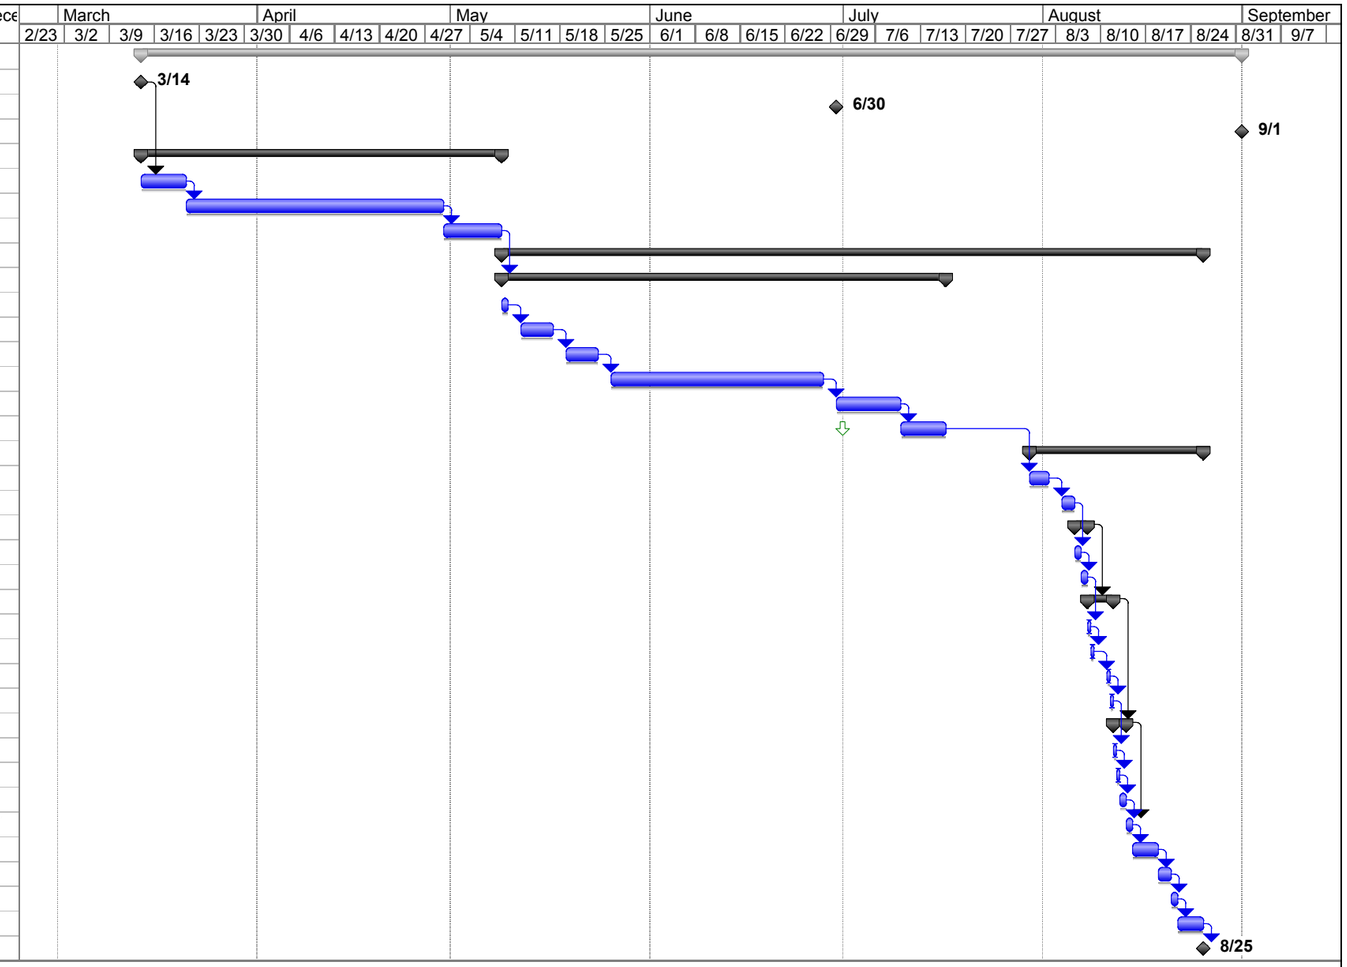

Project: Fuel pipe replacement
Date: Fri 2/14/14

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
